<b>5</b>	<b>B</b> 1	Measure U	Measure S	Measure AA	Measure V		Other Funding	Other Funding	T ( 15	Estimate at	01.1	Bond Funds
Project Number	Project Name	Budget	Budget	Budget	Budget	Interest	Received *	Pending **	Total Budget	Completion	Status	Remaining
U-A	Purchase of BAE Airport Site	\$30,280,878							\$30,280,878	\$30,280,878	Completed	:
U-B	Emeritus College Facility	\$8,909,940					\$693,842		\$9,603,782	\$9,603,782	Completed	:
U-C	Purchase of 1738 Pearl Street	\$749,208							\$749,208	\$749,208	Completed	
U-D	PE Temp. Bldg. Replacement	\$2,797,033							\$2,797,033	\$2,797,033	Completed	,
U-E	Remodel Library Village for Math	\$1,458,690							\$1,458,690	\$1,458,690	Completed	:
U-F	SM Airport Campus Site Improvements	\$4,170,264							\$4,170,264	\$4,170,264	Completed	:
U-G	SM Airport Campus West Building	\$19,709,741							\$19,709,741	\$19,709,741	Completed	
U-H	Theater Arts Renovation	\$19,544,314							\$19,544,314	\$19,544,314	Completed	(
U-I	Earthquake Rpl. Liberal Arts North	\$6,011,584					\$6,496,141		\$12,507,725	\$12,507,725	Completed	Ç
U-K	Earthquake Rpl. Liberal Arts South	\$6,108,150					\$10,625,070		\$16,733,220	\$16,733,220	Completed	!
U-L	Shuttle Replacement Parking	\$18,969,509							\$18,969,509	\$18,969,509	Completed	:
U-M	North Quad Plaza	\$11,388,463							\$11,388,463	\$11,388,463	Completed	!
U-Q	Infrastructure & Safety	\$4,003,084							\$4,003,084	\$4,003,084	Completed	9
U-R	Restroom Improvements	\$17,501							\$17,501	\$17,501	Completed	
S-1	Athletic Fields Phase I, Corsair Field		\$4,372,535				\$67,530		\$4,440,065	\$4,440,065	Completed	9
S-1A	Athletic Fields Phase I, John Adams		\$2,969,807						\$2,969,807	\$2,969,807	Completed	
S-10	Pico Promenade Improvements, Phase I		\$1,018,009						\$1,018,009	\$1,018,009	Completed	:
S-13	Adv. Architecture Related Exp for AA		\$0						\$0	\$0	Completed	:
AA-114	Community Classroom & Facility Projects			\$3,162,183					\$3,162,183	\$3,162,183	Completed	:
U-T	14th and Pico Project	\$319,242		. , . ,					\$319,242	\$319,242	Completed	
U-N	Letters & Sci Demo/Restore	\$0							\$0	\$0	Completed	:
AA-108	Renovation of Corsair Stadium	7.5		\$35,299					\$35,299	\$35,299	Completed	
S-2	Performing Arts Complex		\$37,697,625	700,000			\$2,992,576		\$40,690,201	\$40,690,201	Completed	
U-J	Music Complex	\$2,011,371	ψ3.703.70 <u>2</u> 3				\$2,618,113		\$4,629,484	\$4,629,484	Completed	
S-3, AA-109	Career Opportunity Center	Ψ <b>2</b> ,011,371		\$0			<b>72,010,11</b> 3		\$0	\$0	Completed	
AA-118	Infrastructure & Technology - Utility			\$27,753					\$27,753	\$27,753	Completed	,
AA-111	Business & Facilities Infrastructure			\$1,968,124				1	\$1,968,124	\$1,968,124	Completed	,
AA-117	Infrastructure & Technology - Technology			\$2,434,417					\$2,434,417	\$2,434,417	Completed	
S-7, AA-113	Energy Efficiency Projects		\$293,361	\$3,016,773			\$708,637		\$4,018,771	\$4,018,771	Completed	
S-15	Signage Safety/Information		\$706,713	\$5,010,775			\$706,037		\$706,713	\$706,713	Completed	
AA-102	Infrastructure & Technology - Information Technology Relocation		\$700,713	\$23,140,771			\$19,798		\$23,160,569	\$23,160,569	Completed	
S-8, AA-116	Satellite Campus Parking Facilities and Roadway		\$3,891,747	\$23,140,771			\$19,798		\$6,022,417	\$6,022,417	Completed	
•			\$3,891,747									
AA-107 S-4, AA-104	Madison East Wing Seismic Upgrade Replacement Health/PE/Fitness Central Plant Building		\$11,603,383	\$30,160,902 \$44,428,222			\$208,847		\$30,160,902 \$56,240,452	\$30,160,902 \$56,240,452	Completed Completed	
AA-104			\$11,003,363	\$10,767,251			\$208,847	-	. , ,	· · ·		
	Environmental Performance - Central Plant Connections		Ć45 507						\$10,767,251	\$10,767,251	Completed	
S-14, AA-115	Real Property Acquisition		\$45,597				¢¢ 025 204		\$24,683,983	\$24,683,983	Completed	¢205.6
AA-103	Media and Technology Complex - Academy Site			\$123,714,322			\$6,835,391		\$130,549,713	\$130,549,713	Completed	\$395,64
AA-119	Emergency Lighting, Fire Alarm, and Security System	*** *** ***	4	\$11,520,794	400.004.000	424 524 222	44.004.000		\$11,520,794	\$11,520,794	Completed	\$84,3
15004829	Student Services Building	\$21,131,135	\$45,595,322			\$21,681,308			\$130,224,164	\$130,224,164 I		\$15,004,82
S-5, V-104	Early Childhood Development/Childcare		\$8,858,578		\$15,405,517		\$2,220,533	\$4,441,065	\$30,925,693		In Construction	
S-6, AA-110, V-103	Malibu Site Acquisition and Facility	4	\$25,000,000		\$25,000,000				\$50,000,000	\$50,000,000		\$34,018,73
S, S-11, AA-112, V-109	<u> </u>	\$2,110,430	\$716,428		\$1,000,000				\$4,661,555	\$4,661,555	In Design	\$883,48
U-P, AA-106, V-101	Replacement Math and Science Extension Building	\$308,336		\$2,244,008			\$2,584,000	\$37,504,000	\$124,958,336	\$124,958,336	In Design	\$79,632,4
AA-105, V-110	Drescher - Academic Modernization, Bookstore, Pico Promenade II			\$5,082	\$13,000,000				\$13,005,082	\$13,005,082	In Planning	\$13,000,0
V-105	Art Building Replacement				\$24,000,000			\$8,914,000	\$32,914,000	\$32,914,000	In Planning	\$23,551,02
V-106	Business Building Renovation				\$12,547,000			\$12,470,000	\$25,017,000	\$25,017,000	In Planning	\$12,547,0
V-107	Air Conditioning				\$10,777,654				\$10,777,654	\$10,777,654	In Design	\$9,998,9
V-108	ADA				\$4,000,000				\$4,000,000	\$4,000,000	In Planning	\$4,000,0
V-111	Outdoor Classroom				\$250,000				\$250,000	\$250,000	In Planning	\$30,7
V-112	SMMUSD				\$20,000,000				\$20,000,000	\$20,000,000	In Design	\$20,000,0
V-113	City of Santa Monica				\$20,000,000				\$20,000,000	\$20,000,000	In Planning	\$20,000,00
V-114	Classrooms Relocation				\$6,900,000				\$6,900,000	\$4,900,000	In Design	\$6,589,6
S-12, V-120	Other Bond Related Expenses		\$609,282		\$300,000				\$909,282	\$909,282	In Planning	\$231,5
V-115	TBD				\$49,076,928				\$49,076,928	\$49,076,928	In Planning	\$49,076,9
S-16, AA-121, V-121	Cost of Issuance		\$119,470	\$498,026	\$800,000				\$1,417,496	\$1,417,496	In Planning	\$508,7
AA-122, V-122	Management Reserve				\$26,000,000				\$37,574,404	\$37,574,404	In Planning	\$29,397,6
U, S-17, AA-123, V-123	3	\$1,127	\$2,143						\$7,441	\$7,441	On-Going	
, , ===,: <b>==</b>	Project Totals	\$160,000,000				H .	4					\$333,126,5

\* City of SM: \$12,427,356; FEMA: \$2,456,388; State: \$8,363,000; Prop T: 2,618,113; DWP: \$86,245; SCE: \$844,284; Gas Co.: \$106,262; Madison Foundation: \$2,992,576; KCRW: \$6,803,412; Emeritus College Foundation: \$693,842; Bond Interest and Cost of Issuance Refund: \$29,858,053

<sup>\*\*</sup> City of SM: 4,441,065; State: \$58,888,000


# Bond Sales / Expenses Report As of September 30, 2019

Measure S Bond \$143,500,000 (1)		
Bond Issue Date		Amount
	2005	\$58,000,000
	2007	\$8,500,000
	2009	\$56,997,857
	2017	\$20,000,000
Total Available		\$143,497,857
Expenses as of 9-30-19		\$134,144,455
Total Available Remaining		\$9,353,402
Unsold Bond Amount	·	\$2,143
Total Available as of 10-1-19		\$9,355,545

Measure AA Bond \$295,000,000		
Bond Issue Date		Amount
	2010	\$100,000,000
	2014	\$144,995,829
	2017	\$50,000,000
Total Available		\$294,995,829
Expenses as of 9-30-19		\$290,878,348
Total Available Remaining		\$4,117,481
Unsold Bond Amount		\$4,171
Total Available as of 10-1-19		\$4,121,652

Measure V Bond \$345,000,000		
Bond Issue Date		Amount
	2018	\$180,000,000
Total Available		\$180,000,000
Expenses as of 9-30-19		\$25,344,381
Total Available Remaining		\$154,655,619
Unsold Bond Amount		\$165,000,000
Total Available as of 10-1-19		\$319,655,619

Total Bond	\$783,500,000
Total Available	\$618,493,686
Total Expenses as of 9-30-19	\$450,367,184
Total Available Remaining	\$168,126,502
Total Unsold Bond	\$165,006,314

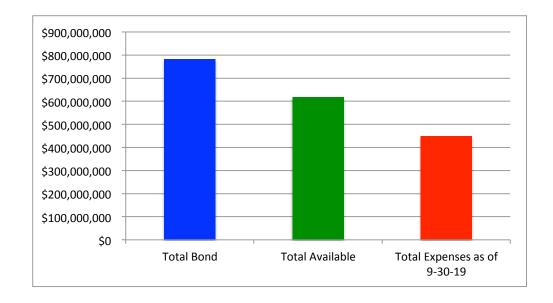

Interest	Measure S	Measure AA	Measure V
As of 6-30-19	\$11,877,416	\$6,792,485	\$4,097,721
Expenditure / Arbitrage as of 6-30-19	\$9,853,563	\$5,192,948	\$0
Available Interest as of 7-1-19	\$2,023,853	\$1,599,537	\$4,097,721


Cost of Issuance Refund	Measure S
As of 6-30-19	\$35,575
Expenditure as of 6-30-19	\$0
Available as of 7-1-19	\$35,575

<sup>(1)</sup> Original Bond \$135,000,000.00, refunding on 2-15-07 received additional \$8,500,000.00

# **Measure S Bond Budget**

As of September 30, 2019

	Project Name	Completion	Project Budget	Measure S Allocation	Other Funding	Measure S Expenditures as of 9/30/19	Measure S Expenditures as of 6/30/19	Measure S Expenditures Last Period	Total Measure S Remaining
1	Athletic Fields Phase I, Corsair Field	Completed	\$4,440,065	\$4,372,535	\$67,530	\$4,372,535	\$4,372,535	\$0	\$0
1A	Athletic Fields Phase I, John Adams	Completed	\$2,969,807	\$2,969,807	\$0	\$2,969,807	\$2,969,807	\$0	\$0
2	Performing Arts Complex	Completed	\$40,690,201	\$37,697,625	\$2,992,576	\$37,697,625	\$37,697,625	\$0	\$0
3	Career Opportunity Center	Completed	\$0	\$0	\$0	\$0	\$0	\$0	\$0
4	Replacement Health/PE/Fitness Building	Completed	\$58,272,030	\$11,603,383	\$46,668,647	\$11,603,383	\$11,603,383	\$0	\$0
5	Early Childhood Development/Childcare	June 2020	\$30,925,693	\$8,858,578	\$22,067,115	\$8,676,356	\$8,674,099	\$2,257	\$182,222
6	Malibu Site Acquisition and Facility	April 2022	\$25,000,000	\$25,000,000	\$0	\$15,981,270	\$15,075,576	\$905,694	\$9,018,730
7	Energy Efficiency Projects	Completed	\$510,683	\$293,361	\$217,322	\$293,361	\$293,361	\$0	\$0
8	Satellite Campus Parking Facilities and Roadway Improvements	Deferred	\$7,022,417	\$3,891,747	\$3,130,670	\$3,891,747	\$3,891,747	\$0	\$0
9	Parking Garage, Grounds and Equipment - Student Services	Completed	\$130,224,164	\$45,595,322	\$84,628,842	\$45,595,322	\$45,595,322	\$0	\$0
10	Pico Promenade Improvements	Completed	\$1,018,009	\$1,018,009	\$0	\$1,018,009	\$1,018,009	\$0	\$0
11	Master Planning	Completed	\$716,428	\$716,428	\$0	\$716,428	\$716,428	\$0	\$0
12	Other Bond Related Expenses	On-Going	\$609,282	\$609,282	\$0	\$456,832	\$452,879	\$3,953	\$152,450
13	Adv. Architecture Related Exp for AA	Completed	\$0	\$0	\$0	\$0	\$0	\$0	\$0
14	Real Property Acquisition	Completed	\$45,597	\$45,597	\$0	\$45,597	\$45,597	\$0	\$0
15	Signage Safety/Information	Completed	\$706,713	\$706,713	\$0	\$706,713	\$706,713	\$0	\$0
16	Cost of Issuance	Completed	\$119,470	\$119,470	\$0	\$119,470	\$119,470	\$0	\$0
17	Unissuable Bond	Completed	\$2,143	\$2,143	\$0	\$0	\$0	\$0	\$2,143
	Project Totals		\$303,270,559	\$143,500,000	\$159,772,702	\$134,144,455	\$133,232,551	\$911,904	\$9,355,545

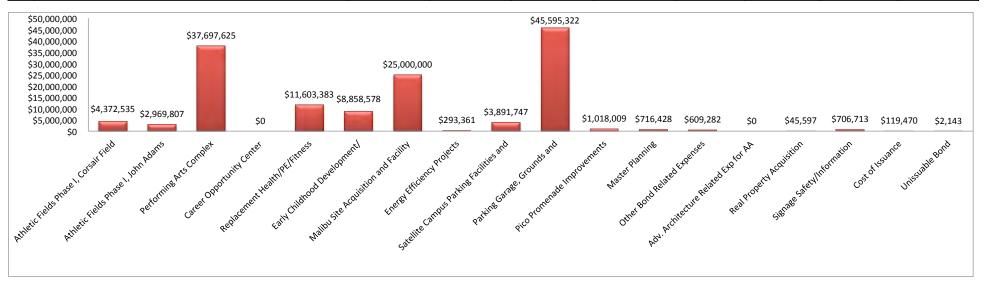


# Measure S Bond Budget History

as of September 30, 2019

	Project Name	Completion	Preliminary Measure S Budget	Measure S Budget as of 6/30/19	Measure S Budget as of 9/30/19	Variance	Measure S Remaining as of 9/30/19
1	Athletic Fields Phase I, Corsair Field	Completed	\$1,800,000	\$4,372,535	\$4,372,535	\$0	\$0
1A	Athletic Fields Phase I, John Adams	Completed	\$35,200,000	\$2,969,807	\$2,969,807	\$0	\$0
2	Performing Arts Complex	Completed	\$24,000,000	\$37,697,625	\$37,697,625	\$0	\$0
3	Career Opportunity Center	Completed	\$20,000,000	\$0	\$0	\$0	\$0
4	Replacement Health/PE/Fitness Building	Completed	\$20,000,000	\$11,603,383	\$11,603,383	\$0	\$0
5	Early Childhood Development/Childcare	June 2020	\$7,000,000	\$8,858,578	\$8,858,578	\$0	\$182,222
6	Malibu Site Acquisition and Facility	April 2022	\$25,000,000	\$25,000,000	\$25,000,000	\$0	\$9,018,730
7	Energy Efficiency Projects	Completed	\$2,000,000	\$293,361	\$293,361	\$0	\$0
8	Satellite Campus Parking Facilities and Roadway Improvements	Deferred	\$0	\$3,891,747	\$3,891,747	\$0	\$0
9	Parking Garage, Grounds and Equipment - Student Services	Completed	\$0	\$45,595,322	\$45,595,322	\$0	\$0
10	Pico Promenade Improvements, Phase I	Completed	\$0	\$1,018,009	\$1,018,009	\$0	\$0
11	Master Planning	Completed	\$0	\$716,428	\$716,428	\$0	\$0
12	Other Bond Related Expenses	On-Going	\$0	\$609,282	\$609,282	\$0	\$152,450
13	Adv. Architecture Related Exp for AA	Completed	\$0	\$0	\$0	\$0	\$0
14	Real Property Acquisition	Completed	\$0	\$45,597	\$45,597	\$0	\$0
15	Signage Safety/Information	Completed	\$0	\$706,713	\$706,713	\$0	\$0
16	Cost of Issuance	Completed	\$0	\$119,470	\$119,470	\$0	\$0
17	Unissuable Bond	Completed	\$0	\$2,143	\$2,143	\$0	\$2,143
	Project Totals		\$135,000,000	\$143,500,000	\$143,500,000	\$0	\$9,355,545

# SANTA MONICA COMMUNITY COLLEGE DISTRICT **Measure AA Bond Budget** As of September 30, 2019

	Project Name	Completion	Project Budget	Measure AA Allocation	Other Funding	Measure AA Expenditures as of 9/30/19	Measure AA Expenditures as of 6/30/19	Measure AA Expenditures Last Period	Total Measure AA Remaining
101	Environmental Performance - Central Plant Connections	Completed	\$10,767,251	\$10,767,251	\$0	\$10,767,251	\$10,767,251	\$0	\$0
102	Infrastructure & Technology - Information Technology Relocation	Completed	\$23,160,569	\$23,140,771	\$19,798	\$23,140,771	\$23,140,771	\$0	\$0
103	Media and Technology Complex - Academy Site	Completed	\$130,549,713	\$123,714,322	\$6,835,391	\$123,318,677	\$123,267,536	\$51,141	\$395,645
104	Replacement Health/PE/Fitness/ Dance Building with Central Plant	Completed	\$56,240,452	\$44,428,222	\$11,812,230	\$44,428,222	\$44,428,222	\$0	\$0
105	Drescher - Academic Modernization, Bookstore, Pico Promenade	Deferred	\$13,005,082	\$5,082	\$13,000,000	\$5,082	\$5,082	\$0	\$0
106	Replacement Math and Science Extension Building	May 2023	\$124,958,336	\$2,244,008	\$122,714,328	\$2,004,184	\$2,004,184	\$0	\$239,824
107	Madison East Wing Seismic Upgrade	Completed	\$30,160,902	\$30,160,902	\$0	\$30,160,902	\$30,160,902	\$0	\$0
108	Renovation of Corsair Stadium	Completed	\$35,299	\$35,299	\$0	\$35,299	\$35,299	\$0	\$0
109	Career Opportunity and Advancement Center (Bundy)	Completed	\$0	\$0	\$0	\$0	\$0	\$0	\$0
110	Malibu Center	April 2022	\$25,000,000	\$0	\$25,000,000	\$0	\$0	\$0	\$0
111	Business & Facilities Infrastructure	Completed	\$1,968,124	\$1,968,124	\$0	\$1,968,124	\$1,968,124	\$0	\$0
112	Master Planning, Program Management, Overhead	On-Going	\$834,697	\$834,697	\$0	\$834,697	\$834,697	\$0	\$0
113	Energy Efficiency Projects	Completed	\$3,508,088	\$3,016,773	\$491,315	\$3,016,773	\$3,016,773	\$0	\$0
114	Community Classroom & Facility Projects	Completed	\$3,162,183	\$3,162,183	\$0	\$3,162,183	\$3,162,183	\$0	\$0
115	Real Property Acquisition	Completed	\$24,638,386	\$24,638,386	\$0	\$24,638,386	\$24,638,386	\$0	\$0
116	Roadways, Walkways, Grounds, Parking Lots, and Garages	Completed	\$7,022,417	\$2,130,670	\$4,891,747	\$2,130,670	\$2,130,670	\$0	\$0
117	Infrastructure & Technology - Technology	Completed	\$2,434,417	\$2,434,417	\$0	\$2,434,417	\$2,434,417	\$0	\$0
118	Infrastructure & Technology - Utility	Completed	\$27,753	\$27,753	\$0	\$27,753	\$27,753	\$0	\$0
119	Emergency Lighting, Fire Alarm, and Security System	On-Going	\$11,520,794	\$11,520,794	\$0	\$11,436,441	\$11,436,441	\$0	\$84,353
120	Student Services	Completed	\$130,224,164	\$6,870,490	\$123,353,674	\$6,870,490	\$6,870,490	\$0	\$0
121	Cost of Issuance	Completed	\$498,026	\$498,026	\$0	\$498,026	\$498,026	\$0	\$0
122	Management Reserve	On-Going	\$3,397,659	\$3,397,659	\$0	\$0	\$0	\$0	\$3,397,659
123	Unissuable Bond	Completed	\$4,171	\$4,171	\$0	\$0	\$0	\$0	\$4,171
	Project Totals		\$599,716,653	\$295,000,000	\$308,118,483	\$290,878,348	\$290,827,207	\$51,141	\$4,121,652




# SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure AA Bond Budget History as of September 30, 2019

			Preliminary	Measure AA	Measure AA		Measure AA
	Project Name	Completion	Measure AA	Budget as of	Budget as of	Variance	Remaining as
			Budget	6/30/19	9/30/19		of 6/30/19
101	Environmental Performance - Central Plant Connections	Completed	\$12,034,042	\$10,767,251	\$10,767,251	\$0	
102	Infrastructure & Technology - Information Technology Relocation	Completed	\$13,287,218	\$23,140,771	\$23,140,771	\$0	\$0
	Media and Technology Complex - Academy Site	Completed		\$123,714,322	\$123,714,322	\$0	1 /
104	Replacement Health/PE/Fitness/ Dance Building with Central Plant	Completed	\$29,232,317	\$44,479,800	\$44,428,222	-\$51,578	\$0
105	Drescher - Academic Modernization, Bookstore, Pico Promenade II	Deferred	\$34,026,480	\$5,082	\$5,082	\$0	\$0
106	Replacement Math and Science Extension Building	May 2023	\$68,259,000	\$2,244,008	\$2,244,008	\$0	\$239,824
107	Madison East Wing Seismic Upgrade	Completed	\$6,146,000	\$30,178,822	\$30,160,902	-\$17,920	
108	Renovation of Corsair Stadium	Completed	\$11,203,000	\$35,299	\$35,299	\$0	
109	Career Opportunity and Advancement Center (Bundy)	Completed	\$32,384,000	\$0	\$0	\$0	
110	Malibu Center	April 2022	\$6,069,031	\$0	\$0	\$0	
111	Business & Facilities Infrastructure	Completed	\$17,506,952	\$1,968,124	\$1,968,124	\$0	
112	Master Planning, Program Management, Overhead	On-Going	\$2,000,000	\$834,697	\$834,697	\$0	
113	Energy Efficiency Projects	Completed	\$5,371,136	\$3,016,773	\$3,016,773	\$0	
114	Community Classroom & Facility Projects	Completed	\$0	\$3,162,183	\$3,162,183	\$0	
115	Real Property Acquisition	Completed	\$0	\$24,638,386	\$24,638,386	\$0	
116	Roadways, Walkways, Grounds, Parking Lots, and Garages	Completed	\$0	\$2,130,670	\$2,130,670	\$0	
117	Infrastructure & Technology - Technology	Completed	\$0	\$2,434,417	\$2,434,417	\$0	\$0
118	Infrastructure & Technology - Utility	Completed	\$0	\$27,753	\$27,753	\$0	\$0
119	Emergency Lighting, Fire Alarm, and Security System	On-Going	\$0	\$11,520,794	\$11,520,794	\$0	\$84,353
120	Student Services	Completed	\$0	\$6,870,490	\$6,870,490	\$0	\$0
121	Cost of Issuance	Completed	\$0	\$498,026	\$498,026	\$0	\$0
122	Management Reserve	On-Going	\$0	\$3,328,161	\$3,397,659	\$69,498	\$3,397,659
123	Unissuable Bond	Completed	\$0	\$4,171	\$4,171	\$0	\$4,171
	Project Totals		\$295,000,000	\$295,000,000	\$295,000,000	\$0	\$4,121,652

# **Measure V Bond Budget**

As of September 30, 2019

	Project Name	Completion	Project Budget	Measure V Allocation	Other Funding	Measure V Expenditures as of 9/30/19	Measure V Expenditures as of 6/30/19	Measure V Expenditures Last Period	Total Measure V Remaining
101	Replacement Math and Science Extension Building	May 2023	\$124,958,336	\$82,317,992	\$42,640,344	\$2,925,338	\$2,899,578	\$25,760	\$79,392,654
102	Student Services	Completed	\$130,224,164	\$33,624,909	\$96,599,255	\$18,620,080	\$18,328,709	\$291,371	\$15,004,829
103	Malibu Center	April 2022	\$50,000,000	\$25,000,000	\$25,000,000	\$0	\$0	\$0	\$25,000,000
104	Early Childhood Development/Childcare	June 2020	\$30,925,693	\$15,405,517	\$15,520,176	\$1,412,988	\$0	\$1,412,988	\$13,992,529
105	Art Building Replacement	December 2022	\$32,914,000	\$24,000,000	\$8,914,000	\$448,974	\$444,648	\$4,326	\$23,551,026
106	Business Building Renovation	December 2023	\$25,017,000	\$12,547,000	\$12,470,000	\$0	\$0	\$0	\$12,547,000
107	Air Conditioning	June 2020	\$10,777,654	\$10,777,654	\$0	\$778,677	\$778,677	\$0	\$9,998,977
108	ADA	On-Going	\$4,000,000	\$4,000,000	\$0	\$0	\$0	\$0	\$4,000,000
109	Master Planning	March 2021	\$1,000,000	\$1,000,000	\$0	\$116,515	\$116,515	\$0	\$883,485
110	Drescher Hall Modernization	On-Going	\$13,005,082	\$13,000,000	\$5,082	\$0	\$0	\$0	\$13,000,000
111	Outdoor Classroom	On-Going	\$250,000	\$250,000	\$0	\$219,228	\$219,228	\$0	\$30,772
112	SMMUSD	August 2021	\$20,000,000	\$20,000,000	\$0	\$0	\$0	\$0	\$20,000,000
113	City of Santa Monica	On-Going	\$20,000,000	\$20,000,000	\$0	\$0	\$0	\$0	\$20,000,000
114	Classrooms Relocation	April 2020	\$6,900,000	\$6,900,000	\$0	\$310,377	\$266,216	\$44,161	\$6,589,623
115	TBD	On-Going	\$49,076,928	\$49,076,928	\$0	\$0	\$0	\$0	\$49,076,928
120	Other Bond Related Expenses	On-Going	\$300,000	\$300,000	\$0	\$220,927	\$217,899	\$3,028	\$79,073
121	Cost of Issuance	On-Going	\$800,000	\$800,000	\$0	\$291,277	\$291,277		\$508,723
	Management Reserve	On-Going	\$26,000,000	\$26,000,000		\$0	\$0	\$0	\$26,000,000
123	Unissuable Bond	On-Going	\$0	\$0	\$0		\$0	\$0	\$0
	Project Totals		\$546,148,857	\$345,000,000	\$201,148,857	\$25,344,381	\$23,562,747	\$1,781,634	\$319,655,619

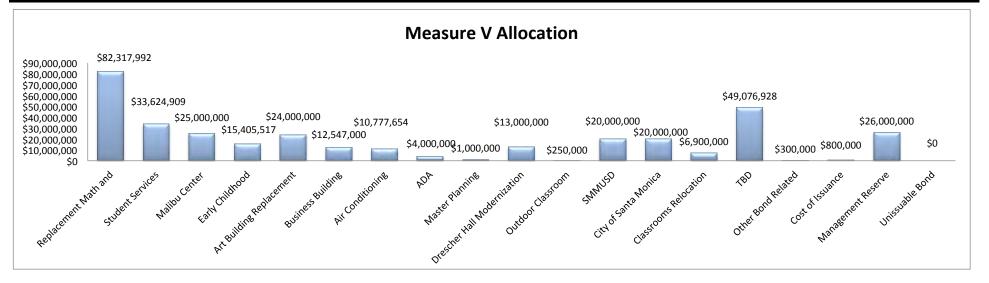

# SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure V Bond Budget History

as of September 30, 2019

	Project Name	Completion	Preliminary Measure V	Measure V Budget as of	Measure V Budget as of	Variance	Measure V Remaining as
			Budget	6/30/19	9/30/19		of 3/31/19
101	Replacement Math and Science Extension Building	May 2023	\$82,317,992	\$82,317,992	\$82,317,992	\$0	\$79,392,654
102	Student Services	Completed	\$21,130,252	\$33,624,909	\$33,624,909	\$0	\$15,004,829
103	Malibu Center	April 2022	\$25,000,000	\$25,000,000	\$25,000,000	\$0	\$25,000,000
104	Early Childhood Development/Childcare	June 2020	\$15,405,517	\$15,405,517	\$15,405,517	\$0	\$13,992,529
105	Art Building Replacement	December 2022	\$24,000,000	\$24,000,000	\$24,000,000	\$0	\$23,551,026
106	Business Building Renovation	December 2023	\$12,547,000	\$12,547,000	\$12,547,000	\$0	\$12,547,000
107	Air Conditioning	June 2020	\$10,777,654	\$10,777,654	\$10,777,654	\$0	\$9,998,977
108	ADA	On-Going	\$4,000,000	\$4,000,000	\$4,000,000	\$0	\$4,000,000
109	Master Planning	March 2021	\$450,000	\$1,000,000	\$1,000,000	\$0	\$883,485
110	Drescher Hall Modernization	On-Going	\$13,000,000	\$13,000,000	\$13,000,000	\$0	\$13,000,000
111	Outdoor Classroom	On-Going	\$10,000,000	\$250,000	\$250,000	\$0	\$30,772
112	SMMUSD	August 2021	\$20,000,000	\$20,000,000	\$20,000,000	\$0	\$20,000,000
113	City of Santa Monica	On-Going	\$20,000,000	\$20,000,000	\$20,000,000	\$0	\$20,000,000
114	Classrooms Relocation	April 2020	\$0	\$4,900,000	\$6,900,000	\$2,000,000	\$4,589,623
115	TBD	On-Going	\$57,271,585	\$49,076,928	\$49,076,928	\$0	\$49,076,928
120	Other Bond Related Expenses	On-Going	\$300,000	\$300,000	\$300,000	\$0	\$79,073
121	Cost of Issuance	On-Going	\$800,000	\$800,000	\$800,000	\$0	\$508,723
122	Management Reserve	On-Going	\$28,000,000	\$28,000,000	\$26,000,000	-\$2,000,000	\$28,000,000
123	Unissuable Bond	On-Going	\$0	\$0	\$0	\$0	
	Project Totals		\$345,000,000	\$345,000,000	\$345,000,000	\$0	\$319,655,619

# **Measure S Project Schedule** As of September 30, 2019


	Project Name	Completion	2018	2019	2020	2021	2022
1	Athletic Fields Phase I, Corsair Field	Completed					
1A	Athletic Fields Phase I, John Adams	Completed					
2	Performing Arts Center	Completed					
3	Career Opportunity Center	Completed					
4	Replacement Health/PE/Fitness Building	Completed					
5	Early Childhood Development/Childcare	June 2020					
6	Malibu Site Acquisition and Facility	April 2022					
7	Energy Efficiency Projects	Completed					
8	Satellite Campus Parking Facilities and Roadway Improvements	Deferred					
9	Parking Garage, Grounds and Equipment - Student Services	Completed					
10	Pico Promenade Improvements	Completed					
11	Master Planning	Completed					
12	Other Bond Related Expenses	On-Going					
13	Adv. Architecture Related Exp for AA	Completed					
14	Real Property Acquisition	Completed					
15	Signage Safety/Information	Completed					
16	Cost of Issuance	Completed					
17	Unissuable Bond	Completed					
			In Planni		In Constr		

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20	Combined Totals
S7100019																		
Athletic Field Phase I, Corsair Field (1)																		
Legal		\$0	\$0	\$0	\$301	\$175	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$476
Building & Additions		\$0	\$0	\$0	\$300,380	\$2,579,095	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,879,475
Architect		\$27,332	\$43,815	\$197,557	\$252,736	\$279,173	\$26,563	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$827,176
Inspection & Testing		\$0	\$0	\$0	\$23,411	\$57,585	\$640	\$296	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$81,932
Project Management		\$0	\$0	\$0	\$9,871	\$42,374	\$565	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$52,810
Cap Equipment		\$0	\$0	\$0	\$0	\$483,017	\$35,271	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$518,288
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$2,066	\$10,312	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$12,378
Total		\$27,332	\$43,815	\$197,557	\$586,699	\$3,443,485	\$73,350	\$296	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,372,535
Project Budget	\$4,440,065	Received										•						
Less Other Funding*	\$67,530			* Other Fundin	g Source:													
Net	\$4,372,535	,		Metropolitan W	ater District \$6	7,530 received												
Actual Measure S Expenditures	\$4,372,535	1																
Running Balance	\$0	1																

# Athletic Field Phase I, Corsair Field Project Description: Renovation of the Corsair Field, stadium lighting and sound system Status: Completed, 2009

Architect: CO Architects


Contractor: Byrom Davey, Inc.



As of S	eptemb	er 30.	201


Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20	Combined Totals
S7100038																		
Athletic Field Phase I, John Adams (1A)																		
Legal		\$0	\$0	\$0	\$75	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$75
Building & Additions		\$0	\$0	\$0	\$16,556	\$1,395,261	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,411,817
Architect		\$0	\$5,807	\$93,941	\$12,150	\$31,818	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$143,715
Inspection & Testing		\$0	\$2,874	\$3,207	\$0	\$49,984	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$56,066
Project Management		\$0	\$0	\$0	\$10,921	\$45,170	\$38	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$56,128
Cap Equipment		\$0	\$0	\$0	\$0	\$1,290,672	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,290,672
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$11,334	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$11,334
Total		\$0	\$8,681	\$97,148	\$39,701	\$2,824,239	\$38	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,969,807
Project Budget	\$2,969,807											•		•				
Less Other Funding	\$0																	
Net	\$2,969,807	Ī																
Actual Measure S Expenditures	\$2,969,807	ĺ																
Running Balance	\$0																	

Athletic Fiel	d Phase I, John Adams
Project Desc Renovation of	ription: f John Adams Field and lighting
Status: Completed, 2	008
Architect: Caldwell Arch	itects
Contractor: Byrom Davey	, Inc.



Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20	Combined Totals
110,000	Daugot	0.0001	00/00 / ///	00/07 1 11101	01700111141	00,00 1 11101	00/10 1 11141			12/10/11/01	1000000000	1-11-10-1-11-11	1 .0	10/1/11/01	11710111141	10/10/11/11		Tombinou rotaio
S7100012																		
Performing Arts Center (2)																		
Consultants		\$0	\$0	\$0	\$121,790	\$76,639	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	
Other Contract Services		\$0	\$0	\$4,269	\$0	\$22,729	\$22	\$68		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	
Supplies		\$0	\$0	\$0	\$14,565	\$5,810	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$20,375
Legal		\$0	\$0	\$34,329	\$275,667	\$492,731	\$15,629	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$818,356
Advertising		\$0	\$0	\$0	\$320	\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0	\$0		\$0	
Building & Additions		\$7,784,151	\$10,292,986	\$8,930,813	\$2,991,903	\$1,629,990	\$50,000	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$31,679,843
Architect		\$0	\$811,312	\$182,457	\$412,309	\$121,588	\$108	\$1,962	\$0	\$0	\$87,054	\$0	\$0	\$0	\$0	\$0	\$0	\$1,616,790
Engineering		\$0	\$3,600	\$5,250	\$1,500	\$9,650		\$0	\$0	\$0	ų vi	\$0			\$0	<b>Φ</b> U	\$0	
Inspection & Testing		\$104,308	\$722,685	\$411,193	\$210,381	\$22,256		\$0	\$0	\$0	\$0	J		\$0	\$0		\$0	
Project Management		\$31,984	\$155,732	\$248,876	\$263,690	\$47,915	\$3,244	\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$751,441
Cap Equipment		\$0	\$0	\$130,218	\$292,565	\$342,693	\$0	\$0		\$0	\$0	) \$U		\$0	\$0		\$0	
Non-Cap Equipment		\$0	\$0	\$15,124	\$93,106	\$220,455	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0		\$0	
Total		\$7,920,443	\$11,986,315	\$9,962,528	\$4,677,797	\$2,992,455	\$69,003	\$2,030	\$0	\$0	\$87,054	\$0	\$0	\$0	\$0	\$0	\$0	\$37,697,625
Project Budget	\$40,690,201	Received																
Less Other Funding*	\$2,992,576			* Other Funding														
Net	\$37,697,625			Madison Project	ct Foundation \$	2,992,576 rece	eived											
Actual Measure S Expenditures	\$37,697,625	1																
Running Balance	\$0																	

Performing Arts Center
Project Description: Construction of a state-of-the-art 499 seat performing arts theater
Status: Completed, 2008
Architect: Renzo Zecchetto
Contractor: FTR International



Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20	Combined Totals
S7100033, S7100144, S7100060										-								
Replacement Health/PE/Fitness Building (4)																		
Supplies		\$4.809	\$288	\$0	\$0	\$0	\$163	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$5,260
Legal		\$4,009	\$200			\$1.413		\$0		\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$1,488
Other Contract Services		\$1.634	\$25,934	\$0	\$0	\$253		\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$27,985
Repair Facility		\$1,034	\$4.861			\$0				\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$4,861
Building & Additions		\$0	\$4,001			\$112.410		\$0		\$0	\$0	\$6.037.080	\$4,775,714	\$0	\$0		\$0	\$11.451.757
Architect		\$0	\$0	\$0	\$0	\$112,410		\$0	\$0	\$0	\$0	\$0,037,000	\$0	\$0	\$0	\$0	\$0	\$41,044
Inspection & Testing		\$0	\$0			\$6,518		\$0		\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$20,881
Project Management		\$0	\$0			\$9,070	\$23,425	\$0		\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$32,495
Cap Equipment		\$0	\$0	\$0	\$0	\$9,070		\$17,613	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$17,613
Total		\$6.443	\$31.083					\$17,613		\$0		\$6.037.080	\$4,775,714	\$0	SO		\$0	\$11,603,383
Project Budget	\$58,272,030	ψ0,440	ψ01,000	Ų.	<b>\$0</b>	Ψ125,000	<b>4000,707</b>	Ψ17,010	<b>40</b>	ΨΟ	40	ψ0,007,000	ψ4,770,714	ΨΟ	-	40	<del>***</del>	\$11,000,000
Less Other Fundina*	\$46,668,647			* Other Fundin	a Source:													
Net	\$11,603,383			Measure AA \$4		cated												
Actual Measure S Expenditures	\$11,603,383			SCE \$190.847			d											
Running Balance	\$11,003,363			30L \$130,047	.20, Gas Co. ş	10,000 receive	u											
Truming Balance	ΨΟ																	
S7100045																		
Early Childhood Development/Childcare (5)																		
Supplies		\$0	\$0			\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0	\$294	\$0	\$0	\$294
Consultants		\$0	\$0			\$0				\$4,800	\$12,930	\$14,078	\$1,388	\$0	\$0		\$0	\$42,395
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,690	\$6,905	\$0	\$0	\$0	\$8,595
Building & Additions		\$0	\$0			\$0				\$0	\$0	\$0	\$0	\$242	\$747,457	\$5,197,194	\$0	\$5,944,893
Architect		\$0	\$0			\$0				\$51,792	\$142,428	\$142,968	\$476,827	\$78,408	\$67,918	\$329,152	\$0	\$1,290,458
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,888	\$0	\$3,888
Inspection & Testing		\$0	\$0			\$0			\$0	\$37,796	\$7,475	\$823	\$2,323	\$0	\$4,085	\$296,806	\$2,256	\$351,564
Project Management		\$0	\$0			\$0			\$21,980	\$58,247	\$33,435	\$8,803	\$3,118	\$0	\$307,493		\$0	\$1,034,270
Total		\$0	\$0	\$0	\$9,200	\$0	\$0	\$1,246	\$22,946	\$152,635	\$196,268	\$166,670	\$485,344	\$85,555	\$1,127,247	\$6,426,989	\$2,256	\$8,676,356
Project Budget	\$30,925,693																	
Less Other Funding*	\$22,067,115	\$2,220,533		* Other Fundin														
Net	\$8,858,578			City of Santa M	1onica \$6,661,5	98 commited												
Actual Measure S Expenditures	\$8,676,356			Measure V \$15	5,405,517 alloca	ated												
Running Balance	\$182,222																	
S7100077, S7100015  Malibu Site Acquisition and Facilities (6)																		
			\$0		20	000 000	20		070 457	000 100	000.040	800.077	200 000	00.400	0.47	00		0000 570
Consultants		\$0 \$0	\$0 \$27,722		\$0 \$6,159	\$30,000 \$504				\$68,109	\$30,342	\$66,277	\$60,262	\$3,406	\$17		\$0	\$330,570
Legal		\$0 \$0				\$504 \$0				\$0	\$1,360	\$78,851	\$40,114	\$7,353	\$6,324		\$0 \$0	\$185,174 \$119,178
Other Contract Services			\$0		\$0					\$0	\$0	\$1,820	\$0	\$0	\$0			
Building & Additions		\$0	\$0 \$0			\$0				\$0	\$536	\$0	\$0	\$0	\$2,019,660		\$813,388	\$5,969,636
Architect		\$0 \$0				\$0				\$257,584	\$732,891	\$173,610	\$34,753	\$151,772	\$341,307		\$5,500	\$2,029,810
Engineering			\$0			\$0 \$0				\$785	\$562	\$0	\$0	\$0	\$0		\$0	\$1,346
Inspection & Testing		\$4,388 \$0	\$3,750		\$0 \$0	\$0				\$15,575	\$22,939	\$10,960	\$0	\$0	\$39,460		\$45,426	\$704,216
Project Management		\$0 \$0	\$0 \$2,500,000	\$220	\$0 \$0	\$2,500,000	\$0		\$55,064 \$0	\$53,185	\$47,778	\$118,144	\$97,856	\$46,400	\$431,268		\$41,380	\$1,641,339
Storm/Waste Water Treatment Center				\$0						\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$5,000,000
Total	#05 000 CCC	\$4,388	\$2,531,472	\$158,468	\$6,159	\$2,530,504	\$0	\$2,886	\$228,301	\$395,237	\$836,407	\$449,662	\$232,985	\$208,931	\$2,838,036	\$4,652,138	\$905,694	\$15,981,270
Project Budget	\$25,000,000 \$0																	
Less Other Funding*	ΨΟ																	
Net	\$25,000,000																	
Actual Measure S Expenditures	\$15,981,270																	
Running Balance	\$9,018,730																	

# SANTA MONICA COMMUNITY COLLEGE DISTRICT MEASURE S EXPENDITURES FUND 42.3

As of	Septe	mber	30,	201

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20	Combined Totals
S7100043, S7100066																		
Energy Efficiency Projects (7)																		
Legal		\$0	\$0	\$0	\$0	\$988	\$0	\$0	\$0	\$0		\$0		\$0			\$0	
Building & Additions		\$0	\$0	\$0	\$0	\$106,921	\$355,294	-\$180,342		\$0		\$0		\$0			\$0	
Engineering		\$0	\$0	\$0	\$10,500	\$0	\$0	\$0	\$0	\$0		\$0		\$0			\$0	
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0			\$0	
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0		\$0	\$0	\$0	\$0	
Total		\$0	\$0	\$0	\$10,500	\$107,910	\$355,294	-\$180,342	\$0	\$0	\$0	\$0	\$0	\$0	0 \$0	\$0	\$0	\$293,361
Project Budget	\$510,683	Received																
Less Other Funding*	\$217,322	\$217,322		<ul> <li>Other Funding</li> </ul>														
Net	\$293,361			SCE & The Ga	s Co. \$217,322	received												
Actual Measure S Expenditures	\$293,361																	
Running Balance	\$0																	
S7100091, S7100092, S7100147																		
Satellite Campus Parking Facilities and Roadway Im	provements (8)																	
Legal		\$0	\$0	\$0	\$300	\$175	\$0	\$0	\$0	\$0		\$0	\$0	\$0			\$0	
Other Contract Services		\$0	\$0	\$0	\$300	\$0 \$0	\$0	\$0	\$0	\$0		\$0 \$0	\$0	\$0			\$0	
Advertising		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0			\$0	\$0	\$0			\$0	
Consultants		\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0		\$0	\$0			\$0	\$0	
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0			\$0	\$0				\$0	\$0
Building & Additions		\$0	\$0	\$0	\$278,178	\$1,860,152	\$449,543	\$37,777	\$0			\$64					\$0	
Architect		\$0	\$0	\$324,919	\$324,864	\$136,911	\$34,490	\$1,397	\$2,289			\$0		\$0			\$0	
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$30,896	\$5,470					\$0	
Inspection & Testing		\$0	\$0	\$0	\$31,100	\$185,947	\$28,218	\$360	\$0		\$0	\$0		\$0			\$0	
Project Management		\$0	\$0	\$0	\$18,288	\$64,880	\$31,137	\$8,659		\$2,569	\$10,730	\$6,046					\$0	
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$3,387	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,387
Total		\$0	\$0	\$324,919	\$653,031	\$2,248,065	\$546,775	\$48,194	\$2,289	\$2,569	\$41,626	\$11,580	\$12,700	\$0	0 \$0	\$0	\$0	\$3,891,747
Project Budget	\$7,022,417																	
Less Other Funding	\$3,130,670			* Other Funding														
Net	\$3,891,747			Measure AA \$2	2,130,670, Mea	sure V \$1,000,	000 allocated											
Actual Measure S Expenditures	\$3,891,747																	J
Running Balance	\$0																	

# SANTA MONICA COMMUNITY COLLEGE DISTRICT MEASURE S EXPENDITURES FUND 42.3

		014	D 72		
As	of S	epte	mber	30,	201

\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$1,745 \$20,700 \$2,154 \$1,508	\$0 \$0 \$17,486 \$10,952	\$0 \$0 \$4,800	\$648 \$0 \$2,257	\$0 \$0 \$17,221	\$0 \$0 \$0	\$813 \$0	\$0 \$1,740	\$0 \$0	\$0 \$0	\$0 \$0	\$0	\$3,206
\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$20,700 \$2,154			\$0	\$0 \$0 \$17,221	\$0 \$0 \$0	\$0	\$0 \$1,740	\$0 \$0	\$0 \$0	\$0 \$0	\$0	
\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$20,700 \$2,154			\$0	\$0 \$0 \$17,221	\$0 \$0	\$0	\$0 \$1,740	\$0 \$0	\$0 \$0	\$0 \$0	\$0	
\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$20,700 \$2,154			\$0	\$0 \$0 \$17.221	\$0 \$0	\$0	\$0 \$1,740	\$0 \$0	\$0 \$0	\$0 \$0	\$0	
\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$2,154				\$0 \$17,221	\$0 \$0	\$0	\$1,740	\$0	\$0	90	60	
\$0 \$0 \$0 \$0 \$0 \$0				\$2,257	\$17,221	\$0	00.570					φU	\$22,440
\$0 \$0 \$0 \$0	\$1,508	\$10,952	64 000				\$3,570	\$0	\$0	\$0	\$0	\$0	\$47,488
\$0 \$0	60		\$1,986	\$46	\$0	\$12,083	\$5,034	\$0	\$0	\$0	\$0	\$0	\$31,608
	Φ0]	\$0	\$0	\$0	\$1,086	\$0	\$1,308	\$0	\$0	\$0	\$0	\$0	\$2,394
\$0  \$0	\$2,555,940	\$5,925,152	\$78,717	\$77,320	\$5,509	\$715	\$0	\$3,721	\$11,308,792	\$16,249,515	\$0	\$0	\$36,205,381
\$0 \$2,266,766	\$2,674,054	\$0	\$37,111	\$75,163	\$0	\$0	\$0	\$0	\$0	\$287,176	\$0	\$0	\$5,340,270
\$0 \$0	\$4,813	\$38,330	\$42,968	\$50,952	\$9,735	\$0	\$0	\$0	\$0	\$49,171	\$0	\$0	\$195,968
\$0 \$0	\$131,009	\$161,847	\$54,069	\$32,306	\$30,909	\$4,123	\$22,296	\$38,186	\$516,217	\$851,397	\$0	\$0	\$1,842,359
\$0 \$0	\$158,766	\$373,559	\$184,088	\$92,118	\$224,994	\$59,525	\$29,714	\$50,380	\$285,057	\$420,233	\$0	\$0	\$1,878,433
\$0 \$0	\$0	\$14,393	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$14,393
\$0 \$0	\$0	\$0	\$0	\$11,381	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$11,381
\$0 \$2,266,766	\$5,550,689	\$6,541,719	\$403,737	\$342,192	\$289,454	\$76,445	\$62,735	\$94,027	\$12,110,066	\$17,857,492	\$0	\$0	\$45,595,322
Other Funding Source:	•	•	•	•	•		•		•	•	•		
State of California \$1,321,000	received												
Mease U \$21,131,135, Measur	re AA \$6,870,49	90, Measure V	\$33,624,909 all	located									
	21,681,308 allo	cated											
St Vle	Other Funding Source: ate of California \$1,321,000 ease U \$21,131,135, Measu	Other Funding Source: ate of California \$1,321,000 received pase U \$21,131,135, Measure AA \$6,870,4	Other Funding Source: ate of California \$1,321,000 received	Other Funding Source: ate of California \$1,321,000 received ease U \$21,131,135, Measure AA \$6,870,490, Measure V \$33,624,909 al	\$0 \$2,266,766 \$5,550,689 \$6,541,719 \$403,737 \$342,192 Other Funding Source: ate of California \$1,321,000 received base U \$21,131,135, Measure AA \$6,870,490, Measure V \$33,624,909 allocated	\$0 \$2,266,766 \$5,550,689 \$6,541,719 \$403,737 \$342,192 \$289,454 Other Funding Source: ate of California \$1,321,000 received pase U \$21,131,135, Measure AA \$6,870,490, Measure V \$33,624,909 allocated	\$0 \$2,266,766 \$5,550,689 \$6,541,719 \$403,737 \$342,192 \$289,454 \$76,445 Other Funding Source: ate of California \$1,321,000 received aase U \$21,131,135, Measure AA \$6,870,490, Measure V \$33,624,909 allocated	\$0 \$2,266,766 \$5,550,689 \$6,541,719 \$403,737 \$342,192 \$289,454 \$76,445 \$62,735 Other Funding Source: ate of California \$1,321,000 received aase U \$21,131,135, Measure AA \$6,870,490, Measure V \$33,624,909 allocated	\$0 \$2,266,766 \$5,550,689 \$6,541,719 \$403,737 \$342,192 \$289,454 \$76,445 \$62,735 \$94,027 Other Funding Source: at of California \$1,321,000 received ease U \$21,131,135, Measure AA \$6,870,490, Measure V \$33,624,909 allocated	\$0 \$2,266,766 \$5,550,689 \$6,541,719 \$403,737 \$342,192 \$289,454 \$76,445 \$62,735 \$94,027 \$12,110,066 Other Funding Source: ate of California \$1,321,000 received asse U \$21,131,135, Measure AA \$6,870,490, Measure V \$33,624,909 allocated	\$0 \$2,266,766 \$5,550,689 \$6,541,719 \$403,737 \$342,192 \$289,454 \$76,445 \$62,735 \$94,027 \$12,110,066 \$17,857,492 20ther Funding Source: ate of California \$1,321,000 received asse U \$21,131,135, Measure AA \$6,870,490, Measure V \$33,624,909 allocated	\$0 \$2,266,766 \$5,550,689 \$6,541,719 \$403,737 \$342,192 \$289,454 \$76,445 \$62,735 \$94,027 \$12,110,066 \$17,857,492 \$0  Ther Funding Source: ate of California \$1,321,000 received asse U \$21,131,135, Measure AA \$6,870,490, Measure V \$33,624,909 allocated	\$0 \$2,266,766 \$5,550,689 \$6,541,719 \$403,737 \$342,192 \$289,454 \$76,445 \$62,735 \$94,027 \$12,110,066 \$17,857,492 \$0 \$0  Ther Funding Source: ate of California \$1,321,000 received asse U \$21,131,135, Measure AA \$6,870,490, Measure V \$33,624,909 allocated

Parking Garage and Grounds - Student Services

Actual Measure S Expenditures
Running Balance

Project Description:
Consolidates various student services departments and college administration in a single complex at the front of the campus


Facility Size: 110,000 sq/ft & 500 cars underground parking

Phase 1 completed Phase 2 In construction

Architect:

Steinberg Architects, Morris Architects

Contractor: Minaco, Bernards



Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20	Combined Totals
	g																	
S7100044																		
Pico Promenade Improvements (10)																		
Building & Additions		\$0				\$883,401	\$0	\$0		\$0	\$0	\$0	\$0		\$0		\$0	
Architect		\$0			\$69,190	\$28,540	\$864	\$0		\$0	\$0	\$0	\$0		\$0		\$0	\$98,595
Inspection & Testing		\$0			\$0	\$7,591	\$0	\$0		\$0	\$0	\$0	\$0		\$0		\$0	
Project Management		\$0				\$25,548		\$0		\$0	\$0	\$0	\$0		\$0		\$0	
Total		\$0	\$0	\$0	\$72,066	\$945,080	\$864	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,018,009
Project Budget	\$1,018,009																	
Less Other Funding	\$0																	
Net	\$1,018,009																	
Actual Measure S Expenditures	\$1,018,009																	
Running Balance	\$0																	
			_															
S7100004																		
Master Planning (11)		-			20	**	6444 540	640.000		**	20			20				0454.000
Consultants		\$0			\$0	\$0		\$13,320		\$0	\$0	\$0	\$0		\$0		\$0	
Printing		\$0			\$0	\$0		\$0		\$0	\$0	\$0	\$0		\$0		\$0	\$4,157
Advertising		\$0 \$0			\$0 \$0	\$0 \$0	\$3,000	\$0 \$200	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0		\$0 \$0	\$0 \$0	\$0 \$0	
Other Contract Services								\$200 \$24,736		\$0 \$0	\$0 \$0	\$0 \$0	\$0					\$642
Architect		\$0				\$0							\$0		\$0		\$0	
Project Management		\$0 \$0			\$0 \$0	\$0	\$16,638	\$9,341 \$2,842		\$0	\$7,845 \$0	\$0 \$0	\$0		\$0	\$0	\$0	
Filling Fees						\$0				\$0			\$0		\$0		\$0	
Total		\$0	\$0	\$0	\$0	\$0	\$658,143	\$50,439	\$0	\$0	\$7,845	\$0	\$0	\$0	\$0	\$0	\$0	\$716,428
Project Budget	\$716,428	4																
Less Other Funding	\$0	4																
Net	\$716,428																	
Actual Measure S Expenditures	\$716,428																	
Running Balance	\$0																	
S7100048																		
Other Bond Related Expenses (12)																		
Consultants		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,971	\$2,524	\$6,239	\$1,354	\$0	\$0	\$0	\$0	\$13,089
Lease/Rental		\$0			\$0	\$0	\$0	\$0		\$15.099	\$15,285	\$14,809	\$13,418		\$16,611	\$17,281	\$3.953	\$120,717
Supplies		\$0				\$0		\$0		\$10,099	\$10,200	\$14,009	\$13,410		\$10,011		\$0,555	\$3.638
Legal		\$0				\$0		\$15,649		\$450	\$503	\$38,130	\$9,186		\$0		\$0	\$86,236
Software License		\$0				\$0		\$1,049		\$3,565	\$003	\$4,200	\$9,100		\$0		\$0 \$0	
Advertising		\$0			\$0	\$0		\$1,997		\$3,303	\$0	\$4,200	\$0		\$0		\$0	
Other Contract Services		\$0				\$1,800		\$23,558		\$15,816	\$13,627	\$13,952	\$12,963		\$18,900		\$0	
Moving Services		\$0				\$1,800		\$23,558 \$0		\$15,616	\$13,627	\$13,952	\$12,963		\$18,900		\$0	
Project Management		\$0			\$0	\$0		\$13,179		\$0	\$0	\$0	\$0		\$0 \$0		\$0 \$0	
Cap Equipment		\$0				\$0		\$10,086		\$0	\$0	\$0	\$0		\$0		\$0	
Non-Cap Equipment		\$0				\$0 \$0		\$10,086		\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0		\$0 \$0		\$0 \$0	
Total		\$0				\$1.800		\$2,860		\$37,901	\$31,939	\$77,330	\$36.921		\$35.511		\$3.953	
Project Budget	\$609.282		1 \$0	, \$U	\$0	φ1,000	<b>300,100</b>	φ01,328	300,713	\$31,3UT	\$31,939	φιι, <b>33</b> 0	\$30, <b>3</b> 21	\$45,144	<b>\$35,511</b>	\$32,5Ub	<b>\$3,953</b>	\$400,03Z
Less Other Funding	\$609,282																	
Less Other Funding Net	\$609,282																	
Actual Measure S Expenditures	\$609,282 \$456.832																	
Running Balance	\$152,450	1																

Figuresing	Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20	Combined Totals
Act Actions (Cornel Service)																			
Section   Sect																			
Communicate Sentence																			
Archaed   \$0																			
Suppose   Supp															\$0	\$			
Imperior of February (1997) (1																		\$0	
Project Management																			
Trial (1997)	Inspection & Testing			\$0	\$0	\$0				\$0	\$0		\$0		\$0	\$1	0 \$0	\$0	\$0
Fines Diagret   50   50   50   50   50   50   50   5																			
Net				\$0	\$0	\$0	\$45,734	-\$45,734	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$	0 \$0	\$0	\$0
Net	Project Budget	\$0	j		•		•				•		•	•			•	•	
Net	Less Other Funding	\$0	J]																
ST006598T Acquisition (16)	Net	\$0	آز																
ST006598T Acquisition (16)	Actual Measure S Expenditures	\$0	آز																
ST006598T Acquisition (16)	Running Balance	\$0	أد																
Real Property Acquisition (14)    Control Control Services   50   50   50   50   50   50   50   5	<b>J</b>																		
Real Property Acquisition (14)    Control Control Services   50   50   50   50   50   50   50   5	S7100057																		
Other Contract Services		+	+				-							+					
Engineering   \$0   \$0   \$0   \$0   \$0   \$0   \$0   \$		+	60	¢Λ	en	<u> </u>	en	\$18 721	en.	¢∩	er.	•	90	60	en.	e.	n en	en	\$18 721
Engineering   \$0   \$0   \$0   \$0   \$0   \$0   \$0   \$		+		\$0 \$0	90	90	\$0 \$0		\$0	\$0 \$0	\$0	90	\$0		\$0 \$0	9	0 80	\$0	
Impector A Testing   S0   S0   S0   S0   S0   S0   S0   S		-													90	9			
Project Management   So   So   So   So   So   So   So   S		+																	
Total		+			90	30			\$0				φO		φ <u>0</u>	9	0 00	\$0	
Project Budget		+																	
Lies Other Funding		C45 507		<b>\$</b> U	Şu	)  \$0	<b>\$</b> 0]	\$45,59 <i>1</i>	<b>\$</b> 0	ŞU	şι	J  \$U	\$U	ŞU	<b>\$</b> 0	<b>)</b>	ιυ <b>ఫ</b> υ	<b>\$</b> 0	\$45,597
Net Actual Measure S. Expenditures																			
Actual Measure S Expenditures																			
Running Balance   S0   S7100072																			
\$7100072 Campus \$ignage (15) \$50 \$50 \$50 \$50 \$50 \$50 \$50 \$50 \$50 \$50																			
Campus Signage (15)   So   So   So   So   So   So   So   S	Running Balance	\$0	1																
Campus Signage (15)   So   So   So   So   So   So   So   S					,														,
Supplies																			
Chief Contract Services   S0   S0   S0   S0   S0   S0   S0   S																			
Chief Contract Services   S0   S0   S0   S0   S0   S0   S0   S				\$0	\$0	\$0	\$0		\$303	\$0	\$0	\$0	\$0		\$0		50 \$0	\$0	\$303
Architect					1 80	)  \$0												1 \$0	
Building & Additions   \$0   \$0   \$0   \$0   \$0   \$0   \$0   \$			\$0									SI \$01							
Inspection & Testing	Other Contract Services		\$0 \$0	\$0	\$0	\$0								\$0				\$0	
Project Management \$ 0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	Architect		\$0 \$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0			0 \$0	\$0 \$0	\$0
Cap Equipment	Architect Building & Additions		\$0 \$0 \$0 \$0	\$0 \$0 \$0	\$0 \$0 \$0	\$0 \$0 \$0 \$0	\$0 \$0	\$0 \$0	\$0 \$638	\$0 \$0	\$( \$(	\$0 \$1,440	\$0 \$1,325	\$0 \$416,937	\$0 \$0	\$	0 \$0 0 \$0	\$0 \$0 \$0	\$0 \$420,339
Cap Equipment	Architect Building & Additions Inspection & Testing		\$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0	\$0 \$0 \$0	\$0 \$638 \$0	\$0 \$0 \$0	\$( \$( \$(	\$0 \$1,440 \$0 \$0	\$0 \$1,325 \$0	\$0 \$416,937 \$0	\$0 \$0 \$0	\$ \$ \$	60 \$0 60 \$0 60 \$0	\$0 \$0 \$0 \$0	\$0 \$420,339 \$0
Non-Cap Equipment   \$0   \$0   \$0   \$0   \$0   \$0   \$0   \$	Architect Building & Additions Inspection & Testing		\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0	\$0 \$638 \$0 \$22,953	\$0 \$0 \$0 \$0	\$( \$( \$( \$(	\$0 \$1,440 \$0 \$8,260	\$0 \$1,325 \$0 \$8,388	\$0 \$416,937 \$0 \$28,622	\$0 \$0 \$0 \$165	\$ \$ \$	50 \$0 50 \$0 50 \$0 50 \$0	\$0 \$0 \$0 \$0	\$0 \$420,339 \$0 \$68,388
\$0   \$0   \$0   \$0   \$0   \$0   \$0   \$0	Architect Building & Additions Inspection & Testing Project Management		\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0	\$0 \$638 \$0 \$22,953	\$0 \$0 \$0 \$0 \$0	\$( \$( \$( \$( \$(	\$0 \$1,440 \$0 \$0 \$8,260 \$0	\$0 \$1,325 \$0 \$8,388 \$0	\$0 \$416,937 \$0 \$28,622 \$0	\$0 \$0 \$0 \$165 \$0	\$ \$ \$ \$	0 \$0 0 \$0 0 \$0 0 \$0 0 \$0	\$0 \$0 \$0 \$0 \$0	\$0 \$420,339 \$0 \$68,388 \$156,258
Froject Budget	Architect Building & Additions Inspection & Testing Project Management Cap Equipment		\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0	\$0 \$638 \$0 \$22,953 \$156,258	\$0 \$0 \$0 \$0 \$0	\$( \$( \$( \$( \$(	\$0 \$1,440 \$0 \$0 \$8,260 \$0	\$0 \$1,325 \$0 \$8,388 \$0	\$0 \$416,937 \$0 \$28,622 \$0	\$0 \$0 \$0 \$165 \$0	\$ \$ \$ \$	0 \$0 0 \$0 0 \$0 0 \$0 0 \$0	\$0 \$0 \$0 \$0 \$0	\$0 \$420,339 \$0 \$68,388 \$156,258
Less Other Funding   \$0   Net   \$706,713   \$706,713   \$706,713   \$10,470   \$119,470	Architect Building & Additions Inspection & Testing Project Management Cap Equipment Non-Cap Equipment		\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0	\$0 \$638 \$0 \$22,953 \$156,258 \$0	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$1,440 \$0 \$8,260 \$0 \$8,260 \$0 \$0	\$0 \$1,325 \$0 \$8,388 \$0 \$0	\$0 \$416,937 \$0 \$28,622 \$0 \$0	\$0 \$0 \$0 \$165 \$0 \$3,402	\$ \$ \$ \$ \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$420,339 \$0 \$68,388 \$156,258 \$3,402
Net	Architect Building & Additions Inspection & Testing Project Management Cap Equipment Non-Cap Equipment Total	\$706,713	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0	\$0 \$638 \$0 \$22,953 \$156,258 \$0	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$1,440 \$0 \$8,260 \$0 \$8,260 \$0 \$0	\$0 \$1,325 \$0 \$8,388 \$0 \$0	\$0 \$416,937 \$0 \$28,622 \$0 \$0	\$0 \$0 \$0 \$165 \$0 \$3,402	\$ \$ \$ \$ \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$420,339 \$0 \$68,388 \$156,258 \$3,402
Actual Measure S Expenditures   \$706,713	Architect Building & Additions Inspection & Testing Project Management Cap Equipment Non-Cap Equipment Total Project Budget		\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0	\$0 \$638 \$0 \$22,953 \$156,258 \$0	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$1,440 \$0 \$8,260 \$0 \$8,260 \$0 \$0	\$0 \$1,325 \$0 \$8,388 \$0 \$0	\$0 \$416,937 \$0 \$28,622 \$0 \$0	\$0 \$0 \$0 \$165 \$0 \$3,402	\$ \$ \$ \$ \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$420,339 \$0 \$68,388 \$156,258 \$3,402
S	Architect Building & Additions Inspection & Testing Project Management Cap Equipment Non-Cap Equipment Total Project Budget Less Other Funding	\$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0	\$0 \$638 \$0 \$22,953 \$156,258 \$0	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$1,440 \$0 \$8,260 \$0 \$8,260 \$0 \$0	\$0 \$1,325 \$0 \$8,388 \$0 \$0	\$0 \$416,937 \$0 \$28,622 \$0 \$0	\$0 \$0 \$0 \$165 \$0 \$3,402	\$ \$ \$ \$ \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$420,339 \$0 \$68,388 \$156,258 \$3,402
S Cost of Issuance (16) Cost of Issuance Sit o	Architect Building & Additions Inspection & Testing Project Management Cap Equipment Non-Cap Equipment Total Project Budget Less Other Funding Net	\$0 \$706,713	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0	\$0 \$638 \$0 \$22,953 \$156,258 \$0	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$1,440 \$0 \$8,260 \$0 \$8,260 \$0 \$0	\$0 \$1,325 \$0 \$8,388 \$0 \$0	\$0 \$416,937 \$0 \$28,622 \$0 \$0	\$0 \$0 \$0 \$165 \$0 \$3,402	\$ \$ \$ \$ \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$420,339 \$0 \$68,388 \$156,258 \$3,402
Cost of Issuance \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	Architect Building & Additions Inspection & Testing Project Management Cap Equipment Non-Cap Equipment Total Project Budget Less Other Funding Net Actual Measure S Expenditures	\$0 \$706,713 \$706,713	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0	\$0 \$638 \$0 \$22,953 \$156,258 \$0	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$1,440 \$0 \$8,260 \$0 \$8,260 \$0 \$0	\$0 \$1,325 \$0 \$8,388 \$0 \$0	\$0 \$416,937 \$0 \$28,622 \$0 \$0	\$0 \$0 \$0 \$165 \$0 \$3,402	\$ \$ \$ \$ \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$420,339 \$0 \$68,388 \$156,258 \$3,402
Cost of Issuance \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	Architect Building & Additions Inspection & Testing Project Management Cap Equipment Non-Cap Equipment Total Project Budget Less Other Funding Net Actual Measure S Expenditures	\$0 \$706,713 \$706,713	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0	\$0 \$638 \$0 \$22,953 \$156,258 \$0	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$1,440 \$0 \$8,260 \$0 \$8,260 \$0 \$0	\$0 \$1,325 \$0 \$8,388 \$0 \$0	\$0 \$416,937 \$0 \$28,622 \$0 \$0	\$0 \$0 \$0 \$165 \$0 \$3,402	\$ \$ \$ \$ \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$420,339 \$0 \$68,388 \$156,258 \$3,402
Cost of Issuance \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	Architect Building & Additions Inspection & Testing Project Management Cap Equipment Non-Cap Equipment Total Project Budget Less Other Funding Net Actual Measure S Expenditures	\$0 \$706,713 \$706,713	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0	\$0 \$638 \$0 \$22,953 \$156,258 \$0	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$1,440 \$0 \$8,260 \$0 \$8,260 \$0 \$0	\$0 \$1,325 \$0 \$8,388 \$0 \$0	\$0 \$416,937 \$0 \$28,622 \$0 \$0	\$0 \$0 \$0 \$165 \$0 \$3,402	\$ \$ \$ \$ \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$420,339 \$0 \$68,388 \$156,258 \$3,402
Total   \$0   \$0   \$0   \$0   \$0   \$0   \$0   \$	Architect Building & Additions Inspection & Testing Project Management Cap Equipment Non-Cap Equipment Total Project Budget Less Other Funding Net Actual Measure S Expenditures Running Balance	\$0 \$706,713 \$706,713	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0	\$0 \$638 \$0 \$22,953 \$156,258 \$0	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$1,440 \$0 \$8,260 \$0 \$8,260 \$0 \$0	\$0 \$1,325 \$0 \$8,388 \$0 \$0	\$0 \$416,937 \$0 \$28,622 \$0 \$0	\$0 \$0 \$0 \$165 \$0 \$3,402	\$ \$ \$ \$ \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$420,339 \$0 \$68,388 \$156,258 \$3,402
Project Budget         \$119,470           Less Other Funding         \$0           Net         \$119,470           Actual Measure AA Expenditures         \$119,470	Architect Building & Additions Inspection & Testing Project Management Cap Equipment Non-Cap Equipment Total Project Budget Less Other Funding Net Actual Measure S Expenditures Running Balance  S Cost of Issuance (16)	\$0 \$706,713 \$706,713	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$32,225	\$0 \$638 \$0 \$22,953 \$156,258 \$0 \$204,064	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$( \$( \$( \$) \$( \$) \$( \$)	\$0 \$1,440 \$0 \$0 \$0 \$8,260 \$0 \$0 \$5 \$9,700	\$0 \$1,325 \$0 \$8,388 \$0 \$0 \$9,712	\$0 \$416,937 \$0 \$28,622 \$0 \$0 \$445,559	\$0 \$0 \$0 \$165 \$0 \$3,402 \$4,618	\$ \$	00 \$0 00 \$0 10 \$0 00 \$0 00 \$0 00 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$420,339 \$0 \$68,388 \$156,258 \$3,402 \$706,713
Less Other Funding         \$0           Net         \$119,470           Actual Measure AA Expenditures         \$119,470	Architect Building & Additions Inspection & Testing Project Management Cap Equipment Non-Cap Equipment Non-Cap Equipment Total Project Budget Less Other Funding Net Actual Measure S Expenditures Running Balance  S Cost of Issuance (16) Cost of Issuance	\$0 \$706,713 \$706,713	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$C \$C \$C \$C \$C \$C \$C \$C \$C \$C \$C \$C \$C \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$32,225	\$0 \$638 \$0 \$22,953 \$156,258 \$204,064	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$( \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3	\$0 \$1,440 \$0 \$0 \$8,260 \$0 \$0 \$9,700	\$0 \$1,325 \$0 \$8,388 \$0 \$0 \$9,712	\$0 \$416,937 \$0 \$28,622 \$0 \$0 \$445,559	\$0 \$0 \$0 \$165 \$0 \$3,402 \$4,618	\$ \$ \$ \$ \$ \$	00 \$0 00 \$0 00 \$0 00 \$0 00 \$0 00 \$0 00 \$0 00 \$0 00 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$00 \$420,339 \$00 \$68,388 \$156,258 \$3,402 \$706,713
Net         \$119,470           Actual Measure AA Expenditures         \$119,470	Architect Building & Additions Inspection & Testing Project Management Cap Equipment Non-Cap Equipment Total Project Budget Less Other Funding Net Actual Measure S Expenditures Running Balance  S Cost of Issuance (16) Cost of Issuance Total	\$0 \$706,713 \$706,713 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$C \$C \$C \$C \$C \$C \$C \$C \$C \$C \$C \$C \$C \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$32,225	\$0 \$638 \$0 \$22,953 \$156,258 \$204,064	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$( \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3	\$0 \$1,440 \$0 \$0 \$8,260 \$0 \$0 \$9,700	\$0 \$1,325 \$0 \$8,388 \$0 \$0 \$9,712	\$0 \$416,937 \$0 \$28,622 \$0 \$0 \$445,559	\$0 \$0 \$0 \$165 \$0 \$3,402 \$4,618	\$ \$ \$ \$ \$ \$	00 \$0 00 \$0 00 \$0 00 \$0 00 \$0 00 \$0 00 \$0 00 \$0 00 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$00 \$420,339 \$00 \$68,388 \$156,258 \$3,402 \$706,713
Actual Measure AA Expenditures \$119,470	Architect Building & Additions Inspection & Testing Project Management Cap Equipment Non-Cap Equipment Total Project Budget Less Other Funding Net Actual Measure S Expenditures Running Balance S Cost of Issuance (16) Cost of issuance Total	\$706,713 \$706,713 \$0 \$119,470	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$C \$C \$C \$C \$C \$C \$C \$C \$C \$C \$C \$C \$C \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$32,225	\$0 \$638 \$0 \$22,953 \$156,258 \$204,064	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$( \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3	\$0 \$1,440 \$0 \$0 \$8,260 \$0 \$0 \$9,700	\$0 \$1,325 \$0 \$8,388 \$0 \$0 \$9,712	\$0 \$416,937 \$0 \$28,622 \$0 \$0 \$445,559	\$0 \$0 \$0 \$165 \$0 \$3,402 \$4,618	\$ \$ \$ \$ \$ \$	00 \$0 00 \$0 00 \$0 00 \$0 00 \$0 00 \$0 00 \$0 00 \$0 00 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$00 \$420,339 \$00 \$68,388 \$156,258 \$3,402 \$706,713
	Architect Building & Additions Inspection & Testing Project Management Cap Equipment Non-Cap Equipment Total Project Budget Less Other Funding Net Actual Measure S Expenditures Running Balance  S Cost of Issuance (16) Cost of Issuance Total Project Budget Less Other Funding Net Actual Measure S Expenditures Running Balance	\$119,470 \$10,713	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$C \$C \$C \$C \$C \$C \$C \$C \$C \$C \$C \$C \$C \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$32,225	\$0 \$638 \$0 \$22,953 \$156,258 \$204,064	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$( \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3	\$0 \$1,440 \$0 \$0 \$8,260 \$0 \$0 \$9,700	\$0 \$1,325 \$0 \$8,388 \$0 \$0 \$9,712	\$0 \$416,937 \$0 \$28,622 \$0 \$0 \$445,559	\$0 \$0 \$0 \$165 \$0 \$3,402 \$4,618	\$ \$ \$ \$ \$ \$	00 \$0 00 \$0 00 \$0 00 \$0 00 \$0 00 \$0 00 \$0 00 \$0 00 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$00 \$420,339 \$00 \$68,388 \$156,258 \$3,402 \$706,713
Running Balance \$0	Architect Building & Additions Inspection & Testing Project Management Cap Equipment Non-Cap Equipment Total Project Budget Less Other Funding Net Actual Measure S Expenditures Running Balance S Cost of Issuance (16) Cost of Issuance Total Project Budget Less Other Funding Net Actual Measure S Expenditures Running Balance S Cost of Issuance (16) Cost of Issuance Total Project Budget Less Other Funding Net	\$119,470 \$119,470	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$C \$C \$C \$C \$C \$C \$C \$C \$C \$C \$C \$C \$C \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$32,225	\$0 \$638 \$0 \$22,953 \$156,258 \$204,064	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$( \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3	\$0 \$1,440 \$0 \$0 \$8,260 \$0 \$0 \$9,700	\$0 \$1,325 \$0 \$8,388 \$0 \$0 \$9,712	\$0 \$416,937 \$0 \$28,622 \$0 \$0 \$445,559	\$0 \$0 \$0 \$165 \$0 \$3,402 \$4,618	\$ \$ \$ \$ \$ \$	00 \$0 00 \$0 00 \$0 00 \$0 00 \$0 00 \$0 00 \$0 00 \$0 00 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$00 \$420,339 \$00 \$68,388 \$156,258 \$3,402 \$706,713
	Architect Building & Additions Inspection & Testing Project Management Cap Equipment Non-Cap Equipment Total Project Budget Less Other Funding Net Actual Measure S Expenditures Running Balance  S Cost of Issuance (16) Cost of Issuance Total Project Budget Less Other Funding Net Less Other Funding Net Actual Measure A Expenditures Running Balance	\$119,470 \$119,470 \$119,470	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$C \$C \$C \$C \$C \$C \$C \$C \$C \$C \$C \$C \$C \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$32,225	\$0 \$638 \$0 \$22,953 \$156,258 \$204,064	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$( \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3	\$0 \$1,440 \$0 \$0 \$8,260 \$0 \$0 \$9,700	\$0 \$1,325 \$0 \$8,388 \$0 \$0 \$9,712	\$0 \$416,937 \$0 \$28,622 \$0 \$0 \$445,559	\$0 \$0 \$0 \$165 \$0 \$3,402 \$4,618	\$ \$ \$ \$ \$ \$	00 \$0 00 \$0 00 \$0 00 \$0 00 \$0 00 \$0 00 \$0 00 \$0 00 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$00 \$420,339 \$00 \$68,388 \$156,258 \$3,402 \$706,713
	Architect Building & Additions Inspection & Testing Project Management Cap Equipment Non-Cap Equipment Total Project Budget Less Other Funding Net Actual Measure S Expenditures Running Balance  S Cost of Issuance (16) Cost of Issuance Total Project Budget Less Other Funding Net Actual Measure S Expenditures Running Balance	\$119,470 \$119,470 \$119,470	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$C \$C \$C \$C \$C \$C \$C \$C \$C \$C \$C \$C \$C \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$32,225	\$0 \$638 \$0 \$22,953 \$156,258 \$204,064	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$( \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3 \$3	\$0 \$1,440 \$0 \$0 \$8,260 \$0 \$0 \$9,700	\$0 \$1,325 \$0 \$8,388 \$0 \$0 \$9,712	\$0 \$416,937 \$0 \$28,622 \$0 \$0 \$445,559	\$0 \$0 \$0 \$165 \$0 \$3,402 \$4,618	\$ \$ \$ \$ \$ \$	00 \$0 00 \$0 00 \$0 00 \$0 00 \$0 00 \$0 00 \$0 00 \$0 00 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$00 \$420,339 \$00 \$68,388 \$156,258 \$3,402 \$706,713

\$7,958,606 \$14,601,366 \$10,740,621 \$8,321,918 \$20,819,624 \$8,933,245 \$617,492 \$651,441 \$878,632 \$1,287,285 \$6,814,769 \$6,083,251 \$12,554,384 \$21,858,285 \$11,111,633 \$911,903 \$134,144,455

Grand Total

# SANTA MONICA COMMUNITY COLLEGE DISTRICT MEASURE S EXPENDITURES FUND 42.3

1 0110 42.0	
As of September 30.	2019

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20	Combined Totals
Measure S Interest		17/18 Final	18/19 Final															
Parking Garage and Grounds - Student Services (9)																		
Site Imptovement		\$568	\$0															
Building & Additions		\$8,224,377	\$629,869															
Architect		\$189,078	\$67,105															
Engineering		\$11,000	\$15,000															
nspection & Testing		\$125,080	\$0															
Project Management		\$171,448	\$0															
Total		\$8,721,552	\$711,974															
Project Budget	\$9,433,526																	
Actual Measure S Interest Expenditures	\$9,433,526																	
Running Balance	\$0																	

# Measure AA Project Schedule As of September 30, 2019

	Project Name	Completion	2018	2019	2020	2021	2022
101	Environmental Performance - Central Plant Connections	Completed					
102	Infrastructure & Technology - Information Technology Relocation	Completed					
103	Media and Technology Complex - Academy Site	Completed					
104	Replacement Health/PE/Fitness/Dance Building with Central Plant	Completed					
105	Drescher - Academic Modernization, Bookstore, Pico Promenade	Deferred					
106	Replacement Math and Science Extension Building	May 2023					
107	Madison East Wing Seismic Upgrade	Completed					
108	Renovation of Corsair Stadium	Completed					
109	Career Opportunity and Advancement Center (Bundy)	Completed					
110	Malibu Center	April 2022					
111	Business & Facilities Infrastructure	Completed					
112	Master Planning, Program Management, Overhead	On-Going					
113	Energy Efficiency Projects	Completed					
114	Community Classroom & Facility Projects	Completed					
115	Real Property Acquisition	Completed					
116	Roadways, Walkways, Grounds, Parking Lots, and Garages	Completed					
117	Infrastructure & Technology - Technology	Completed					
118	Infrastructure & Technology - Utility	Completed					
119	Emergency Lighting, Fire Alarm, and Security System	On-Going					
120	Student Services	Completed					
121	Cost of Issuance	Completed					
122	Management Reserve	On-Going					
123	Unissuable Bond	Completed					
				Disconi			
			l l lu	Planning	In Consti	ruction	

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20	Combined Totals
AA 7100062													
Environmental Performance - Central Plant Connections (101)													
Legal		\$0	\$0	\$0	\$125	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$125
Other Contract Services		\$0	\$0	\$49,837	\$16,239	\$0	\$0	\$0	\$0	\$9,920	\$0	\$0	\$75,996
Consultants		\$0	\$0	\$0	\$0	\$28	\$0	\$0	\$0	\$0	\$0	\$0	\$28
Building & Additions		\$0	\$0	\$0	\$361	\$729	\$640	\$1,328,592	\$6,934,044	\$446,861	\$0	\$0	\$8,711,229
Architect		\$0	\$385	\$148,311	\$176,897	\$36,256	\$0	\$0	\$0	\$0	\$15,699	\$0	\$377,547
Engineering		\$48,500	\$0	\$4,000	\$0	\$152,010	\$39,638	\$66,918	\$138,887	\$62,883	\$0	\$0	\$512,836
Inspection & Testing		\$0	\$0	\$7,688	\$0	\$0	\$0	\$7,310	\$137,150	\$4,382	\$0	\$0	\$156,529
Project Management		\$0	\$17,263	\$55,116	\$48,685	\$61,908	\$19,313	\$104,575	\$526,072	\$99,840	\$190	\$0	\$932,961
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$48,500	\$17,648	\$264,951	\$242,307	\$250,931	\$59,591	\$1,507,396	\$7,736,152	\$623,886	\$15,889	\$0	\$10,767,251
Project Budget	\$10,767,251	•		•			•		•		•		
Less Other Funding	\$0												
Net	\$10,767,251												
Actual Measure AA Expenditures	\$10,767,251												
Running Balance	\$0												

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20	Combined Totals
Flojects	Duuget	03/10 1 11101	10/1111111111	11/12 I IIIai	12/13 1 11101	13/14 1 11101	14/13 1 11101	13/10 1 11101	10/17 1 11101	17/10111101	10/13 1 11101	13/20	Combined Totals
AA 7100063	1					1	1						
Infrastructure & Technology - IT Relocation (102)													
		\$0	\$0	\$965	\$8,442	\$3,137	\$2,600	\$0	\$0	\$0	\$0	\$0	\$15,144
Supplies Consultants		\$0 \$0	\$0	\$903	\$0,442	\$408	\$2,000	\$7.800	\$0	\$0 \$0	\$0 \$0	\$0	
Maintenance Contract		\$0 \$0	\$0	\$0 \$0	\$0 \$0	\$107,390	\$0	\$7,000	\$0 \$79	\$0 \$0	\$0 \$0		
		\$0 \$0	\$0	\$0 \$0					\$79	\$0 \$0	\$0 \$0		
Legal					\$1,363	\$50	\$0	\$0	Ψ°			\$0	
Printing		\$0		\$0 \$0	\$0	\$1,624	\$0	\$0	\$0	\$0	\$0		
Postage		\$0		ΨΟ	\$0	\$1,567	\$0	\$0	\$0		\$0		
Other Contract Services		\$0		\$2,163	\$15,259	\$23,356	\$0	\$19,050	\$4,500		\$0		
Moving		\$0	\$0	\$0	\$577	\$266	\$27,655		\$0	\$0	\$0	\$0	
Site Improvement		\$0	\$0	\$0	\$24	\$0	\$0	\$0	\$0	\$0	\$0		
Building & Additions		\$0	\$0	\$0	\$1,767,083	\$9,667,362	\$4,288,987	\$1,203,916	\$165,229		\$0		
Architect		\$105,049	\$482,261	\$505,580	\$183,181	\$287,201	\$236,860	\$120,091	\$0	\$0	\$0		
Engineering		\$0	\$0	\$10,037	\$11,065	\$17,147	\$19,512		\$1,956		\$0		
Inspection & Testing		\$10,291	\$8,793	\$21,449	\$137,523	\$499,982	\$200,262	\$568	\$0	\$0	\$0		
Project Management		\$33,460	\$76,290	\$84,991	\$331,754	\$431,730	\$297,951	\$22,978	\$1,500	\$0	\$0		
Cap Equipment		\$0	\$0	\$0	\$29,422	\$645,830	-\$29,090	\$589,604	\$9,811	\$0	\$0	\$0	
Non-Cap Equipment		\$0	\$0	\$0	\$18,344	\$10,852	\$277,219	\$1,891	\$20,689	\$0	\$0	\$0	\$328,994
Total		\$148,800	\$567,344	\$625,185	\$2,504,035	\$11,697,901	\$5,321,956	\$2,091,584	\$203,764	-\$19,798	\$0	\$0	\$23,140,771
Project Budget	\$23,160,569	Received	,	•						,	•		
Less Other Funding	\$19,798	\$19,798	* Other Funding So	ource:									
Net	\$23,140,771		Edison \$19,798 re	ceived									
Actual Measure AA Expenditures	\$23,140,771												
Running Balance	\$0												



**Project Description:**Relocation of IT/Telecom Departments, and renovation of Media Center


Facility Size: 9,230 sq/ft

Status: Completed

Architect:

Morris Architects

Contractor: Minco, Bernards Brothers



Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20	Combined Totals
				•	•		•			•			
AA 7100061													
Media and Technology Complex - Academy Site (103)													
Consultants		\$0	\$0	\$20,675	\$12,576	\$9,488	\$7,789	\$2,102	\$0	\$12,922	\$0	\$0	\$65,551
Supplies		\$0	\$0	\$0	\$19,481	\$1,048	\$289	\$0	\$9,251	\$40,519	\$937	\$0	
Maintenance Contract		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$15,922	\$23,561	\$0		
Legal		\$16,903	\$0	\$7,958	\$43,363	\$5,066	\$26,186	\$49,155	\$15,435	\$36,221	\$26,991	\$0	
Software Support		\$0	\$0	\$0	\$1,982	\$0	\$0	\$0	\$6,548	\$6,975	\$0	\$0	\$15,505
Service Fee		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$17,000	\$0	\$0	\$0	
Other Contract Services		\$3,993	\$5,763	\$13,456	\$39,188	\$0	\$0	\$5,853	\$22,622	\$18,628	\$7,690	\$7,550	\$124,743
Moving Expenses		\$0	\$0	\$0	\$38,756	\$0	\$0	\$0	\$0	\$97,543	\$17,556	\$0	
Site Improvement		\$0	\$0	\$0	\$100,505	\$664	\$606	\$476	\$622	\$526	\$0	\$0	
Building & Additions		\$0	\$538	\$1,498,660	\$3,543,657	\$11,820,615	\$17,734,534	\$23,465,347	\$16,267,550	\$25,548,089	\$219,234	\$0	\$100,098,223
Architect		\$2,097,553	\$2,508,588	\$295,753	\$265,481	\$778,015	\$517,794	\$1,048,935	\$991,386	\$869,801	\$151,886	\$43,416	
Engineering		\$16,459	\$29,293	\$9,102	\$29,223	\$8,203	\$72,993	\$118,368	\$72,786	\$51,971	\$37,259	\$0	\$445,657
Inspection & Testing		\$64,905	\$27,527	\$123,842	\$235,287	\$563,746	\$1,381,801	\$641,972	\$525,264	\$207,240	\$27,210	\$0	
Project Management		\$121,786	\$233,826	\$269,249	\$506,917	\$800,315	\$930,115	\$1,207,850	\$1,121,670	\$859,779	\$50,681	\$175	
Cap Equipment		\$0	\$0	\$0	\$186,301	\$0	\$0	\$0	\$0	\$1,458,273	\$6,604	\$0	
Non-Cap Equipment		\$0	\$0	\$0	\$10,782	\$0	\$0	\$0	\$326,845	\$490,727	\$7,167	\$0	
Total		\$2,321,599	\$2,805,534	\$2,238,694	\$5,033,499	\$13,987,159	\$20,672,105	\$26,540,059	\$19,392,902	\$29,722,772	\$553,215	\$51,141	\$123,318,677
Project Budget	\$130,549,713	Received											
Less Other Funding*	\$6,835,391		<ul> <li>Other Funding So</li> </ul>										
Net	\$123,714,322		KCRW Foundation		ed								
Actual Measure AA Expenditures	\$123,318,677		Edison \$31,979.48	received									
Running Balance	\$395,645												

# Media and Technology Complex -Academy Site

## **Project Description:**


Renovation and new extension to the existing building, new building for KCRW, and a new parking structure

Facility Size: Building - 116,000 sq/ft Parking Structure - 450 spaces

Status: In construction

Architect: Clive Wilkinson Architects

Contractor: H.B. Parkco Construction Fast Track Construction CW Driver



Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20	Combined Totals
AA 7100060													1
Repl. Health/PE/Fitness/Dance Building with Central Plant (104)													1
Consultants		\$0	\$0	\$0	\$14	\$62	\$2,304	\$184	\$0	\$0	\$0		\$2,564
Supplies		\$0	\$0	\$0	\$0	\$7,089	\$195	\$484	\$20,947	\$0	\$0		\$28,715
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$663	\$80	\$0	\$0		
Software Support		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,209	\$0	\$0		
Site Improvement		\$0	\$0	\$0	\$0	\$0	\$559	\$440	\$575	\$0	\$0		
Off Campus Printing		\$0	\$0	\$0	\$0	\$0	\$2,165	\$0	\$0	\$0	\$0	\$0	\$2,165
Postage		\$0	\$0	\$0	\$0	\$0	\$1,505	\$0	\$0	\$0	\$0	\$0	\$1,505
Other Contract Services		\$120	\$38	\$112	\$32,634	\$0	\$1,019	\$581	\$0	\$2,644	\$0		
Building & Additions		\$0	\$0	\$0	\$817	\$4,188	\$1,623	\$13,783,023	\$14,880,829	\$5,315,393	-\$148,184	\$0	\$33,837,688
Architect		\$256,076	\$1,568,564	\$1,790,207	\$518,973	\$177,583	\$364,853	\$585,900	\$373,345	\$210,312	\$108,264	\$0	\$5,954,078
Engineering		\$0	\$8,507	\$31,650	\$7,871	\$6,529	\$9,276	\$76,712	\$51,025	\$11,318	\$2,900	\$0	\$205,788
Inspection & Testing		\$36,892	\$490	\$21,150	\$1,285	\$360	\$133,756	\$846,765	\$358,724	\$60,826	\$1,330	\$0	\$1,461,579
Project Management		\$34,968	\$113,379	\$118,783	\$94,768	\$108,528	\$463,418	\$564,240	\$487,065	\$312,539	\$20,242	\$0	\$2,317,928
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$164,793	\$68,425	\$0		
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$9,015	\$0	\$206,229	\$127,078	\$0		
Total		\$328,056	\$1,690,978	\$1,961,901	\$656,362	\$304,338	\$989,689	\$15,858,991	\$16,544,820	\$6,108,535	-\$15,448	\$0	\$44,428,222
Project Budget	\$56,240,452		•			,			•	•	•		
Less Other Funding*	\$11,812,230		Other Funding Sc	urce:									
Net	\$44,428,222		Measure S \$11,603										
Actual Measure AA Expenditures	\$44,428,222	5	SCE \$190,847.28,	Gas Co. \$18,000	received								
Running Balance	\$0												

# Repl. Health/PE/Fitness/Dance Building with Central Plant

## Project Description:

Replacement of locker rooms, fitness center, dance studios, and new central plant

## Facility Size: 62,000 sq/ft

# Status:


In construction

## Architect:

Gensler Architects

## Contractor:


Bernards Brothers



Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20	Combined Totals
AA 7100065													
Drescher - Academic Modernization, Bookstore, Pico Promenade (105)													
Legal Other Contract Services		\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
		\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Site Acquisition		\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0		\$0	\$0			\$0	\$0	\$0	\$0	\$0	
Project Management		\$0			\$0			\$0	\$0	\$0	\$0	\$0	
Total		\$0	\$0	\$5,082	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$5,082
Project Budget	\$13,005,082												
Less Other Funding	\$13,000,000		* Other Funding S										
Net	\$5,082		Measure V 13,00	0,000 allocated									
Actual Measure AA Expenditures	\$5,082												
Running Balance	\$0												
AA 7100090													
Replacement Math and Science Extension Building (106)													
Legal		\$0		\$0	\$0			\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0		\$0	\$0			\$0	\$0	\$1,525	\$0	\$0	\$1,525
Site Acquisition		\$0		\$0	\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$4,796	\$0	\$0	\$4,796
Architect		\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$1,787,824	-\$94,695	\$0	\$1,693,130
Engineering		\$0		\$0	\$0			\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0		\$0	\$0		\$0	\$0	\$0	\$70,223	\$0	\$0	\$70,223
Project Management		\$0			\$0			\$0	\$800	\$228,760	\$0	\$0	\$234,510
Total		\$0	\$0	\$0	\$0	\$4,950	\$0	\$0	\$800	\$2,093,128	-\$94,695	\$0	\$2,004,184
Project Budget	\$124,958,336												
Less Other Funding	\$122,714,328	\$2,584,000	* Other Funding S	ource:									
Net	\$2,244,008			336, Measure V \$83		d							
Actual Measure AA Expenditures	\$2,004,184		State of California	\$40,088,000 alloc	ated								
Running Balance	\$239,824												

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20	Combined Totals
Tiojuus	Dauget	05/10 1 11101	10/11/11/01	11/12 1 11101	12/10/11/10/	10/14111101	14/10/111101	10/10 1 11101	10/1/111101	17/10111101	10/10/111101	10/20	Combined Totals
AA 7100047													
Madison East Wing Seismic Upgrade (107)			1										
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$6,197	\$0	\$0	\$0	\$6,197
Consultants		\$0	\$0	\$0	\$0	\$135	\$28	\$0	\$0	\$0	\$0	\$0	\$163
Off Campus Printing		\$0	\$0	\$0	\$0	\$0	\$285	\$0	\$0	\$0	\$0		\$285
Maintenance Contract		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$357	\$0	\$0	\$0	\$285 \$357
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$7,579	\$11,822	\$8,263	\$0	\$27,663
Software Support		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$806	\$0	\$0	\$0	\$806
Other Contract Services		\$0	\$364	\$997	\$0	\$0	\$1,328	\$711	\$0	\$0	\$0	\$0	\$3,400
Building & Additions		\$0	\$656	\$312,643	\$0	\$4,248	\$6,030,371	\$8,829,626	\$4,949,223	\$3,967,591	\$0		
Architect		\$76,073	\$398,050	\$550,589	\$65,444	\$57,480	\$199,100	\$404,764	\$122,764	\$103,824	\$0	\$0	
Engineering		\$0	\$0	\$10,707	\$778	\$0	\$13,792	\$33,184	\$37,491	\$90	\$0	\$0	
Inspection & Testing		\$0	\$19,848	\$16,752	\$3,036	\$5,851	\$676,323	\$405,443	\$112,876	\$4,703	\$0	\$0	
Project Management		\$5,557	\$128,878	\$112,573	\$67,447	\$118,242	\$494,874	\$481,165	\$322,379	\$31,230	\$11,286	\$0	
Cap Equipment		\$0	\$0	\$30,603	\$0	\$0	\$0	\$0	\$537,627	\$0	\$0	\$0	
Non-Cap Equipment		\$0	\$0	\$71,827	\$9,788	\$0	\$0	\$0	\$285,236	\$0	\$0	\$0	
Total		\$81,630	\$547,796	\$1,106,691	\$146,492	\$185,956	\$7,416,101	\$10,154,894	\$6,382,534	\$4,119,259	\$19,549	\$0	\$30,160,902
Project Budget	\$30,160,902												
Less Other Funding	\$0												
Net	\$30,160,902												
Actual Measure AA Expenditures	\$30,160,902												
Running Balance	\$0												

# Madison East Wing Seismic Upgrade Project Description: Replacement of east wing with a new multipurpose room and additional classrooms Facility Size: 20,838 sq/ft Status: In construction Architect: DLR Group WWCOT Contractor: Bernards Brothers



Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20	Combined Totals
AA 7400000	-	,											
AA 7100068  Renovation to Corsair Stadium (108)													
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0 \$0	\$0	\$0		\$(	\$0
Architect		\$0	\$30,759	\$0		\$0	\$0	\$0 \$0	\$0	\$0		\$(	
Engineering		\$0	\$0,739	\$0		\$0	\$0	\$0	\$0	\$0		\$0	
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	
Project Management		\$0	\$4.540	\$0		\$0	\$0	\$0	\$0	\$0		\$0	
Total		\$0	\$35,299	\$0		\$0	\$0	\$0	\$0	\$0			
Project Budget	\$35,299	40	\$00,E33	40	ΨΟΙ	ΨΟ	Ψ	ΨΟ	40	Ψ0]	ŲŪ,	Ψ.	ų <del>400,233</del>
Less Other Funding	\$0												
Net	\$35,299												
Actual Measure AA Expenditures	\$35,299												
Running Balance	\$0												
,	**												
AA 7100067, 7100152, 7100155, 7100157					Ī	1		1		T			
Business & Facilities Infrastructure (111)													
Supplies		\$0	\$0	\$0	\$1,493	\$4,840	\$0	\$0	\$0	\$0	\$0	\$0	\$6,333
Service Fee		\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0		\$0	\$12,885
Consultants		\$0	\$0	\$0		\$14	\$8	\$0	\$0	\$0		\$0	
Maintenance Contract		\$0	\$0	\$0		\$1,366	\$0	\$0	\$0	\$0		\$0	
Legal		\$0	\$0	\$75	\$0	\$0	\$0	\$1.105	\$0	\$0		\$0	
Software License		\$0	\$0	\$0	\$0	\$375	\$0	\$0	\$0	\$0		\$0	
Other Contract Services		\$0	\$6,289	\$6,988	\$750	\$0	\$2,209	\$0	\$0	\$0		\$0	
Moving Services		\$0	\$0	\$0	\$395	\$0	\$0	\$0	\$0	\$0		\$0	
Building & Additions		\$0	\$34.672	\$198,667	\$200,585	\$284,668	\$0	\$0	\$0	\$0		\$0	
Architect		\$0	\$0	\$80,626	\$170,132	\$37,906	\$0	\$0	\$0	\$0	\$0	\$0	\$288,664
Engineering		\$0	\$0	\$0	\$3,705	\$9,735	\$6,840	\$0	\$0	\$0	\$0	\$0	\$20,280
Inspection & Testing		\$0	\$0	\$8,142	\$10,938	\$10,500	\$0	\$0	\$0	\$0	\$0	\$0	
Project Management		\$0	\$3,073	\$154,904	\$87,291	\$139,821	\$3,571	\$0	\$0	\$0	\$0	\$0	\$388,659
Cap Equipment		\$0	\$0	\$0	\$35,892	\$80,090	\$0	\$0	\$0	\$0	\$0	\$0	\$115,982
Non-Cap Equipment		\$0	\$89,204	\$0		\$193,782	\$0	\$0	\$0	\$0		\$0	
Total		\$0	\$133,238	\$449,401	\$608,656	\$763,095	\$12,628	\$1,105	\$0	\$0	\$0	\$0	\$1,968,124
Project Budget	\$1,968,124	-					-	-					
Less Other Funding	\$0												
Net	\$1,968,124												
Actual Measure AA Expenditures	\$1,968,124												
Running Balance	\$0												
AA 7100004													
Master Planning, Program Management, Overhead (112)													
Supplies		\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0		\$0	
Architect		\$0	\$0	\$0		\$0	\$0	\$139,302	\$187,927	\$245,329	\$1,270	\$0	
Project Management		\$0	\$0	\$0		\$76,015	\$150	\$0	\$49,170	\$135,533	\$0	\$0	
Cap Equipment		\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$0	
Non-Cap Equipment		\$0 <b>\$0</b>	\$0	\$0		\$0	\$0	\$0	\$0	\$0		\$0	
Total Deleted	0004.00	\$0	\$0	\$0	\$0	\$76,015	\$150	\$139,302	\$237,097	\$380,863	\$1,270	\$0	\$834,697
Project Budget	\$834,697												
Less Other Funding	\$0												
Net	\$834,697												
Actual Measure AA Expenditures	\$834,697												
Running Balance	\$0												

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20	Combined Totals
riojecta	Duugel	vario i ilial	.v/ I I I IIIai	11/12   IIIQI	12/13 I midl	i S/ I + I III al	1-1/10 I IIIdl	13/10 I IIIdi	. O/ I/ I IIIal	. // IO I IIIdl	i Or i Ə i iii di	13120	Compiled Totals
AA 7100154		Т		1		ı			1		1		
Energy Efficiency Projects (113)													
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0		\$0	
Building & Additions		\$0	\$0	\$189	\$2,108,853	\$990,389	-\$97,621	\$0	\$0	\$0 \$0		\$0	
Architect		\$0	\$0	\$0	\$0	\$0	\$0 \$0		\$0	\$0 \$0		\$0	
Engineering		\$0	\$0	\$0	\$0 \$0	\$0	\$0		\$0	\$0 \$0		\$0	
Inspection & Testing		\$0	\$0	\$0		\$0	\$10,118	\$0	\$0	\$0 \$0		\$0	
Project Management		\$0	\$0	\$0		\$0	\$825	\$0	\$0	\$0		\$0	
Non-Cap Equipment		\$0	\$0	\$0		\$0	\$0		\$0	\$0		\$0	
Total		\$0	\$0	\$189	\$2,112,873	\$990,389	-\$86,678	\$0	\$0	\$0			
Project Budget	\$3,508,088	40	40	<b>\$100</b>	ΨΣ,112,010	ψ550,005	-400,010	Ψ	40	Ψ	40	ΨŪ	ψ0,010,110
Less Other Funding	\$491,315		* Other Funding So	ource:									
Net	\$3,016,773		DWP \$18.715.00 re										
Actual Measure AA Expenditures	\$3,016,773		SCE \$446.519.77 r										
Running Balance	\$3,010,773		Gas Co. \$26,080 re										
Indining Balance	ΨΟ		Gas Co. \$20,000 fe	eceiveu									
AA 7100064	1			1		T			T		T		
Community Classroom & Facility Projects (114)													
		60	00	\$0	\$124	\$0	60	60	\$0	\$0	\$0	0.0	\$124
Supplies Legal		\$0 \$0	\$0 \$0	\$1.867	\$1,418	\$0 \$0	\$0 \$0		\$0	\$0 \$0		\$0 \$0	
Other Contract Services		\$0	\$3,720	\$1,869	\$1,416	\$0 \$0	\$0 \$0		\$0 \$0	\$0 \$0		\$0	
Building & Additions		\$0	\$434,578	\$1,369,441	\$408,696	-\$1,003	\$0 \$0		\$0	\$0 \$0		\$0	
			\$263,833	\$48,120			\$0 \$0		\$0	\$0 \$0		\$0	
Architect		\$0 \$0	\$203,633	\$3,143	\$1,318 \$0	\$0	\$0 \$0			\$0 \$0		\$0	
Engineering		\$0	\$41,002	\$80,885	\$1,495	\$0 \$0	\$0 \$0		\$0 \$0	\$0 \$0		\$0	
Inspection & Testing Project Management		\$135	\$117,247	\$143,780	\$1,495	\$0 \$0	\$0 \$0		\$0	\$0 \$0		\$0	
Non-Cap Equipment		\$135	\$117,247	\$209,726	\$27,570	\$0] \$0			\$0			\$0	
Total		\$135	\$863,599	\$1,858,831		-\$1.003	\$0 \$0			\$0 \$0			
Project Budget	\$3,162,183	\$135	\$003,599	\$1,050,031	\$440,621	-\$1,003	ψU	ψU	ąυ	<b>\$</b> U	ŞU	ψU	\$3,162,163
Less Other Funding	\$0 \$3,162,183												
Net Actual Measure AA Expenditures													
	\$3,162,183 \$0												
Running Balance	\$0												
A A 74000F7													
AA 7100057													
Real Property Acquisition (115)			00					00	00	0050			8050
Legal Other Contract Services		\$0 \$0	\$0 \$39	\$0			\$0		\$0	\$659		\$0 \$0	
				\$7,000	\$0		\$0		\$0	\$0			
Site Acquisition		\$1,739,979	\$4,001,204	\$9,022,207	\$0	\$0	\$0		\$5,013,226	\$4,821,600		\$0	
Inspection & Testing		\$8,689	\$7,986	\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$0	
Project Management		\$0	\$0	\$0	\$0 <b>\$0</b>	\$0	\$0		\$0	\$0		\$0	
Total	#04 600 000	\$1,748,667	\$4,009,228	\$9,029,207	\$0	\$15,800	\$0	\$0	\$5,013,226	\$4,822,259	\$0	\$0	\$24,638,386
Project Budget	\$24,638,386												
Less Other Funding	\$0												
Net	\$24,638,386												
Actual Measure AA Expenditures	\$24,638,386												
Running Balance	\$0												

Modelman, Walkway, Grounds, Parking Lots, and Garagee (116)   September   Se	Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20	Combined Totals
Modelman, Walkway, Grounds, Parking Lots, and Garagee (116)   September   Se	•		•			•								
Secretary   Secr	AA 7100058, 7100151, 7100156, 7100059													
Separation   Sep	Roadways, Walkways, Grounds, Parking Lots, and Garages (116)													
S5   S9   S8   S46,000   S50,100   S50   S9   S9   S9   S9   S9   S9   S9   S	Supplies		\$0	\$0	\$0	\$0	\$4,616	\$0	\$0	\$0	\$0	\$0	\$0	\$4,616
S5   S9   S8   S46,000   S50,100   S50   S9   S9   S9   S9   S9   S9   S9   S	Legal		\$0	\$0	\$0	\$125	\$0	\$0	\$0	\$0	\$0			\$125
Section   Sect	Consultants		\$0	\$0	\$0	\$48,090	\$5,018	\$0	\$0	\$0	\$0	\$0	\$0	\$53,108
Sulding A, Additions	Other Contract Services		\$218	\$770	\$122	\$25,249	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$26,358
Section   Sect	Building & Additions		\$185,345	\$6,731	\$113,784	\$321,603	\$975,401	\$0		\$0	\$0	\$0	\$0	\$1,602,864
Signature   Sign	Architect							\$1,240						
Separation   S13,080   S17,085   S13,550   S20,126   S42,865   S0   S0   S0   S0   S0   S0   S97,727     Project Management	Engineering				\$0	\$1.095		\$0						
\$24,404   \$12,239   \$21,045   \$54,065   \$10,945   \$1,411   \$0   \$0   \$0   \$0   \$0   \$0   \$0			\$13,380	\$7.865	\$13,553			\$0						
\$223.47    \$223.47														
Freed Budget														
Comparison   S4,8891,747   Measure V \$1,000 000 allocated		\$7,022,417	¥===,+ · · ·	<del>+</del>	*****	70.0,00.	¥ 1,100,01=	4=,44=	**!	**1	***	**		7-,:,
Measure S \$3,891,747, Measure V \$1,000,000 allocated A Expenditures S \$2,130,6770   Measure S \$3,891,747, Measure V \$1,000,000 allocated A Expenditures S \$2,130,6770   Summing Balance S \$3,891,747, Measure V \$1,000,000 allocated S \$3,801,747, Measure V \$1,000,000 allocated S \$3,801,801,801,801,801,801,801,801,801,801				Other Funding Sc	onice.									
Actual Messure Ax Expenditures \$ \$2,136,070    Walkening Eslance \$ \$2,100,070    Ax 710009						1 000 000 allocate	d							
Number   Section   Secti					,,casarc v w	, o o o , o o o allocato	•							
AA 7100099  AA 7100099  Infrastructure & Technology - Technology (117)  Software  Soft														
Infrastructure & Technology - Technology (117)    So   So   So   So   So   So   So   S	Training Balance	Ψ0												
Infrastructure & Technology - Technology (117)    So   So   So   So   So   So   So   S	ΔΔ 7100069													
Software														
Supplies			<b>©</b> 0	90	90	0.9	90	\$218	0.9	\$0	90	en.	91	\$218
Maintenance Contract   S0   \$9.472   \$46,300   \$210,581   \$119,944   \$42,415   \$9.472   \$0   \$0   \$0   \$337,186   \$10													90	
Other Contract Services   S0   S0   S0   S0   S49,889   S0   S0   S0   S0   S49,589														
Sulding Additions   So   So   So   So   So   So   So   S														
S0   S0   S0   S0   S0   S0   S0   S0														
Sep Equipment   Sep S207,423   S33,063   S76,294   S0   S1,145,668   S0   S0   S0   S0   S0   S0   S1,962,444   S0   S1,042,647   S10   S0   S42,627   S50   S0   S44,77   S0   S0   S0   S0   S0   S0   S0													\$(	
Non-Cap Equipment Total  S2.434.417 Project Budget  Less Other Funding  AA7 100150  AT 100150  AA7 4010150  AA7 4010150  AA7 4010150  AA7 601050  S0 50  S0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0														
\$0   \$216,896   \$135,838   \$794,963   \$18,944   \$1,258,304   \$9,472   \$0   \$0   \$0   \$0   \$2,434,417														
Project Budget														
Less Other Funding		CO 404 447	<b>\$</b> 0	\$210,090	\$135,030	\$794,963	\$10,944	\$1,250,304	\$9,472	Şυ	<b>\$</b> U	\$0	31	J \$2,434,41 <i>1</i>
Net														
Actual Measure AA Expenditures \$2,434,417   Sunning Balance \$2,434,417   S														
AA 7100150 Infrastructure & Technology - Utility (118) Sofeware License So														
AA 7100150 Infrastructure & Technology - Utility (118) Sofeware License So														
Infrastructure & Technology - Utility (118)	Running Balance	\$0												
Infrastructure & Technology - Utility (118)														
Sofeware License														
Legal				212 222										210.000
Building & Additions														
Architect   \$0	Legal													
Inspection & Testing														
Project Management														
Cap Equipment         \$0         \$0         \$7,534         \$0         \$0         \$0         \$0         \$0         \$0         \$0         \$0         \$7,534           Non-Cap Equipment         \$0													\$0	
Non-Cap Equipment 50 50 50 50 50 50 50 50 50 50 50 50 50														
Total   \$0 \$20,219 \$7,534 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$27,753   Less Other Funding														
Project Budget         \$27,753           Less Other Funding         \$0           Net         \$27,753           Actual Measure AA Expenditures         \$27,753														
Less Other Funding         \$0           Net         \$27,753           Actual Measure AA Expenditures         \$27,753			\$0	\$20,219	\$7,534	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$(	\$27,753
Net \$27,753 Actual Measure AA Expenditures \$27,753														
Actual Measure AA Expenditures \$27,753														
	Net	\$27,753												
Running Balance \$0														
	Running Balance	\$0												

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20	Combined Totals
·		·								·			
AA 7100153													
Emergency Lighting, Fire Alarm, and Security System (119)													
Supplies		\$0	\$0	\$0			\$0	\$0	\$2,671	\$0	\$0		
Consultants/Legal		\$0	\$0	\$0			\$16	\$0	\$0	\$0	\$442		
Telecom Fee		\$0	\$0	\$0			\$800	\$0	\$0	\$0	\$0		
Maintenance Contract		\$0	\$0	\$648			\$0	\$2,700	\$0	\$0	\$0		
Software Suppoert		\$0	\$0	\$24,765			\$0	\$2,232	\$0	\$0	\$0		
Other Contract Services		\$0	\$0	\$0			\$0	\$4,643	\$1,560	\$0	\$0		
Building & Additions		\$0	\$0	\$0			\$2,648,866	\$4,129,145	\$1,308,230	\$763,170	\$26,375		
Architect		\$0 \$0	\$0 \$0	\$0 \$0			\$18,925	\$0	\$0 \$255.798	\$5,047 \$358,560	\$0 \$114.585		
Enginnering			\$0 \$0				\$389,013	\$156,247		\$358,560	\$114,585 \$0		
Inspection & Testing		\$0	\$0 \$0	\$0 \$0			\$0 \$52.044	\$58,831 \$79,285	\$4,800 \$16,500	\$0 \$49.738	\$0 \$240		
Project Management		\$0 \$0	\$0 \$0	\$0			\$52,044	\$79,285	\$10,500	\$49,738	\$240		
Cap Equipment		\$0	\$0 \$0					\$5,671	\$0 \$0	\$0 \$0	\$0 \$0		
Non-Cap Equipment Total	_	\$0 \$0	\$0 \$0	\$6,087 <b>\$31,500</b>	\$0 <b>\$0</b>		\$8,348 \$3,118,012	\$4,438,953	\$1,589,560	\$1,176,515	\$141,642		
Project Budget	\$11,520,794	\$0	\$0	<b>\$31,500</b>	\$0	<b>\$940,259</b>	\$3,110,U12	\$4,430,953	\$1,508,5bU	\$1,176,515	\$141,642	\$0	\$11,43b,44
Less Other Funding													
Net	\$0 \$11.520.794												
Actual Measure AA Expenditures	\$11,436,441												
Running Balance	\$84,353												
Rulling balance	\$04,333												
A A 7400440												1	
AA 7100142													
Student Services (120)					00		00			00		00	
Supplies		\$0	\$0	\$0				\$0	\$0	\$0	\$0		
Consultants		\$0	\$0	\$0			\$0	\$0	\$0 \$0	\$0	\$0		
Telecom Fee		\$0	\$0 \$0	\$0		\$0 \$0	\$0	\$0 \$0	\$0 \$0	\$0	\$0		
Maintenance Contract		\$0		\$0			\$0			\$0	\$0		
Software Suppoert		\$0	\$0	\$0			\$0	\$0	\$0	\$0 \$0	\$0		
Other Contract Services Building & Additions		\$0	\$0	\$0			\$0	\$0 \$0	\$0 \$0	\$3,165,626	\$0 \$3,704,864		
Architect		\$0 \$0	\$0 \$0	\$0 \$0			\$0 \$0	\$0 \$0	\$0 \$0	\$3,105,626	\$3,704,664		
		\$0	\$0 \$0	\$0			\$0	\$0 \$0	\$0 \$0	\$0	\$0		
Enginnering Inspection & Testing		\$0	\$0 \$0	\$0			\$0	\$0 \$0	\$0 \$0	\$0	\$0 \$0		
		\$0	\$0 \$0	\$0			\$0	\$0 \$0	\$0 \$0	\$0	\$0		
Project Management		\$0	\$0 \$0	\$0			\$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0		
Cap Equipment Non-Cap Equipment		\$0	\$0 \$0	\$0			\$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0		
Total		\$0	\$0 \$0					\$0 \$0	\$0 \$0	\$3,165,626	\$3,704,864		
	\$6,870,490	ΨU	ψŪ	ψŪ	ψU	\$0	\$U	ŞU	ŞU	\$3,165,626	\$3,704,004	Şυ	\$6,670,49
Project Budget Less Other Funding	\$6,670,490		Other Funding S										
Net	\$6,870,490												
Actual Measure AA Expenditures	\$6,870,490		State of California			ure V \$33.624.909	allocated						
	\$6,870,490					uie v \$33,024,909	anocateu						
Running Balance	1 \$0		Measure U, S & A	niterests \$∠1,68	1,300 allocated								
0(()													
Cost of Issuance (121)		-		**	-		#20F 222	***	6040.000		**	\$0	6400.00
Cost of Issuance		\$0 \$0	\$0 \$0	\$0 <b>\$0</b>		\$0 <b>\$0</b>	\$285,000	\$0 <b>\$0</b>	\$213,026	\$0 <b>\$0</b>	\$0 <b>\$0</b>		
Total	6400.000	\$0	\$0	\$0	\$0	\$0	\$285,000	\$0	\$213,026	\$0	\$0	\$0	\$498,02
Project Budget	\$498,026												
Less Other Funding	\$0												
Net A Francisco A	\$498,026												
Actual Measure AA Expenditures	\$498,026												
Running Balance	\$0												
Grand Total		\$4,900,734	\$10,935,584	\$17,864,407	\$13,113,759	\$30,388,248	\$39,049,510	\$60,741,756	\$57,313,878	\$52,193,046	\$4,326,286	\$51,141	\$290,878,34

Measure AA Interest		18/19 Final
Parking Garage and Grounds - Student Services (9)		
Site Imptovement		\$0
Building & Additions		\$5,192,948
Architect		\$0
Engineering		\$0
Inspection & Testing		\$0
Project Management		\$0
Total		\$5,192,948
Project Budget	\$5,192,948	
Actual Measure S Interest Expenditures	\$5,192,948	
Running Balance	\$0	

# **Measure V Project Schedule** As of September 30, 2019

	Project Name	Completion	2018	8	2019	2020	2021	2022	2023
101	Replacement Math and Science Extension Building	May 2023							
102	Student Services	Completed							
103	Malibu Center	April 2022							
104	Early Childhood Development/Childcare	June 2020							
105	Art Building Replacement	December 2022							
106	Business Building Renovation	December 2023							
107	Air Conditioning	June 2020							
108	ADA	On-Going							
109	Master Planning	March 2021							
110	Drescher Hall Modernization	On-Going							
111	Outdoor Classroom	On-Going							
112	SMMUSD	August 2021							
113	City of Santa Monica	On-Going							
114	Classrooms Relocation	April 2020							
115	TBD	On-Going							
120	Other Bond Related Expenses	On-Going							
121	Cost of Issuance	On-Going							
122	Management Reserve	On-Going							
123	Unissuable Bond	On-Going							
			In PI	lanning	g Ir	Construction			

Projects	Budget	17/18 Final	18/19 Final	19/20	Combined Totals
L/740000					
V 7100090					
Replacement Math and Science Extension Building (101)		60	Ć0	40	40
Legal		\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0
Moving Services		\$0	\$0	\$0	\$0
Building & Additions		\$675	\$12,987	\$0	\$13,662
Architect		\$2,047,911	\$14,446	\$0	\$2,062,357
Engineering		\$0	\$0	\$0	\$0
Inspection & Testing		\$30,804	\$44,077	\$0	\$74,880
Project Management		\$130,874	\$617,805	\$25,760	\$774,439
Cap Equipment		\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0
Total	¢424.050.226	\$2,210,264	\$689,315	\$25,760	\$2,925,338
Project Budget	\$124,958,336	Received			
Less Other Funding	\$42,640,344	\$2,584,000	* Other Funding		** 62 244 000 11
Net	\$82,317,992				ire AA \$2,244,008 allocated
Actual Measure V Expenditures	\$2,925,338		State of Califo	rnia \$40,088,0	UU allocated
Running Balance	\$79,392,654				
V 7100142					
Student Services Building (102)					
Supplies		\$0	\$71,445	\$0	\$71,445
Consultants		\$0	\$0	\$687	\$687
Software Support		\$0	\$189,120	\$087	\$189,120
Moving Services		\$0	\$55,062	\$0	\$55,062
Building & Additions		\$0	. ,	\$150,721	\$12,505,781
Architect		\$0	\$419,829	\$130,721	\$419,829
Engineering		\$0	\$140,458	\$14,511	\$154,969
Inspection & Testing		\$55,202	\$296,732	\$47,867	\$399,801
Project Management		\$0		\$39,563	\$939,896
Cap Equipment		\$0		\$0	\$1,565,928
Non-Cap Equipment		\$0	. , ,	\$38,022	\$2,317,563
Total		\$55,202	- , ,	\$291,371	\$18,620,080
Project Budget	\$130,224,164	<b>400,202</b>	* Other Funding		¥10,020,000
Less Other Funding	\$96,599,255		State of Califo		0 received
Net	\$33,624,909			. , ,	ure S 45,595,322,
Actual Measure V Expenditures	\$18,620,080		Measure AA \$		
Running Balance	\$15,004,829				\$21,681,308 allocated
naming balance	\$15,00 <del>4</del> ,025		Wicasarc 0, 5	& AA IIICICSIS	721,001,500 dilocated
V 7100104					
Early Childhood Development/Childcare (104)					
Other Contract Services		\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$1,329,380	\$1,329,380
Architect		\$0	\$0	\$0	\$0
Engineering		\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$33,368	\$33,368
Project Management		\$0	\$0	\$50,240	\$50,240
Total		\$0	\$0	\$1,412,988	\$1,412,988
Project Budget	\$15,405,517	Received			
Less Other Funding	\$0	\$2,220,533		* Other Funding	g Source:
Net	\$15,405,517		•	City of Santa N	Monica \$6,661,598 commited
Actual Measure V Expenditures	\$1,412,988				.858,578 allocated
Running Balance	\$13,992,529			,	
-					

Projects	Budget	17/18 Final	18/19 Final	19/20	Combined Totals
V 7100240					
Art Complex (105)					
Legal		\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0
Moving Services		\$0	\$0	\$0	\$0
Building & Additions		\$184	\$407,369	\$0	\$407,553
Architect		\$0	\$0	\$1,126	\$1,126
Engineering		\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$35,495	\$0	\$35,495
Project Management		\$0	\$1,600	\$3,200	\$4,800
Cap Equipment		\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0
Total		\$184	\$444,464	\$4,326	\$448,974
Project Budget	\$32,914,000		•		
Less Other Funding	\$8,914,000	,	Other Funding	Source:	
Net	\$24,000,000		State of Califor	nia \$8,914,000	pending
Actual Measure V Expenditures	\$448,974				
Running Balance	\$23,551,026				
V 7100188					
Air Conditioning (107)					
Other Contract Services		\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0
Architect		4.0			
		\$0	\$79,000	\$0	\$79,000
Engineering		\$417,960	\$79,000 \$217,966	\$0 \$0	\$79,000 \$635,927
Engineering Inspection & Testing					\$635,927
<u> </u>		\$417,960	\$217,966	\$0	
Inspection & Testing		\$417,960 \$0	\$217,966 \$54,810	\$0 \$0	\$635,927 \$54,810
Inspection & Testing Project Management	\$10,777,654	\$417,960 \$0 \$4,370	\$217,966 \$54,810 \$4,570	\$0 \$0 \$0	\$635,927 \$54,810 \$8,940
Inspection & Testing Project Management Total	\$10,777,654 \$0	\$417,960 \$0 \$4,370	\$217,966 \$54,810 \$4,570	\$0 \$0 \$0	\$635,927 \$54,810 \$8,940
Inspection & Testing Project Management Total Project Budget		\$417,960 \$0 \$4,370	\$217,966 \$54,810 \$4,570	\$0 \$0 \$0	\$635,927 \$54,810 \$8,940
Inspection & Testing Project Management Total Project Budget Less Other Funding	\$0	\$417,960 \$0 \$4,370	\$217,966 \$54,810 \$4,570	\$0 \$0 \$0	\$635,927 \$54,810 \$8,940

Projects	Budget	17/18 Final	18/19 Final	19/20	Combined Totals
				Ī	
V 7100004					
Master Plan (109)					
Other Contract Services		\$0	\$0	\$0	\$0
Advertising		\$0	\$641	\$0	\$641
Architect		\$0	\$112,073	\$0	\$112,073
Engineering		\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0
Project Management		\$0	\$3,800	\$0	\$3,800
Total		\$0	\$116,515	\$0	\$116,515
Project Budget	\$1,000,000				
Less Other Funding	\$0				
Net	\$1,000,000				
Actual Measure V Expenditures	\$116,515				
Running Balance	\$883,485				
V 7100237					
Outdoor Classroom (111)					
Other Contract Services		\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0
Architect		\$100,000	\$102,023	\$0	\$202,023
Engineering		\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0
Project Management		\$0	\$17,205	\$0	\$17,205
Total		\$100,000	\$119,228	\$0	\$219,228
Project Budget	\$250,000			•	
Less Other Funding	\$0				
Net	\$250,000				
Actual Measure V Expenditures	\$219,228				
Punning Palanco	\$20.772				

\$30,772

Running Balance

Projects	Budget	17/18 Final	18/19 Final	19/20	Combined Totals
V 7100243					
Classrooms Relocation (114)					
Other Contract Services		\$0	\$0	\$0	\$0
Building & Additions		\$0	\$3,467	\$0	\$3,467
Architect		\$0	\$184,434	\$2,482	\$186,915
Engineering		\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$16,795	\$0	\$16,795
Project Management		\$0	\$61,520	\$41,680	\$103,200
Total		\$0	\$266,216	\$44,162	\$310,377
Project Budget	\$6,900,000				
Less Other Funding	\$0				
Net	\$6,900,000				
Actual Measure V Expenditures	\$310,377				
Running Balance	\$6,589,623				
S7100048					
Other Bond Related Expenses (116)					
Consultants		\$0	\$0	\$0	\$0
Lease/Rental		\$0	\$13,590	\$3,029	\$16,619
Supplies		\$0	\$0	\$0	\$0
Legal		\$0	\$0	\$0	\$0
Software License		\$0	\$0	\$0	\$0
Advertising		\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0
Building & Additions		\$184	\$191,065	\$0	\$191,249
Inspection & Testing		\$0	\$13,060	\$0	\$13,060
Project Management		\$0	\$0	\$0	\$0
Cap Equipment		\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0
Total		\$184	\$217,715	\$3,029	\$220,927
Project Budget	\$300,000				
Less Other Funding	\$0				
Net	\$300,000				
Actual Measure V Expenditures	\$220,927				
Running Balance	\$79,073				
Cost of Issuance (117)					
Cost of Issuance		\$291,277	\$0	\$0	\$291,277
Total		\$291,277	\$0	\$0	\$291,277
Project Budget	\$800,000				
Less Other Funding	\$0				
Net	\$800,000				
Actual Measure V Expenditures	\$291,277				
Running Balance	\$508,723				

\$3,079,439 \$20,483,307 \$1,781,635

Grand Total

\$25,344,381

# SMC Bond Program Contractor List as of 9-30-2019

Student Services (Measure U #0, Measure S #9, Measure AA #120, Measure V #102):

Architect – Steinberg Architects, Morris Architects

Contractor - Minco, Bernards Brothers, Spinitar

Engineering – IVA, Cogent Energy Engineering, XL Fire

Inspection & Testing – Geo Labs, BTC Labs - Vertical V, Peak Survey, LPI Rango Inc., Twining

Project Management - LPI

Replacement Health/PE/Fitness/Dance Building (Measure S #4, Measure AA #104):

Architect - Gensler Architects

Contractor – Bernards Brothers

Engineering – IVA, Glumac

Inspection & Testing – Geo Labs, Ellis Environmental, Twining, Rango Inc.

Project Management - LPI

Early Childhood Development (Measure S #5, Measure V #104):

Architect - Carde Ten Architects

Consultant - Child Educational Center

Contractor - The Nazerian Group

Engineering – Jacobs

Inspection & Testing – Geo Labs, Rango Inc., Twining

Project Management - LPI, Vanir

Malibu Site (Measure S #6, Measure AA #110, Measure V #103):

Architect - Quatro Design Group

Contractor – Master Contracting, Icon West

Consultant – m2 Strategic, Parker Environmental

Engineering – Ensitu Services, Jacobs

Inspection & Testing – Peak Surveys, Ellis Environmental, JL Inspection, Ninyo

& Moore

Project Management – LPI, m6 Strategic, Vanir

Energy Efficiency Projects (Measure S #7, Measure AA #113):

Architect - N/A

Contractor – Compass Energy Solutions, Johnson Controls

Engineering – Compass Energy Solutions, Johnson Controls

Inspection & Testing – Ellis Environmental

Environmental Performance (Measure AA #101):

Architect - Kishimoto Architects

Contractor – SJ Amoroso Construction

Engineering – P2S Engineering

Inspection & Testing - Cannon, Peak Surveys

Project Management - LPI

Information Technology Relocation (Measure AA #102):

Architect - Morris Architects

Contractor - Minco, Bernards Brothers, Eidim AV Technology

Engineering – IVA, P2S Engineering

Inspection & Testing – Cannon, Peak Surveys, Geo Labs, Ellis Environmental, Twining, JL Inspection, Rango Inc.

Project Management – LPI, CCS Presentation

Media and Technology Complex (Measure AA #103):

Architect - Clive Wilkinson Architects, Morris Architects

Contractor – H.B. Parkco Construction, Fast Track Construction, CW Driver, Dimension Data, Key Code Media, Omega Construction

Consultant - EEG Services

Engineering – IVA, P2S Engineering

Inspection & Testing - Twining, Geo Labs, BTC Labs - Vertical V,

JL Inspection, EEG Services, Ellis Environmental, Rango

Inc., Cannon

Project Management - LPI

Madison East Wing Seismic Upgrade (Measure AA #107):

Architect - DLR Group - WWCOT, LPI

Contractor - Trimax, Bernards Brothers, Dimension Data

Engineering – IVA, Glumac

Inspection & Testing – Twining, Peak Surveys, LPI, All Group Engineering, EEG Services, Ellis Environmental

Project Management - LPI

Business & Facilities Infrastructure (Measure AA #111):

Architect - LPI, Gwynne Pugh Urban Studio

Contractor – REC+S, Inc., Omega Construction,

Concept Consultant, Inc.

Engineering – N/A

Inspection & Testing - Ellis Environmental, JL Inspection

Project Management - LPI

Community Classroom & Facility Project (Measure AA #114)

Architect – Morris Architects

Contractor – Waisman Construction, Spinitar, Trimax

Engineering – IVA

Inspection & Testing – LPI, Twining

Project Management - LPI

Satellite Campus Parking Facilities and Roadway Improvements (Measure S #8)

Architect - N/A

Contractor - N/A

Engineering – MK Engineering Group

Inspection & Testing – N/A

Project Management – LPI

Roadways, walkways, Grounds, Parking Lots, and Garages (Measure AA #116)

Architect - LPI, DLR Group - WWCOT

Contractor – Trimax, Pub Construction

Consultant - Walker Parking

Engineering – MK Engineering

Inspection & Testing – Ellis Environmental, Peak Surveys, LPI

Project Management – LPI

Emergency Lighting, Fire Alarm, and Security System (Measure AA #119)

Architect - N/A

Contractor - Red Hawk Fire and Security, Nexus

Consultant - IVA

Engineering – MDC Engineers

Inspection & Testing - Rango Inc.

Project Management - LPI

Signage Safety/Information (Measure S #15)

Architect - N/A

Contractor - Sign Excellence

Consultant – APCO

Engineering – N/A

Inspection & Testing – N/A

Project Management – LPI

Math and Science Addition (Measure AA #106)

Architect - Cannon Design

Contractor - N/A

Consultant - N/A

Engineering – Arup

Inspection & Testing – N/A

Project Management – Vanir
