		Measure U	Measure S	Measure AA	Measure V	mary as of 6-3		Other Funding		Estimate at		Bond Fund
Project Number	Project Name	Budget	Budget	Budget	Budget	Interest	Received *	Pending **	Total Budget	Completion	Status	Remaining
U-A	Purchase of BAE Airport Site	\$30,280,878		_					\$30,280,878	\$30,280,878	Completed	
U-B	Emeritus College Facility	\$8,909,940					\$693,842		\$9,603,782	\$9,603,782	Completed	1
U-C	Purchase of 1738 Pearl Street	\$749,208							\$749,208	\$749,208	Completed	1
U-D	PE Temp. Bldg. Replacement	\$2,797,033							\$2,797,033	\$2,797,033	Completed	
U-E	Remodel Library Village for Math	\$1,458,690							\$1,458,690	\$1,458,690	Completed	1
U-F	SM Airport Campus Site Improvements	\$4,170,264							\$4,170,264	\$4,170,264	Completed	1
U-G	SM Airport Campus West Building	\$19,709,741							\$19,709,741	\$19,709,741	Completed	1
U-H	Theater Arts Renovation	\$19,544,314							\$19,544,314	\$19,544,314	Completed	1
U-I	Earthquake Rpl. Liberal Arts North	\$6,011,584					\$6,496,141		\$12,507,725	\$12,507,725	Completed	1
U-K	Earthquake Rpl. Liberal Arts South	\$6,108,150					\$10,625,070		\$16,733,220	\$16,733,220	Completed	1
U-L	Shuttle Replacement Parking	\$18,969,509							\$18,969,509	\$18,969,509	Completed	
U-M	North Quad Plaza	\$11,388,463							\$11,388,463	\$11,388,463	Completed	
U-Q	Infrastructure & Safety	\$4,003,084							\$4,003,084	\$4,003,084		
U-R	Restroom Improvements	\$17,501							\$17,501	\$17,501		
S-1	Athletic Fields Phase I, Corsair Field		\$4,372,535				\$67,530		\$4,440,065	\$4,440,065	Completed	
S-1A	Athletic Fields Phase I, John Adams		\$2,969,807						\$2,969,807	\$2,969,807		1
S-10	Pico Promenade Improvements, Phase I		\$1,018,009						\$1,018,009	\$1,018,009		
S-13	Adv. Architecture Related Exp for AA		\$0						\$0			
AA-114	Community Classroom & Facility Projects		·	\$3,162,183					\$3,162,183	\$3,162,183		
U-T	14th and Pico Project	\$319,242							\$319,242	\$319,242		
U-N	Letters & Sci Demo/Restore	\$0							\$0	\$0		
AA-108	Renovation of Corsair Stadium			\$35,299					\$35,299			
S-2	Performing Arts Complex		\$37,697,625	. ,			\$2,992,576		\$40,690,201	\$40,690,201		1
U-J	Music Complex	\$2,011,371	1 = 7 = 7 = -				\$2,618,113		\$4,629,484	\$4,629,484		
S-3, AA-109	Career Opportunity Center	1 /- /-		\$0			1 // -		\$0		· · · · · · · · · · · · · · · · · · ·	
AA-118	Infrastructure & Technology - Utility			\$27,753					\$27,753	\$27,753		
AA-111	Business & Facilities Infrastructure			\$1,968,124					\$1,968,124	\$1,968,124		
AA-117	Infrastructure & Technology - Technology			\$2,434,417					\$2,434,417	\$2,434,417		1
S-7, AA-113	Energy Efficiency Projects		\$293,361	\$3,016,773			\$708,637		\$4,018,771	\$4,018,771		
S-15	Signage Safety/Information		\$706,713	1-77			,,		\$706,713	\$706,713		
AA-102	Infrastructure & Technology - Information Technology Relocation		Ţ: 00): =0	\$23,140,771			\$19,798		\$23,160,569	\$23,160,569		
S-8, AA-116	Satellite Campus Parking Facilities and Roadway		\$3,891,747	\$2,130,670			7-07:00		\$6,022,417	\$6,022,417		
AA-107	Madison East Wing Seismic Upgrade		+ - / / · · · ·	\$30,178,822					\$30,178,822	\$30,178,822		\$20
S-4, AA-104	Replacement Health/PE/Fitness Central Plant Building		\$11,603,383	\$44,479,800			\$208,847		\$56,292,030	\$56,292,030		\$30
AA-101	Environmental Performance - Central Plant Connections		ψ12/003/003	\$10,767,251			Ψ200,017		\$10,767,251	\$10,767,251		
S-14, AA-115	Real Property Acquisition		\$45,597	\$24,638,386					\$24,683,983	\$24,683,983		
AA-103	Media and Technology Complex - Academy Site		ψ .5,557	\$123,714,322			\$6,092,176	\$743,215	\$130,549,713			\$389
AA-119	Emergency Lighting, Fire Alarm, and Security System			\$11,520,794			ψ0,03 2 ,170	ψ, 13, <u>213</u>	\$11,520,794	\$11,520,794		\$84
	Student Services Building	\$21,131,135	\$45 595 322		\$33 624 909	\$21,681,308	\$1,321,000		\$130,224,164		In Construction	\$19,327
S-5, V-104	Early Childhood Development/Childcare	Ψ 2 1,131,133	\$8,858,578	ψο,ονο, 15ο	\$15,405,517		\$2,220,533	\$4,441,065	\$30,925,693		In Construction	\$18,757,
S-6, AA-110, V-103	Malibu Site Acquisition and Facility		\$25,000,000		\$25,000,000		72,220,333	74,441,003	\$50,000,000		In Construction	\$35,567
5, S-11, AA-112, V-109		\$2,110,430	\$716,428	\$834,697	\$1,000,000				\$4,661,555			\$998
J-P, AA-106, V-101	Replacement Math and Science Extension Building	\$308,336	\$710,420	· · ·	\$82,317,992			\$40.088.000	\$124,958,336			\$77,299,
AA-105, V-110	Drescher - Academic Modernization, Bookstore, Pico Promenade II	7308,330		\$5,082	\$13,000,000			340,000,000	\$13,005,082			\$13,000
V-105	Art Building Replacement			75,002	\$24,000,000			\$8,914,000	\$32,914,000	\$32,914,000		\$23,556
V-105 V-106	Business Building Renovation				\$12,547,000			\$12,470,000	\$25,017,000			\$12,547
V-100 V-107	Air Conditioning				\$12,347,000			712,470,000	\$10,777,654			\$10,103
V-107 V-108	ADA				\$4,000,000				\$4,000,000			\$10,103
V-108 V-111	Outdoor Classroom				\$4,000,000				\$4,000,000	\$4,000,000		\$4,000
V-111 V-112	SMMUSD				\$250,000				\$250,000	\$250,000		
V-112 V-113	City of Santa Monica				\$20,000,000				\$20,000,000			\$20,000 \$20,000
	City of Santa Monica Classrooms Relocation									\$20,000,000		
V-114			¢c00 202		\$4,900,000				\$4,900,000	\$4,900,000		\$4,728
S-12, V-120	Other Bond Related Expenses		\$609,282		\$300,000				\$909,282	\$909,282		\$242
V-115	TBD		6446 1=-	6400.00=	\$49,076,928				\$49,076,928			\$49,076
-16, AA-121, V-121	Cost of Issuance		\$119,470	\$498,026	. ,				\$1,417,496			\$508
AA-122, V-122 , S-17, AA-123, V-123	Management Reserve	\$1,127	\$2,143		\$28,000,000	\$3,877,925			\$35,206,086			\$31,328
			C2 4 42 I	\$4,171	ii				\$7,441	\$7,441	On-Going	

^{*} City of SM: \$12,427,356; FEMA: \$1,962,572; State: \$5,779,000; Prop T: 2,618,113; DWP: \$86,245; SCE: \$844,284; Gas Co.: \$106,262; Madison Foundation: \$2,992,576; KCRW: \$6,092,176; Emeritus College Foundation: \$693,842; Bond Interest and Cost of Issuance Refund: \$21,476,400

^{**} City of SM: 4,441,065; KCRW: \$743,215; State: \$40,088,000


SANTA MONICA COMMUNITY COLLEGE DISTRICT Bond Sales / Expenses Report As of June 30, 2019

Measure S Bond \$143,500,000 (1)		
Bond Issue Date		Amount
	2005	\$58,000,000
	2007	\$8,500,000
	2009	\$56,997,857
	2017	\$20,000,000
Total Available		\$143,497,857
Expenses as of 6-30-19		\$129,419,829
Total Available Remaining		\$14,078,028
Unsold Bond Amount		\$2,143
Total Available as of 7-1-19		\$14,080,171

Measure AA Bond \$295,000,000		
Bond Issue Date		Amount
	2010	\$100,000,000
	2014	\$144,995,829
	2017	\$50,000,000
Total Available		\$294,995,829
Expenses as of 6-30-19		\$290,998,286
Total Available Remaining		\$3,997,543
Unsold Bond Amount		\$4,171
Total Available as of 7-1-19		\$4,001,714

Measure V Bond \$345,000,000		
Bond Issue Date		Amount
	2018	\$180,000,000
Total Available		\$180,000,000
Expenses as of 6-30-19		\$21,476,230
Total Available Remaining		\$158,523,770
Unsold Bond Amount	Ī	\$165,000,000
Total Available as of 7-1-19		\$323,523,770

Total Bond	\$783,500,000
Total Available	\$618,493,686
Total Expenses as of 6-30-19	\$441,894,345
Total Available Remaining	\$176,599,341
Total Unsold Bond	\$165,006,314

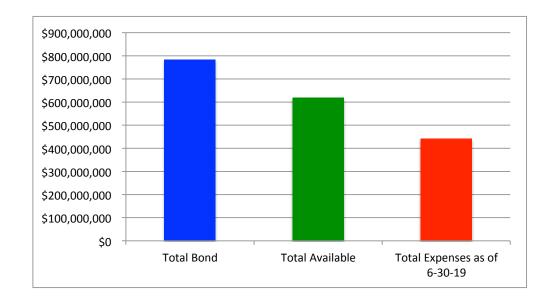

Interest	Measure S	Measure AA	Measure V
As of 6-30-18	\$11,417,370	\$6,375,323	\$676,109
Expenditure / Arbitrage as of 6-30-19	\$9,853,563	\$5,192,948	\$0
Available Interest as of 7-1-19	\$1,563,807	\$1,182,375	\$676,109

Cost of Issuance Refund	Measure S
As of 6-30-18	\$35,575
Expenditure as of 6-30-19	\$0
Available as of 7-1-19	\$35,575


⁽¹⁾ Original Bond \$135,000,000.00, refunding on 2-15-07 received additional \$8,500,000.00

SANTA MONICA COMMUNITY COLLEGE DISTRICT

Measure S Bond Budget

As of June 30, 2019

	Project Name	Completion	Project Budget	Measure S Allocation	Other Funding	Measure S Expenditures as of 6/30/19	Measure S Expenditures as of 3/31/19	Measure S Expenditures Last Period	Total Measure S Remaining
1	Athletic Fields Phase I, Corsair Field	Completed	\$4,440,065	\$4,372,535	\$67,530	\$4,372,535	\$4,372,535	\$0	\$0
1A	Athletic Fields Phase I, John Adams	Completed	\$2,969,807	\$2,969,807	\$0	\$2,969,807	\$2,969,807	\$0	\$0
2	Performing Arts Complex	Completed	\$40,690,201	\$37,697,625	\$2,992,576	\$37,697,625	\$37,697,625	\$0	\$0
3	Career Opportunity Center	Completed	\$0	\$0	\$0	\$0	\$0	\$0	\$0
4	Replacement Health/PE/Fitness Building	Completed	\$58,272,030	\$11,603,383	\$46,668,647	\$11,603,383	\$11,603,383	\$0	\$0
5	Early Childhood Development/Childcare	June 2020	\$30,925,693	\$8,858,578	\$22,067,115	\$5,506,355	\$2,632,856	\$2,873,499	\$3,352,223
6	Malibu Site Acquisition and Facility	December 2021	\$25,000,000	\$25,000,000	\$0	\$14,432,013	\$12,176,529	\$2,255,484	\$10,567,987
7	Energy Efficiency Projects	Completed	\$510,683	\$293,361	\$217,322	\$293,361	\$293,361	\$0	\$0
8	Satellite Campus Parking Facilities and Roadway Improvements	Deferred	\$7,022,417	\$3,891,747	\$3,130,670	\$3,891,747	\$3,891,747	\$0	\$0
9	Parking Garage, Grounds and Equipment - Student Services	Completed	\$130,224,164	\$45,595,322	\$84,628,842	\$45,595,322	\$45,595,322	\$0	\$0
10	Pico Promenade Improvements	Completed	\$1,018,009	\$1,018,009	\$0	\$1,018,009	\$1,018,009	\$0	\$0
11	Master Planning	Completed	\$716,428	\$716,428	\$0	\$716,428	\$716,428	\$0	\$0
12	Other Bond Related Expenses	On-Going	\$609,282	\$609,282	\$0	\$451,464	\$449,235	\$2,229	\$157,818
13	Adv. Architecture Related Exp for AA	Completed	\$0	\$0	\$0	\$0	\$0	\$0	\$0
14	Real Property Acquisition	Completed	\$45,597	\$45,597	\$0	\$45,597	\$45,597	\$0	\$0
15	Signage Safety/Information	Completed	\$706,713	\$706,713	\$0	\$706,713	\$706,713	\$0	\$0
16	Cost of Issuance	Completed	\$119,470	\$119,470	\$0	\$119,470	\$119,470	\$0	\$0
17	Unissuable Bond	Completed	\$2,143	\$2,143	\$0	\$0	\$0	\$0	\$2,143
	Project Totals		\$303,270,559	\$143,500,000	\$159,772,702	\$129,419,829	\$124,288,617	\$5,131,212	\$14,080,171

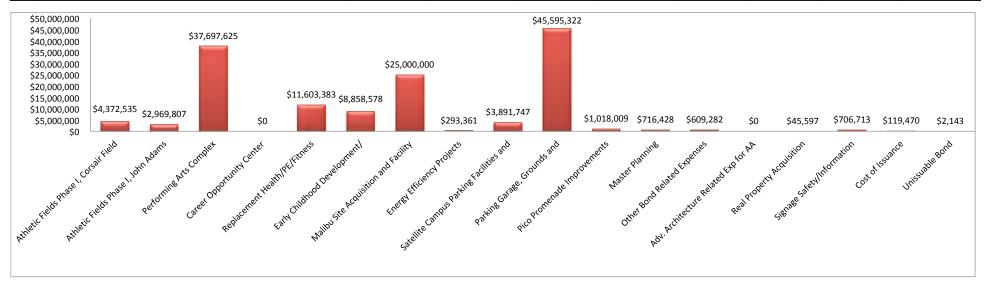


SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure S Bond Budget History

as of June 30, 2019

	Project Name	Completion	Preliminary Measure S Budget	Measure S Budget as of 3/31/19	Measure S Budget as of 6/30/19	Variance	Measure S Remaining as of 6/30/19
1	Athletic Fields Phase I, Corsair Field	Completed	\$1,800,000	\$4,372,535	\$4,372,535	\$0	\$0
1A	Athletic Fields Phase I, John Adams	Completed	\$35,200,000	\$2,969,807	\$2,969,807	\$0	\$0
2	Performing Arts Complex	Completed	\$24,000,000	\$37,697,625	\$37,697,625	\$0	\$0
3	Career Opportunity Center	Completed	\$20,000,000	\$0	\$0	\$0	\$0
4	Replacement Health/PE/Fitness Building	Completed	\$20,000,000	\$11,603,383	\$11,603,383	\$0	\$0
5	Early Childhood Development/Childcare	June 2020	\$7,000,000	\$8,858,578	\$8,858,578	\$0	\$3,352,223
6	Malibu Site Acquisition and Facility	December 2021	\$25,000,000	\$25,000,000	\$25,000,000	\$0	\$10,567,987
7	Energy Efficiency Projects	Completed	\$2,000,000	\$293,361	\$293,361	\$0	\$0
8	Satellite Campus Parking Facilities and Roadway Improvements	Deferred	\$0	\$3,891,747	\$3,891,747	\$0	\$0
9	Parking Garage, Grounds and Equipment - Student Services	Completed	\$0	\$45,595,322	\$45,595,322	\$0	\$0
10	Pico Promenade Improvements, Phase I	Completed	\$0	\$1,018,009	\$1,018,009	\$0	\$0
11	Master Planning	Completed	\$0	\$716,428	\$716,428	\$0	\$0
12	Other Bond Related Expenses	On-Going	\$0	\$609,282	\$609,282	\$0	\$157,818
13	Adv. Architecture Related Exp for AA	Completed	\$0	\$0	\$0	\$0	\$0
14	Real Property Acquisition	Completed	\$0	\$45,597	\$45,597	\$0	\$0
15	Signage Safety/Information	Completed	\$0	\$706,713	\$706,713	\$0	\$0
16	Cost of Issuance	Completed	\$0	\$119,470	\$119,470	\$0	\$0
17	Unissuable Bond	Completed	\$0	\$2,143	\$2,143	\$0	\$2,143
	Project Totals		\$135,000,000	\$143,500,000	\$143,500,000	\$0	\$14,080,171

SANTA MONICA COMMUNITY COLLEGE DISTRICT **Measure AA Bond Budget** As of June 30, 2019

	Project Name	Completion	Project Budget	Measure AA Allocation	Other Funding	Measure AA Expenditures as of 6/30/19	Measure AA Expenditures as of 3/31/19	Measure AA Expenditures Last Period	Total Measure AA Remaining
101	Environmental Performance - Central Plant Connections	Completed	\$10,767,251	\$10,767,251	\$0	\$10,767,251	\$10,767,251	\$0	\$0
102	Infrastructure & Technology - Information Technology Relocation	Completed	\$23,160,569	\$23,140,771	\$19,798	\$23,140,771	\$23,140,771	\$0	\$0
103	Media and Technology Complex - Academy Site	Completed	\$130,549,713	\$123,714,322	\$6,835,391	\$123,324,689	\$123,431,959	-\$107,270	\$389,633
104	Replacement Health/PE/Fitness/ Dance Building with Central Plant	Completed	\$56,292,030	\$44,479,800	\$11,812,230	\$44,449,534	\$46,012,263	-\$1,562,729	\$30,266
105	Drescher - Academic Modernization, Bookstore, Pico Promenade	Deferred	\$13,005,082	\$5,082	\$13,000,000	\$5,082	\$5,082	\$0	\$0
106	Replacement Math and Science Extension Building	December 2022	\$124,958,336	\$2,244,008	\$122,714,328	\$2,098,878	\$2,098,878	\$0	\$145,130
107	Madison East Wing Seismic Upgrade	Completed	\$30,178,822	\$30,178,822	\$0	\$30,158,822	\$30,151,690	\$7,132	\$20,000
108	Renovation of Corsair Stadium	Completed	\$35,299	\$35,299	\$0	\$35,299	\$35,299	\$0	\$0
109	Career Opportunity and Advancement Center (Bundy)	Completed	\$0	\$0	\$0	\$0	\$0	\$0	\$0
110	Malibu Center	December 2021	\$25,000,000	\$0	\$25,000,000	\$0	\$0	\$0	\$0
111	Business & Facilities Infrastructure	Completed	\$1,968,124	\$1,968,124	\$0	\$1,968,124	\$1,968,124	\$0	\$0
112	Master Planning, Program Management, Overhead	On-Going	\$834,697	\$834,697	\$0	\$834,697	\$834,697	\$0	\$0
113	Energy Efficiency Projects	Completed	\$3,508,088	\$3,016,773	\$491,315	\$3,016,773	\$3,016,773	\$0	\$0
114	Community Classroom & Facility Projects	Completed	\$3,162,183	\$3,162,183	\$0	\$3,162,183	\$3,162,183	\$0	\$0
115	Real Property Acquisition	Completed	\$24,638,386	\$24,638,386	\$0	\$24,638,386	\$24,638,386	\$0	\$0
116	Roadways, Walkways, Grounds, Parking Lots, and Garages	Completed	\$7,022,417	\$2,130,670	\$4,891,747	\$2,130,670	\$2,130,670	\$0	\$0
117	Infrastructure & Technology - Technology	Completed	\$2,434,417	\$2,434,417	\$0	\$2,434,417	\$2,434,417	\$0	\$0
118	Infrastructure & Technology - Utility	Completed	\$27,753	\$27,753	\$0	\$27,753	\$27,753	\$0	\$0
119	Emergency Lighting, Fire Alarm, and Security System	On-Going	\$11,520,794	\$11,520,794	\$0	\$11,436,441	\$11,421,054	\$15,387	\$84,353
120	Student Services	Completed	\$130,224,164	\$6,870,490	\$123,353,674	\$6,870,490	\$3,165,626	\$3,704,864	\$0
121	Cost of Issuance	Completed	\$498,026	\$498,026	\$0	\$498,026	\$498,026	\$0	\$0
122	Management Reserve	On-Going	\$3,328,161	\$3,328,161	\$0	\$0	\$0	\$0	\$3,328,161
123	Unissuable Bond	Completed	\$4,171	\$4,171	\$0	\$0	\$0	\$0	\$4,171
	Project Totals		\$599,786,151	\$295,000,000	\$308,118,483	\$290,998,286	\$288,940,902	\$2,057,384	\$4,001,714



SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure AA Bond Budget History as of June 30, 2019


	Project Name	Completion	Preliminary Measure AA Budget	Measure AA Budget as of 3/31/19	Measure AA Budget as of 6/30/19	Variance	Measure AA Remaining as of 6/30/19
101	Environmental Performance - Central Plant Connections	Completed	\$12,034,042	\$11,206,164	\$10,767,251	-\$438,913	\$0
102	Infrastructure & Technology - Information Technology Relocation	Completed	\$13,287,218	\$23,140,771	\$23,140,771	\$0	\$0
103	Media and Technology Complex - Academy Site	Completed	\$57,480,824	\$123,714,322	\$123,714,322	\$0	\$389,633
104	Replacement Health/PE/Fitness/ Dance Building with Central Plant	Completed	\$29,232,317	\$46,459,800	\$44,479,800	-\$1,980,000	\$30,266
105	Drescher - Academic Modernization, Bookstore, Pico Promenade II	Deferred	\$34,026,480	\$5,082	\$5,082	\$0	\$0
106	Replacement Math and Science Extension Building	December 2022	\$68,259,000	\$2,244,008	\$2,244,008	\$0	\$145,130
107	Madison East Wing Seismic Upgrade	Completed	\$6,146,000	\$30,153,816	\$30,178,822	\$25,006	\$0
108	Renovation of Corsair Stadium	Completed	\$11,203,000	\$35,299	\$35,299	\$0	
109	Career Opportunity and Advancement Center (Bundy)	Completed	\$32,384,000	\$0	\$0	\$0	
110	Malibu Center	December 2021	\$6,069,031	\$0	\$0	\$0	
111	Business & Facilities Infrastructure	Completed	\$17,506,952	\$1,968,124	\$1,968,124	\$0	
112	Master Planning, Program Management, Overhead	On-Going	\$2,000,000	\$834,697	\$834,697	\$0	
113	Energy Efficiency Projects	Completed	\$5,371,136	\$3,016,773	\$3,016,773	\$0	
114	Community Classroom & Facility Projects	Completed	\$0	\$3,162,183	\$3,162,183	\$0	
115	Real Property Acquisition	Completed	\$0	\$24,859,475	\$24,638,386	-\$221,089	
116	Roadways, Walkways, Grounds, Parking Lots, and Garages	Completed	\$0	\$2,130,670	\$2,130,670	\$0	
117	Infrastructure & Technology - Technology	Completed	\$0	\$2,434,417	\$2,434,417	\$0	
118	Infrastructure & Technology - Utility	Completed	\$0	\$27,753	\$27,753	\$0	\$0
119	Emergency Lighting, Fire Alarm, and Security System	On-Going	\$0	\$11,520,794	\$11,520,794	\$0	\$84,353
120	Student Services	May 2019	\$0	\$6,870,490	\$6,870,490	\$0	
121	Cost of Issuance	Completed	\$0	\$498,026	\$498,026	\$0	\$0
122	Management Reserve	On-Going	\$0	\$713,165	\$3,328,161	\$2,614,996	\$3,348,161
123	Unissuable Bond	Completed	\$0	\$4,171	\$4,171	\$0	\$4,171
	Project Totals		\$295,000,000	\$295,000,000	\$295,000,000	\$0	\$4,001,714

SANTA MONICA COMMUNITY COLLEGE DISTRICT

Measure V Bond Budget

As of June 30, 2019

Project Name	Completion	Project Budget	Measure V Allocation	Other Funding	Measure V Expenditures as of 6/30/19	Measure V Expenditures as of 3/31/19	Measure V Expenditures Last Period	Total Measure V Remaining
101 Replacement Math and Science Extension Building	December 2022	\$124,958,336	\$82,317,992	\$42,640,344	\$5,163,917	\$4,878,817	\$285,100	\$77,154,075
102 Student Services	Completed	\$130,224,164	\$33,624,909	\$96,599,255	\$14,297,225	\$16,988,471	-\$2,691,246	\$19,327,684
103 Malibu Center	December 2021	\$50,000,000	\$25,000,000	\$25,000,000	\$0	\$0	\$0	\$25,000,000
104 Early Childhood Development/Childcare	June 2020	\$30,925,693	\$15,405,517	\$15,520,176	\$0	\$0	\$0	\$15,405,517
105 Art Building Replacement	September 2022	\$32,914,000	\$24,000,000	\$8,914,000	\$443,048	\$443,048	\$0	\$23,556,952
106 Business Building Renovation	December 2023	\$25,017,000	\$12,547,000	\$12,470,000	\$0	\$0	\$0	\$12,547,000
107 Air Conditioning	December 2019	\$10,777,654	\$10,777,654	\$0	\$673,968	\$672,768	\$1,200	\$10,103,686
108 ADA	On-Going	\$4,000,000	\$4,000,000	\$0	\$0	\$0	\$0	\$4,000,000
109 Master Planning	March 2020	\$1,000,000	\$1,000,000	\$0	\$1,323	\$400	\$923	\$998,677
110 Drescher Hall Modernization	On-Going	\$13,005,082	\$13,000,000	\$5,082	\$0	\$0	\$0	\$13,000,000
111 Outdoor Classroom	On-Going	\$250,000	\$250,000	\$0	\$217,205	\$117,205	\$100,000	\$32,795
112 SMMUSD	August 2021	\$20,000,000	\$20,000,000	\$0	\$0	\$0	\$0	\$20,000,000
113 City of Santa Monica	On-Going	\$20,000,000	\$20,000,000	\$0	\$0	\$0	\$0	\$20,000,000
114 Classrooms Relocation	On-Going	\$4,900,000	\$4,900,000	\$0	\$171,883	\$82,719	\$89,164	\$4,728,117
115 TBD	On-Going	\$49,076,928	\$49,076,928	\$0	\$0	\$0	\$0	\$49,076,928
120 Other Bond Related Expenses	On-Going	\$300,000	\$300,000	\$0	\$216,384	\$204,309	\$12,075	\$83,616
121 Cost of Issuance	On-Going	\$800,000	\$800,000	\$0	\$291,277	\$291,277	\$0	\$508,723
122 Management Reserve	On-Going	\$28,000,000	\$28,000,000				\$0	
123 Unissuable Bond	On-Going	\$0	\$0	\$0	·	·	\$0	
Project Totals		\$546,148,857	\$345,000,000	\$201,148,857	\$21,476,230	\$23,679,014	-\$2,202,784	\$323,523,770

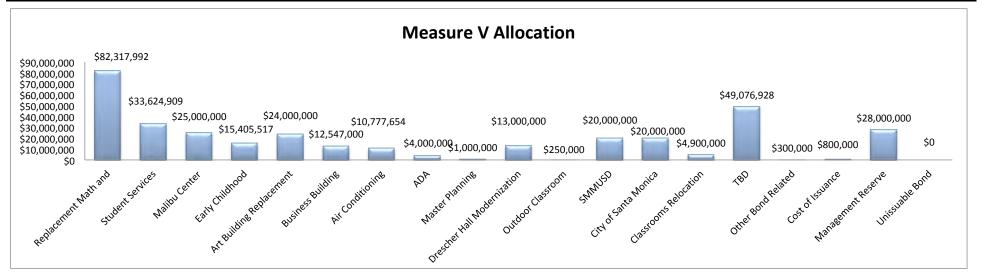

SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure V Bond Budget History

as of June 30, 2019

	Project Name	Completion	Preliminary Measure V	Measure V Budget as of	Measure V Budget as of	Variance	Measure V Remaining as
			Budget	3/31/19	6/30/19		of 3/31/19
101	Replacement Math and Science Extension Building	December 2022	\$82,317,992	\$82,317,992	\$82,317,992	\$0	\$77,154,075
102	Student Services	Completed	\$21,130,252	\$33,624,909	\$33,624,909	\$0	\$19,327,684
103	Malibu Center	December 2021	\$25,000,000	\$25,000,000	\$25,000,000	\$0	\$25,000,000
104	Early Childhood Development/Childcare	June 2020	\$15,405,517	\$15,405,517	\$15,405,517	\$0	\$15,405,517
105	Art Building Replacement	September 2022	\$24,000,000	\$24,000,000	\$24,000,000	\$0	\$23,556,952
106	Business Building Renovation	December 2023	\$12,547,000	\$12,547,000	\$12,547,000	\$0	\$12,547,000
107	Air Conditioning	December 2019	\$10,777,654	\$10,777,654	\$10,777,654	\$0	\$10,103,686
108	ADA	On-Going	\$4,000,000	\$4,000,000	\$4,000,000	\$0	\$4,000,000
109	Master Planning	March 2020	\$450,000	\$1,000,000	\$1,000,000	\$0	\$998,677
110	Drescher Hall Modernization	On-Going	\$13,000,000	\$13,000,000	\$13,000,000	\$0	\$13,000,000
111	Outdoor Classroom	On-Going	\$10,000,000	\$10,000,000	\$250,000	-\$9,750,000	\$32,795
112	SMMUSD	August 2021	\$20,000,000	\$20,000,000	\$20,000,000	\$0	\$20,000,000
113	City of Santa Monica	On-Going	\$20,000,000	\$20,000,000	\$20,000,000	\$0	\$20,000,000
114	Classrooms Relocation	On-Going	\$0	\$4,900,000	\$4,900,000	\$0	\$4,728,117
115	TBD	On-Going	\$57,271,585	\$39,326,928	\$49,076,928	\$9,750,000	\$49,076,928
120	Other Bond Related Expenses	On-Going	\$300,000	\$300,000	\$300,000	\$0	\$83,616
121	Cost of Issuance	On-Going	\$800,000	\$800,000	\$800,000	\$0	\$508,723
122	Management Reserve	On-Going	\$28,000,000	\$28,000,000	\$28,000,000	\$0	\$28,000,000
123	Unissuable Bond	On-Going	\$0	\$0	\$0	\$0	\$0
	Project Totals		\$345,000,000	\$345,000,000	\$345,000,000	\$0	\$323,523,770

SANTA MONICA COMMUNITY COLLEGE DISTRICT

Measure S Project Schedule As of June 30, 2019

	Project Name	Completion	201	8		20	19	20	20		20	21	20	22
1	Athletic Fields Phase I, Corsair Field	Completed												
1A	Athletic Fields Phase I, John Adams	Completed												
2	Performing Arts Center	Completed												
3	Career Opportunity Center	Completed												
4	Replacement Health/PE/Fitness Building	Completed												
5	Early Childhood Development/Childcare	June 2020												
6	Malibu Site Acquisition and Facility	December 2021												
7	Energy Efficiency Projects	Completed												
8	Satellite Campus Parking Facilities and Roadway Improvements	Deferred												
9	Parking Garage, Grounds and Equipment - Student Services	Completed												
10	Pico Promenade Improvements	Completed												
11	Master Planning	Completed												
12	Other Bond Related Expenses	On-Going												
13	Adv. Architecture Related Exp for AA	Completed												
14	Real Property Acquisition	Completed												
15	Signage Safety/Information	Completed												
16	Cost of Issuance	Completed												
17	Unissuable Bond	Completed												
			In P	lanni	ing			In	Cons	struc	ction			


Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19	Combined Totals
													•	•			
S7100019																	
Athletic Field Phase I, Corsair Field (1)																	
Legal		\$0	\$0	\$0	\$301	\$175	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$476
Building & Additions		\$0	\$0	\$0	\$300,380	\$2,579,095	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,879,475
Architect		\$27,332	\$43,815	\$197,557	\$252,736	\$279,173	\$26,563	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$827,176
Inspection & Testing		\$0	\$0	\$0	\$23,411	\$57,585		\$296	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$81,932
Project Management		\$0	\$0	\$0	\$9,871	\$42,374	\$565	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$52,810
Cap Equipment		\$0	\$0	\$0	\$0	\$483,017	\$35,271	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$518,288
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$2,066	\$10,312	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$12,378
Total		\$27,332	\$43,815	\$197,557	\$586,699	\$3,443,485	\$73,350	\$296	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,372,535
Project Budget	\$4,440,065	Received															
Less Other Funding*	\$67,530	\$67,530		* Other Funding													
Net	\$4,372,535			Metropolitan W	ater District \$6	7,530 received											
Actual Measure S Expenditures	\$4,372,535																
Running Balance	\$0																

Athletic Field Phase I, Corsair Field Project Description: Renovation of the Corsair Field, stadium lighting and sound system Status: Completed, 2009 Architect: CO Architects Contractor: Byrom Davey, Inc.




Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19	Combined Totals
S7100038																	
Athletic Field Phase I, John Adams (1A)																	
Legal		\$0	\$0	\$0	\$75	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$75
Building & Additions		\$0	\$0	\$0	\$16,556	\$1,395,261	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,411,817
Architect		\$0	\$5,807	\$93,941	\$12,150	\$31,818	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$143,715
Inspection & Testing		\$0	\$2,874	\$3,207	\$0	\$49,984	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	
Project Management		\$0	\$0	\$0	\$10,921	\$45,170	\$38	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$56,128
Cap Equipment		\$0	\$0	\$0	\$0	\$1,290,672	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,290,672
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$11,334		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	
Total		\$0	\$8,681	\$97,148	\$39,701	\$2,824,239	\$38	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,969,807
Project Budget	\$2,969,807				-		•										
Less Other Funding	\$0																
Net	\$2,969,807	Ī															
Actual Measure S Expenditures	\$2,969,807																
Running Balance	\$0																

Athletic Field Phase I, John Adams Project Description: Renovation of John Adams Field and lighting Status: Completed, 2008 Architect: Caldwell Architects Contractor: Byrom Davey, Inc.



Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19	Combined Totals
S7100012																	
Performing Arts Center (2)																	
Consultants		\$0	\$0	\$0	\$121,790	\$76,639		\$0	\$0		\$0		\$0	\$0	\$0	\$0	\$198,429
Other Contract Services		\$0	\$0	\$4,269	\$0	\$22,729	\$22	\$68	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$27,088
Supplies		\$0	\$0	\$0	\$14,565	\$5,810		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$20,375
Legal		\$0	\$0	\$34,329	\$275,667	\$492,731	\$15,629	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$818,356
Advertising		\$0	\$0	\$0	\$320	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$320
Building & Additions		\$7,784,151	\$10,292,986	\$8,930,813	\$2,991,903	\$1,629,990		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	
Architect		\$0	\$811,312	\$182,457	\$412,309	\$121,588		\$1,962	\$0		\$87,054	\$0	\$0	\$0	\$0	\$0	
Engineering		\$0	\$3,600	\$5,250	\$1,500	\$9,650		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	
Inspection & Testing		\$104,308	\$722,685	\$411,193	\$210,381	\$22,256		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,470,823
Project Management		\$31,984	\$155,732	\$248,876	\$263,690	\$47,915		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$751,441
Cap Equipment		\$0	\$0	\$130,218	\$292,565	\$342,693		\$0	\$0		\$0	\$0	\$0	\$0	\$0	\$0	
Non-Cap Equipment		\$0	\$0	\$15,124		\$220,455		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$328,685
Total		\$7,920,443	\$11,986,315	\$9,962,528	\$4,677,797	\$2,992,455	\$69,003	\$2,030	\$0	\$0	\$87,054	\$0	\$0	\$0	\$0	\$0	\$37,697,625
Project Budget	\$40,690,201	Received															
Less Other Funding*	\$2,992,576	\$2,992,576		 Other Funding 													
Net	\$37,697,625			Madison Project	t Foundation \$	2,992,576 rece	eived										
Actual Measure S Expenditures	\$37,697,625																
Running Balance	\$0																

Performing Arts Center Project Description: Construction of a state-of-the-art 499 seat performing arts theater Status: Completed, 2008 Architect: Renzo Zecchetto Contractor: FTR International



Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19	Combined Totals
S7100033, S7100144, S7100060		-							-								1
Replacement Health/PE/Fitness Building (4)																	
Supplies		\$4.809	\$288	\$0	\$0	\$0	\$163	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$5,260
Legal		\$0	\$0	\$0		\$1,413	\$75	\$0	\$0	\$0	\$0				\$0	\$0	\$1,488
Other Contract Services		\$1.634	\$25,934	\$0	\$0	\$253	\$165	\$0	\$0	\$0	\$0	\$0			\$0	\$0	\$27,985
Repair Facility		\$0	\$4,861	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$4,861
Building & Additions		\$0	\$0	\$0	\$0	\$112,410	\$526,552	\$0	\$0	\$0	\$0	\$6,037,080	\$4,775,714	\$0	\$0	\$0	\$11,451,757
Architect		\$0	\$0	\$0	\$0	\$0	\$41,044	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$41,044
Inspection & Testing		\$0	\$0			\$6,518	\$14,363	\$0	\$0	\$0	\$0	\$0				\$0	\$20,881
Project Management		\$0	\$0			\$9,070	\$23,425	\$0	\$0	\$0	\$0				\$0	\$0	\$32,495
Cap Equipment		\$0	\$0	\$0		\$0	\$0	\$17,613	\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$17,613
Total		\$6,443	\$31,083	\$0	\$0	\$129,663	\$605,787	\$17,613	\$0	\$0	\$0	\$6,037,080	\$4,775,714	\$0	\$0	\$0	\$11,603,383
Project Budget	\$58,272,030																
Less Other Funding*	\$46,668,647			* Other Fundin													
Net	\$11,603,383				16,459,800 alloc												
Actual Measure S Expenditures	\$11,603,383			SCE \$190,847	.28, Gas Co. \$1	8,000 received											
Running Balance	\$0																
S7100045																	
Early Childhood Development/Childcare (5)															2001		***
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0			\$294	\$0	\$294
Consultants		\$0	\$0			\$0	\$0	\$0	\$0	\$4,800	\$12,930	\$14,078			\$0	\$0	\$42,395
Legal Building & Additions		\$0	\$0			\$0 \$0	\$0	\$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0		\$6,905	\$0 \$747.457	\$0	\$8,595 \$3,001,034
Architect		\$0 \$0	\$0 \$0	\$0 \$0		\$0 \$0	\$0 \$0	\$0 \$0	\$966	\$51,792	\$142,428	\$142,968		\$242 \$78,408	\$747,457	\$2,253,335 \$242,666	\$3,001,034
		\$0 \$0	\$0 \$0			\$0 \$0	\$0	\$0	\$900	\$51,792	\$142,420	\$142,900		\$70,400	\$07,910	\$242,000	\$1,203,972
Engineering Inspection & Testing		\$0 \$0	\$0 \$0			\$0 \$0	\$0	\$0	\$0 \$0	\$37.796	\$7.475	\$823		\$0	\$4.085	\$3,000 \$247.366	\$3,000 \$299.868
Project Management		\$0	\$0			\$0 \$0	\$0	\$1,246	\$21.980	\$58,247	\$33,435	\$8.803	\$3,118	\$0	\$307,493	\$511.990	\$946.310
Total		\$0	\$0			\$0	\$0	\$1,246	\$22.946	\$152.635	\$196.268	\$166,670		\$85.555		\$3,259,245	\$5.506.355
Project Budget	\$30,925,693		\$0	φ0	\$5,200	\$ 0	ΨU	\$1,246	\$22,540	\$152,635	\$150,200	\$100,070	\$405,344	\$65,555	\$1,127,247	\$3,239,245	\$5,506,555
Less Other Funding*	\$22.067.115			* Other Fundin	a Source:												
Net	\$8,858,578	ΨΣ,ΣΣΟ,ΟΟΟ			onica \$6,661,5	98 committed											
Actual Measure S Expenditures	\$5,506,355				5,405,517 alloca												
Running Balance	\$3,352,223			Wicasarc v wit	,,400,017 dilocc	itcu											
Training Bulanco	ψ0,002, <u>22</u> 0																
S7100077, S7100015																	
Malibu Site Acquisition and Facilities (6)																	
Consultants		\$0	\$0	\$0		\$30,000	\$0	\$0	\$72,157	\$68,109	\$30,342	\$66,277	\$60,262	\$3,406	\$17	\$0	\$330,570
Legal		\$0	\$27,722	\$16,787	\$6,159	\$504	\$0	\$0	\$0	\$0	\$1,360	\$78,851			\$6,324	\$0	\$185,174
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,092	\$0	\$0	\$1,820	\$0	\$0	\$0	\$115,267	\$119,178
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$536	\$0			\$2,019,660	\$2,885,079	\$4,905,276
Architect		\$0	\$0			\$0	\$0	\$0	\$966	\$257,584	\$732,891	\$173,610			\$341,307	\$118,669	\$1,811,553
Engineering		\$0	\$0			\$0	\$0	\$0	\$0	\$785	\$562	\$0			\$0	\$0	\$1,346
Inspection & Testing		\$4,388	\$3,750	\$141,462	\$0	\$0	\$0	\$0	\$98,022	\$15,575	\$22,939	\$10,960		\$0	\$39,460	\$245,881	\$582,437
Project Management		\$0	\$0	\$220	\$0	\$0	\$0	\$2,886	\$55,064	\$53,185	\$47,778	\$118,144			\$431,268	\$643,680	\$1,496,479
Storm/Waste Water Treatment Center		\$0	\$2,500,000	\$0	\$0	\$2,500,000	\$0	\$0	\$0	\$0	\$0	\$0			\$0	\$0	\$5,000,000
Total		\$4,388	\$2,531,472	\$158,468	\$6,159	\$2,530,504	\$0	\$2,886	\$228,301	\$395,237	\$836,407	\$449,662	\$232,985	\$208,931	\$2,838,036	\$4,008,575	\$14,432,013
Project Budget	\$25,000,000																
Less Other Funding*	\$0																
Net	\$25,000,000																
Actual Measure S Expenditures	\$14,432,013																
Running Balance	\$10,567,987																

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19	Combined Totals
					•		•				•		'				
S7100043, S7100066																	
Energy Efficiency Projects (7)																	
Legal		\$0	\$0	\$0	\$0	\$988	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$988
Building & Additions		\$0		\$0	\$0	\$106,921	\$355,294	-\$180,342	\$0	\$0	\$0	\$0		\$0	\$0	\$0	
Engineering		\$0		\$0	\$10,500	\$0			\$0	\$0	\$0			\$0	\$0	\$0	
Inspection & Testing		\$0		\$0	\$0	\$0		\$0	\$0	\$0	\$0		\$0		\$0	\$0	
Project Management		\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0				\$0	\$0	
Total		\$0	\$0	\$0	\$10,500	\$107,910	\$355,294	-\$180,342	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$293,361
Project Budget	\$510,683	Received		-			-	-									
Less Other Funding*	\$217,322	\$217,322		 Other Funding 													
Net	\$293,361			SCE & The Gas	Co. \$217,322	received											
Actual Measure S Expenditures	\$293,361																
Running Balance	\$0																
•																	•
S7100091, S7100092, S7100147																	
Satellite Campus Parking Facilities and Roadway Im	provements (8)																
Legal		\$0	\$0	\$0	\$300	\$175	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0	
Other Contract Services		\$0		\$0	\$300	\$0			\$0	\$0	\$0	\$0		\$0	\$0	\$0	
Advertising		\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$0
Consultants		\$0		\$0	\$0	\$0			\$0	\$0	\$0			\$0	\$0	\$0	
Supplies		\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0				\$0	\$0	
Building & Additions		\$0		\$0	\$278,178	\$1,860,152	\$449,543		\$0	\$0	\$0	\$64			\$0	\$0	
Architect		\$0		\$324,919	\$324,864	\$136,911	\$34,490	\$1,397	\$2,289	\$0	\$0	\$0		\$0	\$0	\$0	
Engineering		\$0		\$0	\$0	\$0			\$0	\$0	\$30,896	\$5,470				\$0	
Inspection & Testing		\$0		\$0	\$31,100	\$185,947	\$28,218		\$0	\$0	\$0	\$0		\$0	\$0	\$0	
Project Management		\$0		\$0	\$18,288	\$64,880	\$31,137	\$8,659	\$0	\$2,569	\$10,730	\$6,046		\$0	\$0	\$0	
Non-Cap Equipment		\$0		\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0	
Total		\$0	\$0	\$324,919	\$653,031	\$2,248,065	\$546,775	\$48,194	\$2,289	\$2,569	\$41,626	\$11,580	\$12,700	\$0	\$0	\$0	\$3,891,747
Project Budget	\$7,022,417																
Less Other Funding	\$3,130,670			 Other Funding 													
Net	\$3,891,747			Measure AA \$2	,130,670, Meas	sure V \$1,000,	000 allocated										
Actual Measure S Expenditures	\$3,891,747																
Running Balance	\$0																

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19	Combined Totals
											•				•		
S7100142																	
Parking Garage and Grounds - Student Services (9)																	
Supplies		\$0	\$0	\$0	\$0	\$1,745	\$0	\$0	\$648	\$0	\$0	\$813	\$0	\$0	\$0	\$0	\$3,206
Consultants		\$0	\$0	\$0	\$0	\$20,700	\$0	\$0	\$0	\$0	\$0		\$1,740	\$0	\$0	\$0	\$22,440
Legal		\$0	\$0	\$0	\$0	\$2,154	\$17,486		\$2,257	\$17,221			\$0	\$0	\$0	\$0	\$47,488
Other Contract Services		\$0		\$0		\$1,508	\$10,952	\$1,986	\$46	\$0	\$12,083		\$0	\$0	\$0	\$0	\$31,608
Site Improvement		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,086			\$0	\$0	\$0	\$0	
Building & Additions		\$0	\$0	\$0	\$0	\$2,555,940	\$5,925,152	\$78,717	\$77,320	\$5,509	\$715	\$0	\$3,721	\$11,308,792	\$16,249,515	\$0	
Architect		\$0	\$0	\$0	\$2,266,766	\$2,674,054	\$0	\$37,111	\$75,163	\$0	\$0		\$0	\$0	\$287,176	\$0	
Engineering		\$0	\$0	\$0	\$0	\$4,813	\$38,330	\$42,968	\$50,952	\$9,735			\$0	\$0	\$49,171	\$0	
Inspection & Testing		\$0	\$0	\$0	\$0	\$131,009	\$161,847	\$54,069	\$32,306	\$30,909			\$38,186	\$516,217	\$851,397	\$0	
Project Management		\$0	\$0	\$0	\$0	\$158,766	\$373,559	\$184,088	\$92,118	\$224,994	\$59,525	\$29,714	\$50,380	\$285,057	\$420,233	\$0	
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$14,393	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	
Non-Cap Equipment		\$0		\$0	\$0	\$0	\$0	\$0	\$11,381	\$0		\$0	\$0	\$0	\$0	\$0	
Total		\$0	\$0	\$0	\$2,266,766	\$5,550,689	\$6,541,719	\$403,737	\$342,192	\$289,454	\$76,445	\$62,735	\$94,027	\$12,110,066	\$17,857,492	\$0	\$45,595,322
Project Budget	\$130,224,164			* Other Funding	g Source:												
Less Other Funding*	\$84,628,842			State of Califor	nia \$1,321,000	received											
Net	\$45,595,322			Mease U \$21,1	31,135, Measi	re AA \$6,870,4	90, Measure V	/ \$33,624,909 a	llocated								
Actual Measure S Expenditures	\$45,595,322			Measure U, S &	& AA interests :	\$21,681,308 all	ocated										
Running Balance	\$0																

Parking Garage and Grounds - Student Services

Project Description:

Consolidates various student services departments and college administration in a single complex at the front of the campus


Facility Size: 110,000 sq/ft & 500 cars underground parking

Status: Phase 1 completed Phase 2 In construction

Steinberg Architects, Morris Architects

Contractor:

Minaco, Bernards



Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final 1	7/18 Final	18/19	Combined Totals
r==																	
S7100044																	
Pico Promenade Improvements (10)																	
Building & Additions		\$0	\$0		\$690	\$883,401	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$884,091
Architect		\$0	\$0		\$69,190	\$28,540	\$864	\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$98,595
Inspection & Testing		\$0	\$0		\$0	\$7,591	\$0	\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$0	
Project Management		\$0			\$2,185	\$25,548	\$0	\$0		\$0	\$0	\$0		\$0	\$0	\$0	
Total		\$0	\$0	\$0	\$72,066	\$945,080	\$864	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,018,009
Project Budget	\$1,018,009																
Less Other Funding	\$0																
Net	\$1,018,009																
Actual Measure S Expenditures	\$1,018,009																
Running Balance	\$0																
S7100004																	
Master Planning (11)																	
Consultants		\$0			\$0			\$13,320	\$0	\$0	\$0	\$0		\$0	\$0	\$0	
Printing		\$0			\$0	\$0	\$4,157	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,157
Advertising		\$0			\$0			\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	
Other Contract Services		\$0			\$0	\$0	\$442	\$200	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	
Architect		\$0			\$0			\$24,736	\$0	\$0	\$0	\$0		\$0	\$0	\$0	
Project Management		\$0	\$0	\$0	\$0	\$0	\$16,638	\$9,341	\$0	\$0	\$7,845	\$0	\$0	\$0	\$0	\$0	\$33,824
Filling Fees		\$0			\$0	\$0	\$0	\$2,842	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	
Total		\$0	\$0	\$0	\$0	\$0	\$658,143	\$50,439	\$0	\$0	\$7,845	\$0	\$0	\$0	\$0	\$0	\$716,428
Project Budget	\$716,428							-						-	-		
Less Other Funding	\$0																
Net	\$716,428																
Actual Measure S Expenditures	\$716,428																
Running Balance	\$0																
S7100048																	
Other Bond Related Expenses (12)																	
Consultants		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,971	\$2,524	\$6,239	\$1,354	\$0	\$0	\$0	\$13,089
Lease/Rental		\$0	\$0	\$0	\$0			\$0	\$11,142	\$15,099	\$15,285	\$14.809	\$13,418	\$13,120	\$16.611	\$15,866	\$115,350
Supplies		\$0	\$0	\$0	\$0			\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,638
Legal		\$0	\$0	\$0	\$0		\$8,917	\$15,649	\$13,401	\$450	\$503	\$38,130	\$9,186	\$0	\$0	\$0	\$86,236
Software License		\$0	\$0	\$0	\$0	\$0	\$0	\$1,997	\$0	\$3,565	\$0	\$4,200	\$0	\$0	\$0	\$0	\$9,762
Advertising		\$0			\$0		\$2,278	\$0	\$0	\$0	\$0	\$0	\$0	\$864	\$0	\$0	
Other Contract Services		\$0		\$0	\$0	\$1,800	\$17,206	\$23,558	\$19,208	\$15,816	\$13,627	\$13,952	\$12,963	\$11,760	\$18,900	\$15,225	\$164,014
Moving Services		\$0		\$0	\$0		\$400	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$400
Project Management		\$0	\$0		\$0			\$13,179	\$11,963	\$0	\$0	\$0	\$0	\$0	\$0	\$0	
Cap Equipment		\$0	\$0		\$0	\$0		\$10,086	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$10,086
Non-Cap Equipment		\$0	\$0		\$0	\$0	\$0	\$2,860	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,860
Total	1	\$0					\$50.185	\$67,328	\$55.713	\$37.901	\$31.939	\$77.330	\$36.921	\$25.744	\$35.511	\$31.091	
Project Budget	\$609,282	1.1	**	**	**1	7.,		,	. , , , , , , , ,	,		,		. •,	,	,	7.01,101
Less Other Funding	\$0																
Net	\$609.282																
Actual Measure S Expenditures	\$451,464																
Running Balance	\$157,818																
	ψ.σ.,σισ																

Projects	Budget	04/05 Final	05/06 Fi	inal 06/07	Final 07/0	08 Final 0	8/09 Final	09/10 Final	10/11 Final 1	11/12 Final	12/13 Final 1	3/14 Final 1	4/15 Final	15/16 Final	16/17 Final 1	17/18 Final	18/19	Combined Totals
S7100049		1	1	1	1		-	1			T		T	1				
Adv Architecture Related Exp for AA (13)																		
Legal		\$0	n	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0 \$0
Architect	_	\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
		\$(0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0 \$0
Engineering Inspection & Testing		\$(\$0	\$0	\$0	\$45,734	-\$45,734	\$0	\$0	\$0	\$0	\$0 \$0	\$0	\$0	\$0	\$0	\$0 \$0
Project Management		\$(\$0		\$0	\$45,734	-\$45,734 \$0	\$0	\$0	\$0	\$0	\$0			\$0	\$0	\$0
		\$(\$0 \$0	\$0	\$0 \$0					\$0 \$0			\$0 \$0	\$0			\$0 \$0
Total Project Project	-		U	\$0	\$0	\$0	\$45,734	-\$45,734	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Budget	\$0	1																
Less Other Funding	\$0	1																
Net	\$0 \$0																	
Actual Measure S Expenditures	\$0	1																
Running Balance	\$0																	
S7100057																		
Real Property Acquisition (14)																		
Other Contract Services		\$0	0	\$0	\$0	\$0	\$0	\$18,721	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$18,721
Architect		\$(\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Engineering		\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0		\$0	\$0	\$0	\$0	\$6,336	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$6,336
Project Management		\$(\$0	\$0	\$0	\$0	\$20,540	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$20,540
Total		\$(\$0	\$0	\$0	\$0 \$0	\$45,597	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$45,597
Project Budget	\$45,597	Ψ,	·	40	Ψ0	40	ΨΟ	ψ+0,001	Ψ0	ΨΟ	ΨΟ	40	40	40	40	Ψ0	ΨΟ	ψ 1 0,001
Less Other Funding	\$43,387	1																
Net	\$45,597																	
Actual Measure S Expenditures	\$45,597	-																
Running Balance	\$45,597																	
Running Balance	\$0																	
<u> </u>																		
S7100072																		
Campus Signage (15)																		
Supplies		\$0		\$0	\$0	\$0	\$0	\$0	\$303	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$303
Consultants		\$0		\$0	\$0	\$0	\$0 \$0	\$32,225	\$23,725	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$55,950
Other Contract Services		\$0		\$0	\$0	\$0	\$0	\$0	\$187	\$0	\$836	\$0	\$0	\$0	\$1,051	\$0	\$0	\$2,074
Architect		\$0	0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$(0	\$0	\$0	\$0	\$0	\$0	\$638	\$0	\$0	\$1,440	\$1,325	\$416,937	\$0	\$0	\$0	\$420,339
Inspection & Testing		\$(0	\$0	\$0	\$0	\$0 \$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$(0	\$0	\$0	\$0	\$0	\$0	\$22,953	\$0	\$0	\$8,260	\$8,388	\$28,622	\$165	\$0	\$0	\$68,388
Cap Equipment		\$(\$0	\$0	\$0	\$0	\$0	\$156,258	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$156,258
Non-Cap Equipment		\$(\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,402	\$0	\$0	\$3,402
Total		S		\$0	\$0	\$0	\$0	\$32,225	\$204,064	\$0	\$836	\$9,700	\$9,712	\$445,559	\$4,618	\$0	\$0	\$706,713
Project Budget	\$706,713		-	70	7-	7-1	70	ŢJ_,	420.,004	+0	+555	40,.00	¥0,L	Ţ,	Ţ.,J.U	70	70	Ţ. 55,7 10
Less Other Funding	\$700,713																	
Net	\$706,713																	
Actual Measure S Expenditures	\$706,713																	
Running Balance	\$706,713																	
Running balance	1 \$0	L																
r <u>-</u>																		
S			1															
Cost of Issuance (16)																		
Cost of Issuance		\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$119,470	\$0	\$0	\$119,470
Total		\$0	0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$119,470	\$0	\$0	\$119,470
Project Budget	\$119,470			•	•	•				•	•							
Less Other Funding	\$0	1																
Net	\$119,470																	
Actual Measure AA Expenditures	\$119,470																	
Turning building	1 90																	
Running Balance	\$0]																

Grand Total

 \$7,958,606
 \$14,601,366
 \$10,740,621
 \$8,321,918
 \$20,819,624
 \$8,933,245
 \$617,492
 \$651,441
 \$878,632
 \$1,287,285
 \$6,081,769
 \$6,083,251
 \$12,554,384
 \$21,858,285
 \$7,298,911
 \$129,419,831

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19	Combined Totals
									•						-		•
Measure S Interest		17/18	18/19														
Parking Garage and Grounds - Student Services (9)																	
Site Imptovement		\$568	\$0														
Building & Additions		\$8,224,377	\$629,869														
Architect		\$189,078	\$67,105														
ngineering		\$11,000	\$15,000														
nspection & Testing		\$125,080	\$0														
Project Management		\$171,448	\$0														
otal		\$8,721,552	\$711,974														
Project Budget	\$9,433,526																
Actual Measure S Interest Expenditures	\$9,433,526																
Running Balance	\$0																

SANTA MONICA COMMUNITY COLLEGE DISTRICT

Measure AA Project Schedule As of June 30, 2019

	Project Name	Completion	20	18		2	019)	20	20		2	021		202	2
101	Environmental Performance - Central Plant Connections	Completed														\prod
102	Infrastructure & Technology - Information Technology Relocation	Completed														
103	Media and Technology Complex - Academy Site	Completed														
104	Replacement Health/PE/Fitness/Dance Building with Central Plant	Completed														
105	Drescher - Academic Modernization, Bookstore, Pico Promenade	Deferred														
106	Replacement Math and Science Extension Building	December 2022														
107	Madison East Wing Seismic Upgrade	Completed														
108	Renovation of Corsair Stadium	Completed														
109	Career Opportunity and Advancement Center (Bundy)	Completed														
110	Malibu Center	December 2021														
111	Business & Facilities Infrastructure	Completed														
112	Master Planning, Program Management, Overhead	On-Going														
113	Energy Efficiency Projects	Completed														
114	Community Classroom & Facility Projects	Completed														
115	Real Property Acquisition	Completed														
116	Roadways, Walkways, Grounds, Parking Lots, and Garages	Completed														
117	Infrastructure & Technology - Technology	Completed														
118	Infrastructure & Technology - Utility	Completed														
119	Emergency Lighting, Fire Alarm, and Security System	On-Going														
120	Student Services	Completed														
121	Cost of Issuance	Completed														
122	Management Reserve	On-Going														
123	Unissuable Bond	Completed														
					ln	Planr	ning		In (Cons	stru	ctio	n			

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19	Combined Totals
•							,					
AA 7100062												
Environmental Performance - Central Plant Connections (101)												
Legal		\$0	\$0	\$0	\$125	\$0	\$0	\$0	\$0	\$0	\$0	\$125
Other Contract Services		\$0	\$0	\$49,837	\$16,239	\$0	\$0	\$0	\$0	\$9,920	\$0	\$75,996
Consultants		\$0	\$0	\$0	\$0	\$28	\$0	\$0	\$0	\$0	\$0	\$28
Building & Additions		\$0	\$0	\$0	\$361	\$729	\$640	\$1,328,592	\$6,934,044	\$446,861	\$0	\$8,711,229
Architect		\$0	\$385	\$148,311	\$176,897	\$36,256	\$0	\$0	\$0	\$0	\$15,699	\$377,547
Engineering		\$48,500	\$0	\$4,000	\$0	\$152,010	\$39,638	\$66,918	\$138,887	\$62,883	\$0	\$512,836
Inspection & Testing		\$0	\$0	\$7,688	\$0	\$0	\$0	\$7,310	\$137,150	\$4,382	\$0	\$156,529
Project Management		\$0	\$17,263	\$55,116	\$48,685	\$61,908	\$19,313	\$104,575	\$526,072	\$99,840	\$190	\$932,961
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$48,500	\$17,648	\$264,951	\$242,307	\$250,931	\$59,591	\$1,507,396	\$7,736,152	\$623,886	\$15,889	\$10,767,251
Project Budget	\$10,767,251						-					
Less Other Funding	\$0											
Net	\$10,767,251											
Actual Measure AA Expenditures	\$10,767,251											
Running Balance	\$0											

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19	Combined Totals
												-
AA 7100063												
Infrastructure & Technology - IT Relocation (102)												
Supplies		\$0	\$0	\$965	\$8,442	\$3,137	\$2,600	\$0	\$0		\$0	\$15,144
Consultants		\$0	\$0	\$0	\$0	\$408	\$0	\$7,800	\$0	\$0	\$0	\$8,208
Maintenance Contract		\$0	\$0	\$0	\$0	\$107,390	\$0	\$77,074	\$79	\$0	\$0	\$184,543
Legal		\$0	\$0	\$0	\$1,363	\$50	\$0	\$0	\$0		\$0	\$1,413
Printing		\$0	\$0	\$0	\$0	\$1,624	\$0	\$0	\$0		\$0	\$1,624
Postage		\$0	\$0	\$0	\$0	\$1,567	\$0	\$0	\$0	\$0	\$0	\$1,567
Other Contract Services		\$0	\$0	\$2,163	\$15,259	\$23,356	\$0	\$19,050	\$4,500	\$0	\$0	\$64,328
Moving		\$0	\$0	\$0	\$577	\$266	\$27,655	\$22,618	\$0	\$0	\$0	\$51,116
Site Improvement		\$0	\$0	\$0	\$24	\$0	\$0	\$0	\$0		\$0	\$24
Building & Additions		\$0	\$0	\$0	\$1,767,083	\$9,667,362	\$4,288,987	\$1,203,916	\$165,229	-\$19,798	\$0	\$17,072,780
Architect		\$105,049	\$482,261	\$505,580	\$183,181	\$287,201	\$236,860	\$120,091	\$0	\$0	\$0	\$1,920,223
Engineering		\$0	\$0	\$10,037	\$11,065	\$17,147	\$19,512	\$25,994	\$1,956	\$0	\$0	\$85,712
Inspection & Testing		\$10,291	\$8,793	\$21,449	\$137,523	\$499,982	\$200,262	\$568	\$0	\$0	\$0	\$878,868
Project Management		\$33,460	\$76,290	\$84,991	\$331,754	\$431,730	\$297,951	\$22,978	\$1,500	\$0	\$0	\$1,280,653
Cap Equipment		\$0	\$0	\$0	\$29,422	\$645,830	-\$29,090	\$589,604	\$9,811	\$0	\$0	\$1,245,576
Non-Cap Equipment		\$0	\$0	\$0	\$18,344	\$10,852	\$277,219	\$1,891	\$20,689	\$0	\$0	\$328,994
Total		\$148,800	\$567,344	\$625,185	\$2,504,035	\$11,697,901	\$5,321,956	\$2,091,584	\$203,764	-\$19,798	\$0	\$23,140,771
Project Budget	\$23,160,569	Received			-					•		
Less Other Funding	\$19,798	\$19,798	* Other Funding S	ource:								
Net	\$23,140,771	•	Edison \$19,798 re	ceived								
Actual Measure AA Expenditures	\$23,140,771											
Running Balance	\$0											

Infrastructure & Technology -IT Relocation

Project Description:
Relocation of IT/Telecom Departments, and renovation of Media Center


Facility Size: 9,230 sq/ft

Status: Completed

Architect: Morris Architects

Contractor:

Minco, Bernards Brothers



Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19	Combined Totals
					·						·	
AA 7100061												
Media and Technology Complex - Academy Site (103)												
Consultants		\$0	\$0	\$20,675	\$12,576	\$9,488	\$7,789	\$2,102	\$0	\$12,922	\$0	\$65,551
Supplies		\$0	\$0	\$0	\$19,481	\$1,048	\$289	\$0	\$9,251	\$40,519	\$1,764	\$72,352
Maintenance Contract		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$15,922	\$23,561	\$0	\$39,483
Legal		\$16,903	\$0	\$7,958	\$43,363	\$5,066	\$26,186	\$49,155	\$15,435	\$36,221	\$4,543	\$204,829
Software Support		\$0	\$0	\$0	\$1,982	\$0	\$0	\$0	\$6,548	\$6,975	\$0	\$15,505
Service Fee		\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$										
Other Contract Services		\$3,993	\$5,763	\$13,456	\$39,188	\$0	\$0	\$5,853	\$22,622	\$18,628	\$0	\$109,503
Moving Expenses		\$0	\$0	\$0	\$38,756	\$0	\$0	\$0	\$0	\$97,543	\$17,556	\$153,855
Site Improvement		\$0	\$0	\$0	\$100,505	\$664	\$606	\$476	\$622	\$526	\$0	\$103,399
Building & Additions		\$0	\$538	\$1,498,660	\$3,543,657	\$11,820,615	\$17,734,534	\$23,465,347	\$16,267,550	\$25,548,089	\$313,870	\$100,192,858
Architect		\$2,097,553	\$2,508,588	\$295,753	\$265,481	\$778,015	\$517,794	\$1,048,935	\$991,386	\$869,801	\$145,841	\$9,519,146
Engineering		\$16,459	\$29,293	\$9,102	\$29,223	\$8,203	\$72,993	\$118,368	\$72,786	\$51,971	\$37,259	\$445,657
Inspection & Testing		\$64,905	\$27,527	\$123,842	\$235,287	\$563,746	\$1,381,801	\$641,972	\$525,264	\$207,240	\$27,210	\$3,798,793
Project Management		\$121,786	\$233,826	\$269,249	\$506,917	\$800,315	\$930,115	\$1,207,850	\$1,121,670	\$859,779	\$49,381	\$6,100,886
Cap Equipment		\$0	\$0	\$0	\$186,301	\$0	\$0	\$0	\$0	\$1,458,273	\$5,777	\$1,650,351
Non-Cap Equipment		\$0	\$0	\$0	\$10,782	\$0	\$0	\$0	\$326,845	\$490,727	\$7,167	\$835,520
Total		\$2,321,599	\$2,805,534	\$2,238,694	\$5,033,499	\$13,987,159	\$20,672,105	\$26,540,059	\$19,392,902	\$29,722,772	\$610,367	\$123,324,689
Project Budget	\$130,549,713	Received						•		•		
Less Other Funding*	\$6,835,391		* Other Funding So									
Net	\$123,714,322		KCRW Foundation		nited, \$6,092,176	eceived						
Actual Measure AA Expenditures	\$123,324,689	1	Edison \$31,979.48	received								
Running Balance	\$389,633											

Media and Technology Complex -Academy Site

Project Description:

Renovation and new extension to the existing building, new building for KCRW, and a new parking structure


Facility Size: Building - 116,000 sq/ft Parking Structure - 450 spaces

Status:

In construction


Architect: Clive Wilkinson Architects

Contractor: H.B. Parkco Construction Fast Track Construction CW Driver



Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19	Combined Totals
												•
AA 7100060												
Repl. Health/PE/Fitness/Dance Building with Central Plant (104)												
Consultants		\$0	\$0	\$0	\$14	\$62	\$2,304	\$184	\$0	\$0	\$0	\$2,564
Supplies		\$0	\$0	\$0	\$0	\$7,089	\$195	\$484	\$20,947	\$0	\$0	\$28,715
Legal		\$0	\$0	\$0		\$0	\$0	\$663	\$80	\$0	\$0	\$742
Software Support		\$0	\$0	\$0	\$0	\$0 \$0	\$0	\$0	\$1,209	\$0	\$0	\$1,209
Site Improvement		\$0	\$0	\$0	\$0	\$559	\$440	\$575	\$0	\$0	\$1,574	
Off Campus Printing		\$0	\$0	\$0	\$0	\$2,165	\$0	\$0	\$0	\$0	\$2,165	
Postage		\$0 \$0 \$0				\$0	\$1,505	\$0	\$0	\$0	\$0	\$1,505
Other Contract Services		\$120 \$38 \$112			\$32,634	\$0	\$1,019	\$581	\$0	\$2,644	\$0	\$37,147
Building & Additions		\$0	\$0	\$817	\$4,188	\$1,623	\$13,783,023	\$14,880,829	\$5,315,393	-\$148,184	\$33,837,688	
Architect		\$256,076	\$1,568,564	\$1,790,207		\$177,583	\$364,853	\$585,900	\$373,345	\$210,312	\$108,264	\$5,954,078
Engineering		\$0	\$8,507	\$31,650	\$7,871	\$6,529	\$9,276	\$76,712	\$51,025	\$11,318	\$24,213	\$227,101
Inspection & Testing		\$36,892	\$490	\$21,150	\$1,285	\$360	\$133,756	\$846,765	\$358,724	\$60,826	\$1,330	\$1,461,579
Project Management		\$34,968	\$113,379	\$118,783	\$94,768	\$108,528	\$463,418	\$564,240	\$487,065	\$312,539	\$20,242	\$2,317,928
Cap Equipmwnt		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$164,793	\$68,425	\$0	\$233,218
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$9,015	\$0	\$206,229	\$127,078	\$0	\$342,322
Total		\$328,056	\$1,690,978	\$1,961,901	\$656,362	\$304,338	\$989,689	\$15,858,991	\$16,544,820	\$6,108,535	\$5,864	\$44,449,534
Project Budget	\$56,292,030	•								-	•	
Less Other Funding*	\$11,812,230		* Other Funding So									
Net	\$44,479,800		Measure S \$11,60									
Actual Measure AA Expenditures	\$44,449,534		SCE \$190,847.28,	Gas Co. \$18,000	received							
Running Balance	\$30,266											






Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19	Combined Totals	
												1	
AA 7100065													
Drescher - Academic Modernization, Bookstore, Pico Promenade (105)												L	
Legal		\$0	\$0	\$0	\$0	\$0				\$0	\$0	\$0	
Other Contract Services		\$0	\$0	\$0						\$0	\$0		
Site Acquisition		\$0	\$0	\$0	\$0	\$0				\$0	\$0		
Inspection & Testing		\$0	\$0		\$0	\$0				\$0	\$0		
Project Management		\$0			\$0					\$0			
Total		\$0	\$0	\$5,082	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$5,082	
Project Budget	\$13,005,082												
Less Other Funding	\$13,000,000		* Other Funding S										
Net	\$5,082		Measure V 13,00	0,000 allocated									
Actual Measure AA Expenditures	\$5,082												
Running Balance	\$0												
AA 7100090													
Replacement Math and Science Extension Building (106)													
Legal		\$0	\$0							\$0		\$0	
Other Contract Services		\$0	\$0	\$0	\$0	\$0				\$1,525			
Site Acquisition		\$0	\$0							\$0	\$0		
Building & Additions		\$0	\$0							\$4,796	\$0		
Architect		\$0	\$0			\$0				\$1,787,824	\$0		
Engineering		\$0	\$0	\$0		\$0	\$0	\$0		\$0	\$0		
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$70,223	\$0	\$70,223	
Project Management		\$0		\$0		\$4,950	\$0	\$0	\$800	\$228,760	\$0	\$234,510	
Total		\$0	\$0	\$0	\$0	\$4,950	\$0	\$0	\$800	\$2,093,128	\$0	\$2,098,878	
Project Budget	\$124,958,336												
Less Other Funding	\$122,714,328		* Other Funding S										
Net	\$2,244,008		Measure U \$308,3	336, Measure V \$8	2,317,992 allocate	ed .							
Actual Measure AA Expenditures	\$2,098,878		State of California	\$40,088,000 alloc	ated								
Running Balance	\$145,130												

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19	Combined Totals
												•
AA 7100047												
Madison East Wing Seismic Upgrade (107)												
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$6,197	\$0	\$0	\$6,197
Consultants		\$0	\$0	\$0	\$0	\$135	\$28	\$0	\$0	\$0	\$0	
Off Campus Printing		\$0	\$0	\$0	\$0	\$0	\$285	\$0	\$0	\$0	\$0	
Maintenance Contract		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$357	\$0	\$0	
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$7,579	\$11,822	\$8,263	\$27,663
Software Support		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$806	\$0	\$0	\$806
Other Contract Services		\$0	\$364	\$997	\$0	\$0	\$1,328	\$711	\$0	\$0	\$0	\$3,400
Building & Additions		\$0	\$656	\$312,643	\$0	\$4,248	\$6,030,371	\$8,829,626	\$4,949,223	\$3,967,591	\$0	\$24,094,358
Architect		\$76,073	\$398,050	\$550,589	\$65,444	\$57,480	\$199,100	\$404,764	\$122,764	\$103,824	\$0	\$1,978,088
Engineering		\$0	\$0	\$10,707	\$778	\$0	\$13,792	\$33,184	\$37,491	\$90	\$0	
Inspection & Testing		\$0	\$19,848	\$16,752		\$5,851	\$676,323	\$405,443	\$112,876	\$4,703	\$0	
Project Management		\$5,557	\$128,878	\$112,573	\$67,447	\$118,242	\$494,874	\$481,165	\$322,379	\$31,230	\$9,206	\$1,771,549
Cap Equipment		\$0	\$0	\$30,603	\$0	\$0	\$0	\$0	\$537,627	\$0	\$0	\$568,230
Non-Cap Equipment		\$0	\$0	\$71,827		\$0	\$0	\$0	\$285,236	\$0	\$0	
Total		\$81,630	\$547,796	\$1,106,691	\$146,492	\$185,956	\$7,416,101	\$10,154,894	\$6,382,534	\$4,119,259	\$17,469	\$30,158,822
Project Budget	\$30,178,822		-			•		•	-	-		
Less Other Funding	\$0											
Net	\$30,178,822											
Actual Measure AA Expenditures	\$30,158,822											
Running Balance	\$20,000											

Madison East Wing Seismic Upgrade Project Description: Replacement of east wing with a new multipurpose room and additional classrooms Facility Size: 20,838 sq/ft Status: In construction Architect: DLR Group WWCOT Contractor: Bernards Brothers



Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19	Combined Totals
		1										
AA 7100068												
Renovation to Corsair Stadium (108)				***	20	***	•	20	20		•	
Other Contract Services		\$0	\$0	\$0		\$0	\$0		\$0	\$0	\$0	
Building & Additions		\$0	\$0	\$0		\$0	\$0		\$0	\$0	\$0	
Architect		\$0	\$30,759	\$0		\$0	\$0		\$0	\$0	\$0	
Engineering		\$0	\$0	\$0		\$0	\$0		\$0	\$0	\$0	
Inspection & Testing		\$0 \$0	\$0 \$4,540	\$0 \$0		\$0 \$0	\$0 \$0		\$0 \$0	\$0 \$0	\$0 \$0	
Project Management Total		\$0 \$0	\$35,299	\$0 \$0		\$0 \$0	\$0 \$0		\$0 \$0	\$0 \$0	\$0 \$0	
Project Budget	\$35,299	\$ 0	\$35,299	\$0	\$ 0	\$U	ψU	\$0	Ψ 0	\$U	ψŪ	\$35,299
Less Other Funding	\$0											
Net	\$35,299											
Actual Measure AA Expenditures	\$35,299											
Running Balance	\$0											
Ituning Balance	ΨΟ											
AA 7100067, 7100152, 7100155, 7100157		1			1							
Business & Facilities Infrastructure (111)												
Supplies		\$0	\$0	\$0	\$1,493	\$4,840	\$0	\$0	\$0	\$0	\$0	\$6,333
Service Fee		\$0	\$0	\$0		\$0	\$0		\$0	\$0	\$0	
Consultants		\$0	\$0	\$0		\$14	\$8	\$0	\$0	\$0	\$0	
Maintenance Contract		\$0	\$0	\$0		\$1,366	\$0		\$0	\$0	\$0	
Legal		\$0	\$0	\$75		\$0	\$0		\$0	\$0	\$0	
Software License		\$0	\$0	\$0		\$375	\$0		\$0	\$0	\$0	
Other Contract Services		\$0	\$6,289	\$6.988	\$750	\$0	\$2,209		\$0	\$0	\$0	
Moving Services		\$0	\$0	\$0		\$0	\$0		\$0	\$0	\$0	\$395
Building & Additions		\$0	\$34,672	\$198,667	\$200,585	\$284,668	\$0		\$0	\$0	\$0	\$718,592
Architect		\$0	\$0	\$80,626	\$170,132	\$37,906	\$0	\$0	\$0	\$0	\$0	
Engineering		\$0	\$0	\$0		\$9,735	\$6,840	\$0	\$0	\$0	\$0	
Inspection & Testing		\$0	\$0	\$8,142	\$10,938	\$10,500	\$0		\$0	\$0	\$0	
Project Management		\$0	\$3,073	\$154,904	\$87,291	\$139,821	\$3,571	\$0	\$0	\$0	\$0	
Cap Equipment		\$0	\$0	\$0		\$80,090	\$0	\$0	\$0	\$0	\$0	
Non-Cap Equipment		\$0	\$89,204	\$0		\$193,782	\$0		\$0	\$0	\$0	
Total		\$0	\$133,238	\$449,401	\$608,656	\$763,095	\$12,628	\$1,105	\$0	\$0	\$0	\$1,968,124
Project Budget	\$1,968,124											
Less Other Funding	\$0											
Net	\$1,968,124											
Actual Measure AA Expenditures	\$1,968,124											
Running Balance	\$0											
AA 7100004		Т	Т	1	Т	Т		Г	1	Т		 1
Master Planning, Program Management, Overhead (112)					+							
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$0	\$0	\$0		\$0	\$0		\$187,927	\$245,329	\$1,270	\$573,828
Project Management		\$0	\$0	\$0		\$76.015	\$150	\$0	\$49,170	\$135.533	\$0	
Cap Equipment		\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0		\$0	\$0		\$0	\$0	\$0	
Total		\$0	\$0	\$0		\$76,015	\$150		\$237,097	\$380,863	\$1,270	
Project Budget	\$834,697	**	+	40	**	Ţ. I,II	Ţ. 00	Ţ, 002	+ ,,,,,,	¥222,300	Ţ., 	,, .,
Less Other Funding	\$0											
Net	\$834,697											
Actual Measure AA Expenditures	\$834,697											
Running Balance	\$0											
<u> </u>	1 40											

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19	Combined Totals
•							•			·		
AA 7100154												
Energy Efficiency Projects (113)												
Legal										\$0	\$0	
Other Contract Services									\$0	\$0	\$0	
Building & Additions					\$2,108,853	\$990,389	-\$97,621	\$0	\$0	\$0	\$0	\$3,001,81
Architect						\$0				\$0	\$0	\$
Engineering			\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$						\$0	\$0	\$0	\$
Inspection & Testing										\$0	\$0	
Project Management										\$0	\$0	
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$
Total		\$0	\$0	\$189	\$2,112,873	\$990,389	-\$86,678	\$0	\$0	\$0	\$0	\$3,016,77
Project Budget	\$3,508,088			•					•			
Less Other Funding	\$491,315		* Other Funding S	ource:								
Net	\$3,016,773											
Actual Measure AA Expenditures	\$3,016,773											
Running Balance	\$0		Gas Co. \$26,080 i	received								
AA 7100064												
Community Classroom & Facility Projects (114)												
Supplies		\$0	\$0	\$0	\$124	\$0	\$0	\$0	\$0	\$0	\$0	\$12
Legal										\$0	\$0	
Other Contract Services										\$0	\$0	
Building & Additions										\$0	\$0	
Architect										\$0	\$0	
Engineering										\$0	\$0	
Inspection & Testing		\$0	\$41,002		\$1.495	\$0				\$0	\$0	
Project Management		\$135	\$117,247		\$27,570	\$0		\$0	\$0	\$0	\$0	
Non-Cap Equipment		\$0	\$0		\$0	\$0				\$0	\$0	
Total		\$135	\$863.599		\$440.621	-\$1.003					\$0	
Project Budget	\$3,162,183	V.00	+ 000,000	\$1,000,001	Ų,uZ	V.,000	+	Ţ	***	**		+0,102,10
Less Other Funding	\$0											
Net	\$3,162,183											
Actual Measure AA Expenditures	\$3,162,183											
Running Balance	\$0,102,100											
Italiing Balance	\$0											
AA 7100057		1					1					
Real Property Acquisition (115)												
		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$659	\$0	\$65
Legal Other Contract Services		\$0 \$0	\$0 \$39		\$0 \$0					\$659	\$0 \$0	
Site Acquisition		\$1,739,979	\$4,001,204		\$0 \$0	\$15,800			\$5,013,226	\$4,821,600	\$0 \$0	
Inspection & Testing		\$1,739,979	\$4,001,204 \$7.986							\$4,821,600	\$0 \$0	
		\$8,689 \$0								\$0 \$0		
Project Management Total		\$0 \$1,748,667	\$0 \$4,009,228					\$0 \$0	\$5,013,226	\$4,822,259	\$0 \$0	
Project Budget	\$24,638,386	\$1,748,667	\$4,009,228	ф9,029,207	\$U	\$15,800	\$0	\$0	\$5,013,226	\$4,822,259	ŞU	\$24,638,38
Less Other Funding	\$0											
Net	\$24,638,386											
Actual Measure AA Expenditures	\$24,638,386											
Running Balance	\$0											

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19	Combined Totals
									T			
AA 7100058, 7100151, 7100156, 7100059												
Roadways, Walkways, Grounds, Parking Lots, and Garages (116)						21212		•			-	
Supplies		\$0	\$0		\$0		\$0	\$0			\$0	
Legal		\$0	\$0	\$0	\$125	\$0	\$0	\$0			\$0	
Consultants		\$0	\$0		\$48,090	\$5,018	\$0	\$0			\$0	
Other Contract Services		\$218	\$770	\$122	\$25,249	\$0	\$0	\$0			\$0	
Building & Additions		\$185,345	\$6,731	\$113,784	\$321,603	\$975,401	\$0	\$0			\$0	
Architect		\$0	\$0	\$0	\$103,569	\$19,225	\$1,240	\$0			\$0	
Engineering		\$0	\$0		\$1,095	\$1,445	\$0	\$0			\$0	
Inspection & Testing		\$13,380	\$7,865		\$20,126	\$42,865	\$0	\$0			\$0	
Project Management		\$24,404	\$12,439	\$21,945	\$54,095		\$1,411	\$0			\$0	
Total		\$223,347	\$27,804	\$149,403	\$573,951	\$1,153,512	\$2,652	\$0	\$0	\$0	\$0	\$2,130,670
Project Budget	\$7,022,417											
Less Other Funding	\$4,891,747		Other Funding S									
Net	\$2,130,670		Measure S \$3,891	1,747, Measure V \$	1,000,000 allocate	ed						
Actual Measure AA Expenditures	\$2,130,670											
Running Balance	\$0											
- v												
AA 7100069												
Infrastructure & Technology - Technology (117)												
Software		\$0	\$0	\$0	\$0	\$0	\$218	\$0	\$0	\$0	\$0	\$218
Supplies		\$0	\$0		\$7.587	\$0	\$16,966	\$0			\$0	
Maintenance Contract		\$0	\$9.472	\$46,300	\$210,581	\$18,944	\$42,415	\$9,472			\$0	
Other Contract Services		\$0	\$9,472		\$210,381		\$49,589	\$9,472			\$0	
Building & Additions		\$0	\$0 \$0		\$0 \$0		\$0	\$0			\$0	
Project Management		\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0		\$0	\$0 \$0			\$0	
Cap Equipment		\$0 \$0	\$207.423	\$33,063	\$576.294	\$0 \$0	\$1,145,668	\$0 \$0			\$0	
		\$0 \$0	\$207,423	\$42,827	\$576,294 \$500		\$1,145,000	\$0 \$0			\$0	
Non-Cap Equipment						\$0						
Total	20 101 117	\$0	\$216,896	\$135,838	\$794,963	\$18,944	\$1,258,304	\$9,472	\$0	\$0	\$0	\$2,434,417
Project Budget	\$2,434,417											
Less Other Funding	\$0											
Net	\$2,434,417											
Actual Measure AA Expenditures	\$2,434,417											
Running Balance	\$0											
AA 7100150												
Infrastructure & Technology - Utility (118)												
Sofeware License		\$0	\$12,000	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$12,000
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$0	\$0	\$0	\$0		\$0	\$0			\$0	
Inspection & Testing		\$0	\$4,979	\$0	\$0	\$0	\$0	\$0			\$0	
Project Management		\$0	\$3,240	\$0	\$0		\$0	\$0			\$0	
Cap Equipment		\$0	\$0	\$7.534	\$0		\$0	\$0			\$0	
Non-Cap Equipment		\$0	\$0	\$0	\$0		\$0	\$0			\$0	
Total		\$0	\$20,219		\$0		\$0	\$0			\$0	
Project Budget	\$27,753	40	Ψ±0,£13	ψ1,00 4	ΨΟ	40	40	40	1 40	1 40	Ψ	Ψ21,133
Less Other Funding	\$27,755											
Net	\$27,753											
Actual Measure AA Expenditures	\$27,753											
Running Balance	\$0											

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19	Combined Totals
AA 7100153												
Emergency Lighting, Fire Alarm, and Security System (119)		* 0		#0	60	#0.040	60	60	60.074	#0	60	#F 00
Supplies		\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0		\$0 \$16	\$0		\$0 \$0	\$0 \$442	
Consultants/Legal			\$0 \$0	\$0 \$0			\$800	\$0 \$0		\$0 \$0	\$442 \$0	
Telecom Fee Maintenance Contract		\$0 \$0	\$0 \$0	\$648	\$0 \$0		\$800	\$0 \$2,700		\$0 \$0	\$0 \$0	
Software Suppoert		\$0	\$0 \$0	\$24,765	\$0 \$0		\$0	\$2,700	\$0	\$0	\$0 \$0	
Other Contract Services	+	\$0	\$0 \$0	\$24,765	\$0		\$0	\$4,643	\$1,560	\$0	\$0	
Building & Additions		\$0	\$0 \$0	\$0	\$0 \$0		\$2,648,866	\$4,129,145		\$763,170	\$26,375	
Architect	+	\$0	\$0 \$0	\$0	\$0 \$0		\$18,925	\$4,129,143		\$5,047	\$20,375	
Enginnering		\$0	\$0	\$0	\$0 \$0		\$389.013	\$156,247		\$358,560	\$114,585	
Inspection & Testing		\$0	\$0	\$0	\$0		\$0	\$58,831	\$4,800	\$0	\$0	
Project Management		\$0	\$0	\$0	\$0		\$52,044	\$79,285		\$49,738	\$240	
Cap Equipment		\$0	\$0	\$0	\$0		\$0	\$5,871	\$0	\$0	\$0	
Non-Cap Equipment		\$0	\$0	\$6,087	\$0		\$8,348	\$0		\$0	\$0	
Total		\$0	\$0	\$31,500	\$0		\$3,118,012	\$4,438,953	\$1,589,560	\$1,176,515	\$141,642	
Project Budget	\$11,520,794	40	+0	7,000	+	72.23200	+-,··-, *·-	Ţ .,, 000	Ţ.,, 	Ţ.,, 	Ţ : , v : =	, , , , , , , , , , , , , , , , , , ,
Less Other Funding	\$0											
Net	\$11,520,794											
Actual Measure AA Expenditures	\$11,436,441											
Running Balance	\$84,353											
·												
AA 7100142												
Student Services (120)												
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Consultants		\$0	\$0	\$0 \$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0 \$0
Telecom Fee		\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0	\$0
Maintenance Contract		\$0	\$0	\$0	\$0		\$0	\$0		\$0	\$0	\$0
Software Suppoert		\$0	\$0	\$0	\$0		\$0	\$0		\$0	\$0	
Other Contract Services		\$0	\$0	\$0	\$0		\$0	\$0		\$0	\$0	
Building & Additions		\$0	\$0	\$0	\$0		\$0	\$0		\$3,165,626	\$3,704,864	
Architect		\$0	\$0	\$0	\$0		\$0	\$0		\$0	\$0	
Enginnering		\$0	\$0	\$0	\$0		\$0	\$0		\$0	\$0	
Inspection & Testing		\$0	\$0	\$0	\$0		\$0	\$0		\$0	\$0	
Project Management		\$0	\$0	\$0	\$0		\$0	\$0		\$0	\$0	
Cap Equipment		\$0	\$0	\$0	\$0		\$0	\$0		\$0	\$0	
Non-Cap Equipment		\$0	\$0	\$0	\$0		\$0	\$0		\$0	\$0	
Total		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,165,626	\$3,704,864	\$6,870,490
Project Budget	\$6,870,490											
Less Other Funding	\$0		Other Funding S									
Net	\$6,870,490			\$1,321,000 receive								
Actual Measure AA Expenditures	\$6,870,490					ure V \$33,624,909	allocated					
Running Balance	\$0	N	leasure U, S & A	A interests \$21,681	,308 allocated							
Cost of Issuance (121)												
Cost of Issuance		\$0	\$0	\$0	\$0		\$285,000	\$0		\$0	\$0	
Total	0.400.000	\$0	\$0	\$0	\$0	\$0	\$285,000	\$0	\$213,026	\$0	\$0	\$498,026
Project Budget	\$498,026											
Less Other Funding	\$0											
Net	\$498,026											
Actual Measure AA Expenditures	\$498,026											
Running Balance	\$0											
Grand Total	1	\$4,900,734	\$10,935,584	\$17,864,407	\$13,113,759	\$30,388,248	\$39,049,510	\$60,741,756	\$57,313,878	\$52,193,046	\$4,497,365	\$290,998,287

Measure AA Interest		18/19
Parking Garage and Grounds - Student Services (9)		
Site Imptovement		\$0
Building & Additions		\$5,192,948
Architect		\$0
Engineering		\$0
Inspection & Testing		\$0
Project Management		\$0
Total		\$5,192,948
Project Budget	\$5,192,948	
Actual Measure S Interest Expenditures	\$5,192,948	
Running Balance	\$0	

SANTA MONICA COMMUNITY COLLEGE DISTRICT

Measure V Project Schedule As of June 30, 2019

	Project Name	Completion		201	8		201	19		202	0		20	21	2	2022	2	023	
101 F	Replacement Math and Science Extension Building	December 2022																	1
102	Student Services	Completed																	
103 N	Malibu Center	December 2021																	
104 E	Early Childhood Development/Childcare	June 2020																	
105 A	Art Building Replacement	September 2022																	
106 E	Business Building Renovation	December 2023																	
107 A	Air Conditioning	December 2019]
108	ADA	On-Going																	
109 N	Master Planning	March 2020																	
110	Drescher Hall Modernization	On-Going																	
111	Outdoor Classroom	On-Going On-Going			·														
112	SMMUSD	August 2021]
113	City of Santa Monica	On-Going]
114	Classrooms Relocation	On-Going																	1
115	TBD	On-Going																	1
120	Other Bond Related Expenses	On-Going																	1
121	Cost of Issuance	On-Going																	1
122 N	Management Reserve	On-Going																	1
123 U	Unissuable Bond	On-Going																	1
										1									1
		On-Going On-Going		In Pl	lann	ing		In	Con	nstru	ctio	n							

Projects	Budget	17/18 Final	18/19	Combined Totals	
_					
V 7100090					
Replacement Math and Science Extension Building (101)					
Legal		\$0	\$0	\$0	
Other Contract Services		\$0	\$0	\$0	
Moving Services		\$0	\$0	\$0	
Building & Additions		\$675	\$11,890	\$12,565	
Architect		\$2,047,911	\$2,486,631	\$4,534,543	
Engineering		\$0	\$0	\$0	
Inspection & Testing		\$30,804	\$37,189	\$67,992	
Project Management		\$130,874	\$417,943	\$548,816	
Cap Equipment		\$0	\$0	\$0	
Non-Cap Equipment		\$0	\$0	\$0	
T-4-1		£0.040.004	*** ***	\$5.400.04T	
Total	¢124.050.22C	\$2,210,264	\$2,953,653	\$5,163,917	
Project Budget	\$124,958,336		* O# F di	0	
Less Other Funding	\$42,640,344		* Other Funding		
Net	\$82,317,992			08,336, Measure AA \$2,244,008 allocated	
Actual Measure V Expenditures	\$5,163,917		State of Califo	rnia \$40,088,000 allocated	
Running Balance	\$77,154,075				
V 7100142					
Student Services Building (102)		40	440 =00	A40 =00	
Supplies		\$0	\$18,593	\$18,593	
Building & Additions		\$0	\$8,962,329	\$8,962,329	
Architect		\$0	\$265,346	\$265,346	
Engineering		\$0	\$83,886	\$83,886	
Inspection & Testing		\$55,202	\$249,195	\$304,397	
Project Management		\$0	\$846,417	\$846,417	
Cap Equipment		\$0	\$3,794,990	\$3,794,990	
Non-Cap Equipment		\$0	\$21,267	\$21,267	
Total		\$55,202		\$14,297,225	
Project Budget	\$130,224,164	* Other Funding Source:			
Less Other Funding	\$96,599,255			rnia \$1,321,000 received	
Net	\$33,624,909	Mease U \$21,131,135, Measure S 45,595,322,			
Actual Measure V Expenditures	\$14,297,225	Measure AA \$6,870,490 allocated			
Running Balance	\$19,327,684	Measure U, S & AA interests \$21,681,308 allocated			
		1			
V 7100240					
Art Complex (105) Legal		\$0	\$0	\$0	
Other Contract Services		\$0 \$0	\$0 \$0	\$0	
		\$0 \$0	\$0 \$0	\$0	
Moving Services		\$0 \$184	\$407.369	\$0 \$407.553	
Building & Additions		\$184 \$0	, , , , , , , , , , , , , , , , , , , ,	,	
Architect Engineering		\$0 \$0	\$0 \$0	\$0 \$0	
Inspection & Testing		\$0 \$0	\$35,495	\$0 \$35,495	
		\$0 \$0	\$35,495	\$35,495	
Project Management				· ·	
Cap Equipment		\$0 \$0	\$0 \$0	\$0 \$0	
Non-Cap Equipment				· ·	
Total	622.014.000	\$184	\$442,864	\$443,048	
Project Budget	\$32,914,000				
Less Other Funding	\$8,914,000	* Other Funding Source: State of California \$8,914,000 pending			
Net	\$24,000,000				
Actual Measure V Expenditures	\$443,048				
Running Balance	\$23,556,952				

Projects	Budget	17/18 Final	18/19	Combined Totals
V 7100188				
Air Conditioning (107)				
Other Contract Services		\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0
Architect		\$0	\$79,000	\$79,000
Engineering		\$417,960	\$168,367	\$586,328
Inspection & Testing		\$0	\$0	\$0
Project Management		\$4,370	\$4,270	\$8,640
Total		\$422,330	\$251,637	\$673,968
Project Budget	\$10,777,654			
Less Other Funding	\$0			
Net	\$10,777,654			
Actual Measure V Expenditures	\$673,968			
Running Balance	\$10,103,686			
V 7100004		1		
Master Plan (109)				
Other Contract Services		\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0
Architect		\$0	\$323	\$323
Engineering		\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0
Project Management		\$0	\$1,000	\$1,000
Total		\$0	\$1,323	\$1,323
Project Budget	\$1,000,000	40	ψ1,323	Ψ1,323
Less Other Funding	\$1,000,000			
Net	\$1,000,000			
Actual Measure V Expenditures	\$1,323			
Running Balance	\$998,677			
running balance	\$550,077			
V 7100237				
Outdoor Classroom (111)				
Other Contract Services		\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0
Architect		\$100,000	\$100,000	\$200,000
Engineering		\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0
Project Management		\$0	\$17,205	\$17,205
Total		\$100,000	\$117,205	\$217,205
Project Budget	\$250,000			
Less Other Funding	\$0			
Net	\$250,000			
Actual Measure V Expenditures	\$217,205			
Running Balance	\$32,795			

Projects	Budget	17/18 Final	18/19	Combined Totals
		·		
V 7100243				
Classrooms Relocation (114)				
Other Contract Services		\$0	\$0	\$0
Building & Additions		\$0	\$3,467	\$3,467
Architect		\$0	\$149,361	\$149,361
Engineering		\$0	\$0	\$0
Inspection & Testing		\$0	\$16,795	\$16,795
Project Management		\$0	\$2,260	\$2,260
Total		\$0	\$171,883	\$171,883
Project Budget	\$4,900,000	-	-	
Less Other Funding	\$0			
Net	\$4,900,000			
Actual Measure V Expenditures	\$171,883			
Running Balance	\$4,728,117			
S7100048				
Other Bond Related Expenses (116)				
Consultants		\$0	\$0	\$0
Lease/Rental		\$0	\$12,076	\$12,076
Supplies		\$0	\$0	\$0
Legal		\$0	\$0	\$0
Software License		\$0	\$0	\$0
Advertising		\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0
Building & Additions		\$184	\$191,065	\$191,249
Inspection & Testing		\$0	\$13,060	\$13,060
Project Management		\$0	\$0	\$0
Cap Equipment		\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0
Total		\$184	\$216,201	\$216,384
Project Budget	\$300,000			
Less Other Funding	\$0			
Net	\$300,000			
Actual Measure V Expenditures	\$216,384			
Running Balance	\$83,616			
Cost of Issuance (117)				
Cost of Issuance		\$291,277	\$0	\$291,277
Total		\$291,277	\$0	\$291,277
Project Budget	\$800,000			
Less Other Funding	\$0			
Net	\$800,000			
Actual Measure V Expenditures	\$291,277			
Running Balance	\$508,723			

\$3,079,439 \$18,396,790

Grand Total

\$21,476,229

SMC Bond Program Contractor List as of 6-30-2019

Student Services (Measure U #0, Measure S #9, Measure AA #120, Measure V #102):

Architect – Steinberg Architects, Morris Architects

Contractor - Minco, Bernards Brothers, Spinitar

Engineering – IVA, Cogent Energy Engineering, XL Fire

Inspection & Testing – Geo Labs, BTC Labs - Vertical V, Peak Survey, LPI Rango Inc., Twining

Project Management - LPI

Replacement Health/PE/Fitness/Dance Building (Measure S #4, Measure AA #104):

Architect - Gensler Architects

Contractor – Bernards Brothers

Engineering – IVA, Glumac

Inspection & Testing – Geo Labs, Ellis Environmental, Twining, Rango Inc.

Project Management - LPI

Early Childhood Development (Measure S #5, Measure V #104):

Architect - Carde Ten Architects

Consultant - Child Educational Center

Contractor - The Nazerian Group

Engineering – Jacobs

Inspection & Testing – Geo Labs, Rango Inc., Twining

Project Management - LPI, Vanir

Malibu Site (Measure S #6, Measure AA #110, Measure V #103):

Architect - Quatro Design Group

Contractor – Master Contracting, Icon West

Consultant – m2 Strategic, Parker Environmental

Engineering – Ensitu Services, Jacobs

Inspection & Testing – Peak Surveys, Ellis Environmental, JL Inspection, Ninyo

& Moore

Project Management – LPI, m6 Strategic, Vanir

Energy Efficiency Projects (Measure S #7, Measure AA #113):

Architect - N/A

Contractor – Compass Energy Solutions, Johnson Controls

Engineering – Compass Energy Solutions, Johnson Controls

Inspection & Testing – Ellis Environmental

Environmental Performance (Measure AA #101):

Architect - Kishimoto Architects

Contractor – SJ Amoroso Construction

Engineering – P2S Engineering

Inspection & Testing - Cannon, Peak Surveys

Project Management - LPI

Information Technology Relocation (Measure AA #102):

Architect - Morris Architects

Contractor - Minco, Bernards Brothers, Eidim AV Technology

Engineering – IVA, P2S Engineering

Inspection & Testing – Cannon, Peak Surveys, Geo Labs, Ellis Environmental, Twining, JL Inspection, Rango Inc.

Project Management – LPI, CCS Presentation

Media and Technology Complex (Measure AA #103):

Architect - Clive Wilkinson Architects, Morris Architects

Contractor – H.B. Parkco Construction, Fast Track Construction, CW Driver, Dimension Data, Key Code Media, Omega Construction

Consultant - EEG Services

Engineering – IVA, P2S Engineering

Inspection & Testing - Twining, Geo Labs, BTC Labs - Vertical V,

JL Inspection, EEG Services, Ellis Environmental, Rango Inc., Cannon

inc., can

Project Management - LPI

Madison East Wing Seismic Upgrade (Measure AA #107):

Architect - DLR Group - WWCOT, LPI

Contractor - Trimax, Bernards Brothers, Dimension Data

Engineering – IVA, Glumac

Inspection & Testing – Twining, Peak Surveys, LPI, All Group Engineering, EEG Services, Ellis Environmental

Project Management - LPI

Business & Facilities Infrastructure (Measure AA #111):

Architect - LPI, Gwynne Pugh Urban Studio

Contractor – REC+S, Inc., Omega Construction,

Concept Consultant, Inc.

Engineering – N/A

Inspection & Testing - Ellis Environmental, JL Inspection

Project Management - LPI

Community Classroom & Facility Project (Measure AA #114)

Architect – Morris Architects

Contractor – Waisman Construction, Spinitar, Trimax

Engineering – IVA

Inspection & Testing – LPI, Twining

Project Management - LPI

Satellite Campus Parking Facilities and Roadway Improvements (Measure S #8)

Architect - N/A

Contractor - N/A

Engineering – MK Engineering Group

Inspection & Testing – N/A

Project Management – LPI

Roadways, walkways, Grounds, Parking Lots, and Garages (Measure AA #116)

Architect - LPI, DLR Group - WWCOT

Contractor - Trimax, Pub Construction

Consultant – Walker Parking

Engineering – MK Engineering

Inspection & Testing – Ellis Environmental, Peak Surveys, LPI

Project Management – LPI

Emergency Lighting, Fire Alarm, and Security System (Measure AA #119)

Architect - N/A

Contractor - Red Hawk Fire and Security, Nexus

Consultant – IVA

Engineering – MDC Engineers

Inspection & Testing - Rango Inc.

Project Management - LPI

Signage Safety/Information (Measure S #15)

Architect - N/A

Contractor - Sign Excellence

Consultant – APCO

Engineering – N/A

Inspection & Testing – N/A

Project Management – LPI

Math and Science Addition (Measure AA #106)

Architect - Cannon Design

Contractor - N/A

Consultant - N/A

Engineering – Arup

Inspection & Testing – N/A

Project Management – Vanir
