

## Citizens' Bond Oversight Committee (CBOC)

Meeting on July 17<sup>th</sup>, 2024

June 30<sup>th</sup>, 2024 Report

12 Months - FY 2023-24 (Preliminary)

### **BOND CAPITAL CONSTRUCTION REPORTS**

District Management is responsible for the preparation and fair presentation of the statement of expenditures and bond proceeds in accordance with U.S. generally accepted accounting principles; this includes the design, implementation, and maintenance of internal control relevant to the preparation and fair presentation of the statement of expenditures of bond proceeds that is free from material misstatement, whether due to fraud or error.

This report is prepared in accordance with these requirements and all bond expenditures were made in compliance with all applicable laws.

	Project Nilmbor I Project Nilmbor I I Statile I														
Project Number	Project Name	Measure U Budget	Measure S Budget	Measure AA Budget	Measure V Budget	Interest	_	Other Funding Pending **	Total Budget	Estimate at Completion	Status	Bond Funds Remaining			
U-A	Purchase of BAE Airport Site	\$30,280,878							\$30,280,878	\$30,280,878	Completed				
U-B	Emeritus College Facility	\$8,909,940					\$693,842		\$9,603,782	\$9,603,782	Completed				
U-C	Purchase of 1738 Pearl Street	\$749,208							\$749,208	\$749,208	Completed				
U-D	PE Temp. Bldg. Replacement	\$2,797,033							\$2,797,033	\$2,797,033	Completed				
U-E	Remodel Library Village for Math	\$1,458,690							\$1,458,690	\$1,458,690	Completed				
U-F	SM Airport Campus Site Improvements	\$4,170,264							\$4,170,264	\$4,170,264	· · · · · · · · · · · · · · · · · · ·				
U-G	SM Airport Campus West Building	\$19,709,741							\$19,709,741	\$19,709,741	Completed				
U-H	Theater Arts Renovation	\$19,544,314							\$19,544,314	\$19,544,314	Completed				
U-I	Earthquake Rpl. Liberal Arts North	\$6,011,584					\$6,496,141		\$12,507,725	\$12,507,725					
U-K	Earthquake Rpl. Liberal Arts South	\$6,108,150					\$10,625,070		\$16,733,220	\$16,733,220	Completed				
U-L	Shuttle Replacement Parking	\$18,969,509							\$18,969,509	\$18,969,509	Completed				
U-M	North Quad Plaza	\$11,388,463							\$11,388,463	\$11,388,463	<del>                                     </del>				
U-Q	Infrastructure & Safety	\$4,003,084							\$4,003,084	\$4,003,084	Completed				
U-R	Restroom Improvements	\$17,501					1		\$17,501	\$17,501	<del></del>				
S-1	Athletic Fields Phase I, Corsair Field		\$4,372,535				\$67,530		\$4,440,065	\$4,440,065	Completed				
S-1A	Athletic Fields Phase I, John Adams		\$2,969,807						\$2,969,807	\$2,969,807	Completed				
S-10	Pico Promenade Improvements, Phase I		\$1,018,009						\$1,018,009	\$1,018,009	Completed				
S-13	Adv. Architecture Related Exp for AA		\$0						\$0	\$0	Completed				
AA-114	Community Classroom & Facility Projects	6340.010		\$3,162,183					\$3,162,183	\$3,162,183	<del> </del>				
U-T	14th and Pico Project	\$319,242							\$319,242	\$319,242	-				
U-N	Letters & Sci Demo/Restore	\$0		¢4 025 200					\$0	\$0	Completed	Ć026.4			
AA-108	Renovation of Corsair Stadium		627 607 625	\$1,035,299			62.002.570		\$1,035,299	\$1,035,299		\$936,1			
S-2	Performing Arts Complex	62.011.271	\$37,697,625				\$2,992,576		\$40,690,201	\$40,690,201	Completed				
U-J	Music Complex	\$2,011,371		\$0			\$2,618,113		\$4,629,484	\$4,629,484					
S-3, AA-109	Career Opportunity Center			ΨŪ					70	\$0 \$27,753					
AA-118	Infrastructure & Technology - Utility Business & Facilities Infrastructure			\$27,753					\$27,753		•				
AA-111 AA-117	Infrastructure & Technology - Technology			\$1,968,124 \$2,434,417					\$1,968,124	\$1,968,124 \$2,434,417	•				
			\$293,361	. , ,			\$708,637		\$2,434,417 \$4,018,771		Completed				
S-7, AA-113 S-15	Energy Efficiency Projects Signage Safety/Information		\$706,713	\$3,016,773			\$708,637		\$4,018,771	\$4,018,771 \$706,713	Completed				
AA-102	Signage Safety/Information Infrastructure & Technology - Information Technology Relocation		\$700,713	\$23,140,771			\$19,798		\$23,160,569	\$23,160,569	Completed				
S-8, AA-116	Satellite Campus Parking Facilities and Roadway		\$3,891,747	\$2,130,670			\$19,790		\$6,022,417	\$6,022,417	Completed				
AA-107	Madison East Wing Seismic Upgrade		J3,631,747	\$30,161,852					\$30,161,852	\$30,161,852	Completed				
S-4, AA-104	Replacement Health/PE/Fitness Central Plant Building		\$11,603,383	\$44,428,222			\$208,847		\$56,240,452	\$56,240,452	Completed				
AA-101	Environmental Performance - Central Plant Connections		711,003,383	\$10,767,251			7200,847		\$10,767,251	\$10,767,251	Completed				
S-14, AA-115	Real Property Acquisition		\$45,597	\$24,638,386					\$24,683,983	\$24,683,983	· · · · · ·				
AA-103	Media and Technology Complex - Academy Site		<del>7-3,337</del>	\$124,669,502			\$6,835,391		\$131,504,893	\$131,504,893	<del>-</del>	\$1,160,3			
AA-119	Emergency Lighting, Fire Alarm, and Security System			\$11,515,614			70,033,331		\$11,515,614	\$11,515,614	Completed	71,100,5			
15004829	Student Services Building	\$21,131,135	\$45,595,322	\$6,870,490	\$33,624,909	\$21,681,308	\$1,321,000		\$130,224,164	\$130,224,164		\$8,351,7			
S-5, V-104	Early Childhood Development/Childcare	721,131,133	\$8,858,656	70,070,430	\$15,405,517	721,001,300	\$6,661,598		\$30,925,771	\$30,925,771	Completed	\$2,240,9			
S-6, AA-110, V-103	Malibu Center and Site Acquisition		\$25,132,568		\$34,558,420	\$2,294,791			\$61,985,779	\$61,985,779	Completed	\$5,551,3			
· · · · · · · · · · · · · · · · · · ·	Master Planning	\$2,110,430	\$716,428			<i>\$2,23 1,731</i>			\$4,661,555	\$4,661,555	•	\$88,9			
U-P, AA-106, V-101	Replacement Math and Science Extension Building	\$308,336	ψ, 10, 120	\$2,244,008	\$82,317,992		\$31,713,876	\$8,374,124	\$124,958,336		In Construction	\$23,340,4			
AA-105, V-110	Drescher - Academic Modernization, Bookstore, Pico Promenade II	4000,000		\$5,082	\$13,000,000		<del>+</del>	<del>+ 5,5 : :,== :</del>	\$13,005,082	\$13,005,082		\$13,000,0			
V-105	Art Building Replacement			+3,302	\$52,532,040		\$4,626,297	\$6,274,703	\$63,433,040		In Construction	\$43,712,5			
V-106	Business Building Renovation				\$12,547,000			\$12,470,000	\$25,017,000	\$25,017,000	In Planning	\$12,543,6			
V-107	Air Conditioning				\$10,777,654			, _, 5,555	\$10,777,654	\$10,777,654	J	\$646,9			
V-108	ADA				\$4,000,000				\$4,000,000	\$4,000,000	In Planning	\$4,000,0			
V-111	Outdoor Classroom				\$321,723				\$321,723	\$321,723		F : 7000)			
V-112	John Adams MS Auditorium (SMMUSD)				\$20,000,000				\$20,000,000	\$20,000,000	Completed				
V-113	Memorial Park Project				\$20,000,000				\$20,000,000	\$20,000,000	In Planning	\$19,996,5			
V-114	Classrooms Relocation				\$7,400,000				\$7,400,000	\$7,400,000	Completed	\$113,2			
V-124	Parking Structure 3 Improvement Project				\$1,500,000				\$1,500,000	\$1,500,000	In Design	\$1,385,3			
V-125	Gender Neutral Bathrooms				\$3,500,000				\$3,500,000	\$3,500,000		\$3,295,			
V-126	Athletic Facilities				\$20,325,749				\$20,325,749	\$20,325,749	<del>                                     </del>	\$17,566,			
S-12, V-120	Other Bond Related Expenses		\$476,636		\$300,000				\$776,636	\$776,636		\$55,			
V-115	TBD		• -		\$0				\$0	\$0	Completed				
-16, AA-121, V-121	Cost of Issuance		\$119,470	\$498,026	· · · · · · · · · · · · · · · · · · ·				\$1,417,496	\$1,417,496	In Planning	\$55,			
AA-122, V-122	Management Reserve		. , -	\$1,446,709		\$16,654,988			\$29,190,693	\$29,190,693		\$12,535,			
, , , , , , , , , , , , , , , , , , ,	Unissuable	\$1,127	\$2,143						\$7,441	\$7,441					
•	Project Totals	\$160,000,000	-		\$345,000,000	\$40,631,087	\$75,588,716	\$27.118.827	\$1,086,838,630		<del>-</del>	\$170,577,			
				7-55,555							-				


### **Bond Sales / Expenses Report**

As of June 30, 2024 - Preliminary

Total Bond Program (AA and V)	\$640,000,000
Total Bonds Issued	\$639,995,829
Total Expenses as of 6-30-2024	\$469,418,437
Total Available Remaining	\$170,577,392
Total Unsold Bond	\$4,171

Measure AA Bond \$295,000,000	
Bond Issue Date	Amount
2010	\$100,000,000
2014	\$144,995,829
2017	\$50,000,000
Total Available	\$294,995,829
Total Expenses as of 6-30-2024	\$291,212,769
Total Available Remaining	\$3,783,060
Unsold Bond Amount	\$4,171
Total Available as of 7-1-2024	\$3,787,231

Amount
\$180,000,000
\$165,000,000
\$345,000,000
\$178,205,668
\$166,794,332
\$0
\$166,794,332

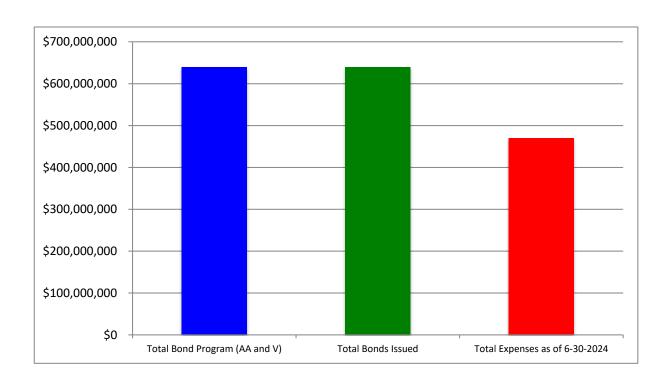


Interest	Measure U	Measure S	Measure AA	Measure V
As of 6-30-23	\$7,034,168	\$12,148,354	\$7,098,976	\$14,349,589
Expenditure / Arbitrage as of 6-30-23	\$7,034,168	\$12,148,354	\$5,192,948	\$0
Available Interest as of 7-1-23	\$0	\$0	\$1,906,028	\$14,349,589

INTEREST TOTALS
\$40,631,087
\$24,375,470
\$16,255,617

# SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure AA Bond Budget

As of June 30, 2024

	Project Name	Completion	Project Budget	Measure AA Allocation	Other Funding	Measure AA Expenditures as of 6/30/24	Measure AA Expenditures as of 3/31/24	Measure AA Expenditures Last Period	Total Measure AA Remaining
101	Environmental Performance - Central Plant Connections	Completed	\$10,767,251	\$10,767,251	\$0	\$10,767,251	\$10,767,251	\$0	\$0
102	Infrastructure & Technology - Information Technology Relocation	Completed	\$23,160,569	\$23,140,771	\$19,798	\$23,140,771	\$23,140,771	\$0	\$0
103	Media and Technology Complex - Academy Site	Completed	\$131,504,893	\$124,669,502	\$6,835,391	\$123,509,130	\$123,509,130	\$0	\$1,160,372
104	Replacement Health/PE/Fitness/ Dance Building with Central Plant	Completed	\$56,240,452	\$44,428,222	\$11,812,230	\$44,428,222	\$44,428,222	\$0	\$0
105	Drescher - Academic Modernization, Bookstore, Pico Promenade	Completed	\$13,005,082	\$5,082	\$13,000,000	\$5,082	\$5,082	\$0	\$0
106	Replacement Math and Science Extension Building	November 2024	\$124,958,336	\$2,244,008	\$122,714,328	\$2,004,184	\$2,004,184	\$0	\$239,824
107	Madison East Wing Seismic Upgrade	Completed	\$30,161,852	\$30,161,852	\$0	\$30,161,852	\$30,161,852	\$0	\$0
108	Renovation of Corsair Stadium	December 2024	\$1,035,299	\$1,035,299	\$0	\$99,144	\$85,899	\$13,245	\$936,155
109	Career Opportunity and Advancement Center (Bundy)	Completed	\$0	\$0	\$0	\$0	\$0	\$0	\$0
110	Malibu Center	Completed	\$61,985,779	\$0	\$61,985,779	\$0	\$0	\$0	\$0
111	Business & Facilities Infrastructure	Completed	\$1,968,124	\$1,968,124	\$0	\$1,968,124	\$1,968,124	\$0	\$0
112	Master Planning, Program Management, Overhead	Completed	\$834,697	\$834,697	\$0	\$834,697	\$834,697	\$0	\$0
113	Energy Efficiency Projects	Completed	\$3,508,088	\$3,016,773	\$491,315	\$3,016,773	\$3,016,773	\$0	\$0
114	Community Classroom & Facility Projects	Completed	\$3,162,183	\$3,162,183	\$0	\$3,162,183	\$3,162,183	\$0	\$0
115	Real Property Acquisition	Completed	\$24,638,386	\$24,638,386	\$0	\$24,638,386	\$24,638,386	\$0	\$0
116	Roadways, Walkways, Grounds, Parking Lots, and Garages	Completed	\$7,022,417	\$2,130,670	\$4,891,747	\$2,130,670	\$2,130,670	\$0	\$0
117	Infrastructure & Technology - Technology	Completed	\$2,434,417	\$2,434,417	\$0	\$2,434,417	\$2,434,417	\$0	\$0
118	Infrastructure & Technology - Utility	Completed	\$27,753	\$27,753	\$0	\$27,753	\$27,753	\$0	\$0
119	Emergency Lighting, Fire Alarm, and Security System	Completed	\$11,515,614	\$11,515,614	\$0	\$11,515,614	\$11,515,614	\$0	\$0
120	Student Services	Completed	\$130,224,164	\$6,870,490	\$123,353,674	\$6,870,490	\$6,870,490	\$0	\$0
121	Cost of Issuance	Completed	\$498,026	\$498,026	\$0	\$498,026	\$498,026	\$0	\$0
122	Management Reserve	On-Going	\$1,446,709	\$1,446,709	\$0	\$0	\$0	\$0	\$1,446,709
123	Unissuable Bond	Completed	\$4,171	\$4,171	\$0	\$0	\$0	\$0	\$4,171
	Project Totals		\$638,653,382	\$295,000,000	\$345,104,262	\$291,212,769	\$291,199,524	\$13,245	\$3,787,231

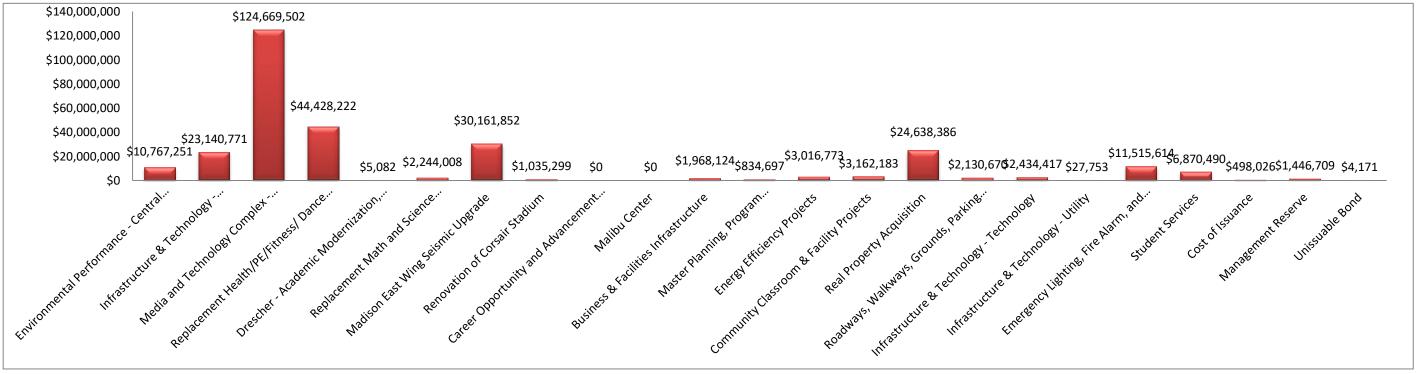

## SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure AA Bond Budget History as of June 30, 2024


	Project Name	Completion	Preliminary Measure AA	Measure AA Budget as of	Measure AA Budget as of	Variance	Measure AA Remaining as
		Compression	Budget	3/31/24	6/30/24		of 6/30/2024
101	Environmental Performance - Central Plant Connections	Completed	\$12,034,042	\$10,767,251	\$10,767,251	\$0	\$0
102	Infrastructure & Technology - Information Technology Relocation	Completed	\$13,287,218	\$23,140,771	\$23,140,771	\$0	\$0
103	Media and Technology Complex - Academy Site	Completed	\$57,480,824	\$124,669,502	\$124,669,502	\$0	\$1,160,372
104	Replacement Health/PE/Fitness/ Dance Building with Central Plant	Completed	\$29,232,317	\$44,428,222	\$44,428,222	\$0	\$0
105	Drescher - Academic Modernization, Bookstore, Pico Promenade II	Completed	\$34,026,480	\$5,082	\$5,082	\$0	\$0
106	Replacement Math and Science Extension Building	November 2024	\$68,259,000	\$2,244,008	\$2,244,008	\$0	\$239,824
107	Madison East Wing Seismic Upgrade	Completed	\$6,146,000	\$30,161,852	\$30,161,852	\$0	\$0
108	Renovation of Corsair Stadium	December 2024	\$11,203,000	\$1,035,299	\$1,035,299	\$0	\$936,155
109	Career Opportunity and Advancement Center (Bundy)	Completed	\$32,384,000	\$0	\$0	\$0	\$0
110	Malibu Center	Completed	\$6,069,031	\$0	\$0	\$0	\$0
111	Business & Facilities Infrastructure	Completed	\$17,506,952	\$1,968,124	\$1,968,124	\$0	\$0
112	Master Planning, Program Management, Overhead	Completed	\$2,000,000	\$834,697	\$834,697	\$0	\$0
113	Energy Efficiency Projects	Completed	\$5,371,136	\$3,016,773	\$3,016,773	\$0	\$0
114	Community Classroom & Facility Projects	Completed	\$0	\$3,162,183	\$3,162,183	\$0	\$0
115	Real Property Acquisition	Completed	\$0	\$24,638,386	\$24,638,386	\$0	\$0
116	Roadways, Walkways, Grounds, Parking Lots, and Garages	Completed	\$0	\$2,130,670	\$2,130,670	\$0	\$0
117	Infrastructure & Technology - Technology	Completed	\$0	\$2,434,417	\$2,434,417	\$0	\$0
118	Infrastructure & Technology - Utility	Completed	\$0	\$27,753	\$27,753	\$0	\$0
119	Emergency Lighting, Fire Alarm, and Security System	Completed	\$0	\$11,515,614	\$11,515,614	\$0	\$0
120	Student Services	Completed	\$0	\$6,870,490	\$6,870,490	\$0	\$0
121	Cost of Issuance	Completed	\$0	\$498,026	\$498,026	\$0	\$0
122	Management Reserve	On-Going	\$0	\$1,446,709	\$1,446,709	\$0	\$1,446,709
123	Unissuable Bond	Completed	\$0	\$4,171	\$4,171	\$0	\$4,171
	Project Totals		\$295,000,000	\$295,000,000	\$295,000,000	\$0	\$3,787,231

### SANTA MONICA COMMUNITY COLLEGE DISTRICT

# Measure AA Project Schedule As of June 30, 2024

	Project Name	Completion	202	0		20	21		2	022	2		202	3	202	14
101	Environmental Performance - Central Plant Connections	Completed														
102	Infrastructure & Technology - Information Technology Relocati	Completed														
103	Media and Technology Complex - Academy Site	Completed														
104	Replacement Health/PE/Fitness/Dance Building with Central Pla	Completed														
105	Drescher - Academic Modernization, Bookstore, Pico Promenad	Completed														
106	Replacement Math and Science Extension Building	November 2024														
107	Madison East Wing Seismic Upgrade	Completed														
108	Restoration of Corsair Stadium	December 2024														
109	Career Opportunity and Advancement Center (Bundy)	Completed														
110	Malibu Center	Completed														
111	Business & Facilities Infrastructure	Completed														
112	Master Planning, Program Management, Overhead	Completed														
113	Energy Efficiency Projects	Completed														
114	Community Classroom & Facility Projects	Completed														
115	Real Property Acquisition	Completed														
116	Roadways, Walkways, Grounds, Parking Lots, and Garages	Completed														
117	Infrastructure & Technology - Technology	Completed														
118	Infrastructure & Technology - Utility	Completed														
119	Emergency Lighting, Fire Alarm, and Security System	Completed														
120	Student Services	Completed														
121	Cost of Issuance	Completed														
122	Management Reserve	On-Going														
123	Unissuable Bond	Completed						1								
			In P	lanr	ning	J		n C	Cons	stru	ctio	n				$\perp$

	1	<del> </del>											-				
Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final 20	/21 Final 21/22	Final	22/23 Final	23/24 (Prelim)	Combined Totals
A.1. = 100000							•						•				
AA 7100062	<u> </u>	(104)															
Environmental Performance - Centra	I Plant Connec	, ,		Φ0	<b>0405</b>	00	Φ0	Φ0	Φ0	Φ0	•	40	Φ0	Φ0	Φ0	Φ0	<b>A</b> 405
Legal		\$0	\$0	\$0	\$125	\$0	\$0	\$0	\$0	\$0	¥ *	\$0	\$0	\$0	\$0		\$125
Other Contract Services		\$0	\$0	\$49,837	\$16,239	\$0	\$0	\$0	\$0	\$9,920	\$0	\$0	\$0	\$0	\$0		\$75,996
Consultants		\$0	\$0	\$0	\$0	\$28	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$28
Building & Additions		\$0	\$0	\$0	\$361	\$729	\$640	\$1,328,592	\$6,934,044	\$446,861	\$0	\$0	\$0	\$0	\$0	\$0	\$8,711,229
Architect		\$0	\$385	\$148,311	\$176,897	\$36,256	\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$0		\$377,547
Engineering		\$48,500	\$0	\$4,000	\$0	\$152,010	\$39,638	\$66,918	\$138,887	\$62,883	\$0	\$0	\$0	\$0	\$0		\$512,836
Inspection & Testing		\$0	\$0	\$7,688	\$0	\$0	\$0	\$7,310	\$137,150	\$4,382	\$0	\$0	\$0	\$0	\$0	\$0	\$156,529
Project Management		\$0	\$17,263	\$55,116	\$48,685	\$61,908	\$19,313	\$104,575	\$526,072	\$99,840	\$190	\$0	\$0	\$0	\$0		\$932,961
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$0		\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$48,500	\$17,648	\$264,951	\$242,307	\$250,931	\$59,591	\$1,507,396	\$7,736,152	\$623,886	\$15,889	\$0	\$0	\$0	\$0	\$0	\$10,767,251
Project Budget																	
Less Other Funding		1															
Net	+ -, - , -	]															
Actual Measure AA Expenditures																	
Running Balance	\$0																
AA 7100063																	
Infrastructure & Technology - IT Relo	ocation (102)																
Supplies		\$0	\$0	\$965	\$8,442	\$3,137	\$2,600	\$0	\$0			\$0	\$0	\$0	\$0	\$0	\$15,144
Consultants		\$0	\$0	\$0	\$0	\$408	\$0	\$7,800	\$0	\$0		\$0	\$0	\$0	\$0	\$0	\$8,208
Maintenance Contract		\$0	\$0	\$0	\$0	\$107,390	\$0	\$77,074	\$79	\$0		\$0	\$0	\$0	\$0		\$184,543
Legal		\$0	\$0	\$0	\$1,363	\$50	\$0	\$0	\$0			\$0	\$0	\$0	\$0		\$1,413
Printing		\$0	\$0	\$0	\$0	\$1,624	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,624
Postage		\$0	\$0	\$0	\$0	\$1,567	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,567
Other Contract Services		\$0	\$0	\$2,163	\$15,259	\$23,356	\$0	\$19,050	\$4,500	\$0	7 -	\$0	\$0	\$0	\$0		\$64,328
Moving		\$0	\$0	\$0	\$577	\$266	\$27,655	\$22,618	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$51,116
Site Improvement		\$0	\$0	\$0	\$24	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$24
Building & Additions		\$0	\$0	\$0	\$1,767,083	\$9,667,362	\$4,288,987	\$1,203,916	\$165,229	-\$19,798	\$0	\$0	\$0	\$0	\$0	\$0	\$17,072,780
Architect		\$105,049	\$482,261	\$505,580	\$183,181	\$287,201	\$236,860	\$120,091	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,920,223
Engineering		\$0	\$0	\$10,037	\$11,065	\$17,147	\$19,512	\$25,994	\$1,956	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$85,712
Inspection & Testing		\$10,291	\$8,793	\$21,449	\$137,523	\$499,982	\$200,262	\$568	\$0	\$0		\$0	\$0	\$0	\$0	\$0	\$878,868
Project Management		\$33,460	\$76,290	\$84,991	\$331,754	\$431,730	\$297,951	\$22,978	\$1,500	\$0		\$0	\$0	\$0	\$0	\$0	\$1,280,653
Cap Equipment	İ	\$0	\$0	\$0		\$645,830	-\$29,090	\$589,604	\$9,811	\$0		\$0	\$0	\$0	\$0	\$0	\$1,245,576
Non-Cap Equipment		\$0	\$0	\$0		\$10,852	\$277,219	\$1,891	\$20,689	\$0		\$0	\$0	\$0	\$0		\$328,994
Total		\$148,800	\$567,344			\$11,697,901			\$203,764				\$0	\$0	\$0		\$23,140,771
Project Budget	\$23,160,569		+,	ţ : <b></b> ; : <b>50</b>	+-,,	· · · · · · · · · · · · · · · · · · ·	+-,,	+-,,	+,-	÷,.	, ,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,	7-1	+-I	7-	40	+•	Ψ= <b>U</b> ,1.T <b>U</b> ,1.1.1
Less Other Funding		\$19,798	Other Fundi	ing Source:													
•	\$23,140,771		1) Edison \$19		1												
Actual Measure AA Expenditures	\$23,140,771	†	., =5.55 φ10	.,	<u>-</u>												
:	<i></i> , · · -, · · ·	4															,

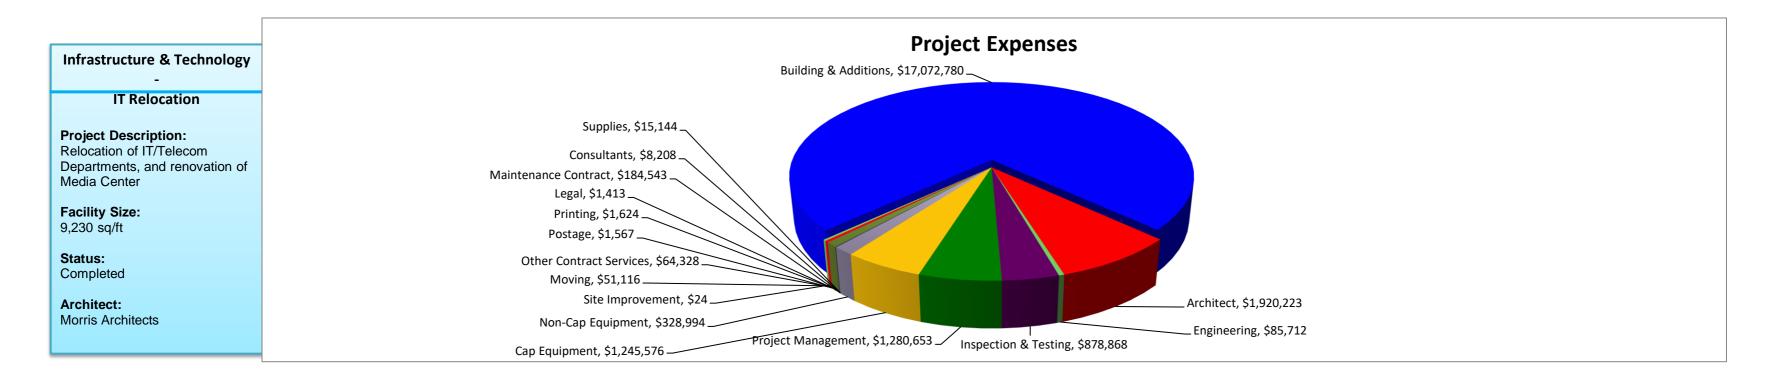

Running Balance

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Final	23/24 (Prelim)	<b>Combined Totals</b>
.,	3															( - ,	
AA 7100061																	
Media and Technology Complex - Ac	ademy Site (10	3)															
Consultants		\$0	\$0	\$20,675	\$12,576	\$9,488	\$7,789	\$2,102	\$0	\$12,922		\$0		\$0	\$0	\$0	\$65,551
Supplies		\$0	\$0	\$0	\$19,481	\$1,048	\$289	\$0	\$9,251	\$40,519		\$0	\$0	\$0	\$0	\$0	\$71,525
Maintenance Contract		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$15,922	\$23,561	\$0	\$0	\$0	\$0	\$0	\$0	\$39,483
Legal		\$16,903	\$0	\$7,958	\$43,363	\$5,066	\$26,186	\$49,155	\$15,435	\$36,221	\$26,991	\$121,256	\$100,053	\$200,783	\$169,704	\$1,500	\$820,572
Software Support		\$0	\$0		\$1,982	\$0	\$0	\$0	\$6,548	\$6,975		\$0	\$0	\$0	\$0	\$0	\$15,505
Service Fee		\$0	\$0	T -	\$0	\$0	\$0	\$0	\$17,000	\$0	Ţ.	\$0	Ψ°	\$0	\$0		\$17,000
Other Contract Services		\$3,993	\$5,763	\$13,456	\$39,188	\$0	\$0	\$5,853	\$22,622	\$18,628		\$7,550		\$0			\$124,743
Moving Expenses		\$0	\$0	\$0	\$38,756	\$0	\$0	\$0	\$0	\$97,543		\$0	\$0	\$0			\$153,855
Site Improvement		\$0	\$0	T -	\$100,505	\$664	\$606	\$476	\$622	\$526		\$526		\$0			\$103,925
Building & Additions		\$0	\$538	. , ,	\$3,543,657		\$17,734,534	\$23,465,347	\$16,267,550	\$25,548,089		\$626,512	-\$67,164	\$0	Ψ°	\$0	\$100,657,570
Architect		\$2,097,553	\$2,508,588	\$295,753	\$265,481	\$778,015	\$517,794	\$1,048,935	\$991,386	\$869,801	\$151,886	\$43,416	\$90,690	\$240,094	-\$1,327,000		\$8,572,392
Engineering		\$16,459	\$29,293	\$9,102	\$29,223	\$8,203	\$72,993	\$118,368	\$72,786	\$51,971	\$37,259	\$0	\$0	\$0	\$0	\$0	\$445,657
Inspection & Testing		\$64,905	\$27,527	\$123,842	\$235,287	\$563,746	\$1,381,801	\$641,972	\$525,264	\$207,240	. ,	\$1,212	\$0	\$0			\$3,800,005
Project Management		\$121,786	\$233,826	\$269,249	\$506,917	\$800,315	\$930,115	\$1,207,850	\$1,121,670	\$859,779		\$27,825	\$2,450	\$0	. ,		\$6,134,649
Cap Equipment		\$0	\$0	\$0	\$186,301	\$0	\$0	\$0	\$0	\$1,458,273		\$0	\$0	\$0		\$0	\$1,651,178
Non-Cap Equipment		\$0	\$0	\$0	\$10,782	\$0	\$0	\$0	\$326,845	\$490,727	\$7,167	\$0	ΨΨ	\$0	\$0	т -	\$835,520
Total		\$2,321,599	\$2,805,534	\$2,238,694	\$5,033,499	\$13,987,159	\$20,672,105	\$26,540,059	\$19,392,902	\$29,722,772	\$553,215	\$828,296	\$126,029	\$440,877	-\$1,155,109	\$1,500	\$123,509,130
	\$131,504,893	Received															
Less Other Funding*	\$6,835,391			ing Source:													
	\$124,669,502		1) KCRW Fo	undation \$6,80	3,412 received	l											
Actual Measure AA Expenditures	. , ,	:	2) Edison \$3	1,979.48 recei	ved												
Running Balance	\$1,160,372																



### **Project Description:**

Renovation and new extension to the existing building, new building for KCRW, and a new parking structure

### Facility Size:

Building - 116,000 sq/ft Parking Structure - 450 spaces


### Status: Completed

•


**Architect:** Clive Wilkinson Architects

### Contractor:

H.B. Parkco Construction Fast Track Construction

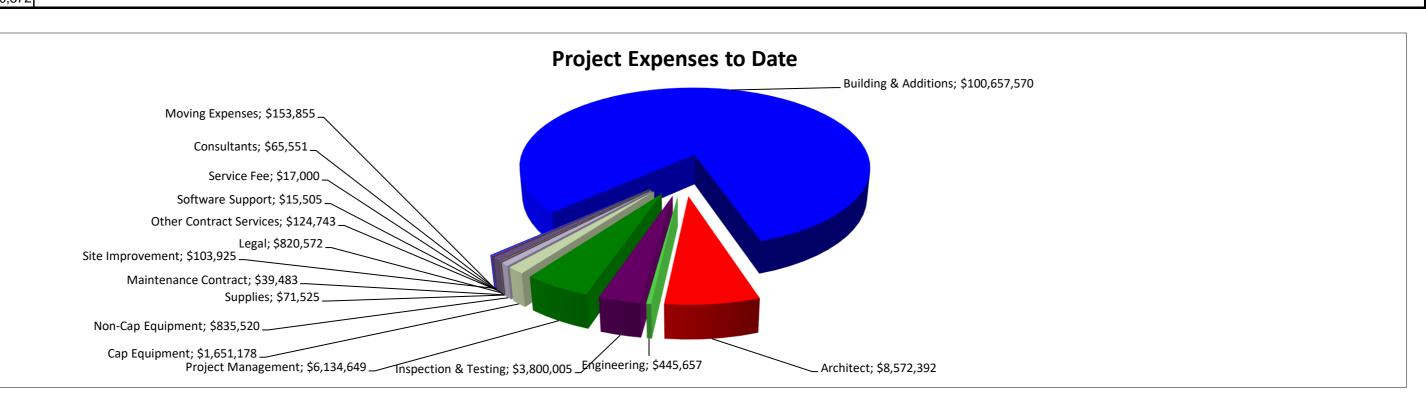


Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Final	23/24 (Prelim)	Combined Totals
		· · ·										•	•		•	· · · ·	
AA 7100060																	
Repl. Health/PE/Fitness/Dance Build	ing with Centra	al Plant (104)															
Consultants		\$0	\$0	\$0	\$14	\$62	\$2,304	\$184	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,564
Supplies		\$0	\$0	\$0	\$0	\$7,089	\$195	\$484	\$20,947	\$0	\$0	\$0	\$0	\$0		\$0	\$28,715
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$663	\$80	\$0		\$0	\$0	\$0		\$0	Ψ· ·=
Software Support		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,209	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,209
Site Improvement		\$0	\$0	\$0	\$0	\$0	\$559	\$440	\$575	\$0	\$0	\$0	\$0	\$0		\$0	\$1,574
Off Campus Printing		\$0	\$0	\$0	\$0	\$0	\$2,165	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,165
Postage		\$0	\$0	\$0	\$0	\$0	\$1,505	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$1,505
Other Contract Services		\$120	\$38	\$112	\$32,634	\$0	\$1,019	\$581	\$0	\$2,644	\$0	\$0	\$0	\$0		\$0	
Building & Additions		\$0	\$0	\$0	\$817	\$4,188	\$1,623	\$13,783,023	\$14,880,829	\$5,315,393	-\$148,184	\$0	\$0	\$0	\$0	\$0	\$33,837,688
Architect		\$256,076	\$1,568,564	\$1,790,207	\$518,973	\$177,583	\$364,853	\$585,900	\$373,345	\$210,312	\$108,264	\$0	\$0	\$0	\$0	\$0	\$5,954,078
Engineering		\$0	\$8,507	\$31,650	\$7,871	\$6,529	\$9,276	\$76,712	\$51,025		\$2,900	\$0	\$0	\$0		\$0	\$205,788
Inspection & Testing		\$36,892	\$490	\$21,150	\$1,285	\$360	\$133,756	\$846,765	\$358,724	\$60,826	\$1,330	\$0	\$0	\$0		\$0	\$1,461,579
Project Management		\$34,968	\$113,379	\$118,783	\$94,768	\$108,528	\$463,418	\$564,240	\$487,065	\$312,539	\$20,242	\$0	\$0	\$0		\$0	\$2,317,928
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$164,793	\$68,425	\$0	\$0	\$0	\$0	\$0	\$0	\$233,218
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$9,015	\$0	\$206,229	\$127,078	\$0	\$0	\$0	\$0		\$0	\$342,322
Total		\$328,056	\$1,690,978	\$1,961,901	\$656,362	\$304,338	\$989,689	\$15,858,991	\$16,544,820	\$6,108,535	-\$15,448	\$0	\$0	\$0	\$0	\$0	\$44,428,222
Project Budge																	
Less Other Funding <sup>3</sup>	\$11,812,230		* Other Fund														
Ne	· · · · · · · · · · · · · · · · · · ·			5 - \$11,603,38													
Actual Measure AA Expenditures		] :	<ol><li>SCE \$190</li></ol>	,847.28, Gas (	Co. \$18,000 red	ceived											
Running Balance	\$0	1															

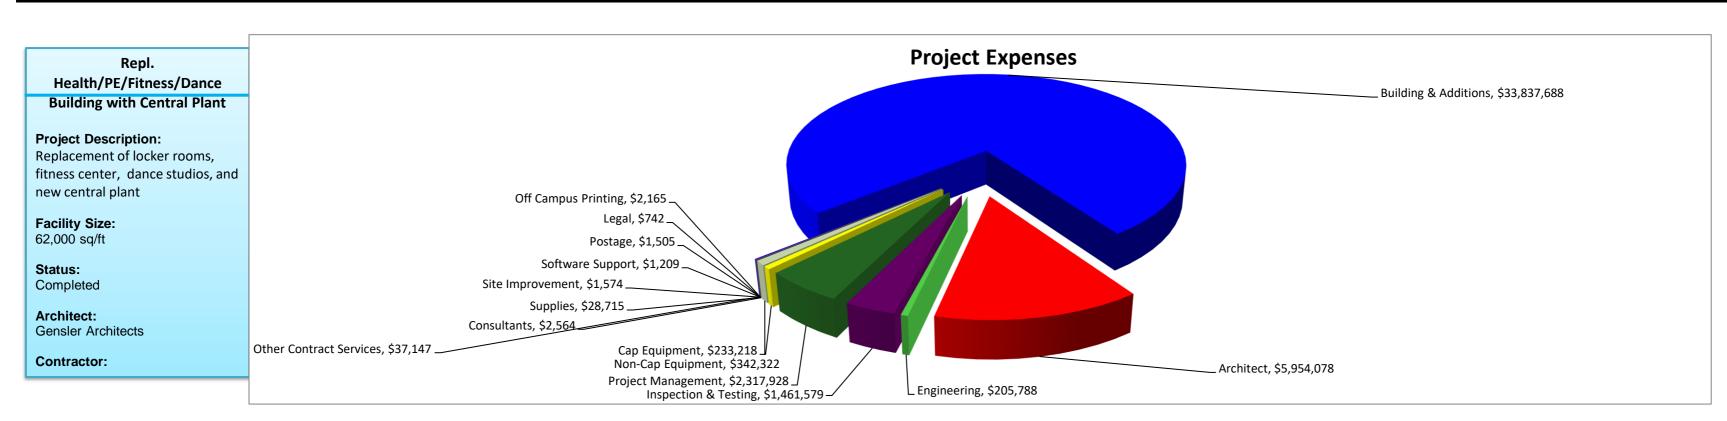

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23		<b>Combined Totals</b>
AA 7100065																	
Drescher - Academic Modernization,	Bookstore, Pic	co Promenade	(105)														
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Site Acquisition		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$0	\$5,082	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$5,082
Total		\$0	\$0	\$5,082	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$5,082
Project Budget	\$13,005,082																
Less Other Funding				ling Source:													
Net	\$5,082		1) Measure \	/ 13,000,000 a	llocated												
Actual Measure AA Expenditures																	
Running Balance	\$0	1															

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Final	23/24 (Prelim)	<b>Combined Totals</b>
AA 7100090																	
Replacement Math and Science Exter	nsion Building	(106)															
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,525		\$0	\$0	\$0	\$0	\$0	\$1,525
Site Acquisition		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,796		\$0	\$0	\$0	\$0	\$0	\$4,796
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,787,824	-\$94,695	\$0	\$0	\$0	\$0	\$0	\$1,693,130
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$70,223		\$0	\$0	\$0	\$0	\$0	\$70,223
Project Management		\$0	\$0	\$0	\$0	\$4,950	\$0	\$0	\$800	\$228,760		\$0	\$0	\$0	\$0	\$0	\$234,510
Total		\$0	\$0	\$0	\$0	\$4,950	\$0	\$0	\$800	\$2,093,128	-\$94,695	\$0	\$0	\$0	\$0	\$0	\$2,004,184
Project Budget																	
Less Other Funding		\$17,743,528		ling Source:													
Net	<del>+-,-</del> :-,		<ol> <li>Measure l</li> </ol>	J \$308,336 2)	Measure V \$	82,317,992 allo	cated										
Actual Measure AA Expenditures			<ol><li>State of C</li></ol>	alifornia \$40,0	88,000 allocate	ed											
Running Balance	\$239,824																

AA 7100047 Madison East Wing Seismic Upgrade (107)		I	T		T	I	I	T								
Supplies	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$6,197	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$6,197
Consultants	\$0	\$0	\$0	\$0	\$135	\$28	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$163
Off Campus Printing	\$0	\$0	\$0	\$0	\$0	\$285	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$285
Maintenance Contract	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$357	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$357
egal	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$7,579	\$11,822	\$8,263	\$950	\$0	\$0	\$0	\$0	\$28,613
Software Support	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$806	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$806
Other Contract Services	\$0	\$364	\$997	\$0	\$0	\$1,328	\$711	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,400
Building & Additions	\$0	\$656	\$312,643	\$0	\$4,248	\$6,030,371	\$8,829,626	\$4,949,223	\$3,967,591	\$0	\$0	\$0	\$0	\$0	\$0	\$24,094,358
rchitect	\$76,073	\$398,050	\$550,589	\$65,444	\$57,480	\$199,100	\$404,764	\$122,764	\$103,824	\$0	\$0	\$0	\$0	\$0	\$0	\$1,978,088
ngineering	\$0	\$0	\$10,707	\$778	\$0	\$13,792	\$33,184	\$37,491	\$90	\$0	\$0	\$0	\$0	\$0	\$0	\$96,042
nspection & Testing	\$0	\$19,848	\$16,752	\$3,036	\$5,851	\$676,323	\$405,443	\$112,876	\$4,703	\$0	\$0	\$0	\$0	\$0	\$0	\$1,244,832
Project Management	\$5,557	\$128,878	\$112,573	\$67,447	\$118,242	\$494,874	\$481,165	\$322,379	\$31,230	\$11,286	\$0	\$0	\$0	\$0	\$0	\$1,773,629
Cap Equipment	\$0	\$0	\$30,603	\$0	\$0	\$0	\$0	\$537,627	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$568,230
Ion-Cap Equipment	\$0	\$0	\$71,827	\$9,788	\$0	\$0	\$0	\$285,236	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$366,851
Total	\$81,630	\$547,796	\$1,106,691	\$146,492	\$185,956	\$7,416,101	\$10,154,894	\$6,382,534	\$4,119,259	\$19,549	\$950	\$0	\$0	\$0	\$0	\$30,161,852
Project Budget \$30,161,852																'
Less Other Funding \$0																
Net \$30,161,852																
Actual Measure AA Expenditures \$30,161,852																,

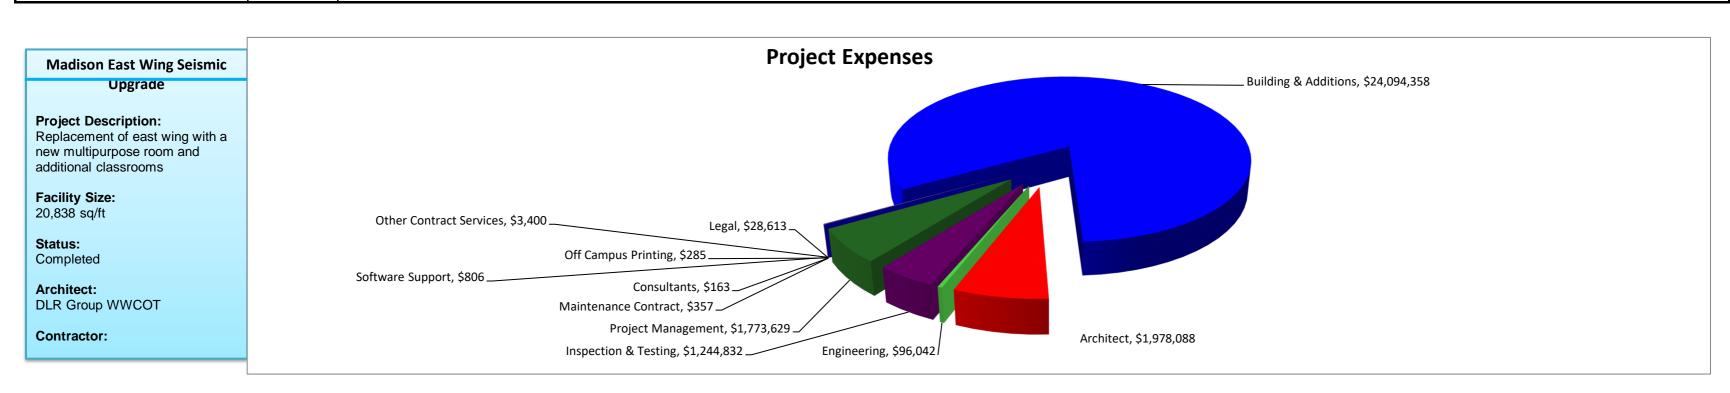

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final 2	1/22 Final	22/23 Final	23/24 (Prelim)	<b>Combined Totals</b>
A A 740000											r		-				
AA 7100068																	
Renovation to Corsair Stadium (108)																	
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$0	\$30,759	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$23,000	\$40,845	\$94,604
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
nspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$4,540	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,540
Total		\$0	\$35,299	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$23,000	\$40,845	
Project Budget	\$1,035,299	•		•		•						-	-	_			-
Less Other Funding	\$0																
Net	\$1,035,299																
Actual Measure AA Expenditures	\$99,144																
Running Balance	\$936,155																

AA 7100067, 7100152, 7100155, 7100157		Т			Т						Т					
Business & Facilities Infrastructure (111)																
Supplies	\$0	\$0	\$0	\$1,493	\$4,840	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$6,333
Service Fee	\$0	\$0	\$0	\$12,885	\$0	\$0	\$0	\$0			\$0	\$0	\$0	\$0	\$0	\$12,885
Consultants	\$0	\$0	\$0	\$0	\$14	\$8	\$0	\$0			\$0	\$0	\$0	\$0	\$0	\$22
Maintenance Contract	\$0	\$0	\$0	\$0	\$1,366	\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0	\$1,366
Legal	\$0	\$0	\$75	\$0	\$0	\$0	\$1,105	\$0			\$0	\$0	\$0	\$0	\$0	\$1,180
Software License	\$0	\$0	\$0	¥ *	\$375	\$0	\$0	\$0	ΨΟ		\$0	\$0	\$0	\$0	\$0	\$375
Other Contract Services	\$0	\$6,289	\$6,988		\$0	\$2,209	\$0				\$0	\$0	\$0	\$0	\$0	\$16,236
Moving Services	\$0	\$0	\$0	ψυσυ	\$0	\$0	\$0				\$0	\$0	\$0	\$0	\$0	\$395
Building & Additions	\$0	\$34,672	\$198,667	\$200,585	\$284,668	\$0	\$0	\$0			\$0	\$0	\$0	\$0	\$0	\$718,592
Architect	\$0	\$0	\$80,626		\$37,906	\$0	\$0	\$0			\$0	\$0	\$0	\$0	\$0	\$288,664
Engineering	\$0	\$0	\$0	\$3,705	\$9,735	\$6,840	\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0	\$20,280
Inspection & Testing	\$0	\$0	\$8,142		\$10,500	\$0	\$0	\$0			\$0	\$0	\$0	\$0	\$0	\$29,580
Project Management	\$0	\$3,073	\$154,904		\$139,821	\$3,571	\$0	\$0			\$0	\$0	\$0	\$0	\$0	\$388,659
Cap Equipment	\$0	\$0	\$0		\$80,090	\$0	\$0	\$0			\$0	\$0	\$0	\$0	\$0	\$115,982
Non-Cap Equipment	\$0	\$89,204	\$0		\$193,782	\$0	\$0	\$0			\$0	\$0	\$0	\$0	\$0	\$367,576
Total	\$0	\$133,238	\$449,401	\$608,656	\$763,095	\$12,628	\$1,105	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,968,124
Project Budget \$1,968,124 Less Other Funding \$0																
Net \$1,968,124																
Actual Measure AA Expenditures \$1,968,124  Running Balance \$0																

AA 7100004																	
Master Planning, Program Managem	ent, Overhead (11	2)															
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$139,302	\$187,927	\$245,329	\$1,270	\$0	\$0	\$0	\$0	\$0	\$573,828
Project Management		\$0	\$0	\$0	\$0	\$76,015	\$150	\$0	\$49,170	\$135,533	\$0	\$0	\$0	\$0	\$0	\$0	\$260,868
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$0	\$0	\$0	\$0	\$76,015	\$150	\$139,302	\$237,097	\$380,863	\$1,270	\$0	\$0	\$0	\$0	\$0	\$834,697
Project Budget	\$834,697	•							•	•	•	-	-	*		•	
Less Other Funding	\$0																
Net	\$834,697																
Actual Measure AA Expenditures	\$834,697																
Running Balance	\$0																

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Final	23/24 (Prelim)	Combined Totals
AA 7400454		1										,	1			1	-
AA 7100154																	
Energy Efficiency Projects (113)																	
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	
Other Contract Services		\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$189	\$2,108,853	\$990,389	-\$97,621	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,001,810
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$4,020	\$0	\$10,118	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$14,138
Project Management		\$0	\$0	\$0	\$0	\$0	\$825	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$0	\$0	\$189	\$2,112,873	\$990,389	-\$86,678	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,016,773
Project Budget	\$3,508,088																
Less Other Funding	\$491,315	1	* Other Fund	ling Source:													
Net	\$3,016,773			715.00 receiv													
Actual Measure AA Expenditures	\$3,016,773		2) SCE \$446														
Running Balance	\$0	1	3) Gas Co. \$	26,080 receive	ed												

AA 7100064					Ι	1	I						I			T	
Community Classroom & Facility Projection	cts (114)																
Supplies		\$0	\$0	\$0	\$124	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$124
Legal		\$0	\$0	\$1,867	\$1,418	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,285
Other Contract Services		\$0	\$3,720	\$1,869	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$5,588
Building & Additions		\$0	\$434,578	\$1,369,441	\$408,696	-\$1,003	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,211,712
Architect		\$0	\$263,833	\$48,120	\$1,318	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$313,272
Engineering		\$0	\$3,220	\$3,143	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$6,363
Inspection & Testing		\$0	\$41,002	\$80,885	\$1,495	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$123,382
Project Management		\$135	\$117,247	\$143,780	\$27,570	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$288,732
Non-Cap Equipment		\$0	\$0	\$209,726	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$209,726
Total		\$135	\$863,599	\$1,858,831	\$440,621	-\$1,003	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,162,183
	\$3,162,183																
Less Other Funding	\$0																
Net	\$3,162,183																
	\$3,162,183																
Running Balance	\$0																

AA 7100057		-			1		[		1							
Real Property Acquisition (115)																
Legal	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$659	\$0	\$0	\$0	\$0	\$0	\$0	\$659
Other Contract Services	\$0	\$39	\$7,000	\$0	\$15,800	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$22,839
Site Acquisition	\$1,739,979	\$4,001,204	\$9,022,207	\$0	\$0	\$0	\$0	\$5,013,226	\$4,821,600	\$0	\$0	\$0	\$0	\$0	\$0	\$24,598,214
Inspection & Testing	\$8,689	\$7,986	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$16,674
Project Management	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total	\$1,748,667	\$4,009,228	\$9,029,207	\$0	\$15,800	\$0	\$0	\$5,013,226	\$4,822,259	\$0	\$0	\$0	\$0	\$0	\$0	\$24,638,386
Project Budget \$24,638,386																
Less Other Funding \$0																
Net \$24,638,386																
Actual Measure AA Expenditures \$24,638,386																
Running Balance \$0																

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Final	23/24 (Prelim)	Combined Totals
AA 7100058, 7100151, 7100156, 71000																	
Roadways, Walkways, Grounds, Par	king Lots, and	Garages (116)															
Supplies		\$0	\$0	\$0	\$0	\$4,616	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,616
Legal		\$0	\$0	\$0	\$125	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$125
Consultants		\$0	\$0	\$0	\$48,090	\$5,018	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$53,108
Other Contract Services		\$218	\$770	\$122	\$25,249	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$26,358
Building & Additions		\$185,345	\$6,731	\$113,784	\$321,603	\$975,401	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	
Architect		\$0	\$0	\$0	\$103,569	\$19,225	\$1,240	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$124,035
Engineering		\$0	\$0	\$0	\$1,095	\$1,445	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,540
Inspection & Testing		\$13,380	\$7,865	\$13,553	\$20,126	\$42,865	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$97,787
Project Management		\$24,404	\$12,439	\$21,945	\$54,095	\$104,943	\$1,411	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$219,237
Total		\$223,347	\$27,804	\$149,403	\$573,951	\$1,153,512	\$2,652	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	
Project Budget	\$7,022,417				•						-			•			
Less Other Funding	\$4,891,747	1	* Other Fund	ding Source:													
Net	\$2,130,670		1) Measure S	S: \$3,891,747													
Actual Measure AA Expenditures	\$2,130,670	Ī	2) Measure \	V: \$1,000,000	allocated												
Running Balance	\$0	Ī															

AA 7100069				I													
Infrastructure & Technology - Technolo	gy (117)																
Software		\$0	\$0	\$0	\$0	\$0	\$218	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$218
Supplies		\$0	\$0	\$13,646	\$7,587	\$0	\$16,966	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$38,200
Maintenance Contract		\$0	\$9,472	\$46,300	\$210,581	\$18,944	\$42,415	\$9,472	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$337,186
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$49,589	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$49,589
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Cap Equipment		\$0	\$207,423	\$33,063	\$576,294	\$0	\$1,145,668	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,962,449
Non-Cap Equipment		\$0	\$0	\$42,827	\$500	\$0	\$3,447	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$46,775
Total		\$0	\$216,896	\$135,838	\$794,963	\$18,944	\$1,258,304	\$9,472	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,434,417
Project Budget Less Other Funding	\$2,434,417 \$0																
	\$2,434,417 \$2,434,417																
Running Balance	\$0																

AA 7100150		1				1		1		Ī		1				
Infrastructure & Technology - Utility (118)																
Software License	\$0	\$12,000	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$12,000
Legal	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing	\$0	\$4,979	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,979
Project Management	\$0	\$3,240	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,240
Cap Equipment	\$0	\$0	\$7,534	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$7,534
Non-Cap Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total	\$0	\$20,219	\$7,534	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$27,753
Project Budget \$27,	753															
Less Other Funding	\$0															
Net \$27,	753															
Actual Measure AA Expenditures \$27,	753															
Running Balance	\$0															

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final 21/2	/22 Final	22/23 Final	23/24 (Prelim)	<b>Combined Totals</b>
							•						•	<u> </u>			
AA 7100153																	
Emergency Lighting, Fire Alarm, a	and Security Syst																
Supplies		\$0	\$0	\$0	\$0	\$2,348	\$0	\$0	\$2,671	\$0		\$0	\$0	\$0		\$0	φ, -
Consultants/Legal		\$0	\$0	\$0	\$0	\$0	\$16	\$0	\$0	\$0		\$0	\$0	\$0		\$0	
Telecom Fee		\$0	\$0	\$0	\$0	\$0	\$800	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$800
Maintenance Contract		\$0	\$0	\$648		\$39,700	\$0	\$2,700	\$0	\$0	\$0	\$0	\$0	\$0		\$0	Ψ 10,0 10
Software Support		\$0	\$0	\$24,765	\$0	\$106,367	\$0	\$2,232	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$133,365
Other Contract Services		\$0	\$0	\$0	\$0	\$47,695	\$0	\$4,643	\$1,560	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$53,897
Building & Additions		\$0	\$0	\$0	\$0	\$110	\$2,648,866	\$4,129,145	\$1,308,230	\$763,170	\$26,375	\$79,172	\$0	\$0	\$0	\$0	\$8,955,068
Architect		\$0	\$0	\$0	\$0	\$0	\$18,925	\$0	\$0	\$5,047	\$0	\$0	\$0	\$0		\$0	\$23,972
Engineering		\$0	\$0	\$0	\$0	\$211,030	\$389,013	\$156,247	\$255,798	\$358,560	\$114,585	\$0	\$0	\$0	\$0	\$0	\$1,485,233
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$58,831	\$4,800	\$0		\$0	\$0	\$0		\$0	\$63,631
Project Management		\$0	\$0	\$0	\$0	\$51,008	\$52,044	\$79,285	\$16,500	\$49,738	\$240	\$0	\$0	\$0	\$0	\$0	\$248,814
Cap Equipment		\$0	\$0	\$0	\$0	\$89,415	\$0	\$5,871	\$0	\$0	\$0	\$0	\$0	\$0		\$0	Ψ00, <b>=</b> 00
Non-Cap Equipment		\$0	\$0	\$6,087	\$0	\$392,586	\$8,348	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	Ψ101,022
Total		\$0	\$0	\$31,500	\$0	\$940,259	\$3,118,012	\$4,438,953	\$1,589,560	\$1,176,515	\$141,642	\$79,172	\$0	\$0	\$0	\$0	\$11,515,614
Project Bud																	
Less Other Fund																	
-	Net \$11,515,614	]															
Actual Measure AA Expenditu	res \$11,515,614																
Running Balar	nce \$0	<u></u>															

AA 7100142																	
Student Services (120)																	
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Consultants		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Telecom Fee		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Maintenance Contract		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Software Support		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,165,626	\$3,704,864	\$0	\$0	\$0	\$0	\$0	\$6,870,490
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,165,626	\$3,704,864	\$0	\$0	\$0	\$0	\$0	\$6,870,490
Project Budget					•	•	•		•							•	
Less Other Funding	\$0	<u>* Oth</u>	<u>ner Fundii</u>	ng Source:													

	Net		1) State of California \$1,321,000 received	
	Actual Measure AA Expenditures	\$6,870,490	2) Measure U \$21,131,135, Measure S \$45,595,322, Measure V \$33,624,909 allocated	
	Running Balance	\$0	3) Measure U, S & AA interests \$21,681,308 allocated	
-				

Cost of Issuance (121)																	
Cost of Issuance		\$0	\$0	\$0	\$0	\$0	\$285,000	\$0	\$213,026	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$498,026
Total		\$0	\$0	\$0	\$0	\$0	\$285,000	\$0	\$213,026	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$498,026
Project Budget	\$498,026		-		-		-	•		-	-			-	-	-	
Less Other Funding	\$0																
Net	\$498,026																
Actual Measure AA Expenditures	\$498,026																
Running Balance	\$0																

Grand Total	\$4,900,734	\$10,935,5841	\$17.864.407	\$13.113.759	\$30.388.248	\$39,049,510	\$60.741.756	\$57,313,878	\$52,193,046	\$4,326,2861	\$908,418	\$126,029	\$440.877	-\$1.132.109	\$42.345	\$291,212,768
Grana rotar	ψ+,500,70+	Ψ. 0,000,00	Ψ11,001,101	Ψ10,110,100	ψου,ουσ, <u>=</u> 10	Ψ03,0 <del>1</del> 3,010	ψου,: 41,: σο	ψοι ,σιο,σιο	ψ02,130,040	ψ 1,020,200	φοσο, τιο	Ψ.20,020	Ψ110,011	Ψ1,102,100	Ψ+2,0+0	\$231,212,700


Measure AA Interest		18/19 Final
Parking Garage and Grounds - Stude	nt Services (9)	
Site Improvement		\$0
Building & Additions		\$5,192,948
Architect		\$0
Engineering		\$0
Inspection & Testing		\$0
Project Management		\$0
Total		\$5,192,948
Project Budget		
ctual Measure AA Interest Expenditures	\$5,192,948	
Running Balance	\$0	

#### SANTA MONICA COMMUNITY COLLEGE DISTRICT

### Measure V Bond Budget

As of June 30, 2024

	Project Name	Completion	Project Budget	Measure V Allocation	Other Funding	Measure V Expenditures as of 6/30/24	Measure V Expenditures as of 3/31/24	Measure V Expenditures Last Period	Total Measure V Remaining
101	Replacement Math and Science Extension Building	November 2024	\$124,958,336	\$82,317,992	\$42,640,344	\$59,217,365	\$52,597,434	\$6,619,931	\$23,100,627
102	Student Services	Completed	\$130,224,164	\$33,624,909	\$96,599,255	\$25,273,115	\$25,177,649	\$95,466	\$8,351,794
103	Malibu Center	Completed	\$61,985,779	\$34,558,420	\$27,427,359	\$29,007,103	\$28,901,822	\$105,281	\$5,551,317
104	Early Childhood Development/Childcare	Completed	\$30,925,771	\$15,405,517	\$15,520,254	\$13,164,608	\$13,159,608	\$5,000	\$2,240,909
105	Art Building Replacement	December 2025	\$63,433,040	\$52,532,040	\$10,901,000	\$8,819,456	\$8,969,149	-\$149,693	\$43,712,584
106	Business Building Renovation	On-Going	\$25,017,000	\$12,547,000	\$12,470,000	\$3,400	\$3,400	\$0	\$12,543,600
107	Air Conditioning	Completed	\$10,777,654	\$10,777,654	\$0	\$10,130,737	\$10,130,737	\$0	\$646,917
108	ADA	On-Going	\$4,000,000	\$4,000,000	\$0	\$0	\$0	\$0	\$4,000,000
109	Master Planning	December 2024	\$1,000,000	\$1,000,000	\$0	\$911,044	\$894,394	\$16,650	\$88,956
110	Drescher Hall Modernization	On-Going	\$13,005,082	\$13,000,000	\$5,082	\$0	\$0	\$0	\$13,000,000
111	Outdoor Classroom	Completed	\$321,723	\$321,723	\$0	\$321,723	\$321,723	\$0	\$0
112	John Adams MS Auditorium (SMMUSD)	Completed	\$20,000,000	\$20,000,000	\$0	\$20,000,000	\$20,000,000	\$0	\$0
113	Memorial Park Project	On-Going	\$20,000,000	\$20,000,000	\$0	\$3,481	\$3,481	\$0	\$19,996,519
114	Classrooms Relocation	Completed	\$7,400,000	\$7,400,000	\$0	\$7,286,719	\$7,286,719	\$0	\$113,281
124	Parking Structure 3 Improvement Project	June 2025	\$1,500,000	\$1,500,000	\$0	\$114,815	\$101,010	\$13,805	\$1,385,185
125	Gender Neutral Bathrooms	June 2025	\$3,500,000	\$3,500,000	\$0	\$204,101	\$195,972	\$8,129	\$3,295,899
126	Athletic Facilities	June 2026	\$20,325,749	\$20,325,749	\$0	\$2,759,295	\$2,245,545	\$513,750	\$17,566,454
120	Other Bond Related Expenses	On-Going	\$300,000	\$300,000	\$0	\$244,554	\$244,554	\$0	\$55,446
121	Cost of Issuance	On-Going	\$800,000	\$800,000	\$0	\$744,152	\$744,152	\$0	\$55,848
122	Management Reserve	On-Going	\$11,088,996	\$11,088,996			\$0		\$11,088,996
123	Unissuable Bond	On-Going	\$0	\$0	-		\$0	\$0	\$0
	Project Totals		\$550,563,294	\$345,000,000	\$205,563,294	\$178,205,668	\$170,977,349	\$7,228,319	\$166,794,332

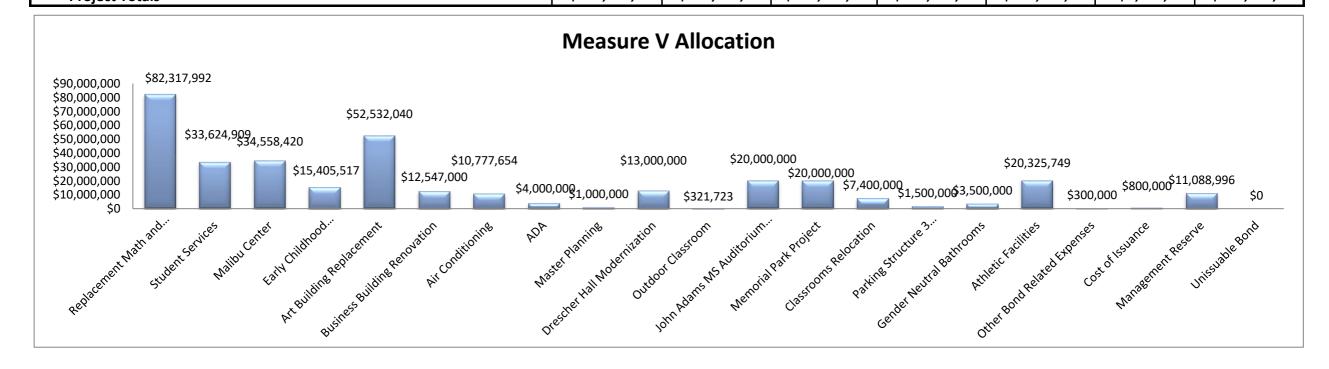

## SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure V Bond Budget History as of June 30, 2024

			Preliminary	Measure V	Measure V		Measure V
	Project Name	Completion	Measure V	Budget as of	Budget as of	Variance	Remaining as
			Budget	3/31/2024	6/30/2024		of 6/30/2024
101	Replacement Math and Science Extension Building	November 2024	\$82,317,992	\$82,317,992	\$82,317,992	\$0	\$23,100,627
102	Student Services	Completed	\$21,130,252	\$33,624,909	\$33,624,909	\$0	\$8,351,794
103	Malibu Center	Completed	\$25,000,000	\$34,558,420	\$34,558,420	\$0	\$5,551,317
104	Early Childhood Development/Childcare	Completed	\$15,405,517	\$15,405,517	\$15,405,517	\$0	\$2,240,909
105	Art Building Replacement	December 2025	\$24,000,000	\$52,532,040	\$52,532,040	\$0	\$43,712,584
106	Business Building Renovation	On-Going	\$12,547,000	\$12,547,000	\$12,547,000	\$0	\$12,543,600
107	Air Conditioning	Completed	\$10,777,654	\$10,777,654	\$10,777,654	\$0	\$646,917
108	ADA	On-Going	\$4,000,000	\$4,000,000	\$4,000,000	\$0	\$4,000,000
109	Master Planning	December 2024	\$450,000	\$1,000,000	\$1,000,000	\$0	\$88,956
110	Drescher Hall Modernization	On-Going	\$13,000,000	\$13,000,000	\$13,000,000	\$0	\$13,000,000
111	Outdoor Classroom	Completed	\$10,000,000	\$321,723	\$321,723	\$0	\$0
112	John Adams MS Auditorium (SMMUSD)	Completed	\$20,000,000	\$20,000,000	\$20,000,000	\$0	\$0
113	Memorial Park Project	December 2025	\$20,000,000	\$20,000,000	\$20,000,000	\$0	\$19,996,519
114	Classrooms Relocation	Completed	\$0	\$7,400,000	\$7,400,000	\$0	\$113,281
124	Parking Structure 3 Improvement Project	June 2025	\$0	\$1,500,000	\$1,500,000	\$0	\$1,385,185
125	Gender Neutral Bathrooms	June 2025	\$0	\$3,500,000	\$3,500,000	\$0	\$3,295,899
126	Athletic Facilities	June 2026	\$0	\$20,325,749	\$20,325,749	\$0	\$17,566,454
115	TBD	On-Going	\$57,271,585	\$0	\$0	\$0	\$0
120	Other Bond Related Expenses	On-Going	\$300,000	\$300,000	\$300,000	\$0	\$55,446
121	Cost of Issuance	On-Going	\$800,000	\$800,000	\$800,000	\$0	\$55,848
122	Management Reserve	On-Going	\$28,000,000	\$11,088,996	\$11,088,996	\$0	\$11,088,996
123	Unissuable Bond	On-Going	\$0	\$0	\$0	\$0	\$0
	Project Totals		\$345,000,000	\$345,000,000	\$345,000,000	\$0	\$166,794,332

### SANTA MONICA COMMUNITY COLLEGE DISTRICT

# Measure V Project Schedule As of June 30, 2024

	Project Name	Completion	2020	2021	2022	2023	2024	2025	2026
101	Replacement Math and Science Extension Building	November 2024							
102	Student Services	Completed							
103	Malibu Center	Completed							
104	Early Childhood Development/Childcare	Completed							
105	Art Building Replacement	December 2025							
106	Business Building Renovation	On-Going							
107	Air Conditioning	Completed							
108	ADA	On-Going							
109	Master Planning	December 2024							
110	Drescher Hall Modernization	On-Going							
111	Outdoor Classroom	Completed							
112	John Adams SMMUSD	Completed							
113	City of Santa Monica	On-Going							
114	Classrooms Relocation	Completed							
124	Parking Structure 3 Improvement Project	June 2025							
125	Gender Neutral Bathrooms	June 2025							
126	Athletic Facilities	June 2026							
127	Memorial Park Project	December 2026							
115	TBD	Completed							
120	Other Bond Related Expenses	On-Going							
121	Cost of Issuance	On-Going							
122	Management Reserve	On-Going							
123	Unissuable Bond	On-Going							
			In Plan	ning Ir	Construction	n			

Projects	Budget	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Final	23/24 (Prelim)	Combined Totals
			ı						
V 7100090									
Replacement Math and Science Extens	sion Building (101)								
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$45,668	\$45,668
Legal		\$0	\$0	\$0	\$0	\$0	\$2,101	\$0	\$2,101
Software Support		\$0	\$0	\$0	\$0	\$0	\$0	\$15,799	\$15,799
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Moving Services		\$0	\$0	\$67,242	\$0	\$0	\$0	\$32,900	\$100,142
Building & Additions		\$675	\$12,987	\$2,633	\$3,697,529	\$13,243,628	\$21,826,672	\$6,922,623	\$45,706,746
Architect		\$2,047,911	\$14,446	\$229,267	\$653,770	\$552,565	\$688,244	\$370,148	\$4,556,351
Engineering		\$0	\$0	\$19,622	\$6,966	\$10,940	\$0	\$25,926	\$63,455
Inspection & Testing		\$30,804	\$44,077	\$60,666	\$225,542	\$919,688	\$632,956	\$508,091	\$2,421,824
Project Management		\$130,874	\$617,805	\$347,350	\$474,483	\$866,097	\$503,615	\$585,345	\$3,525,569
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$91,355	\$91,355
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$90,431	\$2,597,924	\$2,688,355
Total		\$2,210,264	\$689,315	\$726,781	\$5,058,290	\$15,592,919	\$23,744,019	\$11,195,778	\$59,217,365
Project Budget	\$124,958,336	Received							
Less Other Funding	\$42,640,344	\$39,583,344	* Other Funding Sou	rce:					
Net	\$82,317,992		1) Measure U \$308,336	2) Measure AA \$2,244,0	008 allocated				
Actual Measure V Expenditures	\$59,217,365		3) State of California \$40						
Running Balance	\$23,100,627		,						
3 1 1 1	1 -77-								
V 7100142									
Student Services Building (102)									
Supplies		\$0	\$71,445	\$38,162	\$0	\$0	\$0	\$0	\$109,607
Other Contract Services		\$0	\$0	\$59,784	\$6,935	\$0	\$0	\$0	\$66,719
Consultants		\$0	\$0	\$687	\$0	\$0	\$0	\$0	\$687
Software Support		\$0	•	\$0	\$0	\$0	\$0	\$0	\$189,120
Moving Services		\$0	\$55,062	\$9,056	\$0	\$0	\$0	<u> </u>	\$64,118
Building & Additions		\$0		\$4,201,966	\$355,441	\$0	\$75,811	\$469,935	\$17,458,214
Architect		\$0	\$419,829	\$530,797	\$186,296	\$27,836	\$13,527	\$6,640	\$1,184,924
Engineering		\$0	\$140,458	\$67,481	\$130,230	\$0	\$13,327	\$0,040	\$207,939
Inspection & Testing		\$55,202	·	\$131,128	\$21,146	\$0	\$26,636	\$50,663	\$581,507
Project Management		\$0	\$900,333	\$219,425	\$85,310	\$13,020	\$20,030	\$21,706	\$1,239,794
Cap Equipment		\$0	\$1,565,928	\$90,915	\$03,310	\$13,020	\$0	\$21,700	\$1,656,844
Non-Cap Equipment		\$0	\$2,279,541	\$196,313	\$37,790	\$0	\$0	<del>\$0</del>	\$2,513,644
Total		\$55,2 <b>0</b> 2		\$5,545,714	\$692,918	\$40,856	\$115,974	\$548, <b>944</b>	\$25,273,115
	\$130,224,164	Ψ33,202	* Other Funding Sou		φ092,910	\$ <del>40,030</del>	ψ113,97 <b>4</b>	ψ <b>3</b> 40,944	Ψ23,273,113
Project Budget Less Other Funding			1) State of California \$1,						
=	\$96,599,255			1	NE 222				
Net  Actual Massure V Expanditures	\$33,624,909		2) Measure U \$21,131,1	Ī	10,322,				
Actual Measure V Expenditures	\$25,273,115		4) Measure AA \$6,870,4	1					
Running Balance	\$8,351,794		5) Measure U, S & AA in	terests \$21,681,308 allo	ocated				

Projects	Budget	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Final	23/24 (Prelim)	Combined Totals
	•	•	•	•		•	,		
V 7100015									
Malibu Site Acquisition and Center (10	03)								
Supplies		\$0	\$0	\$0	\$0	\$0	\$11,134	\$1,908	\$13,042
Software Support		\$0	\$0	\$0	\$0	\$0	\$8,281	\$8,600	\$16,880
Legal		\$0	\$0	\$0	\$0	\$0	\$181,450	\$86,112	\$267,563
Other Contract Services		\$0	\$0	\$2,713	\$38,163	\$0	\$136,245	\$6,123	\$183,244
Consultants		\$0	\$0	\$0	\$0	\$0	\$51,422	\$52,664	\$104,086
Moving Services		\$0	\$0	\$0	\$0	\$0	\$23,871	\$0	\$23,871
Building & Additions		\$0	\$0	\$2,642,861	\$3,388,666	\$8,734,478	\$7,418,550	\$1,269,672	\$23,454,227
Architect		\$0	\$0	\$0	\$155,448	\$493,355	\$262,129	\$172,286	\$1,083,218
Engineering		\$0	\$0	\$8,482	\$0	\$15,268	\$8,641	\$0	\$32,392
Inspection & Testing		\$0	\$0	\$51,754	\$633,723	\$511,002	\$159,283	\$6,198	\$1,361,958
Project Management		\$0	\$0	\$49,588	\$581,175	\$626,405	\$406,040	\$119,319	\$1,782,527
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$60,513	\$14,162	\$74,674
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$12,015	\$535,594	\$61,814	\$609,422
Total		\$0	\$0	\$2,755,398	\$4,797,174	\$10,392,522	\$9,263,151	\$1,798,857	\$29,007,103
Project Budget	\$61,985,779								
Less Other Funding	\$27,427,359		* Other Funding Sou	ırce:					
Net	\$34,558,420		1) Measure S \$25,132,	568					
Actual Measure V Expenditures	\$29,007,103		2) Interest Allocated \$2	2,294,791					
Running Balance	\$5,551,317								
V 7100104									
Early Childhood Development/Childca	are (104)								
Supplies	• •	\$0	\$0	\$35,150	\$5,332	-\$500	-\$96	\$96	\$39,982
Other Contract Services		\$0	\$0	\$35,344	\$15,128	\$0	\$0	-\$3,744	\$46,728
Consultants		\$0	\$0	\$16	\$0	\$0	\$0	\$0	\$16
Software Support		\$0	\$0	\$6,158	\$0	\$5,677	\$5,677	\$1,656	\$19,169
Legal		\$0	\$0	\$96	\$0	\$0	\$0	\$0	\$96
Building & Additions		\$0	\$0	\$8,879,770	\$1,603,432	\$0	\$73,242	\$36,783	\$10,593,227
Architect		\$0	\$0	\$262,660	\$275,924	\$105,158	\$27,846	\$14,351	\$685,939
Engineering		\$0	\$0	\$19,448	\$0	\$15,550	\$3,149	\$0	\$38,146
Inspection & Testing		\$0	\$0	\$349,661	\$135,767	\$3,700	\$13,249	\$3,290	\$505,667
Project Management		\$0	\$0	\$384,279	\$384,714	\$2,144	\$0	\$0	\$771,137
Cap Equipment		\$0	\$0	\$32,448	\$0	\$0	\$0	\$0	\$32,448
Non-Cap Equipment		\$0	\$0	\$328,242	\$92,913	\$0	\$0	\$10,897	\$432,052
Total		\$0	\$0	\$10,333,272	\$2,513,210	\$131,730	\$123,066	\$63,329	\$13,164,608
Project Budget	\$30,925,771	Received	·		- , ,	· , [	· , l		, , ,
Less Other Funding		\$6,661,598		* Other Funding Sou	rce:				
Net	\$15,405,517			1) City of Santa Monica					
Actual Measure V Expenditures				2) Measure S \$8,858,65					
, , , , , , , , , , , , , , , , , , , ,									

Projects	Budget	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Final	23/24 (Prelim)	Combined Totals
				1	T		ı		_
V 7100240									
Art Complex (105)									
Legal		\$0		\$14,811	\$0	\$0	\$11,547	\$0	\$26,359
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$1,213	\$1,213
Consultants		\$0		\$20,991	\$40,710	\$1,344	\$0	\$0	\$63,045
Moving Services		\$0		\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$184	\$407,369	\$3,040	\$0	\$1,791	\$108,857	\$5,967,677	\$6,488,734
Architect		\$0	\$0	\$39,542	\$569,178	\$28,572	\$85,055	\$74,971	\$797,318
Engineering		\$0	\$0	\$0	\$0	\$40,750	\$0	\$2,105	\$42,855
Inspection & Testing		\$0	\$35,495	\$25,052	\$43,653	\$45,227	\$12,852	\$415,998	\$578,276
Project Management		\$0	\$1,600	\$85,708	\$85,978	\$184,706	\$117,875	\$345,607	\$821,473
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$184	\$444,464	\$189,143	\$739,518	\$302,390	\$336,186	\$6,807,570	\$8,819,456
Project Budget	\$63,433,040	Received							
Less Other Funding	\$10,901,000	\$4,626,297	* Other Funding Sou	ırce:					
Net	\$52,532,040		1) State of California \$6	5,274,703 pending					
Actual Measure V Expenditures	\$8,819,456		,						
Running Balance	\$43,712,584								
	¥ 15/1 ==/55 1								
V 7100243									
<b>Business Building Replacement (106)</b>									
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Consultants		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Moving Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0		\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		<u> </u>	\$0	\$0	\$0	\$0	\$0	<u> </u>	\$0
Project Management		\$0	· •	\$3,400	\$0	\$0	\$0	\$0	\$3,400
Cap Equipment		\$0		\$0	\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		<b>\$0</b>		\$3,400	\$0	<b>\$0</b>	<b>\$0</b>	\$0	\$3,400
Project Budget	\$25,017,000	Ψ.	Ψ•	70,.00	+-	Ψ"	Ψ.	<del></del>	, , , , , , , , , , , , , , , , , , ,
Less Other Funding	\$12,470,000		* Other Funding Sou	ırce:					
Net	\$12,547,000		1) State Funding \$12,47						
Actual Measure V Expenditures	\$3,400		T, State Fallaning 712,47	0,000					
Running Balance	\$12,543,600								
Numing Dalance	712,373,000								

Projects	Budget	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Final	23/24 (Prelim)	Combined Totals
V 7100188					T				T
Air Conditioning (107)									
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Consultants		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$2,451	\$7,537,201	\$733,457	\$0	\$0	\$8,273,110
Architect		\$0	\$79,000	\$0	\$0	\$39,872	\$3,280	\$0	\$122,152
Engineering		\$417,960	\$217,966	\$26,992	\$81,868	\$109,823	\$3,280	\$0	\$857,984
Inspection & Testing		\$0	\$54,810	\$776	\$253,936	\$125,639	\$0	\$0	\$435,160
Project Management		\$4,370	\$4,570	\$35,700	\$365,350	\$32,340	\$0	\$0	\$442,330
Total		\$422,330	\$356,346	\$65,919	\$8,238,355	\$1,041,132	\$6,655	\$0	
Project Budget	\$10,777,654	Ψ+22,000	Ψ000,040	Ψ00,010	ψ0,200,000	Ψ1,0+1,102	ΨΟ,ΟΟΟ	Ψ	ψ10,100,101
Less Other Funding	\$0								
Net	\$10,777,654								
Actual Measure V Expenditures									
	\$10,130,737								
Running Balance	\$646,917								
V 7100004	Т	<u> </u>	<u> </u>	1	T	<u> </u>	T		Ī
V 7100004 Master Plan (100)									
Master Plan (109)							ćo	Ć0 44F	Ć0 445
Legal Other Contract Consises		ćo	ćo	ĆO	ćo	ćo	\$0	\$8,415	
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	·
Consultants		\$0	\$0	\$0	\$0	\$48,000	\$0	\$0	\$48,000
Advertising		\$0	\$641	\$0	\$0	\$0	\$0	\$0	\$641
Architect		\$0	\$112,073	\$528,182	\$37,861	\$0	\$52,150	\$118,822	\$849,088
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0 \$0	\$0
Project Management		\$0 <b>*</b> 0	\$3,800	\$1,100	\$0	\$0	\$0 \$52.450	<u> </u>	\$4,900
Total	¢1 000 000	\$0	\$116,515	\$529,282	\$37,861	\$48,000	\$52,150	\$127,237	\$911,044
Project Budget	\$1,000,000								
Less Other Funding	\$0								
Net	\$1,000,000								
Actual Measure V Expenditures	\$911,044								
Running Balance	\$88,956								
									1
V 7100237									
Outdoor Classroom (111)									
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$100,000	\$102,023	\$102,495	\$0	\$0	\$0	\$0	\$304,518
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$17,205	\$0	\$0	\$0	\$0	\$0	
Total		\$100,000	\$119,228	\$102,495	\$0	\$0	\$0	\$0	\$321,723
	\$321,723								
Project Budget	¥3==): =3								
Project Budget Less Other Funding	\$0								
Less Other Funding	\$0								

Projects	Budget	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Final	23/24 (Prelim)	Combined Totals
V.74002C0		1				1	- 1		
V 7100268  Parking Structure 3 Imp Project (124)									
Parking Structure 3 Imp Project (124)		ćo	ćo	\$0	ćo	ćo	ćo	ćo	ćo
Other Contract Services		\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0
Building & Additions  Architect		\$0	\$0	\$0	\$0 \$0	\$0	· ·	· · ·	\$U \$114.91E
		\$0	\$0	\$0	\$0	\$0	\$26,282 \$0	\$88,533 \$0	\$114,815
Engineering Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0 \$0	\$0	\$0
Project Management		\$0	\$0	\$0	\$0	\$0	\$0 \$0	\$0	\$0
Total		<b>\$0</b>	\$0	\$0	\$0 \$0	\$ <b>0</b>	\$26,282	•	\$114,815
Project Budget	\$1,500,000	ΨΟ	ΨΟ	ΨΟ	ΨΟ	ΨΟ	ΨΖΟ,ΖΟΖ	ψ00,333	ψ114,015
Less Other Funding	\$1,300,000								
<u> </u>									
Net Nessure V Expenditures	\$1,500,000								
Actual Measure V Expenditures	\$114,815								
Running Balance	\$1,385,185								
V 7100270			T		Ī		1		
Gender Neutral Bathroom Project (125	5)								
Other Contract Services	- /	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$0	\$0	\$0	\$0	\$0	\$46,298	•	
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$13,490	\$19,841	\$33,331
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$0	\$0	\$0	\$0	\$0	\$59,788	\$144,314	\$204,101
Project Budget	\$3,500,000	· L	· L	· L	·	· 1	. ,	, ,	, ,
Less Other Funding	\$0								
Net	\$3,500,000								
Actual Measure V Expenditures	\$204,101								
Running Balance	\$3,295,899								
Kullillig Balance	73,233,633								
V 7100271									
Athletic Facilities (126)									
Consultants							\$0	\$13,455	\$13,455
Legal		\$0	\$0	\$0	\$0	\$0	\$9,431	\$23,684	\$33,114
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Land Acquisition							\$0	\$2,194,154	\$2,194,154
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$484,477	\$484,477
Engineering		\$0	\$0	\$0	\$0	\$0	\$0		\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$34,095	\$34,095
Project Management		\$0	\$0	\$0	\$0	\$0	\$0		\$0
Total		\$0	\$0	\$0	\$0	\$0	\$9,431	\$2,749,865	\$2,759,295
Project Budget	\$20,325,749								
Less Other Funding	\$0								
Net	\$20,325,749								
Actual Measure V Expenditures	\$2,759,295								
Running Balance									
	τ /2 - 3/ 13 1								

Projects	Budget	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Final	23/24 (Prelim)	Combined Totals
V 7100272									
Memorial Park Project (113)									
Legal		\$0	\$0	\$0	\$0	\$0	\$3,481	\$0	\$3,481
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$0	\$0	\$0	\$0	\$0	\$3,481	\$0	\$3,481
Project Budget	\$20,000,000								
Less Other Funding	\$0								
Net	\$20,000,000								
Actual Measure V Expenditures	\$3,481								
Running Balance	\$19,996,519								

V 7100243	1								
Classrooms Relocation (114)									
Supplies Supplies		\$0	\$0	\$0	\$0	\$11,963	\$0	\$0	\$11,963
Other Contract Services		<u> </u>	\$0	\$0	\$0	\$0	\$0		\$0
Building & Additions		\$0	\$3,467	\$5,709,329	\$391,967	\$0	\$0	\$0	\$6,104,763
Supplies		\$0	\$0	\$4,982	\$0	\$0	\$0	\$0	\$4,982
Architect		\$0	\$184,434	\$78,179	\$92,082	\$0	\$0	\$0	\$354,695
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$16,795	\$115,194	\$25,996	\$0	\$0	\$0	\$157,985
Project Management		\$0	\$61,520	\$476,831	\$55,650	\$0	\$0	\$0	\$594,001
Non-Cap Equipment		\$0	\$0	\$58,331	\$0	\$0	\$0	\$0	\$58,331
Total		\$0	\$266,216	\$6,442,846	\$565,695	\$11,963	\$0	\$0	\$7,286,719
Project Budget	\$7,400,000		_						
Less Other Funding	\$0								
Net	\$7,400,000								
Actual Measure V Expenditures	\$7,286,719								
Running Balance	\$113,281								

Projects	Budget	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Final	23/24 (Prelim)	Combined Totals
V 7100255									
John Adams MS Auditorium - SMMUS	D (112)								
Building and Additions		\$0	\$0	\$0	\$15,000,000	\$5,000,000	\$0	\$0	\$20,000,000
Total		\$0	\$0	\$0	\$15,000,000	\$5,000,000	\$0	\$0	\$20,000,000
Project Budget	\$20,000,000								
Less Other Funding	\$0								
Net	\$20,000,000								
Actual Measure V Expenditures	\$20,000,000								
Running Balance	\$0								
S7100048									
Other Bond Related Expenses (116)									
Consultants		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Lease/Rental		\$0	\$13,590	\$18,171	\$6,814	\$0	\$0	\$0	\$38,576
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Software License		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Advertising		\$0	\$0	\$0	\$770	\$900	\$0	\$0	\$1,670
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$184	\$191,065	\$0	\$0	\$0	\$0	\$0	\$191,249
Inspection & Testing		\$0	\$13,060	\$0	\$0	\$0	\$0	\$0	\$13,060
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$184	\$217,715	\$18,171	\$7,584	\$900	\$0	\$0	\$244,554
Project Budget	\$300,000								
Less Other Funding	\$0								
Net	\$300,000								
Actual Measure V Expenditures	\$244,554								
Running Balance	\$55,446								

Projects	Budget	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Final	23/24 (Prelim)	<b>Combined Totals</b>
Cost of Issuance (117)									
Cost of Issuance		\$291,277	\$0	\$0	\$0	\$452,875	\$0	\$0	\$744,152
Total		\$291,277	\$0	\$0	\$0	\$452,875	\$0	\$0	\$744,152
Project Budget	\$800,000								
Less Other Funding	\$0								
Net	\$800,000								
Actual Measure V Expenditures	\$744,152								
Running Balance	\$55,848								

Grand Total	\$3,079,440	\$20,483,307	\$26,712,421	\$37,650,605	\$33,015,286	\$33,740,184	\$23,524,425	\$178,205,668

### SMC Bond Program (Measures U, S, AA and V) Bond Contractor List as of 6-30-2024

### Student Services (Measure U #0, Measure S #9, Measure AA #120, Measure V #102):

Architect - Steinberg Architects, Morris Architects, SVA Architects

Contractor – Minco, Bernards Brothers, Spinitar, Nazerian

Engineering – IVA, Cogent Energy Engineering, XL Fire

Inspection & Testing – Geolabs, BTC Labs - Vertical V, Peak Survey, LPI Rango, Twining, AGE

Project Management - LPI, YNL, Vanir

### Replacement Health/PE/Fitness/Dance Building (Measure S #4, Measure AA #104):

Architect - Gensler Architects

Contractor - Bernards Brothers

Engineering – IVA, Glumac

Inspection & Testing - Geolabs, Ellis Environmental, Twining, Rango

Inspection, AGE

Project Management - LPI

### Early Childhood Development (Measure S #5, Measure V #104):

Architect - Carde Ten Architects, SVA Architects

Consultant - Child Educational Center

Contractor - The Nazerian Group, USA Shade

Engineering – Jacobs

Inspection & Testing - Geolabs, Rango Inspection, Twining

Project Management - LPI, Vanir, YNL

#### Malibu Site (Measure S #6, Measure AA #110, Measure V #103):

Architect - Quatro Design Group (QDG)

Contractor - Master Contracting, Icon West

Consultant – m2 Strategic, Parker Environmental, M6 Consultants

Engineering - Ensitu Services, Jacobs, CNA

Inspection & Testing – Peak Surveys, Ellis Environmental, JL Inspection, Ninyo

& Moore, Geolabs, Twining, B2E

Project Management - LPI, M6 Strategic, Vanir, YNL

#### **Energy Efficiency Projects (Measure S #7, Measure AA #113):**

Architect - N/A

Contractor – Compass Energy Solutions, Johnson Controls

Engineering - Compass Energy Solutions, Johnson Controls

Inspection & Testing – Ellis Environmental

### **Environmental Performance (Measure AA #101):**

Architect - Kishimoto Architects

Contractor – SJ Amoroso Construction

Engineering – P2S Engineering

Inspection & Testing – Cannon, Peak Surveys

Project Management - LPI

### **Information Technology Relocation (Measure AA #102):**

Architect - Morris Architects

Contractor - Minco, Bernards Brothers, Eidim AV Technology

Engineering – IVA, P2S Engineering

Inspection & Testing – Cannon, Peak Surveys, Geolabs, Ellis Environmental,

Twining, JL Inspection, Rango

Project Management - LPI, CCS Presentation

### Media and Technology Complex (Measure AA #103):

Architect - Clive Wilkinson Architects, Morris Architects

Contractor – H.B. Parkco Construction, Fast Track Construction, CW Driver, Dimension Data, Key Code Media, Omega

Construction

Consultant - EEG Services

Engineering – IVA, P2S Engineering

Inspection & Testing - Twining, Geolabs, BTC Labs - Vertical V,

IL Inspection, EEG Services, Ellis Environmental, Rango,

Cannon

Project Management – LPI

#### Madison East Wing Seismic Upgrade (Measure AA #107):

Architect - DLR Group - WWCOT, LPI

Contractor - Trimax, Bernards Brothers, Dimension Data

Engineering – IVA, Glumac

Inspection & Testing - Twining, Peak Surveys, LPI, All Group Engineering, EEG

Services, Ellis Environmental

Project Management - LPI

#### **Business & Facilities Infrastructure (Measure AA #111):**

Architect - LPI, Gwynne Pugh Urban Studio

Contractor – REC+S, Inc., Omega Construction,

Concept Consultant, Inc.

Engineering – N/A

Inspection & Testing - Ellis Environmental, JL Inspection

Project Management – LPI

### **Community Classroom & Facility Project (Measure AA #114)**

Architect - Morris Architects

Contractor – Waisman Construction, Spinitar, Trimax

Engineering – IVA

Inspection & Testing – LPI, Twining

Project Management - LPI

### Roadways, walkways, Grounds, Parking Lots, and Garages (Measure AA #116)

Architect - LPI, DLR Group - WWCOT

Contractor – Trimax, Pub Construction

Consultant - Walker Parking

Engineering – MK Engineering

Inspection & Testing - Ellis Environmental, Peak Surveys, LPI

Project Management - LPI

### Emergency Lighting, Fire Alarm, and Security System (Measure AA #119)

Contractor - Red Hawk Fire and Security, Nexus

Engineering - MDC Engineers

Inspection & Testing - Rango

Project Management - LPI

### Math and Science Addition (Measure AA #106/Measure V #101)

Architect - Cannon Design

Contractor – Icon West, The Nazerian Group

Consultant – N/A

Engineering – Arup

Inspection & Testing – AGE, Geolabs, Twining, B2E, JL Inspection

Project Management - Vanir, YNL

#### Classrooms Relocation (Measure V #114)

Architect – Gwynne Pugh

Contractor - The Nazerian Group

Inspection & Testing – AGE

Project Management - Vanir, YNL

#### **Art Building Replacement (Measure V #105)**

Architect – Little Architects

Consultant – Fehr and Peers

Contractor – PCN3, Inc.

Engineering – tk1sc, CNA

Inspection & Testing – B2 Environmental, Geolabs, CNA, Rango, Twining

Project Management – Vanir, YNL

### **Air Conditioning (Measure V #107)**

Architect - P2S

Contractor – A&B Construction, Inc

Engineering – tk1sc, P2S

Inspection & Testing - Rango, Koury, B2 Environmental

Project Management - Vanir, YNL

### Parking Structure 3 Improvement Project (Measure V #124)

Architect – SVA Architects

### **Gender Neutral Bathrooms (Measure V #125)**

Architect – TSK Architects
Inspection & Testing – CNA, Geolabs, Spectrum Fire

### Renovation to Corsair Stadium Project (Measure AA #108)

Architect - SVA Architects

### **Athletic Facilities (Measure V #126)**

Architect – dsk Architects Consultants – Parker Environmental Inspection & Testing – CNA, Geolabs



### Paid Vendors List

(Vendors that Received Payments from Bond Funds)

For the 12-month period July 1, 2023 to June 30, 2024 (FY 2023-24)

All Group Engineering (AGE)

ARC Printing
Arup Engineering
Axelliant Technology

**B2** Environmental

Cannon Design
CDW- Gov Supplies
Charter Communications

**Chris Nelson and Associates** 

CA State DSA
Customs Signs
DLR Architects
Enterprise Security

**Electric Supply Corp** 

Fagen Friedman and Fulfrost (FFF)

Frontier Communications

Grainger Inc Harding Larmore Kutcher

Geolabs

Icon West Construction Company

ITSavvy

JL Inspection
Little Architects
Maintex Products

LPI

Marina Graphic
Design Services
M6 Consulting

**Nazerian Construction** 

PCN3

Parker Environmental QDG Architecture Rango Inspection Saitech Electronics School Specialty Shade Structures Inc

SVA Architects
TSK Architects

tk1sc Engineering
Unisource Solutions

Vanir Construction Management

Virco Furniture Zoll Medical
