SANTA MONICA COMMUNITY COLLEGE DISTRICT

Measure U Project Schedule As of September 30, 2011


	Project Name	Completion	20 ⁻	11	2	201	2		20	13		20	14		201	5
Α	Purchase of BAE Airport Site	Completed														
В	Emeritus College Facility	Completed														
С	Purchase of 1738 Pearl Street	Completed														
D	PE Temp. Bldg. Replacement	Completed														
Е	Remodel Library Village for Math	Completed														
F	SM Airport Campus Site Improvements	Completed														
G	SM Airport Campus West Building	Completed														
н	Theater Arts Renovation	Completed														
I	Earthquake Rpl. Liberal Arts North	Completed														
J	Music Complex	Completed														
К	Earthquake Rpl. Liberal Arts South	Completed														
L	Shuttle Replacement Parking	Completed														
М	North Quad Plaza	Completed														
Ν	Letters & Sci Demo/Restore	Move to AA														
0	Student Services Building	May 2015														
Р	Science Complex Addition	Move to AA														
Q	Infrastructure & Safety	Completed														
R	Restroom Improvements	Completed														
S	Master Planning	Completed														
Т	14th and Pico Project	On Hold														
	* SM Airport Campus also known as Bundy	Sito		In (nstru			_								

SANTA MONICA COMMUNITY COLLEGE DISTRICT

Measure U Bond Budget

As of September 30, 2011

	Project Name	Completion	Project Budget	Measure U Allocation	Other Funding	Measure U Expenditures as of 9/30/11	Measure U Expenditures as of 6/30/11	Measure U Expenditures Last Period	Total Measure U Remaining
Α	Purchase of BAE Airport Site	Completed	\$30,280,878	\$30,280,878	\$0	\$30,280,878	\$30,280,878	\$0	\$0
В	Emeritus College Facility	Completed	\$9,603,782	\$8,909,940	\$693,842	\$8,909,940	\$8,909,940	\$0	\$0
С	Purchase of 1738 Pearl Street	Completed	\$749,208	\$749,208	\$0	\$749,208	\$749,208	\$0	\$0
D	PE Temp. Bldg. Replacement	Completed	\$2,797,033	\$2,797,033	\$0	\$2,797,033	\$2,797,033	\$0	\$0
Е	Remodel Library Village for Math	Completed	\$1,458,690	\$1,458,690	\$0	\$1,458,690	\$1,458,690	\$0	\$0
F	SM Airport Campus Site Improvements	Completed	\$4,170,264	\$4,170,264	\$0	\$4,170,264	\$4,170,264	\$0	\$0
G	SM Airport Campus West Building	Completed	\$19,709,741	\$19,709,741	\$0	\$19,709,741	\$19,709,741	\$0	\$0
Н	Theater Arts Renovation	Completed	\$19,497,949	\$19,497,949	\$0	\$19,496,949	\$19,496,949	\$0	\$1,000
1	Earthquake Rpl. Liberal Arts North	Completed	\$12,507,725	\$6,352,752	\$6,154,973	\$7,633,209	\$7,633,209	\$0	-\$1,280,457
J	Music Complex	Completed	\$4,623,547	\$2,005,434	\$2,618,113	\$2,005,116	\$2,005,116	\$0	\$318
K	Earthquake Rpl. Liberal Arts South	Completed	\$16,733,220	\$6,108,150	\$10,625,070	\$6,108,150	\$6,108,150	\$0	\$0
L	Shuttle Replacement Parking	Completed	\$18,969,509	\$18,969,509	\$0	\$18,969,509	\$18,969,509	\$0	\$0
М	North Quad Plaza	Completed	\$11,388,463	\$11,388,463	\$0	\$11,388,463	\$11,388,463	\$0	\$0
N	Letters & Sci Demo/Restore	Move to AA	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0	Student Services Building	May 2015	\$53,521,913	\$20,816,196	\$32,708,239	\$2,087,584	\$2,082,330	\$5,254	\$18,728,612
Р	Science Complex Addition	Move to AA	\$308,336	\$308,336	\$0	\$308,336	\$308,336	\$0	\$0
Q	Infrastructure & Safety	Completed	\$4,030,284	\$4,030,284	\$0	\$3,961,776	\$3,948,796	\$12,980	\$68,508
R	Restroom Improvements	Completed	\$17,501	\$17,501	\$0	\$17,501	\$17,501	\$0	\$0
S	Master Planning	Completed	\$2,110,430	\$2,110,430	\$0	\$2,110,430	\$2,110,430	\$0	\$0
Т	14th and Pico Project	On Hold	\$319,242	\$319,242	\$0	\$319,242	\$319,242	\$0	\$0
	Project Totals		\$212,800,237	\$160,000,000	\$52,800,237	\$142,482,019	\$142,463,785	\$18,234	\$17,517,981

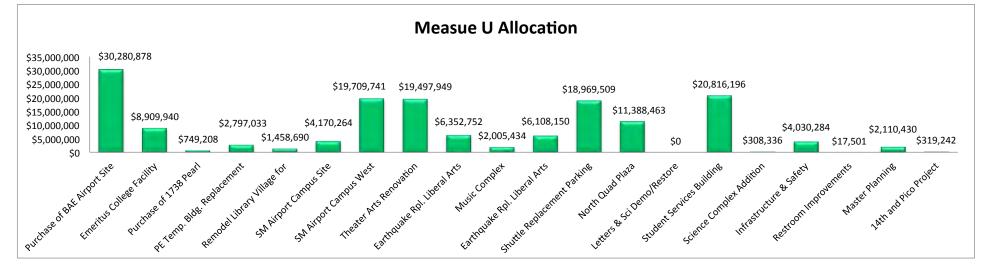

Total S0	Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12	Combined Totals
Purchase of BAE Airport Site (A) 0 <	ιΕ								•				
Site Acquisition Site Acquisition<	U7100010												
Total S0 \$0	Purchase of BAE Airport Site (A)												
Total S0 \$0	Site Acquisition		\$0	\$0	\$0	\$30,280,878	\$0	\$0	\$0	\$0	\$0	\$0	\$30,280,878
Project Budget \$30,200.878 (ses Other Funding \$30,200.878 (solutions) Less Other Funding Actual Measure U Expenditures \$30,200.878 (solutions) solutions) U710028					\$0	\$30,280,878							\$30,280,878
Net S02,280,878 Actual Measure U Expenditures \$30,280,878 Running Balance \$00 U7100028 \$0 Emericus College Facility (B) \$8,658,675 \$0 <td>Project Budget</td> <td>\$30,280,878</td> <td></td> <td></td> <td></td> <td>. , ,</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td>. , ,</td>	Project Budget	\$30,280,878				. , ,							. , ,
Actual Measure U Expenditures \$30,280,878 Running Balance \$0 Emeritus College Facility (B) Emeritus College Facility (B) \$14,649 Stile Acquisition \$14,640 Stile Acquisition \$14,640 Stile Acquisition \$14,640 Stile Acquisition \$14,640 Stile Acquisition \$14,940 Stile Acquisition \$160 Stile Acquisition \$160 Stile Acquisition \$160 Stile Acquisition \$17,986 Stile Acquisition	Less Other Funding	\$0											
Actual Measure U Expenditures \$30,280,876 Running Balance 50 Emeritus College Facility (B)	Net	\$30,280,878											
U710023 Ste Acquisition \$8,656,675 \$0 <	Actual Measure U Expenditures												
Emeritus College Facility (B) 8.656 675 50 \$0	Running Balance	\$0											
Emeritus College Facility (B) 8.656 675 50	· · · ·												
Site Acquisition \$8,658,675 \$0 \$	U7100028												
Legal \$14.649 \$3.009 \$20.421 \$0 <td>Emeritus College Facility (B)</td> <td></td>	Emeritus College Facility (B)												
Architect \$93,735 \$27,831 \$161 \$0 </td <td>Site Acquisition</td> <td></td> <td>\$8,658,675</td> <td>\$0</td> <td>\$0</td> <td></td> <td></td> <td>\$0</td> <td>\$0</td> <td></td> <td></td> <td>\$0</td> <td>\$8,658,675</td>	Site Acquisition		\$8,658,675	\$0	\$0			\$0	\$0			\$0	\$8,658,675
Engineering \$18,400 \$0	Legal		\$14,649	\$3,009	\$20,421	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$38,078
Supply S0 \$4.461 \$0 \$	Architect		\$93,735	\$27,831	\$161	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$121,727
Building & Additions \$0 \$17,496 \$0 \$4,000 \$0 \$0 \$0 \$0 \$0 \$0 \$2 Cap Equipment \$0 \$\$2,197 \$0 \$	Engineering		\$18,400	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$18,400
Cap Equipment Sto \$49,406 \$0 <td>Supply</td> <td></td> <td>\$0</td> <td></td> <td></td> <td></td> <td>\$0</td> <td>\$0</td> <td>\$0</td> <td>\$0</td> <td>\$0</td> <td>\$0</td> <td>\$4,461</td>	Supply		\$0				\$0	\$0	\$0	\$0	\$0	\$0	\$4,461
Non-Cap Equipment \$0 -\$2,197 \$0 -\$108 \$0	Building & Additions		\$0	\$17,496	\$0	\$4,000	\$0	\$0	\$0	\$0	\$0	\$0	\$21,496
Total \$8,785,459 \$100,007 \$20,582 \$3,892 \$0 <	Cap Equipment		\$0	\$49,406	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$49,406
Project Budget \$9,603,782 Received Less Other Funding* \$803,842 \$693,842 \$693,842 \$Charlen Funding Source: Net \$8,909,940 \$8,909,940 *Other Funding Source: Emeritus College Foundation \$693,842 received Running Balance \$0 \$0 \$0 \$0 \$0 \$0 U7100006 \$0 \$0 \$0 \$0 \$0 \$0 \$0 Site Acquisition \$0 \$704,534 \$0 <td>Non-Cap Equipment</td> <td></td> <td>\$0</td> <td>-\$2,197</td> <td>\$0</td> <td>-\$108</td> <td>\$0</td> <td>\$0</td> <td></td> <td></td> <td>\$0</td> <td>\$0</td> <td>-\$2,305</td>	Non-Cap Equipment		\$0	-\$2,197	\$0	-\$108	\$0	\$0			\$0	\$0	-\$2,305
Less Other Funding* \$693,842 \$693,842 \$693,842 * Other Funding Source: Emeritus College Foundation \$693,842 received Net \$8,909,940 \$8,909,940 * Other Funding Source: Emeritus College Foundation \$693,842 received Running Balance \$0 \$0 \$0 \$0 \$0 \$0 U7100006 \$0 \$0 \$0 \$0 \$0 \$0 \$0 V17100006 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 Site Acquisition \$0 \$704,534 \$0	Total		\$8,785,459	\$100,007	\$20,582	\$3,892	\$0	\$0	\$0	\$0	\$0	\$0	\$8,909,940
Net \$8,909,940 Actual Measure U Expenditures \$8,909,940 \$0 Emeritus College Foundation \$693,842 received Running Balance \$0 <t< td=""><td>Project Budget</td><td>\$9,603,782</td><td>Received</td><td>•</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></t<>	Project Budget	\$9,603,782	Received	•									
Net \$8,909,940 Actual Measure U Expenditures \$8,909,940 \$0 Emeritus College Foundation \$693,842 received Running Balance \$0 <t< td=""><td>Less Other Funding*</td><td>\$693,842</td><td>\$693,842</td><td></td><td>* Other Funding</td><td>g Source:</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></t<>	Less Other Funding*	\$693,842	\$693,842		* Other Funding	g Source:							
Actual Measure U Expenditures \$8,909,940 Running Balance \$0 U710006 1738 Pearl Street (C) \$0	Net	\$8,909,940			Emeritus Colle	ge Foundation	\$693,842 recei	ved					
U7100006 Image: Constraint of the street (C) Image: Constraint of the street (C)<	Actual Measure U Expenditures	\$8,909,940				-							
1738 Pearl Street (C) Image: Step of the street (C) Step of the stree	Running Balance	\$0											
1738 Pearl Street (C) Image: Constraint of the street (C) Image: Constreet (C) Stat		•											
1738 Pearl Street (C) Image: Step of the street (C) Step of the stree	U7100006												
Site Acquisition \$0 \$704,534 \$0<													
Site Improvement \$0 \$3,250 \$0 <td></td> <td></td> <td>\$0</td> <td>\$704,534</td> <td>\$0</td> <td>\$0</td> <td>\$0</td> <td>\$0</td> <td>\$0</td> <td>\$0</td> <td>\$0</td> <td>\$0</td> <td>\$704,534</td>			\$0	\$704,534	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$704,534
Building & Additions \$0 \$41,424 \$0	Site Improvement		\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,250
Total \$0 \$749,208 \$0 \$0 \$0 \$0 \$0 \$0 \$749,208 Project Budget \$749,208 \$749,208 \$0 <td>Building & Additions</td> <td></td> <td>\$0</td> <td>\$41,424</td> <td></td> <td>\$0</td> <td>\$0</td> <td>\$0</td> <td>\$0</td> <td>\$0</td> <td>\$0</td> <td>\$0</td> <td>\$41,424</td>	Building & Additions		\$0	\$41,424		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$41,424
Project Budget \$749,208 Less Other Funding \$0 Net \$749,208									\$0	\$0			\$749,208
Less Other Funding \$0 Net \$749,208	Project Budget	\$749,208											
Net \$749,208													
	<u> </u>	\$749,208											
Actual Measure U Expenditures 5/49,208	Actual Measure U Expenditures	\$749,208											
Running Balance \$0	Running Balance	\$0											

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12	Combined Totals
U7100026												
PE Temporary Building Replacement (D)												
Architect		\$148,055	\$42,372	\$6,220	\$485	\$0				\$0	\$0	\$197,133
Building & Additions		\$43,866	\$1,922,493	\$415,932	\$0	\$0				\$0	\$0	\$2,382,291
Inspection & Testing		\$6,455	\$136,510	\$716	\$0	\$0	\$0			\$0	\$0	\$143,681
Project Management		\$4,800	\$56,247	\$5,225	\$0	\$0				\$0	\$0	\$66,272
Advertising and Moving Expenses		\$763	\$0	\$6,893	\$0	\$0				\$0	\$0	\$7,656
Total		\$203,939	\$2,157,622	\$434,987	\$485	\$0	\$0	\$0	\$0	\$0	\$0	\$2,797,033
Project Budget	\$2,797,033											
Less Other Funding	\$0											
Net	\$2,797,033											
Actual Measure U Expenditures	\$2,797,033											
Running Balance	\$0											
U7100310												
Remodel Library Village for Math (E)												
Moving Exp.		\$0	\$38,625	\$0	\$0	\$0	\$0			\$0	\$0	\$38,625
Building & Additions		\$0	\$1,036,490	\$115,653	\$0	\$0	\$0	\$0		\$0	\$0	\$1,152,143
Architect		\$104,992	\$27,141	\$1,340	\$486	\$0				\$0	\$0	\$133,959
Engineering		\$0	\$2,658	\$0	\$0	\$0				\$0	\$0	\$2,658
Inspection & Testing		\$0	\$27,083	\$25,175	\$0	\$0		\$0		\$0	\$0	\$52,258
Project Management		\$0	\$51,679	\$4,400	\$0	\$0				\$0	\$0	\$56,079
Advertising and Moving Expenses		\$207	\$10,137	\$12,623	\$0	\$0				\$0	\$0	\$22,967
Total		\$105,199	\$1,193,813	\$159,191	\$486	\$0	\$0	\$0	\$0	\$0	\$0	\$1,458,690
Project Budget	\$1,458,690											
Less Other Funding	\$0											
Net	\$1,458,690											
Actual Measure U Expenditures	\$1,458,690											
Running Balance	\$0											


Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12	Combined Totals
· · · · · · · ·	•											
U7100027												
SM Airport Campus Site Improvements (F)												
Supplies		\$0	\$26,234	\$975	\$5,873	\$0	\$0	\$0	\$0	\$0	\$0	\$33,082
Misc Fees		\$0	\$25	\$0	\$0	\$34,274	\$0	\$0	\$0	\$0	\$0	\$34,299
Other Contract Services		\$3,860	\$11,508	\$8,434	\$1,501	\$0	\$0			\$0	\$0	\$25,302
Site Improvement		\$0	\$0	\$15,182	\$5,790	\$7,237	\$0	\$0		\$0	\$0	\$28,209
Building & Additions		\$0	\$1,495,697	\$1,670,788	\$4,824	\$0	\$0			\$0	\$0	\$3,171,309
Architect		\$104,934	\$500	\$0	\$43,570	\$0	\$0	\$0	\$0	\$0	\$0	\$149,004
Engineering		\$35,000	\$148,304	\$950	\$10,040	\$0	\$0	\$0	\$0	\$0	\$0	\$194,294
Inspection & Testing		\$5,032	\$118,662	\$191,271	\$0	\$0	\$0			\$0	\$0	\$314,965
Project Management		\$750	\$155,798	\$38,425	\$1,365	\$220	\$0			\$0	\$0	\$196,558
City Fees, Advertising and Security System		\$16,587	\$1,802	\$327	\$150	\$4,375	\$0			\$0	\$0	\$23,241
Total		\$166,163	\$1,958,530	\$1,926,352	\$73,113	\$46,106	\$0	\$0	\$0	\$0	\$0	\$4,170,264
Project Budget	\$4,170,264											
Less Other Funding	\$0											
Net	\$4,170,264											
Actual Measure U Expenditures	\$4,170,264											
Running Balance	\$0											
U7110027												
SM Airport Campus West Building (G)												
Supply		\$0	\$0	\$17,650	\$28,017	\$0	\$0	\$0	\$0	\$0	\$0	\$45,667
Other Contract Services		\$0	\$0	\$0	\$3,576	\$0	\$0	\$0	\$0	\$0	\$0	\$3,576
Moving Expenses		\$0	\$0	\$180	\$15,824	\$0	\$0	\$0	\$0	\$0	\$0	\$16,004
Building & Additions		\$0	\$0	\$15,037,532	\$1,256,065	\$46,946	\$0	\$0	\$0	\$0	\$0	\$16,340,543
Architect		\$0	\$971,954	\$1,043,950	\$49,779	\$1,147	\$0	\$0	\$0	\$0	\$0	\$2,066,830
Engineering		\$0		\$9,800	\$5,010	\$963	\$0			\$0	\$0	\$18,693
Inspection & Testing		\$0	\$21,173	\$126,510	\$9,856	\$0	\$0	\$0	\$0	\$0	\$0	\$157,539
Project Management		\$0	\$14,450	\$313,715	\$13,956	\$0	\$0			\$0	\$0	\$342,121
Cap Equipment		\$0	\$49,795	\$326,382	\$4,792	\$0	\$0			\$0	\$0	\$380,969
Non-Cap Equipment		\$0	\$0	\$280,558	\$57,240	\$0	\$0	\$0		\$0	\$0	\$337,798
Total		\$0	\$1,060,292	\$17,156,277	\$1,444,115	\$49,056	\$0	\$0	\$0	\$0	\$0	\$19,709,741
Project Budget	\$19,709,741											
Less Other Funding	\$0											
Net	\$19,709,741											
Actual Measure U Expenditures	\$19,709,741											
Running Balance	\$0											

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12	Combined Totals
U7100025												
Theatre Arts Renovation (H)												
Supplies		\$0	\$8,904	-\$14	\$12,858		\$0	\$0	\$0		\$0	\$38,367
Legal		\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0	\$0
Moving Services		\$0	\$0	\$0	\$0		\$0	\$0	\$0		\$0	\$14,061
Other Contract Services		\$0	\$0	\$0	\$0		\$0	\$5,245	\$0		\$0	\$5,245
Rental / Lease		\$0	\$1,446	\$2,200	\$0		\$0	\$0	\$0		\$0	
Building & Additions		\$528	\$1,326,630	\$4,540,487	\$10,897,603		\$25,220	\$0	\$0		\$0	\$16,846,590
Architect		\$289,913	\$369,213	\$423,416	\$82,639		\$0	\$0	\$0	\$0	\$0	\$1,165,181
Engineering		\$6,174	\$2,981	\$16,606	\$2,375		\$0	\$0	\$0	\$0	\$0	
Inspection & Testing		\$150	\$14,785	\$353,890	\$297,675	\$1,116	\$0	\$0	\$0	\$0	\$0	\$667,616
Project Management		\$150	\$45,698	\$184,219	\$193,898		\$230	\$0	\$0	\$0	\$0	\$439,013
Cleaning, Storage and Installation		\$0	\$812	\$0	\$2,548	\$2,267	\$0	\$0	\$0	\$0	\$0	
Cap Equipment		\$0	\$31,638	\$0	\$6,458		\$0	\$0	\$0	\$0	\$0	
Non-Cap Equipment		\$0	\$2,388	\$0	\$36,749	\$145,294	\$0	\$0	\$0		\$0	
Total		\$296,915	\$1,804,496	\$5,520,804	\$11,532,803	\$311,236	\$25,450	\$5,245	\$0	\$0	\$0	\$19,496,949
Project Budget	\$19,497,949											
Less Other Funding	\$0											
Net	\$19,497,949											
Actual Measure U Expenditures	\$19,496,949											
Running Balance	\$1,000											
U7100110												
Earthquake Rpl. Liberal Arts North (I)												
Supplies		\$0	\$0	\$0	\$0		\$0	\$75			\$0	\$1,483
Legal		\$0	\$0	\$0	\$0		\$0	\$0	\$0		\$0	\$887
Other Contract Services		\$0	\$0	\$0	\$0		\$0	\$0		\$0	\$0	\$75
Building & Additions		\$265	\$0	\$1,043,660	\$5,916,281	-\$973,001	\$321,345	\$14,898			\$0	\$5,488,685
Architect		\$0	\$611,732	\$102,824	\$209,490	\$216,563	\$21,215	\$3,465	\$0		\$0	\$1,165,289
Engineering		\$3,248	\$4,295	\$0	\$250	\$0	\$250	\$0	\$0	\$0	\$0	
Inspection & Testing		\$0	\$0	\$28,312	\$326,203	\$77,942	\$0	\$0	\$0		\$0	\$432,458
Project Management		\$0	\$26,072	\$33,549	\$128,937	\$124,222	\$255	\$1,155	\$286	\$0	\$0	\$314,475
Advertising and Fees		\$0	-\$4	\$7,334	\$0		\$0	\$0	\$0		\$0	
Cap-Equipment		\$0	\$0	\$0	\$0		\$12,579	\$0		\$0	\$0	\$37,935
Non-Cap Equipment		\$0	\$0	\$0	\$2,033		\$4,093	\$0	\$0		\$0	
Total		\$3,513	\$642,095	\$1,215,679	\$6,583,194	-\$356,123	\$359,737	\$19,592	\$286	-\$834,764	\$0	\$7,633,209
Project Budget	\$12,507,725	Received										
Less Other Funding*	\$6,154,973	\$4,874,517		* Other Funding								
Net	\$6,352,752			City of Santa M								
Actual Measure U Expenditures	\$7,633,209			FEMA \$2,115,2	20 commited,	\$834,764 receive	ed					
Running Balance	-\$1,280,457											

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12	Combined Totals
U7100013. U7100047												1
Music Complex (J)												
Advertising		\$0	\$0	\$436	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$436
Supplies		\$0 \$0	\$0 \$0	\$430 \$0	\$0 \$0		40 \$19,094			\$0	\$0 \$0	
Consultants		\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0		\$36.000	\$0	\$0 \$0	\$0	\$0 \$0	
Other Contract Services		\$0 \$0	\$0 \$0	\$0	\$0 \$0		<u>\$30,000</u> \$180	\$0	\$0 \$0	\$0	\$0 \$0	\$30,000 \$180
Moving Services		\$0	\$0 \$0	\$0	\$0 \$0		\$6.330	\$0	\$0 \$0	\$0	\$0 \$0	\$6,330
Building & Additions		\$0	\$0 \$0	\$356,464	\$1,293,726	-\$737,213	\$273,531	\$0	\$0 \$0	\$0	\$0 \$0	\$1,186,509
Architect		\$0 \$0	\$0 \$187,922	\$22,500	\$37,227	\$38,448	\$4,052		\$0 \$0	\$681	\$0 \$0	
Engineering		\$0 \$0	\$107,922	\$22,500 \$0	\$37,227 \$0				\$0 \$0	\$001	\$0 \$0	
Inspection & Testing		\$0	\$0 \$0	\$29.740	\$19,265		\$35,880		\$0 \$0	\$0	\$0 \$0	\$21,370
Project Management		\$0	\$0 \$170	\$36,739	\$36,351	\$56,914	\$16,200		\$0 \$0	\$0	\$0 \$0	\$147,662
Cap Equipment		\$0 \$0	\$170	\$30,739 \$0	\$30,331 \$0		\$62,600		\$0 \$0	\$0	\$0 \$0	
Non-Cap Equipment		\$0	\$0 \$0	\$0 \$0	\$0 \$0	1.	\$78,582		\$0 \$0	\$0	\$0 \$0	\$108,434
Total		\$0 \$0	\$188,092	\$445,879			\$532,447		\$0 \$0		\$0 \$0	
Project Budget	\$4,623,547	Received	\$100,052	\$ 44 5,075	φ1,300,300	-\$305,500	\$JJZ,447	\$37,014	φυ	\$00 I	φU	\$2,005,110
Less Other Funding*	\$2,618,113	\$2,618,113		* Other Funding	Sourco:							
Net	\$2,005,434	92,010,113		Prop T Refinan		rocoivod						
Actual Measure U Expenditures	\$2,005,116			гтор т кештап	ce 92,010,113	leceiveu						
Running Balance	\$2,003,110											
Running Balance	φ310											
U7100111	1							1				
Earthquake Rpl. Liberal Arts South (K)		\$0	\$0	\$855	\$2,497	\$379	\$23,811	\$75	\$0	\$0	\$0	\$27,618
Supply		\$0 \$0	\$0 \$0	\$055 \$0			\$2.203	\$75	\$0 \$0	\$0	\$0 \$0	\$27,618 \$2,253
Legal		\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0		\$2,203	\$0 \$0	\$0 \$0	\$0	\$0 \$0	\$2,253 \$4,063
Moving Services Consultants		\$0 \$0	\$0 \$0	\$0 \$0	ە 0 \$17,265	\$0 \$41,435	<u>\$4,063</u> \$0			\$0	\$0 \$0	\$4,063 \$58,700
Other Contract Services		\$0 \$0	\$0 \$0	\$0	\$17,205	\$41,435	\$0 \$0		\$0 \$0	\$0	\$0 \$0	\$58,700 \$6,356
		\$0 \$0	\$0 \$0	\$0,154	\$3,091,306	\$0 \$5,706,802			۵ 0 \$91.516	\$0	\$0 \$0	\$6,336
Building & Additions Architect		\$0 \$0	\$0 \$0	\$20,302	-\$503,297	\$5,706,802	-\$4,642,459 \$183,877	\$39,984	\$91,516	\$0	\$0 \$0	\$4,273,467 \$723,174
		\$0 \$0		\$830,555	-\$503,297 \$150	\$163,506	\$103,877					\$723,174 \$9,119
Engineering		\$0 \$0	\$0 \$0	\$3,125	\$150 \$179,798	\$5,344	\$500		\$0 \$0	\$0 \$0	\$0 \$0	\$9,119
Inspection & Testing		\$0 \$0	\$0 \$0	\$0 \$0	\$43,989		\$66,273	\$0 \$1,722	۵ 0 \$1,278	\$0	\$0 \$0	
Project Management		\$0 \$0		\$0 \$0							\$0 \$0	. ,
Cap-Equipment		\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0		\$0 \$45,388		\$0 \$0	\$0	\$0 \$0	\$0 \$97,040
Non-Cap Equipment Total		\$0 \$0	\$0 \$0							\$0	\$0 \$0	
	¢16 700 000		\$0	\$872,991	\$2,831,909	\$6,534,806	-\$4,261,655	\$34,757	\$95,342	\$0	\$0	\$6,108,150
Project Budget	\$16,733,220	Received		* Others Evention	0							
Less Other Funding*	\$10,625,070	\$10,625,070		* Other Funding		70						
Net	\$6,108,150			City of Santa M								
Actual Measure U Expenditures	\$6,108,150			State of Californ	nia \$4,458,000	received						
Running Balance	\$0											

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12	Combined Totals
U7100221												
Shuttle Replacement Parking (L)												
Supplies		\$0	\$0	\$0	\$0	\$0	\$1,347	\$0	\$0	\$0	\$0	\$1,347
Legal		\$0	\$0	\$0	\$8,462	\$35,103	\$0	\$0		\$0	\$0	\$43,565
Site Acquisition		\$0	\$0	\$0	\$0		\$0	\$0		\$0	\$0	\$16,903,087
Site Improvement		\$0	\$0	\$0	\$0	\$3,027	\$0		\$0	\$0	\$0	\$3,027
Building & Additions		\$0	\$0	\$0	\$0	\$484,000	\$1,252,224	\$2,353	\$0	\$0	\$0	\$1,738,577
Architect		\$0	\$0	\$0	\$0	\$51,569	\$7,208	\$0	\$0	\$0	\$0	\$58,777
Inspection & Testing		\$0	\$0	\$0	\$0	\$139,822	\$41,250	\$0		\$0	\$0	\$181,072
Project Management		\$0	\$0	\$0	\$0	\$7,631	\$32,425			\$0	\$0	\$40,056
Total		\$0	\$0	\$0	\$8,462	\$17,624,240	\$1,334,455	\$2,353	\$0	\$0	\$0	\$18,969,509
Project Budget	\$18,969,509											
Less Other Funding	\$0											
Net	\$18,969,509											
Actual Measure U Expenditures	\$18,969,509											
Running Balance	\$0											
U7100321												
North Quad Plaza (M)												
Legal		\$0	\$0	\$0	\$0	\$0	\$3,825	\$5,604	\$0	\$0	\$0	\$9,429
Building & Additions		\$0	\$0	\$0	\$0	-\$443	\$6,130,081	\$3,634,487	\$0	\$0	\$0	\$9,764,125
Architect		\$0	\$231,055	\$8,444	\$140,048	\$435,618	\$171,225	\$68,633	\$2,901	\$10,483	\$0	\$1,068,407
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$186,220	\$107,477	\$328	\$0	\$0	\$294,025
Project Management		\$0	\$0	\$760	\$210	\$2,200	\$135,601	\$55,782	\$606	\$0	\$0	\$195,158
Printing		\$0	\$1,900	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,900
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$55,420	\$0	\$0	\$0	\$55,420
Total		\$0	\$232,955	\$9,204	\$140,258	\$437,375	\$6,626,952	\$3,927,402	\$3,834	\$10,483	\$0	\$11,388,463
Project Budget	\$11,388,463											
Less Other Funding	\$0											
Net	\$11,388,463											
Actual Measure U Expenditures	\$11,388,463											
Running Balance	\$0											

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12	Combined Totals
U7100500, U7126450, U7100334, U7100142												
Student Services Building (O)												
Supplies		\$2,014	\$0	\$0	\$0	\$0	\$0	\$718	\$0	\$0	\$0	\$2,732
PC Upgrades		\$0	\$765	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$765
Consultants		\$0	\$0	\$0	\$0	\$9,334	\$55,693	\$0		\$0	\$0	
Legal		\$0	\$0	\$0	\$0	\$38	\$2,775	\$31,776	\$0	\$0	\$0	\$34,588
Other Contract Services		\$210	\$0	\$0	\$0	\$0	\$17,561	\$17,495	\$18,817	-\$70	\$0	\$54,014
Moving		\$7,571	\$0	\$0	\$0	\$0	\$0	\$616	\$0	\$0	\$0	\$8,187
Building & Additions		\$359,141	\$2,441	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$361,582
Architect		\$31,782	\$0	\$235,230	\$0	\$43,992	\$0	\$690,099	\$208,521	\$38,643	\$5,254	\$1,253,522
Engineering		\$1,838	\$0	\$0	\$0	\$0	\$0	\$6,205	\$27,363	\$3,171	\$0	\$38,576
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$25,670	\$34,687	\$0	\$0	\$0	\$60,358
Project Management		\$4,650	\$0	\$2,470	\$0	\$1,100	\$0	\$124,148	\$0	\$0	\$0	\$132,368
Cap Equipment		\$59,063	\$0	\$0	\$0	\$0	\$8,745	\$8,056	\$0	\$0	\$0	\$75,864
Total		\$466,268	\$3,207	\$237,700	\$0	\$54,464	\$110,445	\$913,802	\$254,701	\$41,744	\$5,254	\$2,087,584
Project Budget	\$53,521,913	Received		* Other Funding	g Source:							
Less Other Funding*	\$32,705,717	\$1,321,000		State of Californ	nia \$16,803,00	0 allocated, \$1,3	321,000 receive	ed				
Net	\$20,816,196			District Capital	Funds \$10,208	,069 commited						
Actual Measure U Expenditures	\$2,087,584			Measure U Inte	rest \$5,694,64	8 allocated						
Running Balance	\$18,728,612											

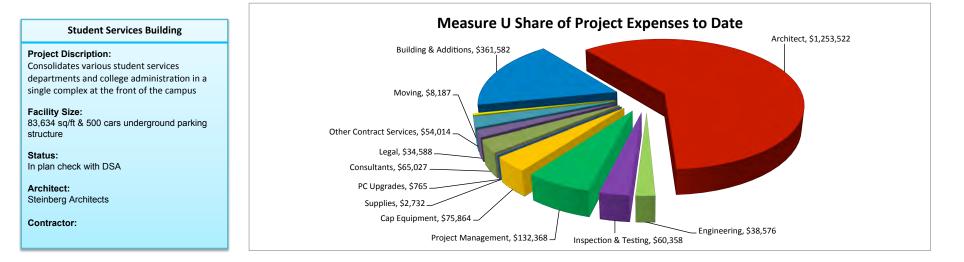

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12	Combined Totals
U7100090												
Science Complex Additional (P)												
Architect		\$0	\$0	\$0	\$0	\$246,425	\$61,911	\$0			\$0	\$308,336
Total		\$0	\$0	\$0	\$0	\$246,425	\$61,911	\$0	\$0	\$0	\$0	\$308,336
Project Budget	\$308,336											
Less Other Funding	\$0											
Net	\$308,336											
Actual Measure U Expenditures	\$308,336											
Running Balance	\$0											
U6780000, U7100022, U7100331, U7100550,												
U7100005, U7100030, U7100031, U7100029,												
U7100003, U7100008, U7100332, U7100072,												
U7100042, U7100056, U7100039												
Infrastructure & Safety (Q)												
Supplies		\$0	\$0	\$254	\$0	\$0	\$0	\$1,700	\$1,393	\$0	\$0	\$3,347
Consultants		\$0	\$0	\$0	\$0	\$0	\$0	\$16,734	\$0	\$0	\$0	\$16,734
Maintenance Agreement		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$14,673	\$12,979	\$27,653
Legal		\$0	\$0	\$0	\$0	\$0	\$3,527	\$3,294	\$0	\$0	\$0	\$6,821
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$7,825	\$81,445	\$203,383	\$3,320	\$0	\$295,973
Building & Additions		\$681,900	\$195,175	\$20,600	\$0	\$200,620	\$733	\$0	\$0	\$0	\$0	\$1,099,028
Architect		\$69,081	\$42,108	\$0	\$155,321	\$448,507	\$91,127	\$4,227	\$0	\$0	\$0	\$810,370
Engineering		\$8,050	\$0	\$0	\$6,750	\$12,000	\$18,429	\$2,360	\$0	\$0	\$0	\$47,589
Inspection & Testing		\$2,241	\$4,250	\$0	\$0	\$0	\$5,807	\$0	\$0	\$0	\$0	\$12,298
Project Management		\$0	\$2,805	\$0	\$0	\$3,520	\$1,840	\$38	\$196	\$0	\$0	\$8,399
Cap Equipment		\$0	\$0	\$343,861	\$0	\$0	\$0	\$895,171	\$349,531	\$40,002	\$0	\$1,628,565
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,216	\$0	\$0	\$4,216
Advertising		\$0	\$785	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$785
Total		\$761,272	\$245,122	\$364,715	\$162,071	\$664,647	\$129,287	\$1,004,968	\$558,718	\$57,995	\$12,979	\$3,961,776
Project Budget	\$4,030,284											
Less Other Funding	\$0											
Net	\$4,030,284											
Actual Measure U Expenditures	\$3,961,776											
Running Balance	\$68,508											

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12	Combined Totals
U7100007												
Restroom Improvement (R)												
Supplies		\$0	\$564	\$0	\$1.075	\$0	\$0	\$0	\$0	\$0	\$0	\$1,639
Other Contract Services		\$0 \$0	\$0	\$0	\$3,803	\$0 \$0	\$0		\$0 \$0		\$0 \$0	\$3,803
Building & Additions		\$0	\$1,305	\$0	\$7,891	\$0	\$0		\$0 \$0		\$0 \$0	\$9,196
Inspection & Testing		\$0	\$2,043	\$0	\$820	\$0	\$0		\$0 \$0		\$0 \$0	\$2,863
Total		\$0	\$3,912	\$0	\$13,589	\$0					\$0 \$0	\$17,501
Project Budget	\$17,501	ψΰ	ψ0,01 Σ	ψυ	ψ10,000	ΨΟ	ψŪ	ψŪ	ψΰ	ψŪ	ψυ	ψ17,00
Less Other Funding	\$0											
Net	\$17,501											
Actual Measure U Expenditures	\$17,501											
Running Balance	\$17,501											
Running Balance	φυ											
U7100004, U7110020												
Master Planning (S)												
Consultants		\$9,000	\$26,516	\$158,449	\$374,329	\$125,404	\$17,998	\$363,342	\$0	\$0	\$0	\$1,075,038
Architect		\$0	\$17,617	\$126,433	\$104,083	\$126,701	\$346,827	\$276,985	\$0		\$0	\$998,647
Rental / Lease		\$0	\$0	\$6.453	\$0	\$0	\$0		\$0	\$0	\$0	\$6,453
Postage		\$0	\$0	\$30,000	\$0	\$0	\$0				\$0	\$30,000
Reimbursement to SMC		\$0	\$0 \$0	\$0	\$180	\$0	\$0		\$0 \$0		\$0	\$180
Project Management		\$0	\$0 \$0	\$0	\$0	\$0	\$0		\$0		\$0	\$113
Total		\$9,000	\$44,133	\$321,335	\$478,593	\$252,105	\$364,825		\$0		\$0	\$2,110,430
Project Budget	\$2,110,430	\$0,000	¥11,100	\$02 1,000	\$ 410,000	<i>4202,100</i>	\$00 4,020	\$010,100	ψũ	ψu	ţ,	\$2,110,400
Less Other Funding	\$0											
Net	\$2,110,430											
Actual Measure U Expenditures	\$2,110,430											
Running Balance	\$0											
	ψυ											
U7100024												
14th and Pico Project (T)												
Consultants		\$0	\$888	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$888
Architect		\$258,601	\$47,343	\$0	\$0	\$0	\$0		\$0		\$0	\$305,944
Inspection & Testing		\$12,070	\$0	\$0	\$0	\$0	\$0				\$0	\$12,070
Project Management		\$0	\$340	\$0	\$0	\$0	\$0		\$0		\$0	\$340
Total		\$270,671	\$48,571	\$0	\$0	\$0					\$0	\$319,242
Project Budget	\$319,242	+=,.	+,		,	\$		÷**	\$	ψu	÷.	, .
Less Other Funding	\$0											
Net	\$319,242											
Actual Measure U Expenditures	\$319,242											
Running Balance	\$0											
	ι ψυ											
Grand Total		\$11.068.400	\$10,432,055	\$28.685.697	\$54,940,416	\$25,278,771	\$5.283.853	\$6,585,573	\$912,880	-\$723,860	\$18,233	\$142,482,019
		÷11,000,400	÷.0,402,000	<i>410,000,001</i>	÷5-,0-0,-+10	÷20,210,771	<i>40,200,000</i>		wo . 2,500	φ. <u>20</u> ,000	ψ10,200	ψι-τ_,-τ0Σ,013

Note: Project N had no expenses

SANTA MONICA COMMUNITY COLLEGE DISTRICT

Measure S Project Schedule As of September 30, 2011


	Project Name	Completion	20	11		20	12		4	201:	3		20 ⁷	14	201	5
1	Athletic Fields Phase I, Corsair Field	Completed														
1A	Athletic Fields Phase I, John Adams	Completed														
2	Performing Arts Center	Completed														
3	Career Opportunity Center	Move to AA														
4	Replacement Health/PE/Fitness Building	May 2014									· ·					
5	Early Childhood Development/Childcare	May 2015														
6	Malibu Site Acquisition and Facility	Not Scheduled														
7	Energy Efficiency Projects	On-Going														
8	Satellite Campus Parking Facilities and Roadway Improvements	Completed														
9	Parking Garage, Grounds and Equipment - Student Services	May 2015	ľ							'						
10	Pico Promenade Improvements	Completed														
11	Master Planning	On-Going														
12	Other Bond Related Expenses	On-Going														
13	Adv. Architecture Related Exp for AA	Completed														
14	Real Property Acquisition	On-Going														
15	Signage Safety/Information	On-Going						1								
			In I	Plann	ing				1	n C	onst	truct	ion			

SANTA MONICA COMMUNITY COLLEGE DISTRICT


Measure S Bond Budget

As of September 30, 2011


	Project Name	Completion	Project Budget	Measure S Allocation	Other Funding	Measure S Expenditures as of 9/30/11	Measure S Expenditures as of 6/30/11	Measure S Expenditures Last Period	Total Measure S Remaining
1	Athletic Fields Phase I, Corsair Field	Completed	\$4,440,768	\$4,373,238	\$67,530	\$4,372,535	\$4,372,535	\$0	\$703
1A	Athletic Fields Phase I, John Adams	Completed	\$2,970,807	\$2,970,807	\$0	\$2,969,807	\$2,969,807	\$0	\$1,000
2	Performing Arts Complex	Completed	\$40,603,541	\$37,610,965	\$2,992,576	\$37,610,571	\$37,610,571	\$0	\$394
3	Career Opportunity Center	Move to AA	\$0	\$0	\$0	\$0	\$0	\$0	\$0
4	Replacement Health/PE/Fitness Building	May 2014	\$40,200,333	\$4,816,093	\$35,384,240	\$790,589	\$790,589	\$0	\$4,025,504
5	Early Childhood Development/Childcare	May 2015	\$11,318,000	\$7,000,000	\$4,318,000	\$11,524	\$10,446	\$1,078	\$6,988,476
6	Malibu Site Acquisition and Facility	Not Scheduled	\$31,069,031	\$25,000,000	\$6,069,031	\$5,235,922	\$5,233,878	\$2,044	\$19,764,078
7	Energy Efficiency Projects	On-Going	\$1,293,570	\$1,076,248	\$217,322	\$293,361	\$293,361	\$0	\$782,887
8	Satellite Campus Parking Facilities and Roadway Improvements	Completed	\$4,875,000	\$4,875,000	\$0	\$3,820,983	\$3,820,983	\$0	\$1,054,017
9	Parking Garage, Grounds and Equipment - Student Services	May 2015	\$53,143,653	\$52,690,653	\$453,000	\$14,968,445	\$14,762,912	\$205,533	\$37,722,208
10	Pico Promenade Improvements	Completed	\$1,018,009	\$1,018,009	\$0	\$1,018,009	\$1,018,009	\$0	\$0
11	Master Planning	On-Going	\$750,000	\$750,000	\$0	\$708,583	\$708,583	\$0	\$41,417
12	Other Bond Related Expenses	On-Going	\$662,764	\$662,764	\$0	\$124,645	\$119,313	\$5,332	\$538,119
13	Adv. Architecture Related Exp for AA	Completed	\$0	\$0	\$0	\$0	\$0	\$0	\$0
14	Real Property Acquisition	On-Going	\$50,000	\$50,000	\$0	\$45,597	\$45,597	\$0	\$4,403
15	Signage Safety/Information	On-Going	\$606,223	\$606,223	\$0	\$236,289	\$236,289	\$0	\$369,934
	Project Totals		\$193,001,699	\$143,500,000	\$49,501,699	\$72,206,860	\$71,992,873	\$213,987	\$71,293,140

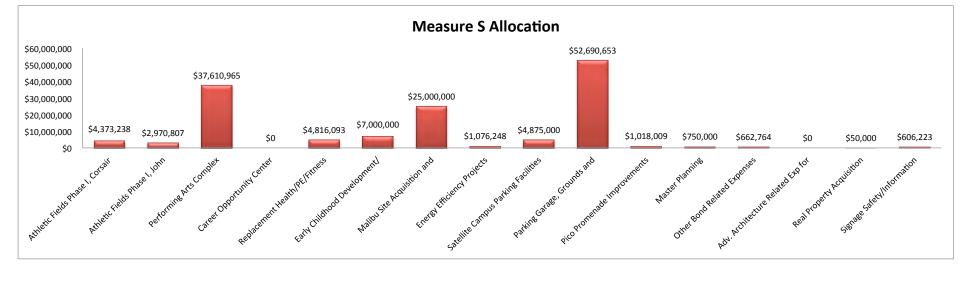

Projects	Budget 04/05 Final 05/06 Final 06/07 Final 07/08 Final 08/09 Final 09/10 Final 10/11 Final 11/12 Combined Totals														
				\$0 \$0 \$301 \$175 \$0 \$0 \$0 \$0 \$300,380 \$2,579,095 \$0 \$0 \$0 \$0 \$0 \$300,380 \$2,579,095 \$0 \$0 \$0 \$2,8 \$3,815 \$197,557 \$252,736 \$279,173 \$26,563 \$0 \$0 \$8 \$0 \$0 \$23,411 \$57,585 \$640 \$296 \$0 \$8 \$0 \$0 \$23,411 \$57,585 \$640 \$296 \$0 \$8 \$0 \$0 \$23,411 \$57,585 \$640 \$296 \$0 \$8 \$0 \$0 \$23,411 \$57,585 \$640 \$296 \$0 \$8 \$0 \$0 \$9,871 \$42,374 \$565 \$0 \$0 \$5 \$0 \$0 \$483,017 \$35,271 \$0 \$0 \$5 \$0 \$0 \$2,066 \$10,312 \$0 \$0 \$5 \$,815 \$197,557 \$586,699 \$3,443,485 \$73,350 \$296 \$0 \$4,3											
S7100019		\$0 \$2,879 \$0 \$0 \$0 \$2,879 \$0 \$0 \$0 \$2,879 \$0 \$0 \$0 \$2,879 \$0 \$0 \$0 \$2,879 \$0 \$0 \$0 \$2,879 \$0 \$0 \$0 \$2,879 \$0 \$0 \$0 \$2,879 \$0 \$0 \$0 \$2,879 \$0 \$0 \$0 \$2,879 \$0 \$0 \$0 \$2,879 \$0 \$0 \$2,879 \$0 \$0 \$0 \$2,879 \$0 \$0 \$0 \$2,879 \$0 \$0 \$0 \$2,879 \$0 \$0 \$0 \$2,879 \$0 \$0 \$0 \$2,879 \$0 \$0													
Athletic Field Phase I, Corsair Field (1)			\$0 \$0 \$300,380 \$2,579,095 \$0 \$0 \$0 \$2,879,475 \$27,332 \$43,815 \$197,557 \$252,736 \$279,173 \$26,563 \$0 \$0 \$827,176 \$0 \$0 \$0 \$23,411 \$57,585 \$640 \$296 \$0 \$81,932 \$0 \$0 \$9,871 \$42,374 \$565 \$0 \$0 \$52,810 \$0 \$0 \$0 \$483,017 \$35,271 \$0 \$0 \$518,288												
Legal		\$0	\$0	\$0	\$301	\$175	\$0	\$0	\$0	\$476					
Building & Additions		\$0	\$0	\$0	\$300,380	\$2,579,095	\$0	\$0	\$0	\$2,879,475					
Architect		\$0 \$0 \$300,380 \$2,579,095 \$0 \$0 \$2,879,475 \$27,332 \$43,815 \$197,557 \$252,736 \$279,173 \$26,563 \$0 \$0 \$827,176 \$0 \$0 \$0 \$23,411 \$57,585 \$640 \$296 \$0 \$81,932 \$0 \$0 \$0 \$9,871 \$42,374 \$565 \$0 \$0 \$52,810 \$0 \$0 \$0 \$0 \$483,017 \$35,271 \$0 \$0 \$518,288 \$0 \$0 \$0 \$0 \$2,066 \$10,312 \$0 \$0 \$12,378													
Inspection & Testing		\$0 \$0 \$30,380 \$2,579,095 \$0 \$0 \$2,879,475 \$27,332 \$43,815 \$197,557 \$252,736 \$279,173 \$26,563 \$0 \$0 \$827,176 \$0 \$0 \$0 \$0 \$23,411 \$57,585 \$640 \$296 \$0 \$81,932 \$0 \$0 \$0 \$0 \$9,871 \$42,374 \$565 \$0 \$0 \$81,932 \$0 \$0 \$0 \$9,871 \$42,374 \$565 \$0 \$0 \$52,810 \$0 \$0 \$0 \$0 \$0 \$483,017 \$35,271 \$0 \$0 \$518,288 \$0 \$0 \$0 \$0 \$2,066 \$10,312 \$0 \$12,378 \$27,332 \$43,815 \$197,557 \$586,699 \$3,443,485 \$73,350 \$296 \$0 \$4,372,535 .768 Received .530 \$67,530 \$0 \$4,372,535 \$197,557													
Project Management		\$0 \$0 \$9,871 \$42,374 \$565 \$0 \$0 \$52,810 \$0 \$0 \$0 \$0 \$483,017 \$35,271 \$0 \$0 \$518,288													
Cap Equipment		\$0 \$0 \$0 \$9,871 \$42,374 \$565 \$0 \$0 \$52,810 \$0 \$0 \$0 \$0 \$483,017 \$35,271 \$0 \$0 \$518,288													
Non-Cap Equipment		\$0 \$0 \$0 \$483,017 \$35,271 \$0 \$0 \$518,288													
Total		\$27,332	\$43,815	\$197,557	\$586,699	\$3,443,485	\$73,350	\$296	\$0	\$4,372,535					
Project Budget	\$4,440,768	Received													
Less Other Funding*	\$67,530														
Net	\$4,373,238														
Actual Measure S Expenditures	\$4,372,535	,535 Metropolitan Water District \$67,530 received													
Running Balance	\$703														

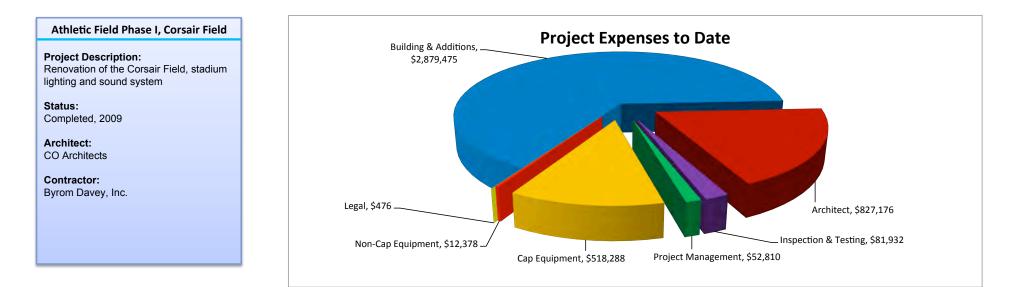

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12	Combined Totals
S7100038										
Athletic Field Phase I, John Adams (1A)										
Legal		\$0	\$0	\$0	\$75	\$0	\$0	\$0	\$0	\$75
Building & Additions		\$0	\$0	\$0	\$16,556	\$1,395,261	\$0	\$0	\$0	\$1,411,817
Architect		\$0	\$5,807	\$93,941	\$12,150	\$31,818	\$0	\$0	\$0	\$143,715
Inspection & Testing		\$0	\$2,874	\$3,207	\$0	\$49,984	\$0	\$0	\$0	\$56,066
Project Management		\$0	\$0	\$0	\$10,921	\$45,170	\$38	\$0	\$0	\$56,128
Cap Equipment		\$0	\$0	\$0	\$0	\$1,290,672	\$0	\$0	\$0	\$1,290,672
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$11,334	\$0	\$0	\$0	\$11,334
Total		\$0	\$8,681	\$97,148	\$39,701	\$2,824,239	\$38	\$0	\$0	\$2,969,807
Project Budget	\$2,970,807									
Less Other Funding	\$0									
Net	\$2,970,807									
Actual Measure S Expenditures	\$2,969,807									
Running Balance	\$1,000									

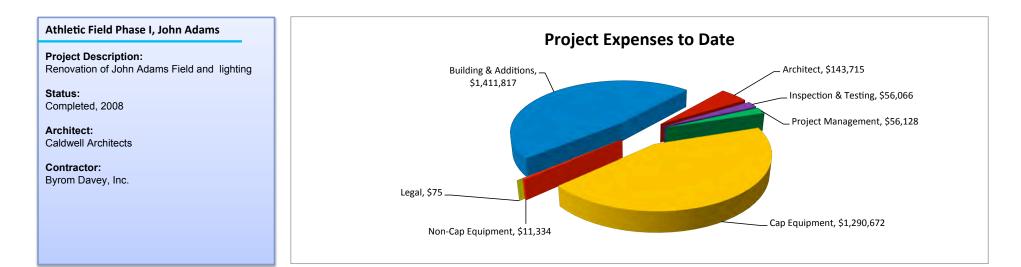

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12	Combined Totals						
			-													
S7100012																
Performing Arts Center (2)																
Consultants		\$0	\$0	\$0	\$121,790	\$76,639	\$0	\$0	\$0	\$198,429						
Other Contract Services		\$0	\$0	\$4,269	\$0	\$22,729	\$22	\$68	\$0	\$27,088						
Supplies		\$0	\$0	\$0	\$14,565	\$5,810	\$0	\$0	\$0	\$20,375						
Legal		\$0	\$0	\$34,329	\$275,667	\$492,731	\$15,629	\$0	\$0	\$818,356						
Advertising		\$0	\$0	\$0	\$320		\$0	\$0	\$0	\$320						
Building & Additions		\$7,784,151	\$10,292,986	\$8,930,813	\$2,991,903	\$1,629,990	\$50,000	\$0	\$0	\$31,679,843						
Architect		\$0	\$0 \$3,600 \$5,250 \$1,500 \$9,650 \$0 \$0 \$0 \$0 \$20,00													
Engineering		\$0	\$0 \$3,600 \$5,250 \$1,500 \$9,650 \$0 \$0 \$0 \$0 \$20,000													
Inspection & Testing		\$104,308	\$104,308 \$722,685 \$411,193 \$210,381 \$22,256 \$0 \$0 \$0 \$1,470,823													
Project Management		\$31,984	\$155,732	\$248,876	\$263,690	\$47,915	\$3,244	\$0	\$0	\$751,441						
Cap Equipment		\$0	\$0	\$130,218	\$292,565	\$342,693	\$0	\$0	\$0	\$765,476						
Non-Cap Equipment		\$0	\$0	\$15,124	\$93,106	\$220,455	\$0	\$0	\$0	\$328,685						
Total		\$7,920,443	\$11,986,315	\$9,962,528	\$4,677,797	\$2,992,455	\$69,003	\$2,030	\$0	\$37,610,571						
Project Budget	\$40,603,541	Received														
Less Other Funding*	\$2,992,576	\$2,992,576 * Other Funding Source:														
Net	\$37,610,965															
Actual Measure S Expenditures	\$37,610,571															
Running Balance	\$394															




Project Description:

Construction of a state-of-the-art 499 seat performing arts theater

Status: Completed, 2008

Architect: Renzo Zecchetto


Contractor: FTR International

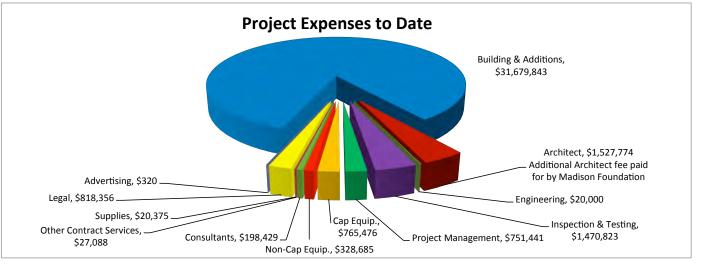

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	11/12	Combined Totals					
S7100033, S7100144													
S7100033, S7100144 Replacement Health/PE/Fitness Building (4)													
Supplies		\$0	\$0	\$0	\$0	\$0	\$163	\$0	\$0	\$163			
Legal	-	\$0 \$0	\$0 \$0	\$0 \$0		پ و \$1,413	\$75	\$0 \$0	\$0 \$0	\$1,488			
Other Contract Services		\$0 \$1,634	\$25,934	\$0 \$0		\$253	\$165	\$0 \$0	\$0 \$0	\$27,985			
Repair Facility		\$0 \$0	\$4,861	\$0 \$0		<u>\$2</u> 33 \$0	\$0	\$0 \$0	\$0 \$0	\$4,861			
Supplies		\$4,809	\$288	\$0		\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$5,097			
Building & Additions		\$0	\$0	\$0		\$112,410	\$526,552	\$0 \$0	\$0 \$0	\$638,962			
Architect		\$0	\$0	\$0		\$0	\$41.044	\$0	\$0	\$41,044			
Inspection & Testing		\$0	\$0	\$0		\$6,518	\$14,363	\$0	\$0	\$20,881			
Project Management		\$0	\$0	\$0		\$9,070	\$23,425	\$0	\$0	\$32,495			
Cap Equipment		\$0	\$0			\$0		\$17.613	\$0	\$17.613			
Total		\$6,443	\$31,083	\$0		\$129,663	\$605,787		\$0	\$790,589			
Project Budget	\$40,200,333	<i>, . ,</i>	,,- ••	, , , , , , , , , , , , , , , , , , ,	, , , , , , , , , , , , , , , , , , ,	,-,-		,, 	<i>**</i>	÷···,•••			
Less Other Funding*	\$35,384,240			* Other Fundin	g Source:								
Net	\$4,816,093				35,384,240 allo	cated							
Actual Measure S Expenditures	\$790,589												
Running Balance	\$4,025,504												
S7100045													
Early Childhood Development/Childcare (5)													
Consultants		\$0	\$0	\$0	\$9,200	\$0	\$0	\$0	\$0	\$9,200			
Project Management		\$0	\$0	\$0		\$0		\$1,246	\$1,078	\$2,324			
Total		\$0	\$0	\$0	\$9,200	\$0	\$0	\$1,246	\$1,078	\$11,524			
Project Budget	\$11,318,000	Received						· · · · ·					
Less Other Funding*	\$4,318,000	\$0		* Other Fundin									
Net	\$7,000,000			City of Santa M	/Ionica \$4,318,0	000 commited							
Actual Measure S Expenditures	\$11,524												
Running Balance	\$6,988,476												
P													
S7100077, S7100015													
Malibu Site Acquisition and Facilities (6)													
Consultants		\$0	\$0	\$0		\$30,000	\$0	\$0	\$0	\$30,000			
Legal		\$0	\$27,722	\$16,787		\$504	\$0	\$0	\$0	\$51,172			
Building & Additions		\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0			
Architect		\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0			
Inspection & Testing		\$4,388	\$3,750	\$141,462		\$0			\$0	\$149,600			
Project Management		\$0	\$0	\$220	\$0	\$0	\$0	\$2,886	\$2,044	\$5,150			
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0			
Storm/Waste Water Treatment Center		\$0	\$2,500,000	\$0		\$2,500,000	\$0	\$0	\$0	\$5,000,000			
Total		\$4,388	\$2,531,472	\$158,468	\$6,159	\$2,530,504	\$0	\$2,886	\$2,044	\$5,235,922			
Project Budget	\$31,069,031												
Less Other Funding*	\$6,069,031			* Other Fundin									
Net	\$25,000,000			Measure AA \$6	easure AA \$6,069,031 allocated								
Actual Measure S Expenditures	\$5,235,922												
Running Balance	\$19,764,078												

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12	Combined Totals
S7100043, S7100066										
Energy Efficiency Projects (7)										
Legal		\$0	\$0	\$0	\$0	\$988	\$0	\$0	\$0	\$988
Building & Additions		\$0	\$0	\$0	\$0	\$106,921	\$355,294	-\$180,342	\$0	\$281,873
Engineering		\$0	\$0	\$0	\$10,500	\$0		\$0	\$0	\$10,500
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$0	\$0	\$0	\$10,500	\$107,910	\$355,294	-\$180,342	\$0	\$293,361
Project Budget	\$1,293,570	Received								
Less Other Funding*	\$217,322	\$217,322		* Other Fundin	g Source:					
Net	\$1,076,248			SCE & The Ga	s Co. \$217,322	2 received				
Actual Measure S Expenditures	\$293,361									
Running Balance	\$782,887									
S7100091, S7100092										
Satellite Campus Parking Facilities and Roadway In	nprovements (8)								
Legal	-	\$0	\$0	\$0	\$300	\$175	\$0	\$0	\$0	\$475
Other Contract Services		\$0	\$0	\$0	\$300	\$0	\$0	\$0	\$0	\$300
Advertising		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Consultants		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$278,178	\$1,860,152	\$449,543	\$37,777	\$0	\$2,625,651
Architect		\$0	\$0	\$324,919	\$324,864	\$136,911	\$34,490	\$1,397	\$0	\$822,582
Inspection & Testing		\$0	\$0	\$0	\$31,100	\$185,947	\$28,218	\$360	\$0	\$245,626
Project Management		\$0	\$0	\$0	\$18,288	\$64,880	\$31,137	\$8,659	\$0	\$122,964
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$3,387	\$0	\$0	\$3,387
Total		\$0	\$0	\$324,919	\$653,031	\$2,248,065	\$546,775	\$48,194	\$0	\$3,820,983
Project Budget	\$4,875,000									
Less Other Funding	\$0									
Net	\$4,875,000									
Actual Measure S Expenditures	\$3,820,983									
Running Balance	\$1,054,017									

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12	Combined Totals					
S7100142															
Parking Garage and Grounds - Student Services (9)														
Supplies		\$0	\$0	\$0	\$0	\$1,745	\$0	\$0	\$648	\$2,393					
Consultants		\$0	\$0	\$0	\$0	\$20,700		\$0	\$0	\$20,700					
Legal		\$0	\$0	\$0	\$0	\$2,154	\$17,486	\$4,800	\$1,603	\$26,043					
Other Contract Services		\$0	\$0	\$0	\$0	\$1,508	\$10,952	\$1,986	\$0	\$14,446					
Building & Additions		\$0	\$0	\$0	\$0	\$2,555,940	\$5,925,152	\$78,717	\$152,523	\$8,712,331					
Architect		\$0													
Engineering		\$0	\$0 \$0 \$0 \$0 \$4,813 \$38,330 \$42,968 \$0 \$86,110												
Inspection & Testing		\$0	\$0	\$0	\$0	\$131,009	\$161,847	\$54,069	\$12,966	\$359,891					
Project Management		\$0	\$0	\$0	\$0	\$158,766	\$373,559	\$184,088	\$37,794	\$754,207					
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$14,393	\$0	\$0	\$14,393					
Total		\$0	\$0	\$0	\$2,266,766	\$5,550,689	\$6,541,719	\$403,737	\$205,533	\$14,968,445					
Project Budget	\$53,143,653	Received	ived												
Less Other Funding*	\$453,000	\$0		* Other Funding	g Source:										
Net	\$52,690,653			State of Califor	nia \$453,000 a	allocated									
Actual Measure S Expenditures	\$14,968,445														
Running Balance	\$37,722,208														

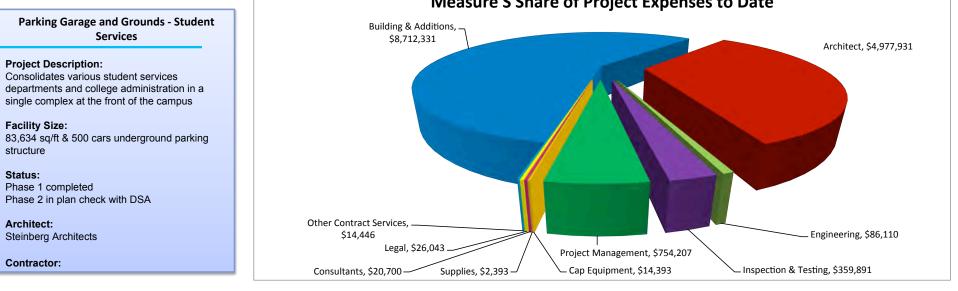

Measure S Share of Project Expenses to Date

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12	Combined Totals
S7100044										
Pico Promenade Improvements (10)										
Building & Additions		\$0	\$0	\$0		\$883,401	\$0	\$0	\$0	\$884,091
Architect		\$0	\$0	\$0	\$69,190	\$28,540	\$864	\$0	\$0	\$98,595
Inspection & Testing		\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$7,591
Project Management		\$0	\$0	\$0	\$2,185	\$25,548	\$0	\$0	\$0	\$27,733
Total		\$0	\$0	\$0	\$72,066	\$945,080	\$864	\$0	\$0	\$1,018,009
Project Budget	\$1,018,009									
Less Other Funding	\$0									
Net	\$1,018,009									
Actual Measure S Expenditures	\$1,018,009									
Running Balance	\$0									
S7100004										
Master Planning (11)										
Consultants		\$0	\$0	\$0	\$0	\$0		\$13,320	\$0	\$454,869
Printing		\$0	\$0					\$0	\$0	\$4,157
Advertising		\$0	\$0	\$0				\$0	\$0	\$3,000
Other Contract Services		\$0	\$0	\$0	\$0			\$200	\$0	\$642
Architect		\$0	\$0	\$0		\$0		\$24,736	\$0	\$217,094
Project Management		\$0	\$0					\$9,341	\$0	\$25,979
Filling Fees		\$0	\$0	\$0				\$2,842	\$0	\$2,842
Total		\$0	\$0	\$0	\$0	\$0	\$658,143	\$50,439	\$0	\$708,583
Project Budget	\$750,000									
Less Other Funding	\$0									
Net	\$750,000									
Actual Measure S Expenditures	\$708,583									
Running Balance	\$41,417									
S7100048										
Other Bond Related Expenses (12)							<u> </u>			<u> </u>
Supplies		\$0	\$0	\$0				\$0	\$0	\$3,638
Legal		\$0	\$0	\$0	\$0	\$0		\$15,649	\$775	\$25,341
Software License		\$0	\$0	\$0				\$1,997	\$0	\$1,997
Advertising		\$0	\$0	\$0	\$0			\$0	\$0	\$2,278
Other Contract Services		\$0 \$0	\$0 \$0				\$17,206	\$23,558	\$1,318	\$43,882
Moving Services		\$0	\$0	\$0				\$0	\$0	\$400
Project Management		\$0 \$0	\$0	\$0 \$0	\$0 \$0			\$13,179	\$1,820	\$32,746
Cap Equipment		\$0	\$0	\$0				\$10,086	\$0	\$10,086
Non-Cap Equipment		\$0	\$0	\$0				\$2,860	\$1,418	\$4,278
Total Device the Durdget	#000 70 (\$0	\$0	\$0	\$0	\$1,800	\$50,185	\$67,328	\$5,332	\$124,645
Project Budget	\$662,764									
Less Other Funding	\$0									
Net	\$662,764									
Actual Measure S Expenditures	\$124,645									
Running Balance	\$538,119									

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12	Combined Totals
S7100049										
Adv Architecture Related Exp for AA (13)										
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0 \$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$45,734	-\$45,734	\$0	\$0	\$0
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$0	\$0	\$0	\$0	\$45,734	-\$45,734	\$0	\$0	\$0
Project Budget	\$0									
Less Other Funding	\$0									
Net	\$0									
Actual Measure S Expenditures	\$0									
Running Balance	\$0									
S7100057										
Real Property Acquisition (14)										
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$18,721	\$0	\$0	\$18,721
Architect		\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0	\$10,721	\$0	\$0 \$0	\$0
Engineering		\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0
Inspection & Testing		\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0	\$6,336	\$0 \$0	\$0 \$0	\$6,336
Project Management		\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$20,540	\$0 \$0	\$0 \$0	\$20,540
Total		\$0 \$0	\$0 \$0	\$0 \$0		\$0 \$0	\$45,597	\$0 \$0	\$0 \$0	\$45,597
Project Budget	\$50,000		φU	φU	φU	φU	φ 4 5,597	φU	φU	\$45,557
Less Other Funding	<u>\$30,000</u> \$0									
Net	\$50,000									
Actual Measure S Expenditures	\$45,597									
	\$4,403									
Running Balance	φ4,403									

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12	Combined Totals
S7100072										
Campus Signage (15)										
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$303	\$0	\$303
Consultants		\$0	\$0	\$0	\$0	\$0	\$32,225	\$23,725	\$0	\$55,950
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$187	\$0	\$187
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$638	\$0	\$638
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$22,953	\$0	\$22,953
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$156,258	\$0	\$156,258
Total		\$0	\$0	\$0	\$0	\$0	\$32,225	\$204,064	\$0	\$236,289
Project Budget	\$606,223									
Less Other Funding	\$0									
Net	\$606,223									
Actual Measure S Expenditures	\$236,289									
Running Balance	\$369,934									

	Grand Total	\$7,958,606	\$14,601,366	\$10,740,621	\$8,321,918	\$20,819,624	\$8,933,245	\$617,492	\$213,987	\$72,206,859
--	-------------	-------------	--------------	--------------	-------------	--------------	-------------	-----------	-----------	--------------


SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure AA Project Schedule

As of September 30, 2011

	Project Name	Completion	20	11		2012	2013		20	014		20	15	201	16
101	Environmental Performance - Central Plant Connections	September 2014													
102	Infrastructure & Technology - Information Technology Relocation	November 2013													
103	Media and Technology Complex - Academy Site	October 2014													
104	Replacement Health/PE/Fitness/Dance Building with Central Plant	May 2014													
105	Drescher - Academic Modernization, Bookstore, Pico Promenade	December 2016												· · ·	
106	Replacement Math and Science Extension Building	December 2016													
107	Madison East Wing Seismic Upgrade	August 2013									Τ				
108	Renovation of Corsair Stadium	Not Scheduled									Τ				
109	Career Opportunity and Advancement Center (Bundy)	Not Scheduled									Τ				
110	Malibu Center	Not Scheduled									Τ				
111	Business & Facilities Infrastructure	On-Going									Τ				
112	Master Planning, Program Management, Overhead	On-Going													
113	Energy Efficiency Projects	On-Going									Τ				
114	Community Classroom & Facility Projects	December 2011									Τ				
115	Real Property Acquisition	On-Going									T				
116	Roadways, Walkways, Grounds, Parking Lots, and Garages	On-Going									T				
				lr	ı Pla	nning	In Con	stru	ctior	1					


SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure AA Bond Budget As of September 30, 2011

	Project Name	Completion	Project Budget	Measure AA Allocation	Other Funding	Measure AA Expenditures as of 9/30/11	Measure AA Expenditures as of 6/30/11	Measure AA Expenditures Last Period	Total Measure AA Remaining
101	Environmental Performance - Central Plant Connections	September 2014	\$4,882,119	\$4,882,119	\$0	\$79,070	\$66,148	\$12,922	\$4,803,049
102	Infrastructure & Technology - Information Technology Relocation	November 2013	\$13,287,218	\$13,287,218	\$0	\$795,905	\$716,143	\$79,762	\$12,491,313
103	Media and Technology Complex - Academy Site	October 2014	\$61,480,824	\$57,700,824	\$3,780,000	\$5,204,123	\$5,127,133	\$76,990	\$52,496,701
104	Replacement Health/PE/Fitness/ Dance Building with Central Plant	May 2014	\$40,200,333	\$35,384,240	\$4,816,093	\$2,047,442	\$2,019,034	\$28,408	\$33,336,798
105	Drescher - Academic Modernization, Bookstore, Pico Promenade	December 2016	\$34,026,480	\$34,026,480	\$0	\$0	\$0	\$0	\$34,026,480
106	Replacement Math and Science Extension Building	December 2016	\$108,103,000	\$68,259,000	\$40,134,000	\$0	\$0	\$0	\$68,259,000
107	Madison East Wing Seismic Upgrade	August 2013	\$12,292,000	\$12,292,000	\$0	\$716,850	\$629,426	\$87,424	\$11,575,150
108	Renovation of Corsair Stadium	Not Scheduled	\$11,203,000	\$11,203,000	\$0	\$35,299	\$35,299	\$0	\$11,167,701
109	Career Opportunity and Advancement Center (Bundy)	Not Scheduled	\$41,391,000	\$29,384,000	\$12,007,000	\$0	\$0	\$0	\$29,384,000
110	Malibu Center	Not Scheduled	\$31,069,031	\$6,069,031	\$25,000,000	\$0	\$0	\$0	\$6,069,031
111	Business & Facilities Infrastructure	On-Going	\$6,140,952	\$6,140,952	\$0	\$149,002	\$133,238	\$15,764	\$5,991,950
112	Master Planning, Program Management, Overhead	On-Going	\$1,650,000	\$1,650,000	\$0	\$0	\$0	\$0	\$1,650,000
113	Energy Efficiency Projects	On-Going	\$4,650,136	\$4,150,136	\$0	\$0	\$0	\$0	\$4,150,136
114	Community Classroom & Facility Projects	December 2011	\$3,221,000	\$3,221,000	\$0	\$1,288,838	\$863,734	\$425,104	\$1,932,162
115	Real Property Acquisition	On-Going	\$6,000,000	\$6,000,000	\$0	\$5,764,895	\$5,757,895	\$7,000	\$235,105
116	Roadways, Walkways, Grounds, Parking Lots, and Garages	On-Going	\$350,000	\$350,000	\$0	\$268,591	\$251,152	\$17,439	\$81,409
117	Infrastructure & Technology - Technology	On-Going	\$500,000	\$500,000	\$0	\$235,840	\$216,896	\$18,944	\$264,160
118	Infrastructure & Technology - Utility	On-Going	\$500,000	\$500,000	\$0	\$20,219	\$20,219	\$0	\$479,781
	Project Totals		\$380,947,093	\$295,000,000	\$85,737,093	\$16,606,074	\$15,836,317	\$769,757	\$278,393,926

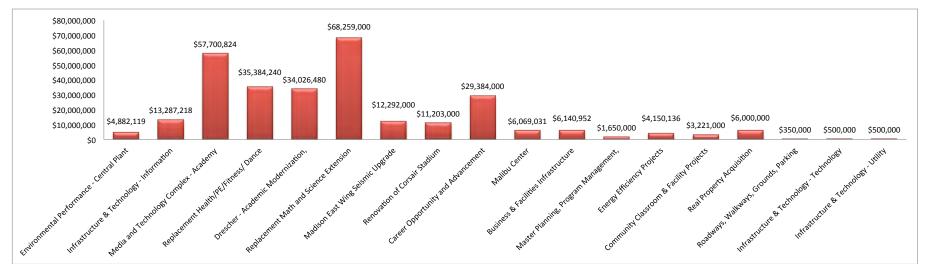


Projects	Budget	09/10 Final	10/11 Final	11/12	Combined Totals
AA 7100062					
Environmental Performance - Central Plant Connections (101)					
Legal		\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0
Consultants		\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0
Architect		\$0	\$385	\$0	\$385
Engineering		\$48,500	\$0	\$0	\$48,500
Inspection & Testing		\$0	\$0	\$0	\$0
Project Management		\$0	\$17,263	\$12,922	\$30,185
Cap Equipment		\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0
Total		\$48,500	\$17,648	\$12,922	\$79,070
Project Budget	\$4,882,119				
Less Other Funding	\$0				
Net	\$4,882,119				
Actual Measure AA Expenditures	\$79,070				
Running Balance	\$4,803,049				


Projects	Budget	09/10 Final	10/11 Final	11/12	Combined Totals
AA 7100063					
Infrastructure & Technology - IT Relocation (102)					
Legal		\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$1,679	\$1,679
Supplies		\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0
Architect		\$105,049	\$482,261	\$60,792	\$648,101
Engineering		\$0	\$0	\$2,198	\$2,198
Inspection & Testing		\$10,291	\$8,793	\$2,171	\$21,255
Project Management		\$33,460	\$76,290	\$12,922	\$122,672
Cap Equipment		\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0
Total		\$148,800	\$567,344	\$79,761	\$795,905
Project Budget	\$13,287,218				
Less Other Funding	\$0				
Net	\$13,287,218				
Actual Measure AA Expenditures	\$795,905				
Running Balance	\$12,491,313				

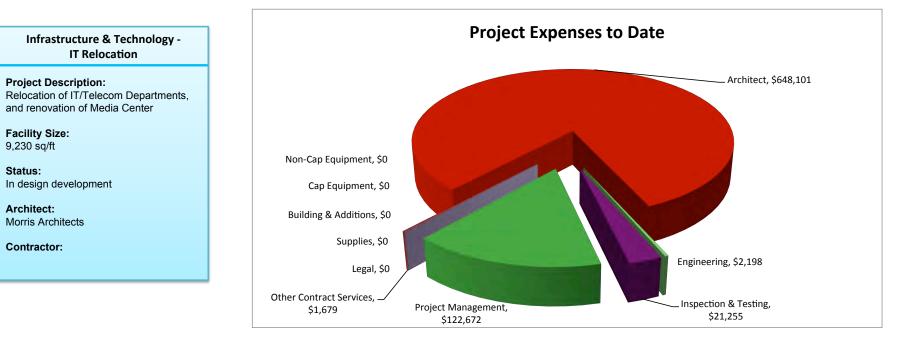


Projects	Budget	09/10 Final	10/11 Final	11/12	Combined Totals
AA 7100061					
Media and Technology Complex - Academy Site (103)					
Consultants		\$0	\$0	\$0	\$0
Supplies		\$0	\$0	\$0	\$0
Legal		\$16,903	\$0	\$0	\$16,903
Other Contract Services		\$3,993	\$5,763	\$2,778	\$12,534
Advertising		\$0	\$0	\$0	\$0
Building & Additions		\$0	\$538	\$0	\$538
Architect		\$2,097,553	\$2,508,588	\$35,000	\$4,641,141
Engineering		\$16,459	\$29,293	\$118	\$45,870
Inspection & Testing		\$64,905	\$27,527	\$0	\$92,432
Project Management		\$121,786	\$233,826	\$39,094	\$394,705
Cap Equipment		\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0
Total		\$2,321,599	\$2,805,534	\$76,990	\$5,204,123
Project Budget	\$61,480,824	Received			
Less Other Funding*	\$3,780,000	\$803,412			
Net		1 * Other Funding Source:			
Actual Measure AA Expenditures	\$5,204,123	3 KCRW Foundation \$3,780,000 commited,			
Running Balance	\$52,496,701	\$803,412 received	b		

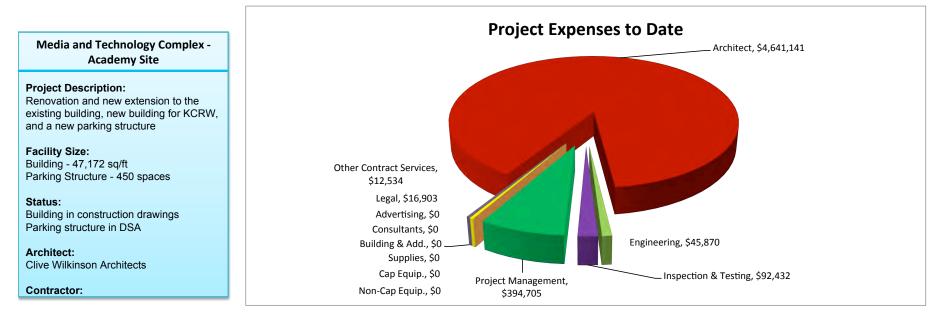

Projects	Budget	09/10 Final	10/11 Final	11/12	Combined Totals	
AA 7100060						
Repl. Health/PE/Fitness/Dance Building with Central Plant (104)						
Consultants		\$0	\$0	\$0	\$0	
Supplies		\$0	\$0	\$0	\$0	
Other Contract Services		\$120	\$38	\$0	\$158	
Building & Additions		\$0	\$0	\$0	\$0	
Architect		\$256,076	\$1,568,564	\$9,335	\$1,833,975	
Engineering		\$0	\$8,507	\$417	\$8,924	
Inspection & Testing		\$36,892	\$490	\$0	\$37,382	
Project Management		\$34,968	\$113,379	\$18,655	\$167,002	
Total		\$328,056	\$1,690,978	\$28,408	\$2,047,442	
Project Budget	\$40,200,333					
Less Other Funding*	\$4,816,093	3 * Other Funding Source:				
Net	\$35,384,240	0 Measure S \$4,816,093 allocated				
Actual Measure AA Expenditures	\$2,047,442					
Running Balance	\$33,336,798					

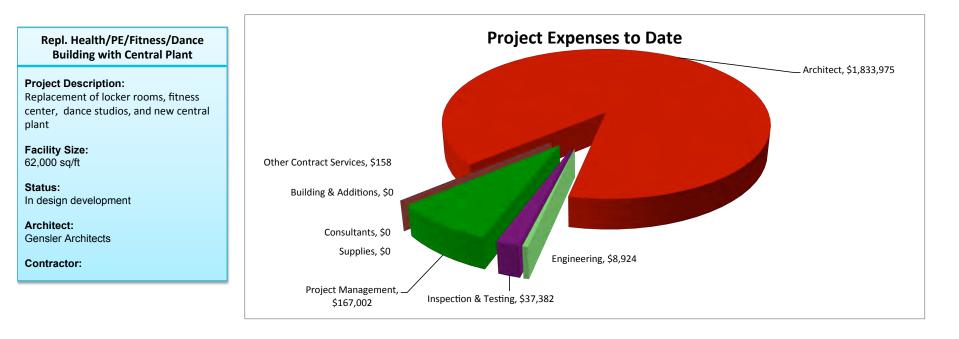

Projects	Budget	09/10 Final	10/11 Final	11/12	Combined Totals
AA 7100047					
Madison East Wing Seismic Upgrade (107)					
Consultants		\$0	\$0	\$0	\$0
Supplies		\$0	\$0	\$0	\$0
Legal		\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$364	\$0	\$364
Building & Additions		\$0	\$656	\$0	\$656
Architect		\$76,073	\$398,050	\$57,898	\$532,021
Engineering		\$0	\$0	\$96	\$96
Inspection & Testing		\$0	\$19,848	\$7,800	\$27,648
Project Management		\$5,557	\$128,878	\$21,630	\$156,065
Total		\$81,630	\$547,796	\$87,424	\$716,850
Project Budget	\$12,292,000				
Less Other Funding	\$0				
Net	\$12,292,000				
Actual Measure AA Expenditures	\$716,850				
Running Balance	\$11,575,150				

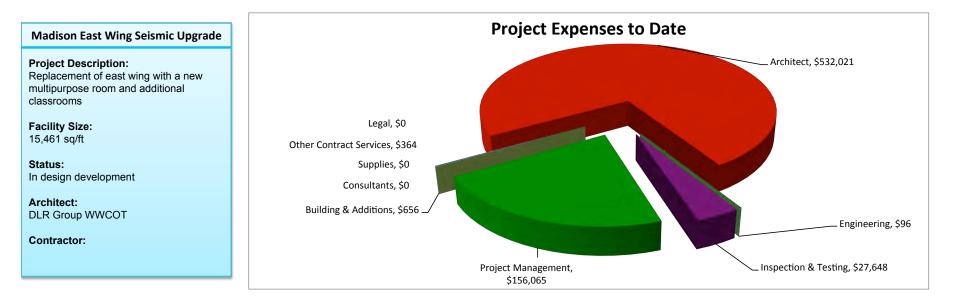

Projects	Budget	09/10 Final	10/11 Final	11/12	Combined Totals
AA 7100068					
Renovation to Corsair Stadium (108)		<u>*</u>	* 0	* 0	*0
Other Contract Services		\$0	\$0	\$0	\$0
Building & Additions		\$0 \$0	\$0	\$0	\$0
Architect Engineering		\$0 \$0	\$30,759 \$0	\$0 \$0	\$30,759
Inspection & Testing		\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0
Project Management		\$0 \$0	\$4,540	\$0 \$0	\$0 \$4,540
Total		\$0 \$0	\$35,299	\$0 \$0	\$35,299
Project Budget	\$11,203,000	ψυ	ψ00,200	ΨΟ	ψ00,200
Less Other Funding	\$0				
Net	\$11,203,000				
Actual Measure AA Expenditures	\$35,299				
Running Balance	\$11,167,701				
AA 7100067					
Business & Facilities Infrastructure (111)					
Other Contract Services		\$0	\$6,289	\$0	\$6,289
Building & Additions		\$0	\$34,672	\$0	\$34,672
Architect		\$0	\$0	\$0	\$0
Engineering		\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0
Project Management		\$0	\$3,073	\$15,764	\$18,837
Non-Cap Equipment		\$0	\$89,204	\$0	\$89,204
Total		\$0	\$133,238	\$15,764	\$149,002
Project Budget	\$6,140,952				
Less Other Funding	\$0				
Net	\$6,140,952				
Actual Measure AA Expenditures	\$149,002				
Running Balance	\$5,991,950				
AA 7100064					
Community Classroom & Facility Projects (114)					
Other Contract Services		\$0	\$3,720	\$1,454	\$5,174
Building & Additions		\$0 \$0	\$434,578	\$349,577	\$784,155
Architect		\$0	\$263,833	\$7.003	\$270,836
Engineering		\$0	\$3,220	\$945	\$4,165
Inspection & Testing		\$0	\$41,002	\$31,249	\$72,251
Project Management		\$135	\$117,247	\$34,876	\$152,258
Total	†	\$135	\$863,599	\$425,104	\$1,288,838
Project Budget	\$3,221,000	,,	,,	, -,	, , , , ,,,,,,,,,
Less Other Funding	\$0				
Net	\$3,221,000				
Actual Measure AA Expenditures	\$1,288,838				
Running Balance	\$1,932,162				

Projects	Budget	09/10 Final	10/11 Final	11/12	Combined Totals
/			•		
AA 7100057					
Real Property Acquisition (115)					
Legal		\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$39	\$7,000	\$7,039
Site Acquisition		\$1,739,979	\$4,001,204	\$0	\$5,741,182
Inspection & Testing		\$8,689	\$7,986	\$0	\$16,674
Project Management		\$0	\$0	\$0	\$0
Total		\$1,748,667	\$4,009,228	\$7,000	\$5,764,895
Project Budget	\$6,000,000				
Less Other Funding	\$0				
Net	\$6,000,000				
Actual Measure AA Expenditures	\$5,764,895				
Running Balance	\$235,105				
	•				
AA 7100058					
Roadways, Walkways, Grounds, Parking Lots, and Garages (116)					
Legal		\$0	\$0	\$0	\$0
Other Contract Services		\$218	\$770	\$122	\$1,110
Building & Additions		\$185,345	\$6,731	\$0	\$192,076
Inspection & Testing		\$13,380	\$7,865	\$0	\$21,245
Project Management		\$24,404	\$12,439	\$17,318	\$54,161
Total		\$223,347	\$27,804	\$17,440	\$268,591
Project Budget	\$350,000				
Less Other Funding	\$0				
Net	\$350,000				
Actual Measure AA Expenditures	\$268,591				
Running Balance	\$81,409				
<u> </u>	•				
AA 7100069					
Infrastructure & Technology - Technology (117)					
Maintenance Contract		\$0	\$9,472	\$18,944	\$28,417
Building & Additions		\$0	\$0	\$0	\$0
Architect		\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0
Project Management		\$0	\$0	\$0	\$0
Cap Equipment		\$0	\$207,423	\$0	\$207,423
Non-Cap Equipment		\$0	\$0	\$0	\$0
Total		\$0	\$216,896	\$18,944	\$235,840
Project Budget	\$500,000	· •	· · ·	· · ·	
Less Other Funding	\$0				
Net	\$500,000				
Actual Measure AA Expenditures	\$235,840				
Running Balance	\$264,160				

Projects	Budget	09/10 Final	10/11 Final	11/12	Combined Totals
AA 7100069					
Infrastructure & Technology - Utility (118)					
Sofeware License		\$0	\$12,000	\$0	\$12,000
Legal		\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0
Architect		\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$4,979	\$0	\$4,979
Project Management		\$0	\$3,240	\$0	\$3,240
Cap Equipment		\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0
Total		\$0	\$20,219	\$0	\$20,219
Project Budget	\$500,000				
Less Other Funding	\$0				
Net	\$500,000				
Actual Measure AA Expenditures	\$20,219				
Running Balance	\$479,781				
Grand Total		\$4,900,734	\$10,935,584	\$769,757	\$16,606,074


SANTA MONICA COMMUNITY COLLEGE DISTRICT Bond Sales / Expenses Report As of September 30, 2011

Measure U Bond \$160,000,000	
Bond Issue Date	Amount
2002	\$25,000,000
2004	\$21,999,971
2005	\$89,999,923
2007	\$11,999,987
2010	\$10,998,992
Total Available	\$159,998,873
Expenses as of 9-30-11	\$142,482,019
Total Available Remaining	\$17,516,854
Unsold Bond Amount	\$1,127
Total Available as of 10-1-11	\$17,517,981

Measure S Bond \$143,500,000 (1)		
Bond Issue Date		Amount
	2005	\$58,000,000
	2007	\$8,500,000
	2009	\$56,997,857
Total Available		\$123,497,857
Expenses as of 9-30-11		\$72,206,860
Total Available Remaining		\$51,290,997
Unsold Bond Amount		\$20,002,143
Total Available as of 10-1-11		\$71,293,140

Measure AA Bond \$295,000,000	
Bond Issue Date	Amount
2010	\$100,000,000
Total Available	\$100,000,000
Expenses as of 9-30-11	\$16,606,074
Total Available Remaining	\$83,393,926
Unsold Bond Amount	\$195,000,000
Total Available as of 10-1-11	\$278,393,926

Total Bond	\$598,500,000
Total Available	\$383,496,730
Total Expenses as of 9-30-11	\$231,294,953
Total Available Remaining	\$152,201,777
Total Unsold Bond	\$215,003,270

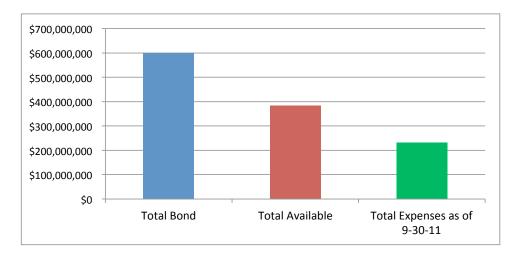

Interest	Measure U	Measure S	Measure AA
As of 6-30-11	\$5,996,729	\$8,106,718	\$1,715,719
Arbitrage Payment as of 6-30-11	\$0	\$393,004	\$0
Available Interest as of 6-30-11	\$5,996,729	\$7,713,714	\$1,715,719

	Cost of Issuance Refund	Measure U	Measure S
)	As of 6-30-11	\$20,688	\$35,575
`			

(1) Original Bond \$135,000,000.00, refunding on 2-15-07 received additional \$8,500,000.00
