

Santa Monica Community College District

Citizens' Bond Oversight Committee MEETING – JANUARY 19, 2011 AGENDA

A meeting of the Santa Monica Community College District Citizens' Bond Oversight Committee will be held on Wednesday, **January 19, 2011 at 8 a.m.**

The meeting will be held in Drescher Hall 300-E (the Loft) at Santa Monica College, 1900 Pico Boulevard, Santa Monica, California.

I. CALL TO ORDER

2. ROLL CALL

Bruce Sultan, Chair
Paul Leoni, Vice-Chair
Deborah Arveson
Clarence Chapman
Todd Flora
Tiffany Inabu
Corin Kahn
Nimish Patel
Christine Thornton

3. APPROVAL OF MINUTES

Citizens' Bond Oversight Committee meeting of October 20, 2010 (enclosed)

4. INTRODUCTION OF NEW MEMBER

At its meeting on January 11, 2011, the SMCCD Board of Trustees appointed Tiffany Inabu as the student representative on the Citizens' Bond Oversight Committee.

5. CONFLICT OF INTEREST FORMS

Please sign and date the enclosed Conflict of Interest form and bring it with you to the meeting.

<u>6.</u> <u>REPORTS and DISCUSSION</u> (reports enclosed)

Measure U

- Project Schedule
- Budget
- Expenditures

Measure S

- Project Schedule
- Budget
- Expenditures

Measure AA

- Project Schedule
- Budget

Bond Sales/Expenses Report

7. PUBLIC COMMENTS

8. SCHEDULE OF MEETINGS, 2010-2011

Wednesdays at 8 a.m. April 20, 2011

8. ADJOURNMENT

The next meeting of the Citizens' Bond Oversight Committee will be held on Wednesday, April 20, 2011 at 8 a.m. (location to be determined).



Citizens' Bond Oversight Committee MEETING – October 20, 2010 MINUTES

A meeting of the Santa Monica Community College District Citizens' Bond Oversight Committee was held on Wednesday, October 20, 2010 in Drescher Hall Room 300-E (the Loft) at Santa Monica College, 1900 Pico Boulevard, Santa Monica, California.

I. CALL TO ORDER - 8:09 a.m.

2. ROLL CALL

Bruce Sultan, Chair - Present
Paul Leoni, Vice-Chair - Present
Deborah Arvesen - Not Present
Clarence Chapman - Present
Todd Flora - Present
Cameron Henton - Present
Corin Kahn - Present
Nimish Patel - Present
Christine Thornton - Present

Others Present:

Greg Brown, Director of Facilities and Planning
Don Girard, Senior Director, Government Relations/Institutional Communications
Bob Isomoto, Vice-President, Business/Administration
Lee Paul, LPI Inc.
Lisa Rose, Committee Coordinator
Charlie Yen, Director, Contracts

3. <u>APPROVAL OF MINUTES – July 21, 2010</u>

Motion was made by Deborah Arvesen and seconded by Clarence Chapman to approve the minutes of July 21, 2010.

Unanimously approved

4. CITIZENS' BOND OVERSIGHT COMMITTEE ANNUAL REPORT, 2009-2010

Motion was made by Paul Leoni and seconded by Christine Thornton to approve the Annual Report 2009-2010 as presented. It was noted that the financial statements included in the Annual Report have not yet been audited; the official audit report for 2009-2010 will be presented to the Committee in January, 2011. *Unanimously approved*

Operation and Maintenance Budgets for Bond Projects/Facilities

In response to a question about financial support for sustaining facilities after they are built, it was reported that the Board evaluates the operational costs of a new project prior to the award of contract for the project. The policy was established in 2004 with the approval of the Measure S bond program. The AET/KCRW project was cited as an example of SMC's evaluation process.

5. OVERVIEW OF FACILITIES MASTER PLAN

The SMCCD Board of Trustees approved the Facilities Master Plan in August, 2010. The following projects are in progress and/or design.

Main campus

- Information Technology Relocation
- Health/Physical Education/Fitness/Central Plant
- Math/Science Extension/Replacement
- Corsair Stadium
- Drescher Hall Renovation

Academy of Entertainment and Technology

- New Parking Structure
- Addition to existing AET Building
- KCRW

Performing Arts Campus

East Wing Replacement Building

Other Projects

- Child Development Center
- Malibu Campus
- Bundy Campus West Building Classrooms
- Bundy Career Opportunity Center

6. REPORTS and DISCUSSION

<u>Bond Construction Program Reports, October 2010</u> (quarterly reports will be sent to the Committee)

Measures U, S and AA (reports included with agenda)

Measure U - expenditures last quarter were \$11,612 (architecture fees for Student Services Project)

Measure S - expenditures last quarter were \$236,231

Measure AA - expenditures last quarter were \$1,071.0002 (mostly architecture fees)

Update on Malibu Site

The District is still in negotiations on the lease agreement with the County of Los Angeles to build a satellite campus on the county-owned land in the Malibu Civic Center.

Bond Sales/Expenses Report

Total available bond funds remaining = \$162,713,711

7. SCHEDULE OF MEETINGS, 2010-2011

Wednesdays at 8 a.m. January 19, 2011 April 20, 2011

8. ADJOURNMENT - 9:26 p.m.

The next meeting of the Citizens' Bond Oversight Committee will be held on Wednesday, January 19, 2011 at 8 a.m. at a Santa Monica College location


The SMC Bond Program website can be accessed at: www.smcbondprogram.com

SANTA MONICA COMMUNITY COLLEGE DISTRICT

Measure U Bond Budget

As of December 31, 2010

	Project Name	Completion	Project Budget	Measure U Allocation	Other Funding	Measure U Expenditures as of 12/31/10	Measure U Expenditures as of 9/30/10	Measure U Expenditures Last Period	Total Measure U Remaining
Α	Purchase of BAE Airport Site	Completed	\$30,280,878	\$30,280,878	\$0	\$30,280,878	\$30,280,878	\$0	\$0
В	Emeritus College Facility	Completed	\$9,603,782	\$8,909,940	\$693,842	\$8,909,940	\$8,909,940	\$0	\$0
С	Purchase of 1738 Pearl Street	Completed	\$749,208	\$749,208	\$0	\$749,208	\$749,208	\$0	\$0
D	PE Temp. Bldg. Replacement	Completed	\$2,797,033	\$2,797,033	\$0	\$2,797,033	\$2,797,033	\$0	\$0
Е	Remodel Library Village for Math	Completed	\$1,458,690	\$1,458,690	\$0	\$1,458,690	\$1,458,690	\$0	\$0
F	SM Airport Campus Site Improvements	Completed	\$4,170,264	\$4,170,264	\$0	\$4,170,264	\$4,170,264	\$0	\$0
G	SM Airport Campus West Building	Completed	\$19,709,741	\$19,709,741	\$0	\$19,709,741	\$19,709,741	\$0	\$0
Н	Theater Arts Renovation	Completed	\$19,497,949	\$19,497,949	\$0	\$19,496,949	\$19,496,949	\$0	\$1,000
1	Earthquake Rpl. Liberal Arts North	Completed	\$13,473,652	\$6,352,752	\$7,120,900	\$8,467,972	\$8,467,972	\$0	-\$2,115,220
J	Music Complex	Completed	\$4,623,547	\$2,005,434	\$2,618,113	\$2,004,434	\$2,004,434	\$0	\$1,000
K	Earthquake Rpl. Liberal Arts South	Completed	\$16,733,220	\$6,108,150	\$10,625,070	\$6,108,150	\$6,108,150	\$0	\$0
L	Shuttle Replacement Parking	Completed	\$18,969,509	\$18,969,509	\$0	\$18,969,509	\$18,969,509	\$0	\$0
М	North Quad Plaza	Completed	\$11,378,981	\$11,378,981	\$0	\$11,377,981	\$11,377,981	\$0	\$1,000
Ν	Letters & Sci Demo/Restore	Move to AA	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0	Student Services Building	May 2014	\$53,521,913	\$20,813,678	\$32,708,239	\$2,071,619	\$2,052,198	\$19,421	\$18,742,059
Р	Science Complex Addition	Move to AA	\$308,336	\$308,336	\$0	\$308,336	\$308,336	\$0	\$0
Q	Infrastructure & Safety	Completed	\$4,042,284	\$4,042,284	\$0	\$3,890,801	\$3,890,801	\$0	\$151,483
R	Restroom Improvements	Completed	\$17,501	\$17,501	\$0	\$17,501	\$17,501	\$0	\$0
S	Master Planning	Completed	\$2,110,430	\$2,110,430	\$0	\$2,110,430	\$2,110,430	\$0	\$0
Т	14th and Pico Project	On Hold	\$319,242	\$319,242	\$0	\$319,242	\$319,242	\$0	\$0
	Project Totals		\$213,766,164	\$160,000,000	\$53,766,164	\$143,218,678	\$143,199,257	\$19,421	\$16,781,322

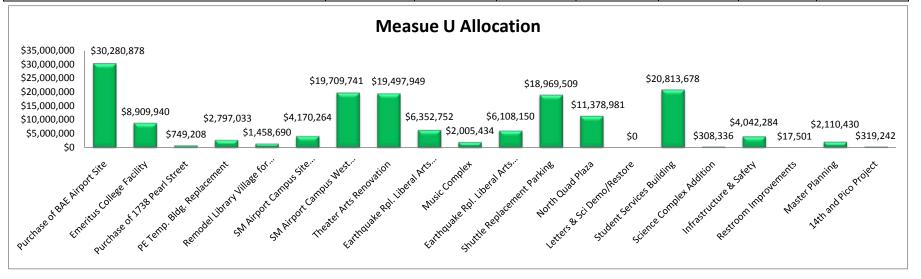

SANTA MONICA COMMUNITY COLLEGE DISTRICT

Measure U Project Schedule As of December 31, 2010

	Project Name	Completion	2010)		201	11	20	012		2013	3	2014
Α	Purchase of BAE Airport Site	Completed											
В	Emeritus College Facility	Completed											
С	Purchase of 1738 Pearl Street	Completed											
D	PE Temp. Bldg. Replacement	Completed											
Е	Remodel Library Village for Math	Completed											
F	SM Airport Campus Site Improvements	Completed											
G	SM Airport Campus West Building	Completed											
Н	Theater Arts Renovation	Completed											
- 1	Earthquake Rpl. Liberal Arts North	Completed											
J	Music Complex	Completed											
K	Earthquake Rpl. Liberal Arts South	Completed											
L	Shuttle Replacement Parking	Completed											
М	North Quad Plaza	Completed											
N	Letters & Sci Demo/Restore	Move to AA											
0	Student Services Building	May 2014											
Р	Science Complex Addition	Move to AA											
Q	Infrastructure & Safety	Completed											
R	Restroom Improvements	Completed											
S	Master Planning	Completed											
Т	14th and Pico Project	On Hold											
	* CM Airport Compus also known as Dur	du Cito	1			4 01 · ~ ·	tion						
	* SM Airport Campus also known as Bun	ay Site	ın		วทร	truct	uon						

FUND 42.2 As of December 31, 2010

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
117400040	ı							T	1		1
U7100010											
Purchase of BAE Airport Site (A)		ФО.	Φ0	Φ0	\$00,000,0 7 0	# 0	# 0	Φ0	*	Φ0	#00.000.070
Site Acquisition		\$0 \$0	\$0		\$30,280,878						\$30,280,878
Total	#00.000.070	\$0	\$0	\$0	\$30,280,878	\$0	\$0	\$0	\$0	\$0	\$30,280,878
Project Budget	\$30,280,878										
Less Other Funding	\$0										
Net	\$30,280,878										
Actual Measure U Expenditures	\$30,280,878										
Running Balance	\$0										
1174,00000	<u> </u>						Π	ı	ı	1	
U7100028											
Emeritus College Facility (B)		#0.050.075	ФО.		ФО.	# 0	CO	C O	C O		#0.050.075
Site Acquisition		\$8,658,675	\$0	\$0 \$20,421	\$0 \$0	\$0 \$0					\$8,658,675
Legal		\$14,649	\$3,009		\$0 \$0	\$0		\$0	\$0	\$0	\$38,078
Architect		\$93,735	\$27,831	\$161	\$0	\$0	\$0	\$0	\$0	\$0	\$121,727
Engineering		\$18,400	\$0	\$0	\$0	\$0	\$0				\$18,400
Supply		\$0	\$4,461	\$0	\$0	\$0					\$4,461
Building & Additions		\$0	\$17,496	\$0	\$4,000	\$0	\$0	\$0	\$0	\$0	\$21,496
Cap Equipment		\$0	\$49,406	\$0	\$0	\$0					\$49,406
Non-Cap Equipment		\$0	-\$2,197	\$0	-\$108	\$0					-\$2,305
Total		\$8,785,459	\$100,007	\$20,582	\$3,892	\$0	\$0	\$0	\$0	\$0	\$8,909,940
Project Budget	\$9,603,782	Received									
Less Other Funding*	\$693,842	\$693,842		* Other Fundi	ng Source:						
Net	\$8,909,940			Emeritus Col	lege Foundation	on \$693,842					
Actual Measure U Expenditures	\$8,909,940										
Running Balance	\$0										
U7100006											
1738 Pearl Street (C)											
Site Acquisition		\$0	\$704,534	\$0	\$0	\$0				\$0	\$704,534
Site Improvement		\$0	\$3,250	\$0	\$0	\$0					\$3,250
Building & Additions		\$0	\$41,424	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$41,424
Total		\$0	\$749,208	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$749,208
Project Budget	\$749,208								•		
Less Other Funding	\$0										
Net	\$749,208										
Actual Measure U Expenditures	\$749,208										
Running Balance	\$0										

1/7/2011 1 of 9

FUND 42.2 As of December 31, 2010

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
											<u>.</u>
U7100026											
PE Temporary Building Replacement (D)											
Architect		\$148,055	\$42,372	\$6,220	\$485	\$0				\$0	\$197,133
Building & Additions		\$43,866	\$1,922,493	\$415,932	\$0	\$0				\$0	\$2,382,291
Inspection & Testing		\$6,455	\$136,510	\$716		\$0	\$0			\$0	\$143,681
Project Management		\$4,800	\$56,247	\$5,225		\$0				\$0	\$66,272
Advertising and Moving Expenses		\$763	\$0	\$6,893	\$0	\$0	\$0	\$0	\$0	\$0	\$7,656
Total		\$203,939	\$2,157,622	\$434,987	\$485	\$0	\$0	\$0	\$0	\$0	\$2,797,033
Project Budget	\$2,797,033										
Less Other Funding	\$0										
Net	\$2,797,033										
Actual Measure U Expenditures	\$2,797,033										
Running Balance	\$0										
U7100310											
Remodel Library Village for Math (E)											
Moving Exp.		\$0	\$38,625	\$0		\$0				\$0	\$38,625
Building & Additions		\$0	\$1,036,490	\$115,653	\$0	\$0		\$0		\$0	\$1,152,143
Architect		\$104,992	\$27,141	\$1,340	\$486	\$0				\$0	\$133,959
Engineering		\$0	\$2,658	\$0	\$0	\$0				\$0	\$2,658
Inspection & Testing		\$0	\$27,083	\$25,175		\$0				\$0	\$52,258
Project Management		\$0	\$51,679	\$4,400	\$0	\$0	\$0	\$0	\$0	\$0	\$56,079
Advertising and Moving Expenses		\$207	\$10,137	\$12,623		\$0	\$0	\$0	\$0	\$0	\$22,967
Total		\$105,199	\$1,193,813	\$159,191	\$486	\$0	\$0	\$0	\$0	\$0	\$1,458,690
Project Budget	\$1,458,690										
Less Other Funding	\$0										
Net	\$1,458,690										
Actual Measure U Expenditures	\$1,458,690										
Running Balance	\$0										

1/7/2011 2 of 9

FUND 42.2 As of December 31, 2010

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
U740007									1		
U7100027											
SM Airport Campus Site Improvements (F)		•	222.224		^-	40				•	***
Supplies		\$0	\$26,234	\$975	\$5,873	\$0	\$0	\$0		\$0	\$33,082
Misc Fees		\$0	\$25	\$0	\$0	\$34,274	\$0			\$0	\$34,299
Other Contract Services		\$3,860	\$11,508	\$8,434	\$1,501	\$0	\$0	\$0	\$0	\$0	\$25,302
Site Improvement		\$0	\$0	\$15,182	\$5,790	\$7,237	\$0		\$0	\$0	\$28,209
Building & Additions		\$0	\$1,495,697	\$1,670,788	\$4,824	\$0	\$0			\$0	\$3,171,309
Architect		\$104,934	\$500	\$0	\$43,570	\$0				\$0	\$149,004
Engineering		\$35,000	\$148,304	\$950	\$10,040	\$0	\$0		\$0	\$0	\$194,294
Inspection & Testing		\$5,032	\$118,662	\$191,271	\$0		\$0	\$0		\$0	\$314,965
Project Management		\$750	\$155,798	\$38,425	\$1,365	\$220	\$0			\$0	\$196,558
City Fees, Advertising and Security System		\$16,587	\$1,802	\$327	\$150	\$4,375					\$23,241
Total		\$166,163	\$1,958,530	\$1,926,352	\$73,113	\$46,106	\$0	\$0	\$0	\$0	\$4,170,264
Project Budget	\$4,170,264										
Less Other Funding	\$0										
Net	\$4,170,264										
Actual Measure U Expenditures	\$4,170,264										
Running Balance	\$0										
•											
U7110027											
SM Airport Campus West Building (G)											
Supply		\$0	\$0	\$17,650	\$28,017	\$0				\$0	\$45,667
Other Contract Services		\$0	\$0	\$0	\$3,576	\$0	\$0				\$3,576
Moving Expenses		\$0	\$0	\$180	\$15,824	\$0	\$0	\$0	\$0	\$0	\$16,004
Building & Additions		\$0	\$0	\$15,037,532	\$1,256,065	\$46,946	\$0		\$0	\$0	\$16,340,543
Architect		\$0	\$971,954	\$1,043,950	\$49,779	\$1,147	\$0	\$0	\$0	\$0	\$2,066,830
Engineering		\$0	\$2,920	\$9,800	\$5,010	\$963	\$0	\$0	\$0	\$0	\$18,693
Inspection & Testing		\$0	\$21,173	\$126,510	\$9,856	\$0	\$0	\$0	\$0	\$0	\$157,539
Project Management		\$0	\$14,450	\$313,715	\$13,956	\$0	\$0	\$0	\$0	\$0	\$342,121
Cap Equipment		\$0	\$49,795	\$326,382	\$4,792	\$0	\$0	\$0	\$0	\$0	\$380,969
Non-Cap Equipment		\$0	\$0	\$280,558	\$57,240	\$0	\$0	\$0	\$0	\$0	\$337,798
Total		\$0		\$17,156,277	\$1,444,115	\$49,056				\$0	\$19,709,741
Project Budget	\$19,709,741	* -	. , , -	. , ,	. , , .	. , ,		* -	, , , ,		. , ,
Less Other Funding	\$0										
Net	\$19,709,741										
Actual Measure U Expenditures	\$19,709,741										
Running Balance	\$0										

1/7/2011 3 of 9

FUND 42.2 As of December 31, 2010

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
U7100025	1	1									
Theatre Arts Renovation (H)											
Supplies		\$0	\$8,904	-\$14	\$12,858	\$16,619	\$0	\$0	\$0	\$0	\$38,367
Legal		\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$0
Moving Services		\$0	\$0	\$0	\$0	\$14,061	\$0	\$0	\$0	\$0	\$14,061
Other Contract Services		\$0	\$0	\$0	\$0	\$0		\$5,245	\$0	\$0	\$5,245
Rental / Lease		\$0	\$1.446	\$2,200	\$0	\$0		\$0	\$0	\$0	\$3.646
Building & Additions		\$528	\$1,326,630		\$10,897,603	\$56,122		\$0	\$0		
Architect		\$289,913	\$369,213	\$423,416	\$82,639	\$0		\$0	\$0	\$0	\$1,165,181
Engineering		\$6,174	\$2,981	\$16,606	\$2,375	\$1,250		\$0	\$0	\$0	\$29,386
Inspection & Testing		\$150	\$14,785	\$353,890	\$297,675	\$1,116		\$0	\$0	\$0	\$667,616
Project Management		\$150	\$45,698	\$184,219	\$193,898	\$14,818		\$0	\$0		
Cleaning, Storage and Installation		\$0	\$812	\$0		\$2,267	\$0	\$0	\$0	\$0	\$5,627
Cap Equipment		\$0	\$31,638	\$0	\$6,458	\$59,689		\$0	\$0	\$0	\$97,785
Non-Cap Equipment		\$0	\$2,388	\$0	\$36,749	\$145,294		\$0	\$0	\$0	
Total		\$296,915			\$11,532,803	\$311,236		\$5,245	\$0	\$0	
Project Budget	\$19,497,949	+ ===,===	V 1,000 1,100	+-,,	* , ,	****	+,	, ,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,	**	**	410,100,010
Less Other Funding	\$0										
Net	\$19,497,949										
Actual Measure U Expenditures	\$19,496,949										
Running Balance	\$1,000										
<u> </u>											Į.
U7100110											
Earthquake Rpl. Liberal Arts North (I)											
Supplies		\$0	\$0	\$0	\$0	\$1,408	\$0	\$75	\$0	\$0	\$1,483
Legal		\$0	\$0	\$0	\$0	\$887	\$0	\$0	\$0	\$0	\$887
Other Contract Services		\$0	\$0	\$0		\$75		\$0	\$0	\$0	\$75
Building & Additions		\$265	\$0	\$1,043,660	\$5,916,281	-\$973,001	\$321,345	\$14,898	\$0	\$0	\$6,323,449
Architect		\$0	\$611,732	\$102,824	\$209,490	\$216,563			\$0		\$1,165,289
Engineering		\$3,248	\$4,295	\$0	\$250	\$0		\$0	\$0	\$0	\$8,043
Inspection & Testing		\$0	\$0	\$28,312	\$326,203	\$77,942	\$0	\$0	\$0	\$0	\$432,458
Project Management		\$0	\$26,072	\$33,549	\$128,937	\$124,222	\$255	\$1,155	\$286	\$0	\$314,475
Advertising and Fees		\$0	-\$4	\$7,334	\$0	\$0	\$0	\$0	\$0	\$0	\$7,330
Cap-Equipment		\$0	\$0	\$0	\$0	\$25,356	\$12,579	\$0		\$0	\$37,935
Non-Cap Equipment		\$0	\$0	\$0	\$2,033	\$170,425		\$0	\$0	\$0	
Total		\$3,513	\$642,095	\$1,215,679	\$6,583,194	-\$356,123	\$359,737	\$19,592	\$286	\$0	
Project Budget	\$13,473,652	Received				-	•			· · · · · · · · · · · · · · · · · · ·	
Less Other Funding*	\$7,120,900	\$4,777,025		* Other Fundi	ng Source:						
Net	\$6,352,752			City of Santa	Monica \$4,039	9,753					
Actual Measure U Expenditures	\$8,467,972			FEMA \$2,115							
Running Balance	-\$2,115,220										

1/7/2011 4 of 9

FUND 42.2 As of December 31, 2010

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
U7100013. U7100047											
Music Complex (J)											
Advertising		\$0	\$0	\$436	\$0	\$0	\$0	\$0	\$0	\$0	\$436
Supplies		\$0	\$0		\$0	\$194				\$0	
Consultants		\$0	\$0		\$0	\$0		\$0		\$0	
Other Contract Services		\$0	\$0	\$0	\$0	\$0				\$0	
Moving Services		\$0	\$0		\$0	\$0				\$0	
Building & Additions		\$0				-\$737,213	\$273,531	\$0		\$0	
Architect		\$0	\$187,922	\$22,500	\$37,227	\$38,448			\$0	\$0	\$304,505
Engineering		\$0	\$0		\$0	\$0				\$0	\$21,370
Inspection & Testing		\$0	\$0	\$29,740	\$19,265	\$26,238	\$35,880	\$0		\$0	\$111,122
Project Management		\$0	\$170	\$36,739	\$36,351	\$56,914			\$0	\$0	
Cap Equipment		\$0	\$0		\$0	\$0	\$62,600	\$0		\$0	
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$29,852	\$78,582	\$0	\$0	\$0	\$108,434
Total		\$0	\$188,092	\$445,879	\$1,386,568	-\$585,566	\$532,447	\$37,014		\$0	
Project Budget	\$4,623,547	Received									
Less Other Funding*	\$2,618,113	\$2,618,113		* Other Fundi	ng Source:						
Net	\$2,005,434		•	Prop T Refina	ince \$2,618,11	13					
Actual Measure U Expenditures	\$2,004,434										
Running Balance	\$1,000										
-											
U7100111											
Earthquake Rpl. Liberal Arts South (K)											
Supply		\$0			\$2,497	\$379	\$23,811	\$75		\$0	
Legal		\$0		\$0	\$0	\$0			\$0	\$0	
Moving Services		\$0	\$0		\$0	\$0	\$4,063	\$0	\$0	\$0	
Consultants		\$0	\$0		\$17,265	\$41,435				\$0	\$58,700
Other Contract Services		\$0	\$0		\$202	\$0				\$0	\$6,356
Building & Additions		\$0			\$3,091,306	\$5,706,802		\$0		\$0	\$4,273,467
Architect		\$0	\$0	\$836,555	-\$503,297	\$163,506		\$39,984	\$2,549	\$0	
Engineering		\$0	\$0	\$3,125	\$150	\$5,344				\$0	
Inspection & Testing		\$0	\$0		\$179,798	\$296,015				\$0	
Project Management		\$0	\$0		\$43,989	\$262,598			\$1,278	\$0	
Cap-Equipment		\$0	\$0	\$0	\$0	\$0				\$0	
Non-Cap Equipment		\$0	\$0		\$0	\$58,726				\$0	
Total		\$0	\$0	\$872,991	\$2,831,909	\$6,534,806	-\$4,261,655	\$34,757	\$95,342	\$0	\$6,108,150
Project Budget	\$16,733,220	Received									
Less Other Funding*	\$10,625,070	\$10,625,070		* Other Fundi							
Net	\$6,108,150			City of Santa							
Actual Measure U Expenditures	\$6,108,150			State of Califo	ornia \$4,458,0	00					
Running Balance	\$0										

1/7/2011 5 of 9

FUND 42.2 As of December 31, 2010

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
U7100221											
Shuttle Replacement Parking (L)											
Supplies		\$0	\$0	\$0	\$0	\$0	\$1,347	\$0	\$0	\$0	\$1,347
Legal		\$0	\$0	\$0	\$8,462	\$35,103	\$0			\$0	\$43,565
Site Acquisition		\$0	\$0	\$0	\$0	\$16,903,087	\$0	\$0		\$0	\$16,903,087
Site Improvement		\$0	\$0	\$0	\$0	\$3,027	\$0	\$0	\$0	\$0	\$3,027
Building & Additions		\$0	\$0	\$0		\$484,000	\$1,252,224	\$2,353	\$0	\$0	\$1,738,577
Architect		\$0	\$0	\$0			\$7,208	\$0	\$0	\$0	\$58,777
Inspection & Testing		\$0	\$0	\$0		\$139,822	\$41,250		\$0	\$0	\$181,072
Project Management		\$0	\$0			\$7,631	\$32,425			\$0	\$40,056
Total		\$0	\$0	\$0	\$8,462	\$17,624,240	\$1,334,455	\$2,353	\$0	\$0	\$18,969,509
Project Budget	\$18,969,509										
Less Other Funding	\$0										
Net	\$18,969,509										
Actual Measure U Expenditures	\$18,969,509										
Running Balance	\$0										
U7100321											
North Quad Plaza (M)											
Legal		\$0	\$0	\$0		\$0	\$3,825	\$5,604		\$0	\$9,429
Building & Additions		\$0	\$0	\$0	\$0	-\$443	\$6,130,081	\$3,634,487	\$0	\$0	\$9,764,125
Architect		\$0	\$231,055	\$8,444	\$140,048	\$435,618	\$171,225	\$68,633	\$2,901	\$0	\$1,057,924
Engineering		\$0	\$0	\$0	\$0	\$0	\$0			\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$186,220	\$107,477	\$328	\$0	\$294,025
Project Management		\$0	\$0	\$760	\$210	\$2,200	\$135,601	\$55,782	\$606	\$0	\$195,158
Printing		\$0	\$1,900	\$0	\$0	\$0	\$0	\$0		\$0	\$1,900
Cap Equipment		\$0	\$0		\$0	\$0	\$0			\$0	\$55,420
Total		\$0	\$232,955	\$9,204	\$140,258	\$437,375	\$6,626,952	\$3,927,402	\$3,834	\$0	\$11,377,981
Project Budget	\$11,378,981										
Less Other Funding	\$0										
Net	\$11,378,981										
Actual Measure U Expenditures	\$11,377,981										
Running Balance	\$1,000										

1/7/2011 6 of 9

FUND 42.2 As of December 31, 2010

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
U7100500, U7126450, U7100334, U7100142											
Student Services Building (O)											
Supplies		\$2,014	\$0	\$0	\$0	\$0	\$0	\$718	\$0	\$0	\$2,732
PC Upgrades		\$0	\$765	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$765
Consultants		\$0	\$0	\$0	\$0	\$9,334	\$55,693	\$0	\$0	\$0	\$65,027
Legal		\$0	\$0	\$0	\$0	\$38	\$2,775	\$31,776	\$0	\$0	\$34,588
Other Contract Services		\$210	\$0	\$0	\$0	\$0	\$17,561	\$17,495	\$18,817	\$0	\$54,084
Moving		\$7,571	\$0	\$0	\$0	\$0	\$0	\$616	\$0	\$0	\$8,187
Building & Additions		\$359,141	\$2,441	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$361,582
Architect		\$31,782	\$0	\$235,230	\$0	\$43,992	\$0	\$690,099	\$208,521	\$27,863	\$1,237,487
Engineering		\$1,838	\$0	\$0	\$0	\$0	\$0	\$6,205	\$27,363	\$3,171	\$38,576
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$25,670	\$34,687	\$0	\$0	\$60,358
Project Management		\$4,650	\$0	\$2,470	\$0	\$1,100	\$0	\$124,148	\$0	\$0	\$132,368
Cap Equipment		\$59,063	\$0	\$0	\$0	\$0	\$8,745	\$8,056	\$0	\$0	\$75,864
Total		\$466,268	\$3,207	\$237,700	\$0	\$54,464	\$110,445	\$913,802	\$254,701	\$31,034	\$2,071,619
Project Budget	\$53,521,913	Received		* Other Fundi	ng Source:						
Less Other Funding*	\$32,708,235	\$1,321,000		State of Califo	ornia \$16,803,	000					
Net	\$20,813,678		•	District Capita	al Funds \$10,2	10,587					
Actual Measure U Expenditures	\$2,071,619			Measure U In	terest \$5,694,0	648					
Running Balance	\$18,742,059										

Student Services Building

Project Discription:

Consolidates various student services departments and college administration in a single complex at the front of the campus

Facility Size:

83,634 sq/ft & 500 cars underground parking structure


Status:

In plan check with DSA

Architect:

Steinberg Architects

Contractor:

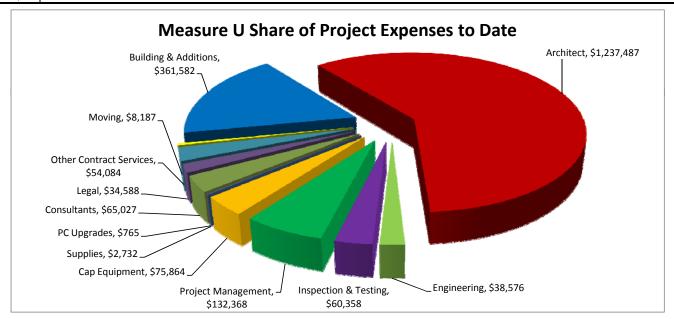

1/7/2011 7 of 9

FUND 42.2 As of December 31, 2010

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
											<u>.</u>
U7100090											
Science Complex Additional (P)											
Architect		\$0	\$0	\$0	\$0	\$246,425	\$61,911	\$0	\$0	\$0	\$308,336
Total		\$0	\$0	\$0	\$0	\$246,425	\$61,911	\$0	\$0	\$0	\$308,336
Project Budget	\$308,336	•		-		-		•	•		·
Less Other Funding	\$0										
Net	\$308,336										
Actual Measure U Expenditures	\$308,336										
Running Balance	\$0										
<u> </u>											<u>, </u>
U6780000, U7100022, U7100331, U7100550, U7100005, U7100030, U7100031, U7100029, U7100003, U7100008, U7100332, U7100072, U7100042, U7100056, U7100039											
Infrastructure & Safety (Q)											
Supplies		\$0	\$0	\$254	\$0	\$0	\$0	\$1,700	\$1,393	\$0	\$3,347
Consultants		\$0	\$0	\$0	\$0	\$0	\$0	\$16,734	\$0	\$0	\$16,734
Legal		\$0	\$0		\$0	\$0	\$3,527	\$3,294	\$0	\$0	\$6,821
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$7,825		\$203,383	\$0	\$292,653
Building & Additions		\$681,900	\$195,175	\$20,600	\$0	\$200,620	\$733	\$0	\$0	\$0	\$1,099,028
Architect		\$69,081	\$42,108	\$0	\$155,321	\$448,507	\$91,127	\$4,227	\$0	\$0	\$810,370
Engineering		\$8,050	\$0	\$0	\$6,750	\$12,000	\$18,429		\$0	\$0	\$47,589
Inspection & Testing		\$2,241	\$4,250	\$0	\$0	\$0	\$5,807	\$0	\$0	\$0	\$12,298
Project Management		\$0	\$2,805	\$0	\$0	\$3,520	\$1,840		\$196	\$0	\$8,399
Cap Equipment		\$0	\$0	\$343,861	\$0	\$0	\$0		\$349,531	\$0	\$1,588,563
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0		\$4,216	\$0	\$4,216
Advertising		\$0	\$785	\$0	\$0	\$0	\$0		\$0	\$0	\$785
Total		\$761,272	\$245,122	\$364,715	\$162,071	\$664,647	\$129,287	\$1,004,968	\$558,718	\$0	\$3,890,801
Project Budget	\$4,042,284									·	
Less Other Funding	\$0										
Net	\$4,042,284										
Actual Measure U Expenditures	\$3,890,801										
Running Balance	\$151,483										

1/7/2011 8 of 9

FUND 42.2 As of December 31, 2010

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
U7100007	1								1		
Restroom Improvement (R)											
Supplies		\$0	\$564	\$0	\$1.075	\$0	\$0	\$0	\$0	\$0	\$1,639
Other Contract Services		\$0	\$0	\$0 \$0		\$0 \$0		\$0			\$3,803
Building & Additions		\$0	\$1,305	\$0 \$0		\$0 \$0		\$0 \$0			\$9,196
Inspection & Testing		\$0	\$2,043	\$0 \$0		\$0 \$0		\$0			\$2,863
Total		\$ 0	\$3,912	\$0		\$0		\$0 \$0			\$17,501
Project Budget	\$17,501	ΨΟ	ψ3,312	ΨΟ	\$15,509	ΨΟ	ΨΟ	ΨΟ	ΨΟ	φυ	\$17,501
Less Other Funding	\$0										
Net	\$17,501										
Actual Measure U Expenditures	\$17,501										
Running Balance	\$0										
Rulling Balance	φυ										
U7100004, U7110020											
Master Planning (S)											
Consultants		\$9,000	\$26,516	\$158,449	\$374,329	\$125,404	\$17,998	\$363,342	\$0	\$0	\$1,075,038
Architect		\$0	\$17,617	\$126,433		\$126,701	\$346,827	\$276,985	\$0	\$0	\$998,647
Rental / Lease		\$0	\$0	\$6,453		\$0		\$0			\$6,453
Postage		\$0	\$0	\$30,000		\$0		\$0			\$30,000
Reimbursement to SMC		\$0	\$0	\$0		\$0		\$0			\$180
Project Management		\$0	\$0	\$0		\$0		\$113			\$113
Total		\$9,000	\$44,133	\$321,335		\$252,105		\$640,439			\$2,110,430
Project Budget	\$2,110,430	. , ,	. ,			, ,		. ,		<u> </u>	, , ,
Less Other Funding	\$0										
Net	\$2,110,430										
Actual Measure U Expenditures	\$2,110,430										
Running Balance	\$0										
U7100024											
14th and Pico Project (T)											
Consultants		\$0	\$888	\$0	\$0	\$0		\$0			\$888
Architect		\$258,601	\$47,343	\$0		\$0		\$0			\$305,944
Inspection & Testing		\$12,070	\$0	\$0		\$0		\$0			\$12,070
Project Management		\$0	\$340	\$0	\$0	\$0		\$0			\$340
Total		\$270,671	\$48,571	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$319,242
Project Budget	\$319,242					-					
Less Other Funding	\$0										
Net	\$319,242										
Actual Measure U Expenditures	\$319,242										
Running Balance	\$0										
Grand Total		\$11,068,400	\$10,432,055	\$28,685,697	\$54,940,416	\$25,278,771	\$5,283,853	\$6,585,573	\$912,880	\$31,034	\$143,218,679

Note: Project N had no expenses


1/7/2011 9 of 9

SANTA MONICA COMMUNITY COLLEGE DISTRICT

Measure S Bond Budget

As of December 31, 2010

	Project Name	Completion	Project Budget	Measure S Allocation	Other Funding	Measure S Expenditures as of 12/31/10	Measure S Expenditures as of 9/30/10	Measure S Expenditures Last Period	Total Measure S Remaining
1	Athletic Fields Phase I, Corsair Field	Completed	\$4,440,768	\$4,373,238	\$67,530	\$4,372,238	\$4,372,238	\$0	\$1,000
1A	Athletic Fields Phase I, John Adams	Completed	\$2,970,807	\$2,970,807	\$0	\$2,969,807	\$2,969,807	\$0	\$1,000
2	Performing Arts Complex	Completed	\$40,602,117	\$37,609,541	\$2,992,576	\$37,608,541	\$37,608,541	\$0	\$1,000
3	Career Opportunity Center	Move to AA	\$0	\$0	\$0	\$0	\$0	\$0	\$0
4	Replacement Health/PE/Fitness Building	November 2013	\$39,983,011	\$4,598,771	\$35,384,240	\$772,976	\$772,976	\$0	\$3,825,795
5	Early Childhood Development/Childcare	In Planning	\$11,318,000	\$7,000,000	\$4,318,000	\$9,200	\$9,200	\$0	\$6,990,800
6	Malibu Site Acquisition and Facility	Not Scheduled	\$31,069,031	\$25,000,000	\$6,069,031	\$5,230,992	\$5,230,992	\$0	\$19,769,008
7	Energy Efficiency Projects	On-Going	\$1,293,570	\$1,293,570	\$0	\$510,684	\$473,704	\$36,980	\$782,886
8	Satellite Campus Parking Facilities and Roadway Improvements	Completed	\$4,876,424	\$4,876,424	\$0	\$3,815,317	\$3,778,324	\$36,993	\$1,061,107
9	Parking Garage, Grounds and Equipment - Student Services	May 2014	\$53,143,653	\$52,690,653	\$453,000	\$14,523,008	\$14,403,411	\$119,597	\$38,167,645
10	Pico Promenade Improvements	Completed	\$1,018,009	\$1,018,009	\$0	\$1,018,009	\$1,018,009	\$0	\$0
11	Master Planning	On-Going	\$750,000	\$750,000	\$0	\$708,583	\$680,281	\$28,302	\$41,417
12	Other Bond Related Expenses	On-Going	\$662,764	\$662,764	\$0	\$69,491	\$60,048	\$9,443	\$593,273
13	Adv. Architecture Related Exp for AA	Completed	\$0	\$0	\$0	\$0	\$0	\$0	\$0
14	Real Property Acquisition	On-Going	\$50,000	\$50,000	\$0	\$45,597	\$45,597	\$0	\$4,403
15	Signage Safety/Information	On-Going	\$606,223	\$606,223	\$0	\$215,988	\$188,483	\$27,505	\$390,235
	Project Totals		\$192,784,377	\$143,500,000	\$49,284,377	\$71,870,431	\$71,611,611	\$258,820	\$71,629,569

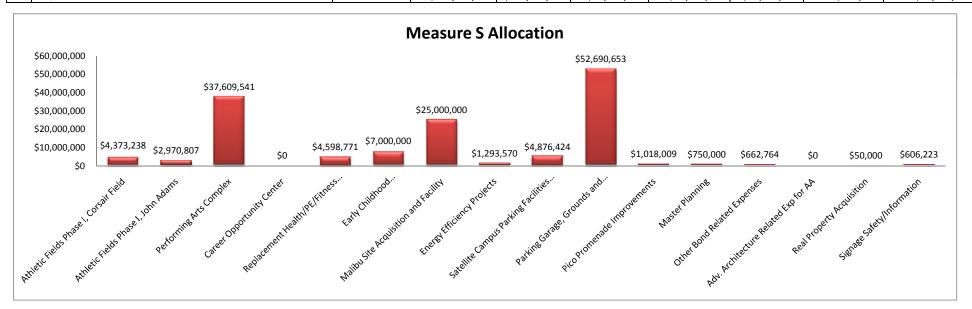

SANTA MONICA COMMUNITY COLLEGE DISTRICT

Measure S Project Schedule As of December 31, 2010

	Project Name	Completion	20	10		20	011	20 1	12		20	13	2	2014	
1	Athletic Fields Phase I, Corsair Field	Completed													
1A	Athletic Fields Phase I, John Adams	Completed													
2	Performing Arts Center	Completed													
3	Career Opportunity Center	Move to AA													
4	Replacement Health/PE/Fitness Building	November 2013													
5	Early Childhood Development/Childcare	In Planning													
6	Malibu Site Acquisition and Facility	Not Scheduled													
7	Energy Efficiency Projects	On-Going													
8	Satellite Campus Parking Facilities and Roadway Improvements	Completed													
9	Parking Garage, Grounds and Equipment - Student Services	May 2014													
10	Pico Promenade Improvements	Completed													
11	Master Planning	On-Going													
12	Other Bond Related Expenses	On-Going													
13	Adv. Architecture Related Exp for AA	Completed													
14	Real Property Acquisition	On-Going													
15	Signage Safety/Information	On-Going													٦
			In	Plar	nnir	ng		In (Con	stru	ctio	n			

FUND 42.3

As of December 31, 2010

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
S7100019									
Athletic Field Phase I, Corsair Field (1)									
Legal		\$0	\$0	\$0	\$301	\$175	\$0	\$0	\$476
Building & Additions		\$0	\$0	\$0	\$300,380	\$2,579,095	\$0	\$0	\$2,879,475
Architect		\$27,332	\$43,815	\$197,557	\$252,736	\$279,173	\$26,563	\$0	\$827,176
Inspection & Testing		\$0	\$0	\$0	\$23,411	\$57,585	\$640	\$0	\$81,636
Project Management		\$0	\$0	\$0	\$9,871	\$42,374	\$565	\$0	\$52,810
Cap Equipment		\$0	\$0	\$0	\$0	\$483,017	\$35,271	\$0	\$518,288
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$2,066	\$10,312	\$0	\$12,378
Total		\$27,332	\$43,815	\$197,557	\$586,699	\$3,443,485	\$73,350	\$0	\$4,372,238
Project Budget	\$4,440,768	Received							
Less Other Funding*	\$67,530	\$67,530							
Net	\$4,373,238		* Other Fundi	ng Source:					
Actual Measure S Expenditures	\$4,372,238		Metropolitan V	Nater District	\$67,530				
Running Balance	\$1,000								

Athletic Field Phase I, Corsair Field

Project Description:Renovation of the Corsair Field, stadium lighting and sound system

Status:


Completed, 2009

Architect:

CO Architects

Contractor:

Byrom Davey, Inc.

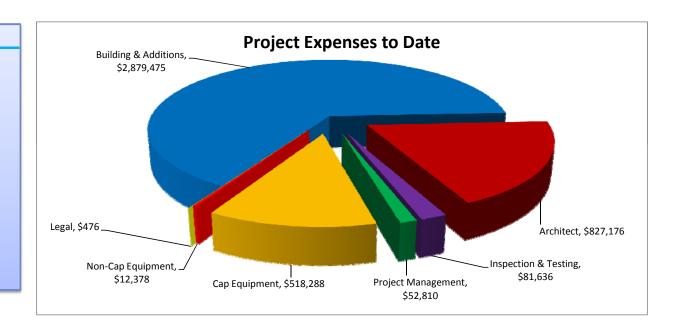

1/7/2011 1 of 9

FUND 42.3

As of December 31, 2010

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
					•				
S7100038									
Athletic Field Phase I, John Adams (1A)									
Legal		\$0	\$0	\$0	\$75	\$0	\$0	\$0	\$75
Building & Additions		\$0	\$0	\$0	\$16,556	\$1,395,261	\$0	\$0	\$1,411,817
Architect		\$0	\$5,807	\$93,941	\$12,150	\$31,818	\$0	\$0	\$143,715
Inspection & Testing		\$0	\$2,874	\$3,207	\$0	\$49,984	\$0	\$0	\$56,066
Project Management		\$0	\$0	\$0	\$10,921	\$45,170	\$38	\$0	\$56,128
Cap Equipment		\$0	\$0	\$0	\$0	\$1,290,672	\$0	\$0	\$1,290,672
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$11,334	\$0	\$0	\$11,334
Total		\$0	\$8,681	\$97,148	\$39,701	\$2,824,239	\$38	\$0	\$2,969,807
Project Budget	\$2,970,807								
Less Other Funding	\$0								
Net	\$2,970,807								
Actual Measure S Expenditures	\$2,969,807								
Running Balance	\$1,000								

Athletic Field Phase I, John Adams

Project Description:Renovation of John Adams Field and lighting

Status:


Completed, 2008

Architect:

Caldwell Architects

Contractor:

Byrom Davey, Inc.

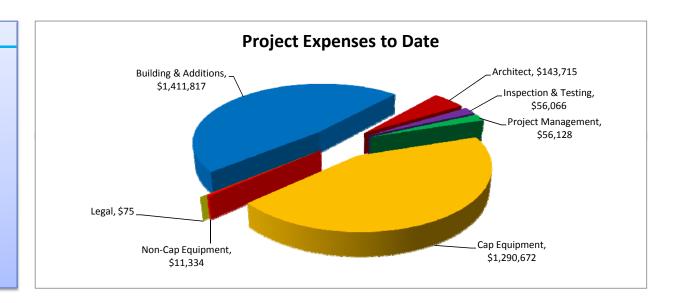

1/7/2011 2 of 9

FUND 42.3

As of December 31, 2010

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
S7100012									
Performing Arts Center (2)									
Consultants		\$0	\$0	\$0	\$121,790	\$76,639	\$0	\$0	\$198,429
Other Contract Services		\$0	\$0	\$4,269	\$0	\$22,729	\$22	\$0	\$27,020
Supplies		\$0	\$0	\$0	\$14,565	\$5,810	\$0	\$0	\$20,375
Legal		\$0	\$0	\$34,329	\$275,667	\$492,731	\$15,629	\$0	\$818,356
Advertising		\$0	\$0	\$0	\$320	\$0	\$0	\$0	\$320
Building & Additions		\$7,784,151	\$10,292,986	\$8,930,813	\$2,991,903	\$1,629,990	\$50,000	\$0	\$31,679,843
Architect		\$0	\$811,312	\$182,457	\$412,309	\$121,588	\$108	\$0	\$1,527,774
Engineering		\$0	\$3,600	\$5,250	\$1,500	\$9,650	\$0	\$0	\$20,000
Inspection & Testing		\$104,308	\$722,685	\$411,193	\$210,381	\$22,256	\$0	\$0	\$1,470,823
Project Management		\$31,984	\$155,732	\$248,876	\$263,690	\$47,915	\$3,244	\$0	\$751,441
Cap Equipment		\$0	\$0	\$130,218	\$292,565	\$342,693	\$0	\$0	\$765,476
Non-Cap Equipment		\$0	\$0	\$15,124	\$93,106	\$220,455	\$0	\$0	\$328,685
Total		\$7,920,443	\$11,986,315	\$9,962,528	\$4,677,797	\$2,992,455	\$69,003	\$0	\$37,608,541
Project Budget	\$40,602,117	Received							
Less Other Funding*	\$2,992,576	\$2,992,576		* Other Fundi	ng Source:				
Net	\$37,609,541		<u>-</u> '	Madison Proje	ect Foundation	n \$2,992,576			
Actual Measure S Expenditures	\$37,608,541	•							
Running Balance	\$1,000	•							

Performing Arts Center

Project Description:

Construction of a state-of-the-art 499 seat performing arts theater

Status:


Completed, 2008

Architect:

Renzo Zecchetto

Contractor:

FTR International

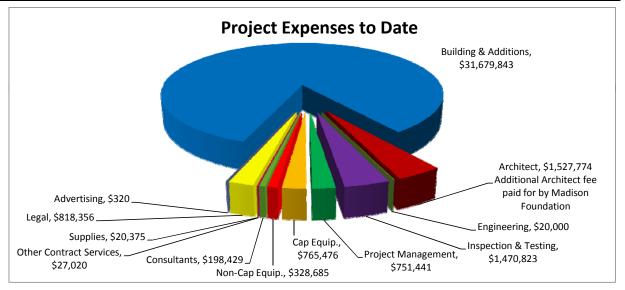

1/7/2011 3 of 9

FUND 42.3

As of December 31, 2010

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
						•			
S7100033, S7100144									
Replacement Health/PE/Fitness Building (4)									
Supplies		\$0	\$0	\$0	\$0	\$0	\$163	\$0	\$163
Legal		\$0	\$0	\$0	\$0	\$1,413	\$75	\$0	\$1,488
Other Contract Services		\$1,634	\$25,934	\$0	\$0	\$253	\$165	\$0	\$27,985
Repair Facility		\$0	\$4,861	\$0	\$0	\$0	\$0	\$0	\$4,861
Supplies		\$4,809	\$288	\$0	\$0	\$0	\$0	\$0	\$5,097
Building & Additions		\$0	\$0	\$0	\$0	\$112,410	\$526,552	\$0	\$638,962
Architect		\$0	\$0	\$0	\$0	\$0	\$41,044	\$0	\$41,044
Inspection & Testing		\$0	\$0	\$0	\$0	\$6,518	\$14,363	\$0	\$20,881
Project Management		\$0	\$0	\$0	\$0	\$9,070	\$23,425	\$0	\$32,495
Total		\$6,443	\$31,083	\$0	\$0	\$129,663	\$605,787	\$0	\$772,976
Project Budget	\$39,983,011	<u> </u>			_				
Less Other Funding*	\$35,384,240			* Other Fundi					
Net	\$4,598,771			Measure AA S	\$35,384,240				
Actual Measure S Expenditures	\$772,976								
Running Balance	\$3,825,795								
S7100045	1	I							1
Early Childhood Development/Childcare (5)			ФО.	¢ο	CO 200	ФО.	¢o.	ф О	ФО 200
Consultants Total		\$0 \$0	\$0 \$0	\$0 \$0	\$9,200 \$9,200	\$0 \$0	\$0 \$0	\$0 \$0	\$9,200 \$9,200
Project Budget	\$11,318,000		\$0	\$0	\$9,200	\$0	\$0	\$ U	\$9,200
Less Other Funding*	\$4,318,000			* Other Fundi	na Couroo:				
Net	\$7,000,000				ng Source. Monica \$4,318	2 000			
Actual Measure S Expenditures	\$9,200			City of Santa	1VIOITICA \$4,510	5,000			
Running Balance	\$6,990,800								
Ruilling balance	\$6,990,600								
S7100077, S7100015									
IIVIALIDU SITE ACQUISITION AND FACILITIES (6)									
Malibu Site Acquisition and Facilities (6) Consultants		\$0	\$0	\$0	\$0	\$30.000	\$0	\$0	\$30.000
Consultants		\$0 \$0	\$0 \$27,722	\$0 \$16,787	\$0 \$6,159	\$30,000 \$504	\$0 \$0	\$0 \$0	\$30,000 \$51,172
Consultants Legal		\$0	\$27,722	\$16,787	\$6,159	\$504	\$0	\$0	\$51,172
Consultants Legal Building & Additions		\$0 \$0	\$27,722 \$0	\$16,787 \$0	\$6,159 \$0	\$504 \$0	\$0 \$0	\$0 \$0	\$51,172 \$0
Consultants Legal Building & Additions Architect		\$0 \$0 \$0	\$27,722 \$0 \$0	\$16,787 \$0 \$0	\$6,159 \$0 \$0	\$504 \$0 \$0	\$0 \$0 \$0	\$0 \$0 \$0	\$51,172 \$0 \$0
Consultants Legal Building & Additions Architect Inspection & Testing		\$0 \$0 \$0 \$4,388	\$27,722 \$0 \$0 \$3,750	\$16,787 \$0 \$0 \$141,462	\$6,159 \$0 \$0 \$0	\$504 \$0 \$0 \$0	\$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0	\$51,172 \$0 \$0 \$149,600
Consultants Legal Building & Additions Architect Inspection & Testing Project Management		\$0 \$0 \$0 \$4,388 \$0	\$27,722 \$0 \$0 \$0 \$3,750 \$0	\$16,787 \$0 \$0 \$141,462 \$220	\$6,159 \$0 \$0 \$0 \$0	\$504 \$0 \$0	\$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0	\$51,172 \$0 \$0
Consultants Legal Building & Additions Architect Inspection & Testing		\$0 \$0 \$0 \$4,388	\$27,722 \$0 \$0 \$3,750 \$0	\$16,787 \$0 \$0 \$141,462	\$6,159 \$0 \$0 \$0 \$0 \$0	\$504 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0	\$51,172 \$0 \$0 \$149,600 \$220 \$0
Consultants Legal Building & Additions Architect Inspection & Testing Project Management Other Contract Services		\$0 \$0 \$0 \$4,388 \$0 \$0	\$27,722 \$0 \$0 \$0 \$3,750 \$0	\$16,787 \$0 \$0 \$141,462 \$220 \$0	\$6,159 \$0 \$0 \$0 \$0	\$504 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0	\$51,172 \$0 \$0 \$149,600 \$220 \$0 \$5,000,000
Consultants Legal Building & Additions Architect Inspection & Testing Project Management Other Contract Services Storm/Waste Water Treatment Center Total	\$31,069,031	\$0 \$0 \$0 \$4,388 \$0 \$0 \$0	\$27,722 \$0 \$0 \$3,750 \$0 \$0 \$2,500,000	\$16,787 \$0 \$0 \$141,462 \$220 \$0 \$0	\$6,159 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$504 \$0 \$0 \$0 \$0 \$0 \$0 \$2,500,000	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0	\$51,172 \$0 \$0 \$149,600 \$220 \$0 \$5,000,000
Consultants Legal Building & Additions Architect Inspection & Testing Project Management Other Contract Services Storm/Waste Water Treatment Center	\$31,069,031 \$6,069,031	\$0 \$0 \$0 \$4,388 \$0 \$0 \$0	\$27,722 \$0 \$0 \$3,750 \$0 \$0 \$2,500,000	\$16,787 \$0 \$0 \$141,462 \$220 \$0 \$0	\$6,159 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$504 \$0 \$0 \$0 \$0 \$0 \$0 \$2,500,000	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0	\$51,172 \$0 \$0 \$149,600 \$220 \$0 \$5,000,000
Consultants Legal Building & Additions Architect Inspection & Testing Project Management Other Contract Services Storm/Waste Water Treatment Center Total Project Budget		\$0 \$0 \$0 \$4,388 \$0 \$0 \$0 \$0 \$4,388	\$27,722 \$0 \$0 \$3,750 \$0 \$0 \$2,500,000	\$16,787 \$0 \$0 \$141,462 \$220 \$0 \$0 \$158,468	\$6,159 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$504 \$0 \$0 \$0 \$0 \$0 \$0 \$2,500,000	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0	\$51,172 \$0 \$0 \$149,600 \$220 \$0 \$5,000,000
Consultants Legal Building & Additions Architect Inspection & Testing Project Management Other Contract Services Storm/Waste Water Treatment Center Total Project Budget Less Other Funding*	\$6,069,031	\$0 \$0 \$0 \$4,388 \$0 \$0 \$0 \$4,388	\$27,722 \$0 \$0 \$3,750 \$0 \$0 \$2,500,000	\$16,787 \$0 \$0 \$141,462 \$220 \$0 \$0 \$158,468	\$6,159 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$504 \$0 \$0 \$0 \$0 \$0 \$0 \$2,500,000	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0	\$51,172 \$0 \$0 \$149,600 \$220 \$0 \$5,000,000

1/7/2011 4 of 9

FUND 42.3	
As of December 31, 2010	

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
S7100043, S7100066									
Energy Efficiency Projects (7)									
Legal		\$0	\$0				\$0	\$0	
Building & Additions		\$0	\$0			\$106,921	\$355,294	\$36,980	\$499,195
Engineering		\$0	\$0			\$0	7 -	\$0	
Inspection & Testing		\$0	\$0					\$0	
Project Management		\$0	\$0	\$0			T -	\$0	
Total		\$0	\$0	\$0	\$10,500	\$107,910	\$355,294	\$36,980	\$510,684
Project Budget	\$1,293,570								
Less Other Funding	\$0								
Net	\$1,293,570								
Actual Measure S Expenditures	\$510,684								
Running Balance	\$782,886								
S7100091, S7100092									
Satellite Campus Parking Facilities and Roa	dway Improveme	ents (8)							
Legal		\$0	\$0	\$0		\$175	\$0	\$0	
Other Contract Services		\$0	\$0				\$0	\$0	
Advertising		\$0	\$0					\$0	\$0
Consultants		\$0	\$0				\$0	\$0	
Supplies		\$0	\$0				\$0	\$0	\$0
Building & Additions		\$0	\$0			\$1,860,152	\$449,543	\$37,777	\$2,625,651
Architect		\$0	\$0			\$136,911	\$34,490	\$0	
Inspection & Testing		\$0	\$0			\$185,947	\$28,218	\$360	\$245,626
Project Management		\$0	\$0			\$64,880	\$31,137	\$4,390	\$118,695
Non-Cap Equipment		\$0	\$0			\$0	\$3,387	\$0	\$3,387
Total		\$0	\$0	\$324,919	\$653,031	\$2,248,065	\$546,775	\$42,527	\$3,815,317
Project Budget	\$4,876,424		•	•	•		•		
Less Other Funding	\$0								
Net	\$4,876,424								
Actual Measure S Expenditures	\$3,815,317								
Running Balance	\$1,061,107								

1/7/2011 5 of 9

FUND 42.3

As of December 31, 2010

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
S7100142									
Parking Garage and Grounds - Student Servi	ces (9)								
Supplies		\$0	\$0	\$0	\$0	\$1,745	\$0	\$0	\$1,745
Consultants		\$0	\$0	\$0	\$0	\$20,700	\$0	\$0	\$20,700
Legal		\$0	\$0	\$0	\$0	\$2,154	\$17,486	\$75	\$19,715
Other Contract Services		\$0	\$0	\$0	\$0	\$1,508	\$10,952	\$200	\$12,660
Building & Additions		\$0	\$0	\$0	\$0	\$2,555,940	\$5,925,152	\$0	\$8,481,092
Architect		\$0	\$0	\$0	\$2,266,766	\$2,674,054	\$0	\$19,734	\$4,960,555
Engineering		\$0	\$0	\$0	\$0	\$4,813	\$38,330	\$37,732	\$80,875
Inspection & Testing		\$0	\$0	\$0	\$0	\$131,009	\$161,847	\$19,569	\$312,426
Project Management		\$0	\$0	\$0	\$0	\$158,766	\$373,559	\$86,524	\$618,849
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$14,393	\$0	\$14,393
Total		\$0	\$0	\$0	\$2,266,766	\$5,550,689	\$6,541,719	\$163,835	\$14,523,008
Project Budget	\$53,143,653	Received							
Less Other Funding*	\$453,000	\$0		* Other Fundi	ng Source:				
Net	\$52,690,653		1	State of Califo	ornia \$453,000)			
Actual Measure S Expenditures	\$14,523,008	•							
Running Balance	\$38,167,645								

Parking Garage and Grounds - Student Services

Project Description:

Consolidates various student services departments and college administration in a single complex at the front of the campus

Facility Size:

83,634 sq/ft & 500 cars underground parking structure


Status:

In plan check with DSA

Architect:

Steinberg Architects

Contractor:

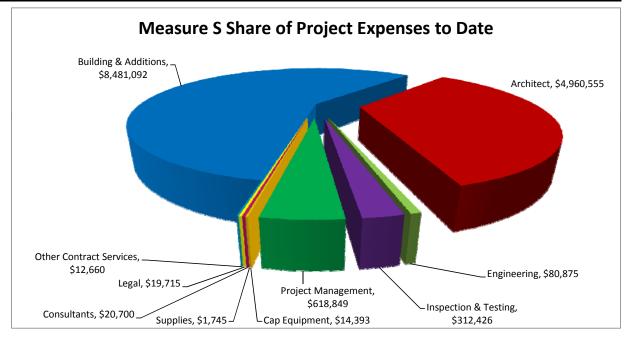

1/7/2011 6 of 9

FUND 42.3

As of December 31, 2010

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
Trojects	Dauget	0 4 /03 i iliai	03/00 1 11141	00/07 1 11101	07700 1 11101	00/03 1 11141	03/10 1 11141	10/11	Odinbilica rotais
S7100044							1		
Pico Promenade Improvements (10)									
Building & Additions		\$0	\$0	\$0	\$690	\$883,401	\$0	\$0	\$884,091
Architect		\$0 \$0	\$0 \$0	\$0 \$0	\$69,190	\$28,540	\$864	\$0 \$0	\$98,595
Inspection & Testing		\$0	\$0 \$0	\$0 \$0	\$09,190		\$004	\$0	\$7,591
Project Management		\$0 \$0	\$0 \$0	\$0 \$0	\$2,185			\$0	\$27,733
Total		\$0 \$0	\$0 \$0	\$0 \$0				\$0 \$0	\$1,018,009
Project Budget	\$1,018,009	φU	φU	ΦU	\$12,000	\$9 4 5,000	\$604	φU	\$1,010,008
Less Other Funding	\$1,018,009								
Ÿ	7 -	L							
Net	\$1,018,009								
Actual Measure S Expenditures	\$1,018,009								
Running Balance	\$0								
\$7100004	<u> </u>						1		
Master Planning (11) Consultants		\$0	\$0	\$0	\$0	\$0	\$441,549	\$13,320	\$454,869
Printing		\$0	\$0	\$0	\$0	\$0	\$4,157	\$0	\$4,157
Advertising		\$0	\$0	\$0	\$0	\$0	\$3,000	\$0	\$3,000
Other Contract Services		\$0	\$0	\$0	\$0	\$0		\$200	\$642
Architect		\$0	\$0	\$0	\$0	\$0		\$24,736	\$217,094
Project Management		\$0	\$0	\$0	\$0			\$9,341	\$25,979
Filling Fees		\$0	\$0	\$0	\$0			\$2,842	\$2,842
Total		\$0	\$0	\$0	\$0	\$0	\$658,143	\$50,439	\$708,583
Project Budget	\$750,000								
Less Other Funding	\$0								
Net	\$750,000								
Actual Measure S Expenditures	\$708,583								
Running Balance	\$41,417								
S7100048									
Other Bond Related Expenses (12)									
Supplies		\$0	\$0	\$0	\$0	\$0	\$3,638	\$0	\$3,638
Legal		\$0	\$0	\$0	\$0	\$0	\$8,917	\$2,561	\$11,477
Advertising		\$0	\$0	\$0	\$0		\$2,278	\$0	\$2,278
Other Contract Services		\$0	\$0	\$0	\$0	\$1,800	\$17,206	\$11,585	\$30,591
Moving Services		\$0	\$0	\$0	\$0		\$400	\$0	\$400
Project Management		\$0	\$0	\$0	\$0			\$3,360	\$21,107
Total		\$0	\$0	\$0	\$0		\$50,185	\$17,506	\$69,491
Project Budget	\$662,764	**		**	***	, ,,,,,,,,,	+,	, , , , , , , , ,	, ,
Less Other Funding	\$0								
Net	\$662,764								
Actual Measure S Expenditures	\$69,491								
Running Balance	\$593,273								
Truining Dalance	ψυσυ,213								

1/7/2011 7 of 9

FUND 42.3 As of December 31, 2010

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
S7100049									
Adv Architecture Related Exp for AA (13)									
Legal		\$0	\$0					\$0	\$0
Other Contract Services		\$0	\$0				\$0	\$0	
Architect		\$0	\$0				\$0	\$0	\$0
Engineering		\$0	\$0				\$0	\$0	\$0
Inspection & Testing		\$0	\$0				-\$45,734	\$0	
Project Management		\$0	\$0					\$0	\$0
Total		\$0	\$0	\$0	\$0	\$45,734	-\$45,734	\$0	\$0
Project Budget	\$0			•	•	•	•		•
Less Other Funding	\$0								
Net	\$0 \$0								
Actual Measure S Expenditures	\$0								
Running Balance	\$0								
				1	r	•	1		T
\$7100057									
Real Property Acquisition (14)									
Other Contract Services		\$0	\$0					\$0	
Architect		\$0	\$0					\$0	\$0
Engineering		\$0	\$0					\$0	
Inspection & Testing		\$0	\$0					\$0	
Project Management		\$0	\$0					\$0	
Total		\$0	\$0	\$0	\$0	\$0	\$45,597	\$0	\$45,597
Project Budget	\$50,000								
Less Other Funding	\$0	4							
Net	\$50,000								
Actual Measure S Expenditures	\$45,597								
Running Balance	\$4,403								

1/7/2011 8 of 9

FUND 42.3 As of December 31, 2010

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
S7100072									
Campus Signage (15)									
Consultants		\$0	\$0	\$0	\$0	\$0	\$32,225	\$23,725	\$55,950
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$3,780	\$3,780
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$156,258	\$156,258
Total		\$0	\$0	\$0	\$0	\$0	\$32,225	\$183,763	\$215,988
Project Budget	\$606,223						•		•
Less Other Funding	\$0	,							
Net	\$606,223								
Actual Measure S Expenditures	\$215,988								
Running Balance	\$390,235	•							


Grand Total	\$7,958,606	\$14,601,366	\$10,740,621	\$8,321,918	\$20,819,624	\$8,933,245	\$495,050	\$71,870,430

Note: Project 3 had no expenses

1/7/2011 9 of 9

SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure AA Bond Budget As of December 31, 2010

	Project Name	Completion	Project Budget	Measure AA Allocation	Other Funding	Measure AA Expenditures as of 12/31/10	Measure AA Expenditures as of 9/30/10	Measure AA Expenditures Last Period	Total Measure AA Remaining
101	Environmental Performance - Central Plant	November 2013	\$4,882,119	\$4,882,119	\$0	\$48,500	\$48,500	\$0	\$4,833,619
102	Infrastructure & Technology - Information Technology Relocation	February 2014	\$13,287,218	\$13,287,218	\$0	\$218,975	\$199,438	\$19,537	\$13,068,243
103	Media and Technology Complex - Academy Site	February 2014	\$61,480,824	\$57,700,824	\$3,780,000	\$3,812,690	\$3,191,526	\$621,164	\$53,888,134
104	Replacement Health/PE/Fitness/ Dance Building with Central Plant	November 2013	\$39,983,011	\$35,384,240	\$4,598,771	\$598,327	\$350,279	\$248,048	\$34,785,913
105	Drescher - Academic Modernization, Bookstore, Pico Promenade	December 2016	\$34,026,480	\$34,026,480	\$0	\$0	\$0	\$0	\$34,026,480
106	Replacement Math and Science Extension Building	December 2016	\$108,103,000	\$68,259,000	\$40,134,000	\$0	\$0	\$0	\$68,259,000
107	Madison East Wing Seismic Upgrade	May 2013	\$12,292,000	\$12,292,000	\$0	\$220,434	\$186,154	\$34,280	\$12,071,566
108	Renovation of Corsair Stadium	November 2016	\$11,203,000	\$11,203,000	\$0	\$2,352	\$0	\$2,352	\$11,200,648
109	Career Opportunity and Advancement Center (Bundy)	Not Scheduled	\$41,391,000	\$29,384,000	\$12,007,000	\$0	\$0	\$0	\$29,384,000
110	Malibu Center	Not Scheduled	\$31,069,031	\$6,069,031	\$25,000,000	\$0	\$0	\$0	\$6,069,031
111	Business & Facilities Infrastructure	On-Going	\$6,140,952	\$6,140,952	\$0	\$3,095	\$0	\$3,095	\$6,137,857
112	Master Planning, Program Management, Overhead	On-Going	\$1,650,000	\$1,650,000	\$0	\$0	\$0	\$0	\$1,650,000
113	Energy Efficiency Projects	On-Going	\$5,150,136	\$5,150,136	\$0	\$0	\$0	\$0	\$5,150,136
114	Community Classroom & Facility Projects	December 2011	\$3,221,000	\$3,221,000	\$0	\$154,472	\$15,828	\$138,644	\$3,066,528
115	Real Property Acquisition	On-Going	\$6,000,000	\$6,000,000	\$0	\$1,868,667	\$1,748,667	\$120,000	\$4,131,333
116	Roadways, Walkways, Grounds, Parking Lots, and Garages	On-Going	\$350,000	\$350,000	\$0	\$232,733	\$231,758	\$975	\$117,267
	Project Totals		\$380,229,771	\$295,000,000	\$85,519,771	\$7,160,245	\$5,972,150	\$1,188,095	\$287,839,755

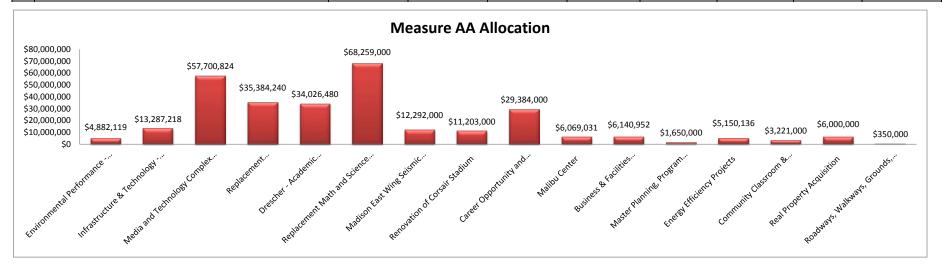

SANTA MONICA COMMUNITY COLLEGE DISTRICT

Measure AA Project Schedule As of December 31, 2010

	Project Name	Completion	2010		2	011	20)12	2	013	;	2014	201	5	20	016
101	Environmental Performance - Central Plant	November 2013														
102	Infrastructure & Technology - Information Technology Relocation	February 2014														
103	Media and Technology Complex - Academy Site	February 2014														
104	Replacement Health/PE/Fitness/Dance Building with Central Plant	November 2013														
105	Drescher - Academic Modernization, Bookstore, Pico Promenade	December 2016														
106	Replacement Math and Science Extension Building	December 2016														
107	Madison East Wing Seismic Upgrade	May 2013														
108	Renovation of Corsair Stadium	November 2016														
109	Career Opportunity and Advancement Center (Bundy)	Not Scheduled														
110	Malibu Center	Not Scheduled														
111	Business & Facilities Infrastructure	On-Going														
112	Master Planning, Program Management, Overhead	On-Going														
113	Energy Efficiency Projects	On-Going														
114	Community Classroom & Facility Projects	December 2011														
115	Real Property Acquisition	On-Going														
116	Roadways, Walkways, Grounds, Parking Lots, and Garages	On-Going														
				In	Plan	ning	In	Cons	tructi	on						

SANTA MONICA COMMUNITY COLLEGE DISTRICT MEASURE AA EXPENDITURES FUND 42.4 As of December 31, 2010

Projects	Budget	09/10 Final	10/11	Combined Totals
AA 7100062				
Environmental Performance - Central Plant (101)				
Legal		\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0
Consultants		\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0
Architect		\$0	\$0	\$0
Engineering		\$48,500	\$0	\$48,500
Inspection & Testing		\$0	\$0	\$0
Project Management		\$0	\$0	\$0
Cap Equipment		\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0
Total		\$48,500	\$0	\$48,500
Project Budget	\$4,882,119			
Less Other Funding	\$0			
Net	\$4,882,119			
Actual Measure AA Expenditures	\$48,500			
Running Balance	\$4,833,619			

SANTA MONICA COMMUNITY COLLEGE DISTRICT MEASURE AA EXPENDITURES **FUND 42.4** As of December 31, 2010

Projects	Budget	09/10 Final	10/11	Combined Totals
AA 7100063				
Infrastructure & Technology - IT Relocation (102)				
Legal		\$0	\$0	\$0
Consultants		\$0	\$0	\$0
Supplies		\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0
Architect		\$105,049	\$35,000	\$140,049
Inspection & Testing		\$10,291	\$490	\$10,781
Project Management		\$33,460	\$34,685	\$68,145
Cap Equipment		\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0
Total		\$148,800	\$70,175	\$218,975
Project Budget	\$13,287,218			
Less Other Funding	\$0			
Net	\$13,287,218			
Actual Measure AA Expenditures	\$218,975			
Running Balance	\$13,068,243			

Infrastructure & Technology -**IT Relocation**

Project Description:Relocation of IT/Telecom Departments, and renovation of Media Center

Facility Size:


9,230 sq/ft

Status:

In design development

Architect:

Morris Architects

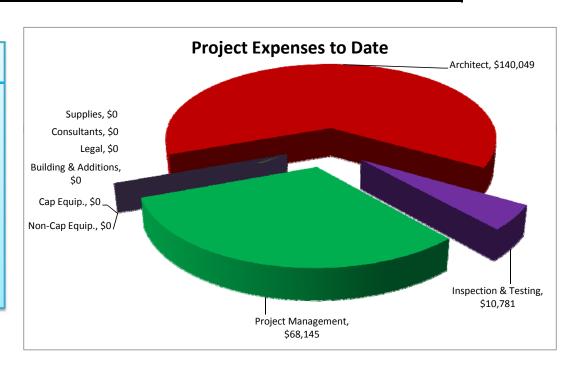

As of December 31, 2010

Projects	Budget	09/10 Final	10/11	Combined Totals	
AA 7100061					
Media and Technology Complex - Academy Site (103)					
Consultants		\$0	\$0		
Supplies		\$0	\$0	\$0	
Legal		\$16,903	\$0		
Other Contract Services		\$3,993	\$1,850	\$5,844	
Advertising		\$0	\$0	\$0	
Building & Additions		\$0	\$0	\$0	
Architect		\$2,097,553	\$1,347,985	\$3,445,538	
Engineering		\$16,459	\$13,526	\$29,986	
Inspection & Testing		\$64,905	\$10,482	\$75,387	
Project Management		\$121,786	\$117,249	\$239,034	
Cap Equipment		\$0	\$0	\$0	
Non-Cap Equipment		\$0	\$0	\$0	
Total		\$2,321,599	\$1,491,092	\$3,812,690	
Project Budget	\$61,480,824	Received			
Less Other Funding*	\$3,780,000	\$803,412			
Net	\$57,700,824	* Other Funding Source:			
Actual Measure AA Expenditures	\$3,812,690	KCRW Foundation \$3,780,000			
Running Balance	\$53,888,134				

Media and Technology Complex - Academy Site

Project Description:

Renovation and new extension to the existing building, new building for KCRW, and a new parking structure

Facility Size:


Building - 47,172 sq/ft Parking Structure - 450 spaces

Status

Building in design development Parking structure in DSA

Architect:

Clive Wilkinson Architects

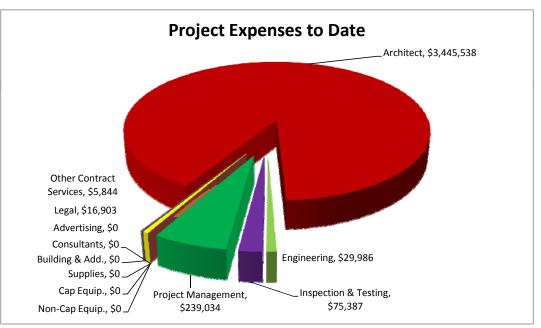

SANTA MONICA COMMUNITY COLLEGE DISTRICT MEASURE AA EXPENDITURES FUND 42.4 As of December 31, 2010

Projects	Budget	09/10 Final	10/11	Combined Totals
AA 7100060				
Repl. Health/PE/Fitness/Dance Building with Central Plant (104)				
Consultants		\$0	\$0	\$0
Supplies		\$0	\$0	\$0
Other Contract Services		\$120	\$0	\$120
Building & Additions		\$0	\$0	\$0
Architect		\$256,076	\$212,951	\$469,027
Inspection & Testing		\$36,892	\$490	\$37,382
Project Management		\$34,968	\$56,830	\$91,798
Total		\$328,056	\$270,271	\$598,327
Project Budget	\$39,983,011			
Less Other Funding*	\$4,598,771			
Net	\$35,384,240		* Other Funding	Source:
Actual Measure AA Expenditures	\$598,327		Measure S \$4,59	98,771
Running Balance	\$34,785,913			

Repl. Health/PE/Fitness/Dance Building with Central Plant

Project Description:

Replacement of locker rooms, fitness center, dance studios, and new central plant

Facility Size:


62,000 sq/ft

Status:

In design development

Architect:

Gensler Architects

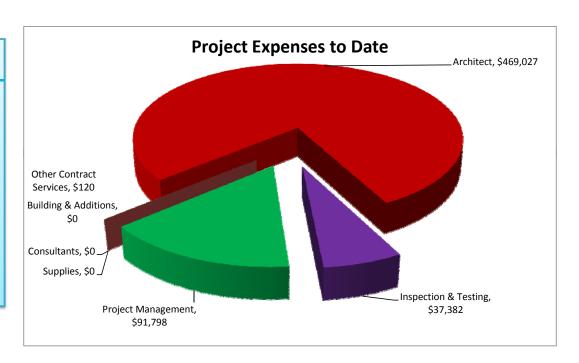

۸ ۵	۰ŧ	Dagam	h ~ r	24	2010	
AS	OI	Decem	ber	31.	2010	ì

Projects	Budget	09/10 Final	10/11	Combined Totals
AA 7100047				
Madison East Wing Seismic Upgrade (107)				
Consultants		\$0	\$0	\$0
Supplies		\$0	\$0	\$0
Legal		\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0
Architect		\$76,073	\$88,417	\$164,490
Inspection & Testing		\$0	\$12,720	\$12,720
Project Management		\$5,557	\$37,667	\$43,224
Total		\$81,630	\$138,804	\$220,434
Project Budget	\$12,292,000	•		
Less Other Funding	\$0			
Net	\$12,292,000			
Actual Measure AA Expenditures	\$220,434			
Running Balance	\$12,071,566			

Madison East Wing Seismic Upgrade

Project Description:
Replacement of east wing with a new multipurpose room and additional classrooms

Facility Size:


15,461 sq/ft

Status:

In design development

Architect:

DLR Group WWCOT

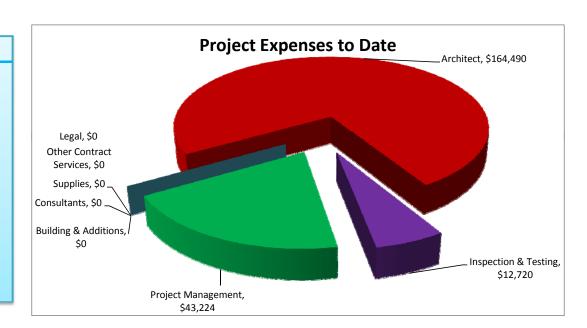

SANTA MONICA COMMUNITY COLLEGE DISTRICT MEASURE AA EXPENDITURES FUND 42.4 As of December 31, 2010

Projects	Budget	09/10 Final	10/11	Combined Totals
AA 7100068				
Renovation to Corsair Stadium (108)				
Other Contract Services		\$0	\$0	\$(
Building & Additions		\$0	\$0	\$(
Architect		\$0	\$0	\$0
Engineering		\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$(
Project Management		\$0	\$2,352	\$2,352
Total		\$0	\$2,352	\$2,352
Project Budget	\$11,203,000			
Less Other Funding	\$0			
Net	\$11,203,000			
Actual Measure AA Expenditures	\$2,352			
Running Balance	\$11,200,648			
AA 7100067 Business & Facilities Infrastructure (111)				
` '		(*0	# 400	# 400
Other Contract Services		\$0	\$169	\$169
Building & Additions		\$0	\$0	\$0
Architect		\$0	\$0	\$0
Engineering		\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0
Project Management		\$0	\$2,926	\$2,926
Total		\$0	\$3,095	\$3,09
Project Budget	\$6,140,952			
Less Other Funding	\$0			
Net	\$6,140,952			
Actual Measure AA Expenditures	\$3,095			
Running Balance	\$6,137,857			
AA 7100064				
Community Classroom & Facility Projects (114)				
Building & Additions		\$0	\$0	\$0
Architect		\$0	\$111,049	\$111,04
Engineering		\$0	\$1,668	\$1,668
Inspection & Testing		\$0	\$1,090	\$1,090
Project Management		\$135	\$40,531	\$40,660
Total		\$135	\$154,337	\$154,472
Project Budget	\$3,221,000	• •	•	•
Less Other Funding	\$0			
Net	\$3,221,000			
Actual Measure AA Expenditures	\$154,472			
Running Balance	\$3,066,528			

SANTA MONICA COMMUNITY COLLEGE DISTRICT MEASURE AA EXPENDITURES FUND 42.4 As of December 31, 2010

Projects	Budget	09/10 Final	10/11	Combined Totals
AA 7100057				
Real Property Acquisition (115)				
Legal		\$0	\$0	\$
Site Acquisition		\$1,739,979	\$120,000	\$1,859,97
Inspection & Testing		\$8,689	\$0	\$8,68
Project Management		\$0	\$0	\$
Total		\$1,748,667	\$120,000	\$1,868,66
Project Budget	\$6,000,000			
Less Other Funding	\$0			
Net	\$6,000,000			
Actual Measure AA Expenditures	\$1,868,667			
Running Balance	\$4,131,333			
	•			
AA 7100058				
Roadways, Walkways, Grounds, Parking Lots, and Garages (116)				
Legal		\$0	\$0	9
Other Contract Services		\$218	\$750	\$96
Building & Additions		\$185,345	\$0	\$185,34
Inspection & Testing		\$13,380	\$3,120	\$16,50
Project Management		\$24,404	\$5,516	\$29,92
Total		\$223,347	\$9,386	\$232,73
Project Budget	\$350,000	<u>.</u>		
Less Other Funding	\$0			
Net	\$350,000			
Actual Measure AA Expenditures	\$232,733			
Running Balance	\$117,267			
Grand Total		\$4,900,734	\$2,259,513	\$7,160,24


SANTA MONICA COMMUNITY COLLEGE DISTRICT Bond Sales / Expenses Report As of December 31, 2010

Measure U Bond \$160,000,000		
Bond Issue Date		Amount
	2002	\$25,000,000
	2004	\$21,999,971
	2005	\$89,999,923
	2007	\$11,999,987
	2010	\$10,998,992
Total Available		\$159,998,873
Expenses as of 12-31-10		\$143,218,678
Total Available Remaining		\$16,780,195
Unsold Bond Amount		\$1,127
Total Available as of 1-1-11		\$16,781,322

Measure S Bond \$143,500,000 (1)		
Bond Issue Date		Amount
	2005	\$58,000,000
	2007	\$8,500,000
	2009	\$56,997,857
Total Available		\$123,497,857
Expenses as of 12-31-10		\$71,870,431
Total Available Remaining		\$51,627,426
Unsold Bond Amount		\$20,002,143
Total Available as of 1-1-11		\$71,629,569

Measure AA Bond \$295,000,000	
Bond Issue Date	Amount
2	\$100,000,000
Total Available	\$100,000,000
Expenses as of 12-31-10	\$7,160,245
Total Available Remaining	\$92,839,755
Unsold Bond Amount	\$195,000,000
Total Available as of 1-1-11	\$287,839,755

Total Bond	\$598,500,000
Total Available	\$383,496,730
Total Expenses as of 12-31-10	\$222,249,354
Total Available Remaining	\$161,247,376
Total Unsold Bond	\$215,003,270

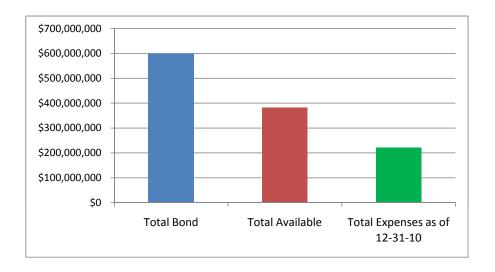

Interest	Measure U	Measure S	Measure AA
As of 6-30-10	\$5,694,648	\$7,329,902	\$512,487
Arbitrage Payment as of 6-30-10	\$0	\$393,004	\$0
Available Interest as of 6-30-10	\$5,694,648	\$6,936,898	\$512,487

Cost of Issuance Refund	Measure U	Measure S
As of 6-30-10	\$20,688	\$35,575
