

Santa Monica Community College District

Citizens' Bond Oversight Committee MEETING – APRIL 20, 2011

AGENDA

A meeting of the Santa Monica Community College District Citizens' Bond Oversight Committee will be held on Wednesday, **April 20, 2011 at 8 a.m.**

The meeting will be held in Drescher 300-E (the Loft) at Santa Monica College, 1900 Pico Boulevard, Santa Monica, California.

I. CALL TO ORDER

2. ROLL CALL

Bruce Sultan, Chair Paul Leoni, Vice-Chair Deborah Arveson Clarence Chapman Todd Flora Tiffany Inabu Corin Kahn Nimish Patel Christine Thornton

3. APPROVAL OF MINUTES

Citizens' Bond Oversight Committee meeting of January 19, 2011 (enclosed)

4 PUBLIC COMMENTS

5. REPORTS and DISCUSSION)

- Articles on Los Angeles Community College District Bond Construction Program
- Role of Citizens' Bond Oversight Committee, to be presented by Lisel Wells, Bond Counsel
- Reports Enclosed

Measure U

- Project Schedule
- Budget
- Expenditures

Measure S

- Project Schedule
- Budget
- Expenditures

Measure AA

- Project Schedule
- Budget
- Expenditures

Bond Sales/Expenses Report

6. ELECTION VICE-CHAIR FOR 2011-2012

Chair Bruce Sultan will conduct the election for Vice-Chair, 2011-2012

7. INFORMATION - Expiring terms of members of the Citizens' Bond Oversight Committee

The terms of the following members of the Citizens' Bond Oversight Committee are expiring effective July 1, 2011 and are eligible for reappointment for a second two-year term:

Clarence Chapman Bruce Sultan

The terms of the following members of the Citizens' Bond Oversight Committee are expiring effective July 1, 2011 and are not eligible for reappointment for a second two-year term:

Deborah Arvesen Paul Leoni

The Board of Trustees will follow a recruitment and application process to appoint/reappoint members to fill the vacancies.

8. SCHEDULE OF MEETINGS, 2011-2012

Wednesdays at 8 a.m. July 20, 2011 October 19, 2011 January 18, 2012 April 18, 2012

9. ADJOURNMENT

The next meeting of the Citizens' Bond Oversight Committee will be held on Wednesday, July 20, 2011 at 8 a.m. at a Santa Monica College location.

Santa Monica Community College District

Citizens' Bond Oversight Committee MEETING - January 19, 2011 **MINUTES**

A meeting of the Santa Monica Community College District Citizens' Bond Oversight Committee was held on Wednesday, January 19, 2011 in Drescher Hall Room 300-E (the Loft) at Santa Monica College, 1900 Pico Boulevard, Santa Monica, California.

I. CALL TO ORDER - 8:05 a.m.

2. **ROLL CALL**

Bruce Sultan, Chair - Present Paul Leoni, Vice-Chair - Present Deborah Arvesen -Present Clarence Chapman - Present Todd Flora - Present Tiffancy Inabu -Present Corin Kahn - Not Present Nimish Patel - Present Christine Thornton - Not Present

Others Present:

Sara Banda, representing Vicenti Lloyd & Stutzman, LLP Chris Bonvenuto, Director of Fiscal Services Greg Brown, Director of Facilities and Planning Don Girard, Senior Director, Government Relations/Institutional Communications Bob Isomoto, Vice-President, Business/Administration Lee Paul, LPI Inc. Lisa Rose, Committee Coordinator Charlie Yen, Director, Contracts

APPROVAL OF MINUTES - October 20, 2010 3.

Motion was made by Paul Leoni and seconded by Clarence Chapman to approve the minutes of October 20, 2010, as corrected.

Paul Leoni Motion made by: Seconded by: Todd Flora

Unanimously approved

4. **INTRODUCTION OF NEW MEMBER**

Tiffany Inabu was appointed by the Board of Trustees to serve as the student representative on the Citizens' Bond Oversight Committee.

5. **CONFLICT OF INTEREST FORMS**

Members were reminded to sign and submit their Conflict of Interest forms for 2011.

6. REPORTS and DISCUSSION

2009-2010 Financial Audit and Performance Audit Reports

Chris Bonvenuto, Director of Fiscal Services, provided an overview of the 2009-2010 Financial Audit and Performance Audit Reports. The Auditor indicated that there were no instances of noncompliance in both audits and did not identify any exceptions or deficiencies. *Highlights are attached*.

Motion was made by Paul Leoni and seconded by Deborah Arvesen to accept without exception the 2009-2010 Audit Reports: *Unanimously approved*.

Measure U, S and AA and Bond Sales Expenses Reports (reports included with agenda)

- Charlie Yen reported that the following clarifications suggested at the last meeting have been incorporated into the detailed oversight reports: All Reports include other funding amounts and sources; Measure S Reports shows Malibu other expenses (Storm/Waste Water Treatment Center)
- The pie charts included on the individual project pages shows expenses to date. Most projects are in the planning stage, so the expenses for architects are the majority of expenses to date.
- The length of time for the Department of State Architect (DSA) to approve construction projects is unbelievably long at this time, about double what it should be. It is planned to start the construction phase on the Student Services project and the parking structure at the Academy of Entertainment and Technology this summer. The delay in DSA affects the sale of bonds, employment for construction projects and sequencing of projects.
- It was suggested that future expenditure/oversight reports indicate funds allocated versus funds appropriated.

Bon	d	Sal	es/	Expenses	R	Report.	

The Bond Sales/Expenses Report indicates total bond amounts, bond issue dates/amounts, unsold bond amount and total available as of January 1, 2011.

7. **PUBLIC COMMENTS** - None

8. SCHEDULE OF MEETINGS, 2010-2011

Wednesdays at 8 a.m. April 20, 2011

9. ADJOURNMENT – 9:13 a.m.

The next meeting of the Citizens' Bond Oversight Committee will be held on Wednesday, April 20, 2011 at 8 a.m. (location to be determined).

SANTA MONICA COMMUNITY COLLEGE DISTRICT Financial Audit - Measure U, MEASURE S AND MEASURE AA Bond Items to Communicate to the Citizens Oversight Committee For the Year Ended June 30, 2010

Vicenti, Lloyd & Stutzman LLP has prepared the following information to communicate to the Citizens Oversight Committee the highlights of the audit report based upon the results of our 2009-10 audit of the Bond Construction Fund.

ITEMS TO COMMUNICATE

Independent Auditors' Report Pages 1 – 2

Provides the auditors' opinion on the fairness of the financial statements of the Bond Building Fund prepared by management and whether the financial statements are prepared in accordance with generally accepted accounting principles.

Fund Financial Statements Pages 3 –7

Fund financial statements follow generally accepted accounting principles as prescribed by the Governmental Accounting Standards Board. There are three statements required:

- 1) Balance Sheet
- 2) Statement of Revenues, Expenditures and Change in Fund Balance.
- Statement of Revenues, Expenditures and Change in Fund Balance – Budget and Actual.

HIGHLIGHT

Our opinion is that the financial statements are fairly presented and follow generally accepted accounting principles.

These financial statements provide a short-term perspective by being prepared on a modified cash basis of accounting. Capital assets and long-term liabilities associated with the Bond Building Fund are accounted for in the basic financial statements of the Santa Monica Community College District.

ITEMS TO COMMUNICATE

Footnotes Pages 8-19

The footnotes are an integral part of the financial statements – the financial statements would be incomplete without footnotes. The footnotes help to explain the accounting policies of the District and give more insight into the numbers included on the financial statements related to the Bond Building Fund.

Internal Control and Compliance Letter Required by Government Auditing Standards Pages 20 –21

This letter discusses whether, during the course of our audit, we noted any material issues of non-compliance with local or state laws and/or regulations; also, whether any internal control issues were noted regarding the processing of "on-going" transactions.

Findings and Responses Page 22

This section includes any compliance and/or internal control findings.

Bond Projects Summary Pages 23-25

This section provides a summary of expenditures by project.

HIGHLIGHT

Some of the key footnotes are:

Note 1 – Accounting Policies

Note 2 - Deposits

Note 4 – Bonded Debt

Note 5 – Commitments

It should be noted that findings are a by-product of the audit and not the primary purpose of the audit. The primary purpose of an audit is to give our opinion on the financial statements as noted above.

There were no findings related to internal controls or compliance.

Provides cumulative information on individual projects funded by each Bond Measure.

This report is intended solely for the use of the Santa Monica Community College District's Citizens Oversight Committee, management and others within the organization.


SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure U Project Schedule As of March 31, 2011

	Project Name	Completion	2010	2011	2012	2013	2014
∢	Purchase of BAE Airport Site	Completed					
В	Emeritus College Facility	Completed					
ပ	Purchase of 1738 Pearl Street	Completed					
□	PE Temp. Bldg. Replacement	Completed					
Ш	Remodel Library Village for Math	Completed					
ш	SM Airport Campus Site Improvements	Completed					
Q	SM Airport Campus West Building	Completed					
ェ	Theater Arts Renovation	Completed					
_	Earthquake Rpl. Liberal Arts North	Completed					
7	Music Complex	Completed					
×	Earthquake Rpl. Liberal Arts South	Completed					
_	Shuttle Replacement Parking	Completed					
Σ	North Quad Plaza	Completed					
z	Letters & Sci Demo/Restore	Move to AA					
0	Student Services Building	May 2014					
Ф	Science Complex Addition	Move to AA					
Ø	Infrastructure & Safety	Completed					
X	Restroom Improvements	Completed					
တ	Master Planning	Completed					
⊢	14th and Pico Project	On Hold					
	* SM Airport Campus also known as Bundy Site	Site	In Cor	In Construction			

SANTA MONICA COMMUNITY COLLEGE DISTRICT

Measure U Bond Budget
As of March 31, 2011

\$17,556,122	-\$774,800	\$143,218,678	\$142,443,878	\$52,800,237	\$160,000,000	\$212,800,237		Project Totals	
\$0	\$0	\$319,242	\$319,242	\$0	\$319,242	\$319,242	On Hold	14th and Pico Project	-
\$0	\$0	\$2,110,430	\$2,110,430	\$0	\$2,110,430	\$2,110,430	Completed	Master Planning	S
\$0	\$0	\$17,501	\$17,501	\$0	\$17,501	\$17,501	Completed	Restroom Improvements	æ
\$99,481	\$40,002	\$3,890,801	\$3,930,803	\$0	\$4,030,284	\$4,030,284	Completed	Infrastructure & Safety	D
\$0	\$0	\$308,336	\$308,336	\$0	\$308,336	\$308,336	Move to AA	Science Complex Addition	₽
\$18,732,580	\$9,479	\$2,071,619	\$2,081,098	\$32,708,239	\$20,813,678	\$53,521,913	May 2014	Student Services Building	0
\$0	\$0	\$0	\$0	\$0	\$0	\$0	Move to AA	Letters & Sci Demo/Restore	z
\$2,518	\$10,482	\$11,377,981	\$11,388,463	\$0	\$11,390,981	\$11,390,981	Completed	North Quad Plaza	≤
\$0	\$0	\$18,969,509	\$18,969,509	\$0	\$18,969,509	\$18,969,509	Completed	Shuttle Replacement Parking	_
\$0	\$0	\$6,108,150	\$6,108,150	\$10,625,070	\$6,108,150	\$16,733,220	Completed	Earthquake Rpl. Liberal Arts South	⋝
\$1,000	\$0	\$2,004,434	\$2,004,434	\$2,618,113	\$2,005,434	\$4,623,547	Completed	Music Complex	ے
-\$1,280,457	-\$834,763	\$8,467,972	\$7,633,209	\$6,154,973	\$6,352,752	\$12,507,725	Completed	Earthquake Rpl. Liberal Arts North	-
\$1,000	\$0	\$19,496,949	\$19,496,949	\$0	\$19,497,949	\$19,497,949	Completed	Theater Arts Renovation	I
\$0	\$0	\$19,709,741	\$19,709,741	\$0	\$19,709,741	\$19,709,741	Completed	SM Airport Campus West Building	വ
\$0	\$0	\$4,170,264	\$4,170,264	\$0	\$4,170,264	\$4,170,264	Completed	SM Airport Campus Site Improvements	П
\$0	\$0	\$1,458,690	\$1,458,690	\$0	\$1,458,690	\$1,458,690	Completed	Remodel Library Village for Math	Ш
\$0	\$0	\$2,797,033	\$2,797,033	\$0	\$2,797,033	\$2,797,033	Completed	PE Temp. Bldg. Replacement	o
\$0	\$0	\$749,208	\$749,208	\$0	\$749,208	\$749,208	Completed	Purchase of 1738 Pearl Street	ဂ
\$0	\$0	\$8,909,940	\$8,909,940	\$693,842	\$8,909,940	\$9,603,782	Completed	Emeritus College Facility	В
\$0	\$0	\$30,280,878	\$30,280,878	\$0	\$30,280,878	\$30,280,878	Completed	Purchase of BAE Airport Site	×
Total Measure U Remaining	Measure U Expenditures Last Period	Measure U Expenditures as of 12/31/10	Measure U Expenditures as of 3/31/11	Other Funding	Measure U Allocation	Project Budget	Completion	Project Name	

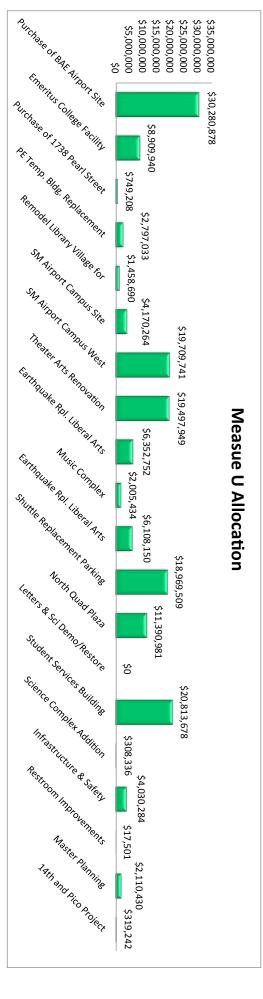

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final 09/10 Final	09/10 Final	10/11	Combined Totals
U7100010											
Purchase of BAE Airport Site (A)											
Site Acquisition		\$0	\$0	\$0	\$30,280,878	\$0	\$0	\$0	\$0	\$0	\$30,280,878
Total		\$0	\$0	\$0	\$30,280,878	\$0	\$0	\$0	\$0	\$0	\$30,280,878
Project Budget	\$30,280,878										•
_ess Other Funding	\$0										
Net	\$30,280,878										
Actual Measure U Expenditures	\$30,280,878										
Running Balance	\$0										
20000											
07100026											
Emeritus College Facility (B)											
Site Acquisition		\$8,658,675	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$8,658,675
Legal		\$14,649	\$3,009	\$20,421	\$0	\$0	\$0	\$0	\$0	\$0	\$38,078
Architect		\$93,735	\$27,831	\$161	\$0	\$0	\$0	\$0	\$0	\$0	\$121,727
Engineering		\$18,400	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$18,400
Supply		\$0	\$4,461	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,461
Building & Additions		\$0	\$17,496	\$0	\$4,000	\$0	\$0	\$0	\$0	\$0	\$21,496
Cap Equipment		\$0	\$49,406	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$49,406
Non-Cap Equipment		\$0	-\$2,197	\$0	-\$108	\$0	\$0	\$0	\$0	\$0	-\$2,305
Total		\$8,785,459	\$100,007	\$20,582	\$3,892	\$0	\$0	\$0	\$0	\$0	\$8,909,940
Project Budget	\$9,603,782	Received									
Less Other Funding*	\$693,842	\$693,842	*	* Other Funding Source:	Source:						
Net	\$8,909,940			Emeritus Colleç	ge Foundation	Emeritus College Foundation \$693,842 received	/ed				
Actual Measure U Expenditures	\$8,909,940										
Running Balance	\$0										
U7100006											
1738 Pearl Street (C)											
Site Acquisition		\$0	\$704,534	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$704,534
Site Improvement		\$0	\$3,250	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,250
Building & Additions		\$0	\$41,424	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$41,424
Total		\$0	\$749,208	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$749,208
Project Budget	\$749,208										
Less Other Funding	\$0										
Net	\$749,208										
Actual Measure U Expenditures	\$749,208										
Running Balance	\$0										

4/5/11 1 of 9

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final 09/10 Final	09/10 Final	10/11	Combined Totals
17100026											
PE Temporary Building Replacement (D)											
Architect		\$148,055	\$42,372	\$6,220	\$485	\$0	\$0	\$0	\$0	\$0	\$197,133
Building & Additions		\$43,866	\$1,922,493	\$415,932	\$0	\$0	\$0	\$0	\$0	\$0	\$2,382,291
Inspection & Testing		\$6,455	\$136,510	\$716	\$0	\$0	\$0	\$0	\$0	\$0	\$143,681
Project Management		\$4,800	\$56,247	\$5,225	\$0	\$0	\$0	\$0	\$0	\$0	\$66,272
Advertising and Moving Expenses		\$763	\$0	\$6,893	\$0	\$0	\$0	\$0	\$0	\$0	\$7,656
Total Total		\$203,939	\$2,157,622	\$434,987	\$485	\$0	\$0	\$0	\$0	\$0	\$2,797,033
Project Budget	\$2,797,033										
Less Other Funding	\$0										
Net	\$2,797,033										
Actual Measure U Expenditures	\$2,797,033										
Running Balance	\$0										
J7100310											
Remodel Library Village for Math (E)											
Moving Exp.		\$0	\$38,625	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$38,625
Building & Additions		\$0	\$1,036,490	\$115,653	\$0	\$0	\$0	\$0	\$0	\$0	\$1,152,143
Architect		\$104,992		\$1,340	\$486	\$0	\$0	\$0	\$0	\$0	\$133,959
Engineering		\$0	\$2,658	\$0		\$0	\$0	\$0	\$0	\$0	\$2,658
Inspection & Testing		\$0		\$25,175	\$0	\$0	\$0	\$0	\$0	\$0	\$52,258
Project Management		\$0		\$4,400		\$0	\$0	\$0	\$0	\$0	\$56,079
Advertising and Moving Expenses		\$207		\$12,623		\$0	\$0	\$0	\$0	\$0	\$22,967
Total		\$105,199	\$1	\$159,191	\$486	\$0	\$0	\$0	\$0	\$0	\$1,458,690
Project Budget	\$1,458,690										
Less Other Funding	\$0										
Net	\$1,458,690										
otical Manager III Figure ditions	\$1.458.600										
Actual Measure o Experiolures	\$1, 1 00,000										

2 of 9

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
J7100027											
SM Airport Campus Site Improvements (F)											
Supplies		\$0	\$26,234	\$975	\$5,873	\$0		\$0	\$0	\$0	\$33,082
Misc Fees		\$0	\$25	\$0		\$34,274		\$0	\$0	\$0	\$34,299
Other Contract Services		\$3,860	\$11,508	\$8,434				\$0	\$0	\$0	\$25,302
Site Improvement		\$0	\$0	\$15,182				\$0	\$0	\$0	\$28,209
Building & Additions		\$0	\$1,495,697	\$1,670,788	\$4,824			\$0	\$0	\$0	\$3,171,309
Architect		\$104,934	\$500	\$0		\$0	\$0	\$0	\$0	\$0	\$149,004
Engineering		\$35,000	\$148,304	\$8		\$0		\$0	\$0	\$0	\$194,294
Inspection & Testing		\$5,032	\$118,662	\$19				\$0	\$0	\$0	\$314,965
Project Management		\$750	\$155,798		\$1,365			\$0	\$0	\$0	\$196,558
City Fees, Advertising and Security System		\$16,587	\$1,802					\$0	\$0	\$0	\$23,241
Total		\$166,163	\$1,958,530	\$1,926,352	\$7	\$46,106	\$0	\$0	\$0	\$0	\$4,170,264
Project Budget	\$4,170,264										
Less Other Funding	\$0										
Net	\$4,170,264										
Actual Measure U Expenditures	\$4,170,264										
Running Balance	\$0										
U7110027											
SM Airport Campus West Building (G)											
Supply		\$0	\$0	\$17,650	\$28,017	\$0	\$0	\$0	\$0	\$0	\$45,667
Other Contract Services		\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0	\$3,576
Moving Expenses		\$0	\$0	\$1		\$0		\$0	\$0	\$0	\$16,00
Building & Additions		\$0	\$0		\$1,	\$46,946		\$0	\$0	\$0	\$16,340,540
Architect		\$0	\$971,954	\$1,043,950				\$0	\$0	\$0	\$2,066,830
Engineering		\$0	\$2,920			\$963	\$0	\$0	\$0	\$0	\$18,693
Inspection & Testing		\$0	\$21,173	\$126,510	\$9,856		\$0	\$0	\$0	\$0	\$157,538
Project Management		\$0	\$14,450	\$313,715			\$0	\$0	\$0	\$0	\$342,121
Cap Equipment		\$0	\$49,795	\$326,382		\$0	\$0	\$0	\$0	\$0	\$380,969
Non-Cap Equipment		\$0	\$0	\$280,558	•	\$0	\$0	\$0	\$0	\$0	\$337,798
Total		\$0		\$17,156,277	\$1,444,115	\$49,056	\$0	\$0	\$0	\$0	\$19,709,741
Project Budget	\$19,709,741		\$1,060,292			+					
Less Other Funding			\$1,060,292			,					
	\$0		\$1,060,292			1 - 2 - 2 - 2 - 2					
Net	\$0 \$19,709,741		\$1,060,292			7 - 7					
Net Actual Measure U Expenditures	\$0 \$19,709,741 \$19,709,741		\$1,060,292			1					

3 of 9

Projects	Budget	02/03 Final	03/04 Final	02/03 Final 03/04 Final 04/05 Final 05/06 Final		06/07 Final	07/08 Final	07/08 Final 08/09 Final 09/10 Final	/10 Final	10/11 C	Combined Totals
7100025											
Theatre Arts Renovation (H)											
Supplies		\$0	\$8,904	-\$14	\$12,858	\$16,619	\$0	\$0	\$0	\$0	\$38,367
-egal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
oving Services		\$0	\$0	\$0	\$0	\$14,061	\$0	\$0	\$0	\$0	\$14,061
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$5,245	\$0	\$0	\$5,245
Rental / Lease		\$0	\$1,446	\$2,200	\$0	\$0	\$0	\$0	\$0	\$0	\$3,64
Building & Additions		\$528	\$1,326,630	\$4,540,487	\$10,897,603	\$56,122	\$25,220	\$0	\$0	\$0	\$16,846,590
Architect		\$289,913	\$369,213	\$423,416	\$82,639	\$0	\$0	\$0	\$0	\$0	\$1,165,181
Engineering		\$6,174	\$2,981	\$16,606	\$2,375	\$1,250	\$0	\$0	\$0	\$0	\$29,386
nspection & Testing		\$150	\$14,785	\$353,890	\$297,675	\$1,116	\$0	\$0	\$0	\$0	\$667,616
Project Management		\$150	\$45,698	\$184,219	\$193,898	\$14,818	\$230	\$0	\$0	\$0	\$439,01
Cleaning, Storage and Installation		\$0	\$812	\$0	\$2,548	\$2,267	\$0	\$0	\$0	\$0	\$5,627
Cap Equipment		\$0	\$31,638	\$0	\$6,458	\$59,689	\$0	\$0	\$0	\$0	\$97,78
Non-Cap Equipment		\$0	\$2,388	\$0	\$36,749	\$145,294	\$0	\$0	\$0	\$0	\$184,432
Total		\$296,915	\$1,804,496	\$5,520,804	\$11,532,803	\$311,236	\$25,450	\$5,245	\$0	\$0	\$19,496,949
Project Budget	\$19,497,949										
Less Other Funding	\$0										
Net	\$19,497,949										
Actual Measure U Expenditures	\$19,496,949										
Running Balance	\$1,000										
U7100110											
Earthquake Rpl. Liberal Arts North (I)											
Supplies		\$0	\$0	\$0	\$0	\$1,408	\$0	\$75	\$0	\$0	\$1,483
-egal		\$0	\$0	\$0	\$0	\$887	\$0	\$0	\$0	\$0	\$887
Other Contract Services		\$0	\$0	\$0	\$0	\$75	\$0	\$0	\$0	\$0	\$7
Building & Additions		\$265	\$0	\$1,043,660	\$5,916,281	-\$973,001	\$321,345	\$14,898	\$0	-\$834,764	\$5,488,685
Architect		\$0	\$611,732	\$102,824	\$209,490	\$216,563	\$21,215	\$3,465	\$0	\$0	\$1,165,289
ngineering		\$3,248	\$4,295	\$0	\$250	\$0	\$250	\$0	\$0	\$0	\$8,04
Inspection & Testing		\$0	\$0	\$28,312	\$326,203	\$77,942	\$0	\$0	\$0	\$0	\$432,458
Project Management		\$0	\$26,072	\$33,549	\$128,937	\$124,222	\$255	\$1,155	\$286	\$0	\$314,475
Advertising and Fees		\$0	-\$4	\$7,334	\$0	\$0	\$0	\$0	\$0	\$0	\$7,33
Cap-Equipment		\$0	\$0	\$0	\$0	\$25,356	\$12,579	\$0		\$0	\$37,935
Non-Cap Equipment		\$0	\$0	\$0	\$2,033	\$170,425	\$4,093	\$0	\$0	\$0	\$176,550
Total Total		\$3,513	\$642,095	\$1,215,679	\$6,583,194	-\$356,123	\$359,737	\$19,592	\$286	-\$834,764	\$7,633,209
Project Budget	\$12,507,725	Received									
_ess Other Funding*	\$6,154,973	\$4,874,517		* Other Funding Source:	Source:						
Net	\$6,352,752		_	City of Santa Monica \$4,039,753 received	onica \$4,039,75	3 received					
Actual Measure U Expenditures	\$7,633,209			FEMA \$2,115,22	20 commited, \$8	FEMA \$2,115,220 commited, \$834,764 received	ŭ				
Dinning Balance	_\$1 280 457										

4 of 9

Projects	Budget	02/03 Final 03/04 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final 08/09 Final 09/10 Final	08/09 Final ()9/10 Final	10/11	Combined Totals
J7100013, U7100047											
Music Complex (J)											
Advertising		\$0	\$0	\$436	\$0	\$0	\$0	\$0	\$0	\$0	\$436
Supplies		\$0	\$0	\$0	\$0	\$194	\$19,094	\$0	\$0	\$0	\$19,288
Consultants		\$0	\$0	\$0	\$0	\$0	\$36,000	\$0	\$0	\$0	\$36,000
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$180	\$0	\$0	\$0	\$180
Moving Services		\$0	\$0	\$0	\$0	\$0	\$6,330	\$0	\$0	\$0	\$6,33
Building & Additions		\$0	\$0	\$356,464	\$1,293,726	-\$737,213	\$273,531	\$0	\$0	\$0	\$1,186,509
Architect		\$0	\$187,922	\$22,500	\$37,227	\$38,448	\$4,052	\$14,356	\$0	\$0	\$304,505
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$21,370	\$0	\$0	\$21,370
Inspection & Testing		\$0	\$0	\$29,740	\$19,265	\$26,238	\$35,880	\$0	\$0	\$0	\$111,122
Project Management		\$0	\$170	\$36,739	\$36,351	\$56,914	\$16,200	\$1,288	\$0	\$0	\$147,66
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$62,600	\$0	\$0	\$0	\$62,600
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$29,852	\$78,582	\$0	\$0	\$0	\$108,434
Total		\$0	\$188,092	\$445,879	\$1,386,568	-\$585,566	\$532,447	\$37,014	\$0	\$0	\$2,004,434
Project Budget	\$4,623,547	Received									
ess Other Funding*	\$2,618,113	\$2,618,113	*	* Other Funding Source:	Source:						
Net	\$2,005,434		T	Prop T Refinant	Prop T Refinance \$2,618,113 received	eceived					
Actual Measure U Expenditures	\$2,004,434										
Running Balance	\$1,000										
U7100111											
Earthquake Rpl. Liberal Arts South (K)											
Supply		\$0	\$0	\$855	\$2,497	\$379	\$23,811	\$75	\$0	\$0	\$27,61
_egal		\$0	\$0	\$0	\$0	\$0	\$2,203	\$50	\$0	\$0	\$2,25
Moving Services		\$0	\$0	\$0	\$0	\$0	\$4,063	\$0	\$0	\$0	\$4,063
Consultants		\$0	\$0	\$0	\$17,265	\$41,435	\$0	\$0	\$0	\$0	\$58,70
Other Contract Services		\$0	\$0	\$6,154	\$202	\$0	\$0	\$0	\$0	\$0	\$6,356
Building & Additions		\$0	\$0	\$26,302	\$3,091,306	\$5,706,802	-\$4,642,459	\$0	\$91,516	\$0	\$4,273,467
Architect		\$0	\$0	\$836,555	-\$503,297	\$163,506	\$183,877	\$39,984	\$2,549	\$0	\$723,17
Engineering		\$0	\$0	\$3,125	\$150	\$5,344	\$500	\$0	\$0	\$0	\$9,11
nspection & Testing		\$0	\$0	\$0	\$179,798	\$296,015	\$68,273	\$0	\$0	\$0	\$544,086
Project Management		\$0	\$0	\$0	\$43,989	\$262,598	\$52,690	\$1,722	\$1,278	\$0	\$362,276
Cap-Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$58,726	\$45,388	-\$7,074	\$0	\$0	\$97,040
Total Total		\$0	\$0	\$872,991	\$2,831,909	\$6,534,806	-\$4,261,655	\$34,757	\$95,342	\$0	\$6,108,150
Project Budget	\$16,733,220	Received				,					
_ess Other Funding*	\$10,625,070	\$10,625,070	*	* Other Funding Source:	Source:						
Vet	\$6,108,150		0	City of Santa M	City of Santa Monica \$6,167,070 received	0 received					
Actual Measure U Expenditures	\$6,108,150		(0	State of Californ	State of California \$4,458,000 received	eceived					
	+										

5 of 9

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final 09/10 Final	09/10 Final	10/11	Combined Totals
117100221											
Shuttle Replacement Parking (L)											
Supplies		\$0	\$0	\$0	\$0	\$0	\$1,347	\$0	\$0	\$0	\$1,347
Legal		\$0	\$0	\$0	\$8,462	\$35,103		0\$	\$0	\$0	\$43,565
Site Acquisition		\$0	\$0	\$0	\$0	\$16,903,087	0\$	0\$	\$0	\$0	\$16,903,087
Site Improvement		\$0	\$0	\$0	\$0	\$3,027		0\$	\$0	\$0	\$3,027
Building & Additions		\$0	\$0	\$0	\$0	\$484,000	\$1,252,2	\$2,3	\$0	\$0	\$1,738,577
Architect		\$0	\$0	\$0	\$0	\$51,569			\$0	\$0	\$58,777
Inspection & Testing		\$0	\$0	\$0	\$0	\$139,822		\$0	\$0	\$0	\$181,072
Project Management		\$0	\$0	\$0	\$0	\$7,631			\$0	\$0	\$40,056
Total		\$0	\$0	\$0	\$8,462	\$17,624,240	\$1,334,455	\$2,	\$0	\$0	\$18,969,509
Project Budget	\$18,969,509										
Less Other Funding	\$0										
Net	\$18,969,509										
Actual Measure U Expenditures	\$18,969,509	_									
Running Balance	\$0										
J7100321											
North Quad Plaza (M)											
Legal		\$0	\$0	\$0	\$0	\$0	\$3,825		\$0	\$0	\$9,429
Building & Additions		\$0	\$0	\$0	\$0	-\$443	\$6,`		\$0	\$0	\$9,764,125
Architect		\$0	\$231,055	\$8,444	\$140,048	\$435,618		\$68,633	\$2,901	\$10,483	\$1,068,407
Engineering		\$0	\$0	\$0	\$0	\$0			\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0			\$328	\$0	\$294,025
Project Management		\$0	\$0	\$760	\$210	\$2,200	\$135,601		\$606	\$0	\$195,158
Printing		\$0	\$1,900	\$0	\$0	\$0		0\$	\$0	\$0	\$1,900
Cap Equipment		\$0	\$0	\$0	\$0	\$0			\$0	\$0	\$55,420
Total		\$0	\$232,955	\$9,204	\$140,258	\$437,375	\$6,626,952	40	\$3,834	\$10,483	\$11,388,463
Project Budget	\$11,390,981										
Less Other Funding	\$0										
Net	\$11,390,981										
Actual Measure U Expenditures	\$11,388,463										
Running Balance	\$2.518										

6 of 9

02/03 Final | 03/04 Final | 04/05 Final | 05/06 Final | 06/07 Final | 07/08 Final | 08/09 Final | 09/10 Final |

10/11

Combined Totals

Budget

Student Services Building

Project Discription:


single complex at the front of the campus departments and college administration in a Consolidates various student services

Facility Size: 83,634 sq/ft & 500 cars underground parking structure

Status: In plan check with DSA

Architect: Steinberg Architects

Contractor:

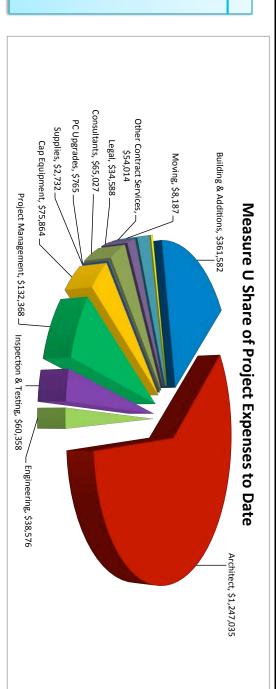

4/5/11 7 of 9

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final 09/10 Final	09/10 Final	10/11	Combined Totals
U7100090											
Science Complex Additional (P)											
Architect		\$0	\$0	\$0	\$0	\$246,425	\$61,911	\$0	\$0	\$0	\$308,336
Total		\$0	\$0	\$0	\$0	\$246,425	\$61,911	\$0	\$0	\$0	\$308,336
Project Budget	\$308,336										
Less Other Funding	0\$										
Net	\$308,336										
Actual Measure U Expenditures	\$308,336										
Running Balance	\$0										
U6780000, U7100022, U7100331, U7100550,											
U/100005, U/100030, U/100031, U/100029, UZ100003 UZ100008 UZ100332 UZ1000Z2											
U7100042, U7100056, U7100039											
Infrastructure & Safety (Q)											
Supplies		\$0	\$0	\$254	\$0	\$0	\$0	\$1,700	\$1,393	\$0	\$3,347
Consultants		\$0	\$0	\$0	\$0	\$0	\$0	\$16,734	\$0	\$0	\$16,734
Legal		\$0	\$0	\$0	\$0	\$0	\$3,527	\$3,294	\$0	\$0	\$6,821
Other Contract Services		\$0	\$0	\$0	\$0		\$7,825	\$81,445	\$203,383	\$0	\$292,653
Building & Additions		\$681,900	\$195,175	\$20,600	\$0	\$200	\$733	\$0	\$0		\$1,099,028
Architect		\$69,081	\$42,108	\$0	\$155,321	\$448	\$91,127	\$4,227	\$0		\$810,370
Engineering		\$8,050	\$0	\$0	\$6,750	\$12	\$18,429	\$2,360	\$0		\$47,589
Inspection & Testing		\$2,241	\$4,250	\$0	\$0	\$0	\$5,807	\$0	\$0		\$12,298
Project Management		\$0	\$2,805	\$0	\$0	\$3,520	\$1,840	\$38	\$196		\$8,399
Cap Equipment		\$0	\$0	\$343,861	\$0	\$0	\$0	\$895,171	\$349,531		\$1,628,565
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,216		\$4,216
Advertising		\$0	\$785	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$785
Total		\$761,272	\$245,122	\$364,715	\$162,071	\$664,647	\$129,287	\$1,004,968	\$558,718	\$40,002	\$3,930,803
Project Budget	\$4,030,284										
Less Other Funding	\$0										
Net	\$4,030,284										
Actual Measure U Expenditures	\$3,930,803										
Running Balance	\$99,481										

8 of 9

Manual (R) So So So So So So So S	24 22 442 670	€742 767	\$912 880	\$6 585 573	\$5 283 853	\$25 278 771	\$E 4 0 44 0					
Part												
Problems 1975 197											\$0	Running Balance
Manual (R)											\$319,242	Actual Measure U Expenditures
Transition Tra											\$319,242	
Manufillures Si Si Si Si Si Si Si S											\$0	Less Other Funding
Month (R) Spi Seed Spi Spi											\$319,242	Project Budget
March (Fb) \$0 \$564 \$0 \$1075 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$319,242	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$48,571	\$270,671		Total
Mont (R) Sign Sig	\$340	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$340	\$0		Project Management
Marie (R) Scot Sc	\$12,070	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$12,070		nspection & Testing
Marie (P) So So So So So So So S	\$305,944	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$47,343	\$258,601		Architect
Manual (R) So So So So So So So S	\$888	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$888	\$0		Consultants
ST SO SO SO SO SO SO SO												14th and Pico Project (T)
Manual (R)												U7100024
Ment (R) Si Si Si Si Si Si Si S												
Manual (R) So So So So So So So S											\$0	Running Balance
Mart (R) S S S S S S S S S											\$2,110,430	Actual Measure U Expenditures
Minor (R) Signature Sign											\$2,110,430	
ment (R) 50 \$564 90 \$1,075 \$0 \$0 \$0 \$0 \$0 \$1,075 \$0											\$0	Less Other Funding
Ment (R) Side Sid											\$2,110,430	Project Budget
Ment (R)	\$2,110,430	\$0	\$0	\$640,439		\$252,105	\$478,593	\$321,335	\$44,133	\$9,000		Total
The mant (R)	\$113	\$0	\$0	\$113		\$0	\$0	\$0	\$0	\$0		Project Management
Menent (R)	\$180	\$0	\$0	\$0		\$0	\$180	\$0	\$0	\$0		Reimbursement to SMC
Manual (R)	\$30,000	\$0	\$0	\$0		\$0		\$30,000	\$0	\$0		Postage
Menent (R)	\$6,453	\$0	\$0	\$0		\$0		\$6,453	\$0	\$0		Rental / Lease
Ment (R)	\$998,647	\$0	\$0	\$276,985		\$126,701		\$126,433	\$17,617	\$0		Architect
ment (R) \$0 \$564 \$0 \$1,075 \$0	\$1,075,038	\$0	\$0	\$363,342	\$17,998	\$125,404	\$374,329	\$158,449	\$26,516	\$9,000		Consultants
ment (R) 50 \$564 \$0 \$1,075 \$0												Master Planning (S)
ment (R) \$0 \$564 \$0 \$1,075 \$0												U7100004, U7110020
ment (R) \$0 \$564 \$0 \$1,075 \$0												
ment (R) \$0 \$564 \$0 \$1,075 \$0											\$0	Running Balance
ment (R) \$0 \$564 \$0 \$1,075 \$0 \$0 \$0 \$0 ces \$0 \$1,305 \$0 \$1,075 \$0 \$0 \$0 \$0 ces \$0 \$1,305 \$0 \$3,803 \$0											\$17,501	Actual Measure U Expenditures
ment (R) \$0 \$564 \$0 \$1,075 \$0 \$0 \$0 \$0 ices \$0 \$1,305 \$0 \$1,075 \$0 \$0 \$0 \$0 \$0 \$1,305 \$0 \$1,305 \$0											\$17,501	
ment (R) \$0 \$564 \$0 \$1,075 \$0											\$0	Less Other Funding
ment (R) \$0 \$564 \$0 \$1,075 \$0 \$0 \$0 \$0 ices \$0 \$1,305 \$0 \$3,803 \$0 \$0 \$0 \$0 \$0 \$1,305 \$0 \$7,891 \$0 \$0 \$0 \$0 \$0 \$2,043 \$0 \$0 \$0 \$0 \$0 \$0 \$3,912 \$0 \$0 \$0 \$0											\$17,501	Project Budget
ment (R) \$0 \$564 \$0 \$1,075 \$0 \$0 \$0 \$0 ices \$0 \$1,305 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$2,043 \$0 \$820 \$0 \$0 \$0 \$0	\$17,501	\$0	\$0	\$0	\$0	\$0	\$13,589	\$0	\$3,912	\$0		Total
ment (R) \$0 \$564 \$0 \$1,075 \$0 \$0 \$0 \$0 ices \$0 \$1,305 \$0 \$1,075 \$0 \$0 \$0 \$0 ices \$0 \$1,305 \$0 \$1,305 \$0 \$0 \$0 \$0	\$2,863	\$0	\$0	\$0	\$0	\$0	\$820	\$0	\$2,043	\$0		Inspection & Testing
ment (R) \$0 \$564 \$0 \$1,075 \$0 \$0 \$0 \$0 ices \$0 \$0 \$0 \$3,803 \$0 \$0 \$0 \$0	\$9,196	\$0	\$0	\$0	\$0		\$7,891	\$0	\$1,305	\$0		Building & Additions
\$0 \$564 \$0 \$1,075 \$0 \$0 \$0 \$0 \$0 \$564 \$0 \$1,075 \$0 \$0 \$0	\$3,803	\$0	\$0	\$0	\$0		\$3,803	\$0	\$0	\$0		Other Contract Services
	\$1,639	\$0	\$0	\$0	\$0		\$1,075	\$0	\$564	\$0		Supplies
												Restroom Improvement (R)
												U7100007
			30,101	3000	0.00	30,01	30,00	0	⊢	H	ļ	


Note: Project N had no expenses

SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure S Project Schedule As of March 31, 2011

	15	14	13	12	1	10	9	œ	7	6	5	4	ω	2	1A	_	
	Signage Safety/Information	Real Property Acquisition	Adv. Architecture Related Exp for AA	Other Bond Related Expenses	Master Planning	Pico Promenade Improvements	Parking Garage, Grounds and Equipment - Student Services	Satellite Campus Parking Facilities and Roadway Improvements	Energy Efficiency Projects	Malibu Site Acquisition and Facility	Early Childhood Development/Childcare	Replacement Health/PE/Fitness Building	Career Opportunity Center	Performing Arts Center	Athletic Fields Phase I, John Adams	Athletic Fields Phase I, Corsair Field	Project Name
	On-Going	On-Going	Completed	On-Going	On-Going	Completed	May 2014	Completed	On-Going	Not Scheduled	In Planning	June 2014	Move to AA	Completed	Completed	Completed	Completion
In Planning																	2010
g																	2011
In Construction																	2012
iction																	2013
																	2014

SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure S Bond Budget As of March 31, 2011

hase I, Corsair Field hase I, John Adams Complex Project Name Complex Development/Childcare Distition and Facility Sy Projects Se Parking Facilities and Roadway Improvements Improvements Red Expenses Related Expenses Related Exp for AA Cquisition Information	Project Totals \$193,00	15 Signage Safety/Information \$60	On-Going	13 Adv. Architecture Related Exp for AA Completed	12 Other Bond Related Expenses On-Going \$66	11 Master Planning On-Going \$75	10 Pico Promenade Improvements Completed \$1,01	9 Parking Garage, Grounds and Equipment - Student Services May 2014 \$53,14	8 Satellite Campus Parking Facilities and Roadway Improvements Completed \$4,87	7 Energy Efficiency Projects On-Going \$1,29	6 Malibu Site Acquisition and Facility Not Scheduled \$31,06	5 Early Childhood Development/Childcare In Planning \$11,31	4 Replacement Health/PE/Fitness Building June 2014 \$40,20	3 Career Opportunity Center Move to AA	2 Performing Arts Complex \$40,60	1A Athletic Fields Phase I, John Adams Completed \$2,97	1 Athletic Fields Phase I, Corsair Field \$4,44	Completion
		On-Going	On-Going	Completed	On-Going	On-Going	Completed	May 2014	Completed	On-Going	Not Scheduled	In Planning	June 2014	Move to AA	Completed	Completed	Completed	Completion
Completed Completed Completed Completed Completed Move to AA June 2014 In Planning Not Scheduled On-Going Completed On-Going Completed On-Going On-Going On-Going On-Going On-Going	\$193,001,699	\$606,223	\$50,000	\$0	\$662,764	\$750,000	\$1,018,009	\$53,143,653	\$4,876,424	\$1,293,570	\$31,069,031	\$11,318,000	\$40,200,333	\$0	\$40,602,117	\$2,970,807	\$4,440,768	Project Budget
Pa	\$143,500,000	\$606,223	\$50,000	\$0	\$662,764	\$750,000	\$1,018,009	\$52,690,653	\$4,876,424	\$1,076,248	\$25,000,000	\$7,000,000	\$4,816,093	\$0	\$37,609,541	\$2,970,807	\$4,373,238	Measure S Allocation
\$4,440,768 \$2,970,807 \$40,602,117 \$40,200,333 \$11,318,000 \$31,069,031 \$1,293,570 \$4,876,424 \$53,143,653 \$1,018,009 \$750,000 \$662,764 \$9 \$50,000 \$606,223 \$193,001,699	\$49,501,699	\$0	\$0	\$0	\$0	\$0	\$0	\$453,000	\$0	\$217,322	\$6,069,031	\$4,318,000	\$35,384,240	\$0	\$2,992,576	\$0	\$67,530	Other Funding
Project Budget Measure S Allocation Other Funding \$4,440,768 \$4,373,238 \$67,530 \$2,970,807 \$2,970,807 \$0 \$40,602,117 \$37,609,541 \$2,992,576 \$0 \$40,200,333 \$4,816,093 \$35,384,240 \$11,318,000 \$7,000,000 \$4,318,000 \$1,293,570 \$1,076,248 \$217,322 \$4,876,424 \$4,876,424 \$0 \$53,143,653 \$52,690,653 \$453,000 \$750,000 \$750,000 \$0 \$750,000 \$750,000 \$0 \$0 \$750,000 \$0 \$0 \$50,2764 \$662,764 \$0 \$50,000 \$0 \$0 \$50,000 \$0 \$0 \$50,000 \$0 \$0 \$50,000 \$0 \$0 \$50,000 \$0 \$0 \$50,000 \$0 \$0 \$606,223 \$0 \$0 \$49,501,699	\$71,770,392	\$222,732	\$45,597	\$0	\$97,403	\$708,583	\$1,018,009	\$14,598,721	\$3,820,689	\$293,361	\$5,230,992	\$10,446	\$772,976	\$0	\$37,608,541	\$2,969,807	\$4,372,535	Measure S Expenditures as of 3/31/11
Project Budget Measure S Allocation Other Funding Sependitures of 3/31/11 Measure Sependitures of 3/31/11 \$4,440,768 \$4,373,238 \$67,530 \$4,372,1 \$2,970,807 \$2,970,807 \$0 \$2,969,8 \$40,602,117 \$37,609,541 \$2,992,576 \$37,608,6 \$40,200,333 \$4,816,093 \$35,384,240 \$772,0 \$11,318,000 \$7,000,000 \$4,318,000 \$10,2 \$1,293,570 \$1,076,248 \$217,322 \$239,3 \$4,876,424 \$4,876,424 \$4,876,424 \$0 \$3,820,6 \$53,143,653 \$52,690,653 \$453,000 \$1,018,009 \$1,018,009 \$1,018,009 \$1,018,009 \$1,018,009 \$1,018,009 \$0 \$708,1 \$662,764 \$662,764 \$662,764 \$0 \$97. \$97. \$606,223 \$606,223 \$0 \$222,1 \$1,770,2 \$1,770,2 \$193,001,699 \$143,500,000 \$49,501,699 \$71,770,2 \$1,770,2 \$1,770,2 \$1,770,2 \$1,770,2 \$1,770,2 \$1,770,2 \$1,770	\$71,870,431	\$215,988	\$45,597	\$0	\$69,491	\$708,583	\$1,018,009	\$14,523,008	\$3,815,317	\$510,684	\$5,230,992	\$9,200	\$772,976	\$0	\$37,608,541	\$2,969,807	\$4,372,238	Measure S Expenditures as of 12/31/10
Project Budget Measure S Allocation Other Funding Sexpenditures as Sexpenditures as S	-\$100,039	\$6,744	\$0	\$0	\$27,912	\$0	\$0	\$75,713	\$5,372	-\$217,323	\$0	\$1,246	\$0	\$0	\$0	\$0	\$297	Measure S Expenditures Last Period
Project Budget Measure S Allocation Other Funding S2,970,807 Measure S Expenditures as S62,970,807 Measure S Expenditures S5,970,807 Measure S Expenditures S5,971,111 Measure S Expenditures S5,971,111 Measure S Expenditures S5,971,111 Measure S Expenditures S5,117,111 Expenditures S5,117,111 Expenditures S5,	\$71,729,608	\$383,491	\$4,403	\$0	\$565,361	\$41,417	\$0	\$38,091,932	\$1,055,735	\$782,887	\$19,769,008	\$6,989,554	\$4,043,117	\$0	\$1,000	\$1,000	\$703	Total Measure S Remaining

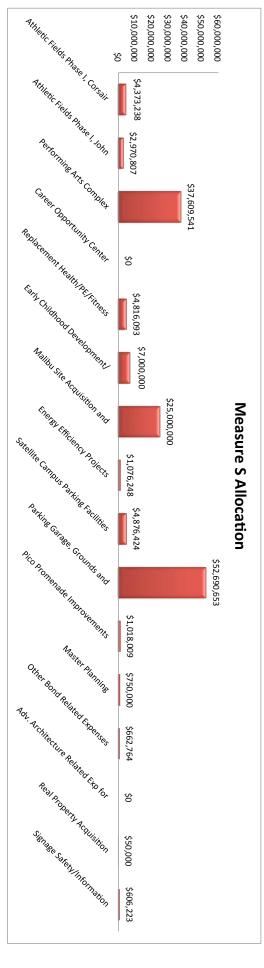

SANTA MONICA COMMUNITY COLLEGE DISTRICT MEASURE S EXPENDITURES FUND 42.3

As of March 31, 2011

Projects	Budget	04/05 Final	05/06 Final	06/07 Final 07/08 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
S7100019									
Athletic Field Phase I, Corsair Field (1)									
Legal		\$0	\$0	\$0	100\$	\$175	\$0	\$0	\$476
Building & Additions		\$0	\$0	\$0	088,008	\$2,579,095	\$0	\$0	\$2,879,475
Architect		\$27,332	\$43,815	\$197,557	\$252,736	\$279,173	\$26,563	\$0	\$827,176
Inspection & Testing		\$0	\$0	\$0	\$23,411	\$57,585	\$640	\$296	\$81,932
Project Management		\$0	\$0	\$0	\$9,871	\$42,374	\$565	\$0	\$52,810
Cap Equipment		\$0	\$0	\$0	\$0	\$483,017	\$35,271	\$0	\$518,288
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$2,066	\$10,312	\$0	\$12,378
Total		\$27,332	\$43,815	\$197,557	\$586,699	\$3,443,485	\$73,350	\$296	\$4,372,535
Project Budget	\$4,440,768	Received							
Less Other Funding*	\$67,530	\$67,530							
Net	\$4,373,238		* Other Funding Source:	J Source:					
Actual Measure S Expenditures	\$4,372,535		Metropolitan Water District \$67,530 received	ater District \$6	7,530 received				
Running Balance	\$703								


Athletic Field Phase I, Corsair Field

Project Description:
Renovation of the Corsair Field, stadium lighting and sound system

Status: Completed, 2009

Architect:
CO Architects

Contractor:Byrom Davey, Inc.

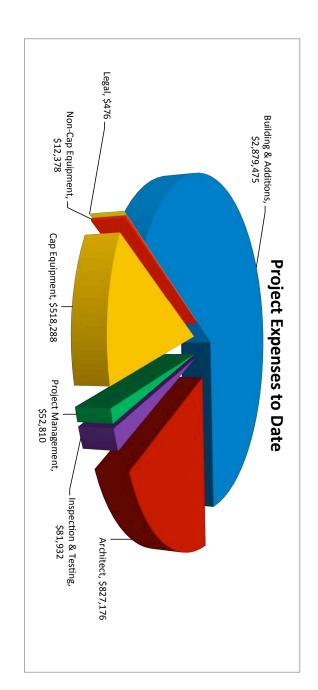

1 of 9

4/6/11

Projects	Budget	04/05 Final 05/06 Final 06/07 Final 07/08 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final 09/10 Final	09/10 Final	10/11	Combined Totals
S7100038									
Athletic Field Phase I, John Adams (1A)									
Legal		\$0	\$0	\$0	\$75	\$0	\$0	\$0	\$75
Building & Additions		\$0	\$0	\$0	\$16,556	\$1,395,261	\$0	\$0	\$1,411,817
Architect		\$0	\$5,807	\$93,941	\$12,150	\$31,818	\$0	\$0	\$143,715
Inspection & Testing		\$0	\$2,874	\$3,207	\$0	\$49,984	\$0	\$0	\$56,066
Project Management		\$0	\$0	\$0	\$10,921	\$45,170	\$38	\$0	\$56,128
Cap Equipment		\$0	\$0	\$0	\$0	\$1,290,672	\$0	\$0	\$1,290,672
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$11,334	\$0	\$0	\$11,334
Total		\$0	\$8,681	\$97,148	\$39,701	\$2,824,239	\$38	\$0	\$2,969,807
Project Budget	\$2,970,807								
Less Other Funding	\$0								
Net	\$2,970,807								
Actual Measure S Expenditures	\$2,969,807								
Running Balance	\$1,000								


Athletic Field Phase I, John Adams

Project Description:Renovation of John Adams Field and lighting

Status: Completed, 2008

Architect: Caldwell Architects

Contractor:Byrom Davey, Inc.

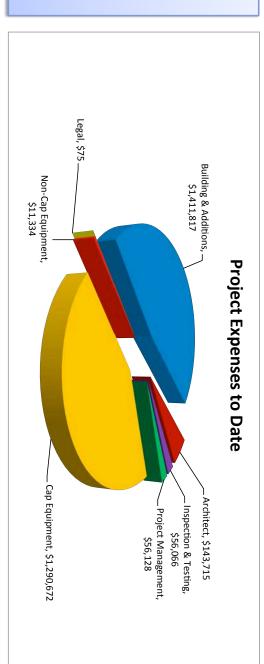

4/6/11 2 of 9

SANTA MONICA COMMUNITY COLLEGE DISTRICT MEASURE S EXPENDITURES FUND 42.3

As of March 31, 2011

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
S7100012									
Performing Arts Center (2)									
Consultants		\$0	\$0	\$0	\$121,790	\$76,639	\$0	\$0	\$198,429
Other Contract Services		\$0	\$0	\$4,269	\$0	\$22,729	\$22	\$0	\$27,020
Supplies		\$0	\$0	\$0	\$14,565	\$5,810	\$0	\$0	\$20,375
Legal		\$0	\$0	\$34,329	\$275,667	\$492,731	\$15,629	\$0	\$818,356
Advertising		\$0	\$0	\$0	\$320	\$0	\$0	\$0	\$320
Building & Additions		\$7,784,151	\$10,292,986	\$8,930,813	\$2,991,903	\$1,629,990	\$50,000	\$0	\$31,679,843
Architect		\$0	\$811,312	\$182,457	\$412,309	\$121,588	\$108	\$0	\$1,527,774
Engineering		\$0	\$3,600	\$5,250	\$1,500	\$9,650	\$0	\$0	\$20,000
Inspection & Testing		\$104,308	\$722,685	\$411,193	\$210,381	\$22,256	\$0	\$0	\$1,470,823
Project Management		\$31,984	\$155,732	\$248,876	\$263,690	\$47,915	\$3,244	\$0	\$751,441
Cap Equipment		\$0	\$0	\$130,218	\$292,565	\$342,693	\$0	\$0	\$765,476
Non-Cap Equipment		\$0	\$0	\$15,124	\$93,106	\$220,455	\$0	\$0	\$328,685
Total		\$7,920,443	\$11,986,315	\$9,962,528	\$4,677,797	\$2,992,455	\$69,003	\$0	\$37,608,541
Project Budget	\$40,602,117	Received							
Less Other Funding*	\$2,992,576	\$2,992,576		* Other Funding Source:	g Source:				
Net	\$37,609,541		_	Madison Project Foundation	≕	on \$2,992,576 received	ived		
Actual Measure S Expenditures	\$37,608,541								
Running Balance	\$1,000								


Performing Arts Center

Project Description:Construction of a state-of-the-art 499 seat performing arts theater

Status: Completed, 2008

Architect: Renzo Zecchetto

Contractor: FTR International

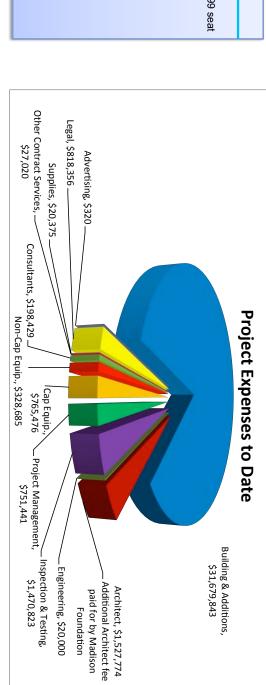

4/6/11 3 of 9

Projects	Budget	04/05 Final	05/06 Final	04/05 Final 05/06 Final 06/07 Final 07/08	07/08 Final	08/09 Final 09/10 Final	09/10 Final	10/11	Combined Totals
\$7100033 \$7100144									
Replacement Health/PE/Fitness Building (4)									
Supplies		\$0	\$0	\$0	\$0	\$0	\$163	\$0	\$163
Legal		\$0	\$0	\$0	\$0	\$1,413	\$75	\$0	\$1,488
Other Contract Services		\$1,634	\$25,934	\$0	\$0	\$253	\$165	\$0	\$27,985
Repair Facility		\$0	\$4,861	\$0	\$0	\$0		\$0	\$4,861
Supplies		\$4,809	\$288	\$0	\$0	\$0		\$0	\$5,097
Building & Additions		\$0	\$0	\$0	\$0	\$112,410		\$0	\$638,962
Architect		\$0	\$0	\$0	\$0	\$0	\$41,044	\$0	\$41,044
nspection & Testing		\$0	\$0	\$0	\$0	\$6,518	\$14,363	\$0	\$20,881
Project Management		\$0	\$0	\$0	\$0	\$9,070	\$23,425	\$0	\$32,495
Total		\$6,443	\$31,083	\$0	\$0	\$129,663	\$605,787	\$0	\$772,976
Project Budget	\$40,200,333								
Less Other Funding*	\$35,384,240			* Other Funding Source:	Source:				
Net	\$4,816,093			Measure AA \$3	5,384,240 allocated	cated			
Actual Measure S Expenditures	\$772,976								
Running Balance	\$4,043,TT/								
S7100045 Early Childhood Davelopment/Children (5)									
Consultants		. \$ 0	.s.o	\$0	\$9 200	. \$0	.\$0	. \$ 0	
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$1,246	\$1,246
Total		\$0	\$0	\$0	\$9,200	\$0	\$0	\$1,246	\$10,446
Project Budget	\$11,318,000	Received							
Less Other Funding*	\$4,318,000	\$0		* Other Funding Source:	Source:				
Net	\$7,000,000			City of Santa Monica \$	onica \$4,318,0	4,318,000 commited			
Actual Measure S Expenditures	\$10,446								
d									
S7100077, S7100015									
Malibu Site Acquisition and Facilities (6)									
Consultants		\$0	\$0	\$0	\$0	\$30,000	\$0	\$0	\$30,000
Legal		\$0	\$27,722	\$16,787	\$6,159	\$504		\$0	\$51,172
Building & Additions		\$0	\$0	\$0	\$0	\$0		\$0	\$0
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$4,388	\$3,750	\$141,462	\$0	\$0		\$0	\$149,600
Project Management		\$0	\$0	\$220	\$0	\$0		\$0	\$220
Other Contract Services		\$0	\$0	\$0	\$0	\$0		\$0	\$0
Storm/Waste Water Treatment Center		\$0	\$2,500,000	\$0	\$0	\$2,500,000		\$0	\$5,000,000
Total		\$4,388	\$2,531,472	\$158,468	\$6,159	\$2,530,504		\$0	\$5,230,992
Project Budget	\$31,069,031								
Less Other Funding*	\$6,069,031			* Other Funding Source:	3 Source:				
Net	\$25,000,000			Measure AA \$6,069,03	,069,031 allocated	ated			
Actual Measure S Expenditures	\$5,230,992								
Running Balance	\$19,769,008								

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
S7100043, S7100066									
Energy Efficiency Projects (7)									
Legal		\$0	\$0	\$0	\$0	\$988		\$0	\$988
Building & Additions		\$0	\$0	\$0	\$0	\$106,921	\$355,294	-\$180,342	\$281,873
Engineering		\$0	\$0	\$0	\$10,500	\$0		\$0	\$10,500
Inspection & Testing		\$0	\$0	\$0	\$0	\$0		\$0	\$0
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$0	\$0	\$0	\$10,500	\$107,910		-\$180,342	\$293,361
Project Budget	\$1,293,570	Received							
Less Other Funding*	\$217,322	\$217,322		* Other Funding Source:	g Source:				
Net	\$1,076,248			SCE & The Gas Co. \$217	s Co. \$217,322	322 received			
Actual Measure S Expenditures	\$293,361								
Running Balance	\$782,887								
S7100091, S7100092									
Satellite Campus Parking Facilities and Roadway Improvements	nprovements (8)	8)							
Legal		\$0	\$0	\$0	\$300	\$175	\$0	\$0	\$475
Other Contract Services		\$0	\$0	\$0	\$300			\$0	
Advertising		\$0	\$0	\$0	\$0			\$0	
Consultants		\$0	\$0	\$0	\$0			\$0	
Supplies		\$0	\$0	\$0	\$0			\$0	\$0
Building & Additions		\$0	\$0	\$0	\$278,178	٠		\$37,777	\$2,625,6
Architect		\$0	\$0	\$324,919	\$324,864			\$1,397	
Inspection & Testing		\$0	\$0	\$0	\$31,100			\$360	\$245,626
Project Management		\$0	\$0	\$0	\$18,288	\$64,880	\$31,137	\$8,365	\$122,670
Non-Cap Equipment		\$0	\$0	\$0	\$0			\$0	\$3,387
Total		\$0	\$0	\$324,919	\$653,031	\$2,248,0	\$546,775	\$47,900	\$3,820,689
Project Budget	\$4,876,424								
Less Other Funding	\$0								
Net	\$4,876,424								
Actual Measure S Expenditures	\$3,820,689								
Running Balance	\$1,055,735								

5 of 9

4/6/11

SANTA MONICA COMMUNITY COLLEGE DISTRICT MEASURE S EXPENDITURES FUND 42.3

As of March 31, 2011

04/05 Final | 05/06 Final | 06/07 Final | 07/08 Final | 08/09 Final | 09/10 Final | 10/11

Combined Totals

Budget

								\$38,091,932	Running Balance
								\$14,598,721	Actual Measure S Expenditures
			allocated		State of California \$453,000			\$52,690,653	Net
				g Source:	* Other Funding Source:		\$0	\$453,000	Less Other Funding*
							Received	\$53,143,653	Project Budget
\$14,598,721	\$239,547	\$6,541,719	\$5,550,689	\$2,266,766	\$0	\$0	\$0		Total
\$14,393	\$0	\$14,393	\$0	\$0	\$0	\$0	\$0		Cap Equipment
\$660,880	\$128,555	\$373,559	\$158,766	\$0	\$0	\$0	\$0		Project Management
\$326,349	\$33,492	\$161,847	\$131,009	\$0	\$0	\$0	\$0		Inspection & Testing
\$86,110	\$42,968	\$38,330	\$4,813	\$0	\$0	\$0	\$0		Engineering
\$4,970,637	\$29,817	\$0	\$2,674,054	\$2,266,766	\$0	\$0	\$0		Architect
\$8,481,091	\$0	\$5,925,152	\$2,555,940	\$0	\$0	\$0	\$0		Building & Additions
\$12,838	\$378	\$10,952	\$1,508	\$0	\$0	\$0	\$0		Other Contract Services
\$23,977	\$4,337	\$17,486	\$2,154	\$0	\$0	\$0	\$0		Legal
\$20,700	\$0	\$0	\$20,700	\$0	\$0	\$0	\$0		Consultants
\$1,745	\$0	\$0	\$1,745	\$0	\$0	\$0	\$0		Supplies
									Parking Garage and Grounds - Student Services (9)
									S7100142

Parking Garage and Grounds - Student Services

Project Description:
Consolidates various student services
departments and college administration in a
single complex at the front of the campus


Facility Size: 83,634 sq/ft & 500 cars underground parking structure

Status:

In plan check with DSA

Architect: Steinberg Architects

Contractor:

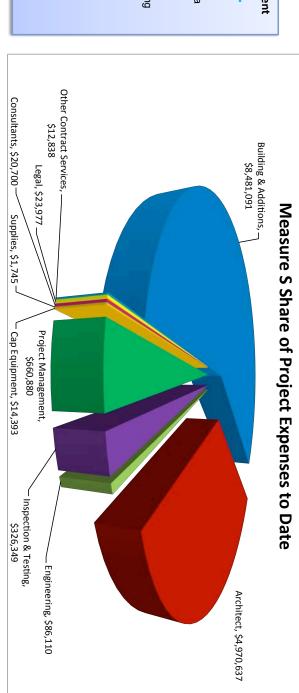

4/6/11 6 of 9

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
S7100044									
Pico Promenade Improvements (10)									
Building & Additions		\$0	\$0	\$0	\$690	\$883,401	\$0	\$0	\$884,091
Architect		\$0	\$0	\$0	\$69,190	\$28,540	\$864	\$0	\$98,595
Inspection & Testing		\$0	\$0	\$0	\$0	\$7,591	\$0	\$0	\$7,591
Project Management		\$0	\$0	\$0	\$2,185	\$25,548	\$0	\$0	\$27,733
Total		\$0	\$0	\$0	\$72,066	\$945,080	\$864	\$0	\$1,018,009
Project Budget	\$1,018,009								
Less Other Funding	\$0								
Net	\$1,018,009								
Actual Measure S Expenditures	\$1,018,009								
Running Balance	\$0								

S7100004									
Master Planning (11)									
Consultants		\$0	\$0	\$0	\$0	\$0	\$441,549	\$13,320	\$454,869
Printing		\$0	\$0	\$0	\$0	\$0	\$4,157	\$0	\$4,157
Advertising		\$0	\$0	\$0	\$0	\$0	\$3,000	\$0	\$3,000
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$442	\$200	\$642
Architect		\$0	\$0	\$0	\$0	\$0	\$192,358	\$24,736	\$217,094
Project Management		\$0	\$0	\$0	\$0	\$0	\$16,638	\$9,341	\$25,979
Filling Fees		\$0	\$0	\$0	\$0	\$0	\$0	\$2,842	\$2,842
Total		\$0	\$0	\$0	\$0	\$0	\$658,143	\$50,439	\$708,583
Project Budget	\$750,000								
Less Other Funding	\$0								
Net	\$750,000								
Actual Measure S Expenditures	\$708,583								
Running Balance	\$41,417								
		_		-	-		-		
S7100048									

								\$565,361	Running Balance
								\$97,403	Actual Measure S Expenditures
								\$662,764	Net
								\$0	Less Other Funding
								\$662,764	Project Budget
\$97,40	\$45,418	\$50,185	\$1,800	\$0	\$0	\$0	\$0		Total
\$5,07	\$5,071	\$0	\$0	\$0	\$0	\$0	\$0		Non-Cap Equipment
€	\$10,086	\$0	\$0	\$0	\$0	\$0	\$0		Cap Equipment
\$22,524	\$4,777	\$17,747	\$0	\$0	\$0	\$0	\$0		Project Management
	\$0	\$400	\$0	\$0	\$0	\$0	\$0		Moving Services
\$38,102	\$19,097	\$17,206	\$1,800	\$0	\$0	\$0	\$0		Other Contract Services
\$2,27	\$0	\$2,278	\$0	\$0	\$0	\$0	\$0		Advertising
\$1,997	\$1,997	\$0	\$0	\$0	\$0	\$0	\$0		Software License
\$13,30	\$4,390	\$8,917	\$0	\$0	\$0	\$0	\$0		Legal
	\$0	\$3,638	\$0	\$0	\$0	\$0	\$0		Supplies
									Other Bond Related Expenses (12)
									S7100048

		4	2100	20/07	100.10	2000	00/40 1::-01	40/44	Cambinad Tatala
rivects	budget	04/03	00/00	00/0/	07/00	00/09 a	OS/ TO FILIA	i	Combined locals
S7100049									
Adv Architecture Related Exp for AA (13)									
Legal		\$0	\$0	\$0	\$0			\$0	\$0
Other Contract Services		\$0	\$0	\$0	0\$			\$0	\$0
Architect		\$0	\$0	\$0	0\$	\$0	0\$	\$0	\$0
Engineering		\$0	\$0	\$0	0\$			\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0			\$0	\$0
Project Management		\$0	\$0	\$0	0\$			\$0	\$0
Total		\$0	\$0	\$0	\$0	\$45,7	-\$45,734	\$0	\$0
Project Budget	\$0								
Less Other Funding	\$0								
Net	\$0								
Actual Measure S Expenditures	\$0								
Running Balance	\$0								
2700057									
Real Property Acquisition (14)									
Other Contract Services		\$0	\$ 0	\$0	80	\$ 0	\$18.721	\$0	\$18 721
Architect		\$0	\$0	\$0	0\$			\$0	\$0
Engineering		0\$	\$0	\$0	0\$			\$0	\$0
Inspection & Testing		\$0	\$0	\$0	0\$			\$0	\$6,336
Project Management		\$0	\$0	\$0	0\$,	\$0	\$20,540
Total		\$0	\$0	\$0	\$0			\$0	\$45,597
Project Budget	\$50,000								
Less Other Funding	\$0								
Net	\$50,000								
Actual Measure S Expenditures	\$45,597								
Running Balance	\$4,403								

8 of 9

4/6/11

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
S700017S									
Campus Signage (15)									
Supplies		0\$	\$0	0\$	0\$	\$0	0\$	\$303	\$303
Consultants		0\$	\$0	0\$	\$0	0\$	\$32,225	\$23,725	356,55\$
Other Contract Services		\$0	\$0	\$0		\$0	0\$	\$0	\$(
Architect		\$0	\$0	\$0	\$0	\$0	0\$	\$0	3\$
Inspection & Testing		0\$	\$0	0\$		\$0	0\$	\$0	3\$
Project Management		0\$	\$0	0\$		\$0	0\$	\$10,220	\$10,220
Cap Equipment		0\$	\$0	0\$	0\$	0\$	0\$	\$156,258	\$156,258
Total		0\$	\$0	0\$	\$0	\$0	\$32,225	\$190,507	\$222,732
Project Budget	\$606,223								
Less Other Funding	\$0								
Net	\$606,223								
Actual Measure S Expenditures	\$222,732								
Running Balance	\$383,491								

Note: Project 3 had no expenses

Grand Total

\$7,958,606 \$14,601,366 \$10,740,621 \$8,321,918 \$20,819,624 \$8,933,245 \$395,011


9 of 9

4/6/11

SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure AA Project Schedule As of March 31, 2011

	Project Name	Completion	2010	2011	2012	2013	2014	2015	2016
101	Environmental Performance - Central Plant	September 2014							
102	Infrastructure & Technology - Information Technology Relocation	February 2014							
103	Media and Technology Complex - Academy Site	September 2014							
104	Replacement Health/PE/Fitness/Dance Building with Central Plant	June 2014							
105	Drescher - Academic Modernization, Bookstore, Pico Promenade	December 2016							
106	Replacement Math and Science Extension Building	December 2016							
107	Madison East Wing Seismic Upgrade	May 2013							
108	Renovation of Corsair Stadium	November 2016							
109	Career Opportunity and Advancement Center (Bundy)	Not Scheduled							
110	Malibu Center	Not Scheduled							
111	Business & Facilities Infrastructure	On-Going							
112	Master Planning, Program Management, Overhead	On-Going							
113	Energy Efficiency Projects	On-Going							
114	Community Classroom & Facility Projects	December 2011							
115	Real Property Acquisition	On-Going							
116	Roadways, Walkways, Grounds, Parking Lots, and Garages	On-Going							
			ln F	Planning	In Construction	ıction			

Media and Technology Complex - Academy Site Replacement Health/PE/Fitness/ Dance Building with Central Plant June 201 Drescher - Academic Modernization, Bookstore, Pico Promenade Replacement Math and Science Extension Building Madison East Wing Seismic Upgrade Renovation of Corsair Stadium Career Opportunity and Advancement Center (Bundy) Master Planning, Program Management, Overhead Energy Efficiency Projects Community Classroom & Facility Projects Community Classroom & Facility Projects Community Classroom & Facility Projects Community Classroom & Technology - Technology Froject Totals S80,000,000 \$30,000,000 \$40,000,000 \$4,882,119 \$4,882,119 \$57,700,824 \$57,700,824 \$58,259,000 \$1,000,000 \$4,882,119 \$4,882,119 \$57,700,824 \$57,700,824 \$57,700,824 \$57,700,824 \$57,700,824 \$57,700,824 \$58,259,000 \$1,000,000 \$4,882,119 \$4,882,119 \$57,700,824		Project Name Environmental Performance - Central Plant	Completion September 201	4	Proj	Project Budget Al	Project Budget Allocation Other Funding \$4,882,119 \$4,882,119 \$0	Project Budget Allocation Other Funding Expenditures as \$4,882,119 \$4,882,119 \$0 \$51,132	Project Budget Allocation Other Funding Expenditures as Expend of 3/31/11 of 12/	Project Budget Allocation Other Funding Expenditures as Expend
Media and Technology Complex - Academy Site September 2014 Replacement Health/PE/Fitness/ Dance Building with Central Plant Dine 2014 Replacement Health/PE/Fitness/ Dance Building with Central Plant Dine 2015 Replacement Math and Science Extension Building Madison East Wing Seismic Upgrade Malbiu Center Mallibu Center Mallibu Center Master Planning, Program Management, Overhead Energy Efficiency Projects Community Classroom & Facility Projects Community Classroom & Technology - Technology Project Totals S50,000,000 \$13,287,218 S50,000,000 \$10,000,000 \$10,000,000 \$4,882,119 S50,000,000 \$4,882,119 S50,000,000 \$4,882,119 S50,000,000 \$4,882,119 S50,000,000 S50,		ll Performance - Central Plant & Technology - Information Technology Relocation	September 2014 February 2014	\$4 \$13	\$4,882,119 \$13,287,218	49	\$4,882,119 \$13,287,218	\$4,882,119 \$0 \$13,287,218 \$0	\$4,882,119 \$0 \$51,132 \$13,287,218 \$0 \$376,009 \$	\$4,882,119 \$0 \$51,132 \$48,500 \$13,287,218 \$0 \$376,009 \$218,975 \$1
Replacement Health/PE/Fitness/ Dance Building with Central Plant Drescher - Academic Modernization, Bookstore, Pico Promenade December 2016 Replacement Math and Science Extension Building Replacement Math Advancement Center (Bundy) Robert Policien Projects Replacement Center (Bundy) Robert Policien Projects Replacement (Bundy) Rob		chnology Complex - Academy Site	September 2014	\$61,	\$61,480,824		\$57,700,824 \$3,780,0	\$57,700,824 \$3,780,000 \$4	\$57,700,824 \$3,780,000 \$4,881,617 \$	\$57,700,824 \$3,780,000 \$4,881,617 \$3,812,690 \$
Descenter - Academic Modernization, Bookstore, Pico Promenade December 2016	104 Replacement l	Health/PE/Fitness/ Dance Building with Central Plant	June 2014	\$40,2	\$40,200,333	200,333 \$35,384,240		\$35,384,240	\$35,384,240 \$4,816,093	\$35,384,240 \$4,816,093 \$1,234,609
Replacement Math and Science Extension Building Madison East Wing Seismic Upgrade Madison East Wing Seismic Upgrade May 2013 Renovation of Corsair Stadium Renovation of Corsair Stadium Renovation of Corsair Stadium May 2013 Renovation of Corsair Stadium November 2016 November 2016 November 2016 Not Scheduled Nor-Going Con-Going Community Classroom & Facility Projects Community Classroom & Facility	_	ademic Modernization, Bookstore, Pico Promenade	December 2016	\$34,0	\$34,026,480)26,480 \$34,026,480		\$34,026,480	\$34,026,480 \$0	\$34,026,480 \$0 \$0
Madison East Wing Seismic Upgrade		Math and Science Extension Building	December 2016	\$108,1	\$108,103,000	103,000 \$68,259,000		\$68,259,000 \$4	\$68,259,000 \$40,134,000	\$68,259,000 \$40,134,000 \$0
Renovation of Corsair Stadium Career Opportunity and Advancement Center (Bundy) Malibu Center Business & Facilities Infrastructure Master Planning, Program Management, Overhead Community Classroom & Facility Projects Community Classroom & Facility Projects Community Classroom & Facility Projects Real Property Acquisition Real Property Acquisition Real Property Acquisition Real Property Acquisition Froject Totals Project Totals \$13,287,218 \$13,287,218 \$13,287,218 \$13,287,218 \$13,384,240 \$14,025,480 \$12,292,000 \$1,000,000		Wing Seismic Upgrade	May 2013	\$12,2	\$12,292,000	92,000 \$12,292,000		\$12,292,000	\$12,292,000 \$0	\$12,292,000 \$0 \$467,035
Carreer Opportunity and Advancement Center (Bundy) Malibu Center Business & Facilities Infrastructure Master Planning, Program Management, Overhead Community Classroom & Facility Projects Community Classroom & Con-Going Community Classroom & Facility Projects Community Classroom & Con-Going Community Classroom & Facility Projects Community Classroom & Con-Going Community Classroom & Facility Projects Community Classroom & Con-Going Con-Goin		· Corsair Stadium	November 2016	\$11,2	\$11,203,000	03,000 \$11,203,000		\$11,203,000	\$11,203,000 \$0	\$11,203,000 \$0 \$13,714
Mailibu Center Mailibu Center		tunity and Advancement Center (Bundy)	Not Scheduled	\$41,3	\$41,391,000	91,000 \$29,384,000		\$29,384,000	\$29,384,000 \$12,007,000	\$29,384,000 \$12,007,000 \$0
Business & Facilities Infrastructure Master Planning, Program Management, Overhead Community Classroom & Facility Projects Real Property Acquisition Real Property Acquisition Roadways, Walkways, Grounds, Parking Lots, and Garages Infrastructure & Technology - Technology Infrastructure & Technology - Utility Project Totals \$57,700,824 \$58,259,000 \$10,000,000 \$13,287,218 \$13,287,218 \$13,287,218 \$13,287,218 \$4,488,119			Not Scheduled	\$31,0	\$31,069,031	69,031 \$6,069,031		\$6,069,031 \$2	\$6,069,031 \$25,000,000	\$6,069,031 \$25,000,000 \$0
Master Planning, Program Management, Overhead Energy Efficiency Projects Community Classroom & Facility Projects Community Classroom & Facility Projects Real Property Acquisition Roadways, Walkways, Grounds, Parking Lots, and Garages Infrastructure & Technology - Utility Project Totals \$80,000,000 \$50,000,000 \$50,000,000 \$50,000,000 \$50,000,000 \$50,000,000 \$50,000,000 \$10,000,000		cilities Infrastructure	On-Going	\$6,1	\$6,140,952	\$6,140,952		\$6,140,952	\$6,140,952 \$0	\$6,140,952 \$0 \$130,172
Energy Efficiency Projects		ng, Program Management, Overhead	On-Going	\$1,65	\$1,650,000	50,000 \$1,650,000		\$1,650,000	\$1,650,000 \$0	\$1,650,000 \$0 \$0
Community Classroom & Facility Projects December 2011		ncy Projects	On-Going	\$4,6	\$4,650,136	50,136 \$4,150,136		\$4,150,136	\$4,150,136 \$0	\$4,150,136 \$0 \$0
Real Property Acquisition		lassroom & Facility Projects	December 2011	\$3,2	\$3,221,000	21,000 \$3,221,000		\$3,221,000	\$3,221,000 \$0	\$3,221,000 \$0 \$288,970
Roadways, Walkways, Grounds, Parking Lots, and Garages		Acquisition	On-Going	\$6,0	\$6,000,000	00,000 \$6,000,000		\$6,000,000	\$6,000,000 \$0	\$6,000,000 \$0 \$5,781,653
Infrastructure & Technology - Utility		alkways, Grounds, Parking Lots, and Garages	On-Going	\$3	\$350,000	50,000 \$350,000		\$350,000	\$350,000 \$0	\$350,000 \$0 \$240,787
Infrastructure & Technology - Utility	117 Infrastructure	& Technology - Technology	On-Going	\$5	\$500,000	00,000 \$500,000		\$500,000	\$500,000	\$500,000 \$0 \$216,896
\$68,259,000 \$57,700,824 \$35,384,240 \$34,026,480 \$4,882,119 \$4,882,119 \$13,287,218 \$4,882,119 \$4,882	118 Infrastructure	& Technology - Utility	On-Going	\$.	\$500,000	\$500,000 \$500,000		\$500,000	\$500,000 \$0	\$500,000 \$0 \$2,760
\$13,287,218 \$35,384,240 \$34,026,480 \$12,292,000 \$17,700,824 \$35,384,240 \$34,026,480 \$12,292,000 \$17,29	Project Total	Is		\$380,9	\$380,947,093	47,093 \$295,000,000		\$295,000,000 \$85,	\$295,000,000 \$85,737,093	\$295,000,000 \$85,737,093 \$13,685,354
\$57,700,824 \$35,384,240 \$34,026,480 \$12,292,000 \$1,4882,119 \$3,287,218 \$4,882,119 \$13,287,218 \$4,882,119 \$1,000,000 \$1,00	\$80,000,00	00	\$68,259,000							
\$35,384,240 \$34,026,480 \$4,882,119 \$4,882,119 \$13,287,218 \$4,882,119 \$13,287,218 \$4,882,119 \$10,000 \$1,292,000 \$1,	\$60,000,00	\$57,700,824								
\$13,287,218 \$12,292,000 \$1,292,000 \$1,4882,119 \$12,292,000 \$1,292,	\$30,000,00 \$30,000,00		30		\$29,384	\$29,384,000	\$29,384,000	\$29,384,000	\$29,384,000	\$29,384,000
The State of the S	\$20,000,00 \$10,000,00	\$4,882,119	\$12,292,0)00 \$11,203,	000		\$6,069,031 \$6,140,952 \$1,650,000	\$6,069,031 \$6,140,952 \$1,650,000 \$4,150,136	\$6,069,031 \$6,140,952 \$1,650,000 \$4,150,136 \$3,221,000 \$6,000,000	\$6,069,031 \$6,140,952 \$1,650,000 \$4,150,136 \$3,221,000
		Academy Academy	nic Up	Sali St.	ON ORCEPTERY	dyancenent daliby Center	okancenent Salida Center Salid	Garcenent Statuture Statut	Concented Control Cont	Garcenent Statuture Statut

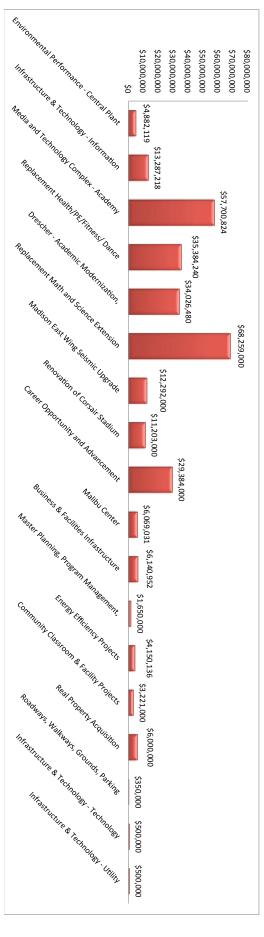

Projects	Budget	09/10 Final	10/11	Combined Totals
AA 7100062				
Environmental Performance - Central Plant (101)				
Legal		\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0
Consultants		\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0
Architect		\$0	\$0	\$0
Engineering		\$48,500	\$0	\$48,500
Inspection & Testing		\$0	\$0	\$0
Project Management		\$0	\$2,632	\$2,632
Cap Equipment		\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0
Total		\$48,500	\$2,632	\$51,132
Project Budget	\$4,882,119			
Less Other Funding	\$0			
Net	\$4,882,119			
Actual Measure AA Expenditures	\$51,132			
Running Balance	\$4,830,987			

		20/40	40.44	
Projects	Budget	09/10 Final	10/11	Combined lotals
AA 7100063				
Infrastructure & Technology - IT Relocation (102)				
Legal		\$0	\$0	\$0
Consultants		\$0	\$0	\$0
Supplies		\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0
Architect		\$105,049	\$168,291	\$273,340
Inspection & Testing		\$10,291	\$3,642	\$13,933
Project Management		\$33,460	\$55,276	\$88,736
Cap Equipment		\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0
Total		\$148,800	\$227,209	\$376,009
Project Budget	\$13,287,218			
Less Other Funding	\$0			
Net	\$13,287,218			
Actual Measure AA Expenditures	\$376,009			
Running Balance	\$12,911,209			


Infrastructure & Technology -IT Relocation

Project Description:Relocation of IT/Telecom Departments, and renovation of Media Center

Facility Size: 9,230 sq/ft

Status: In design development

Architect: Morris Architects

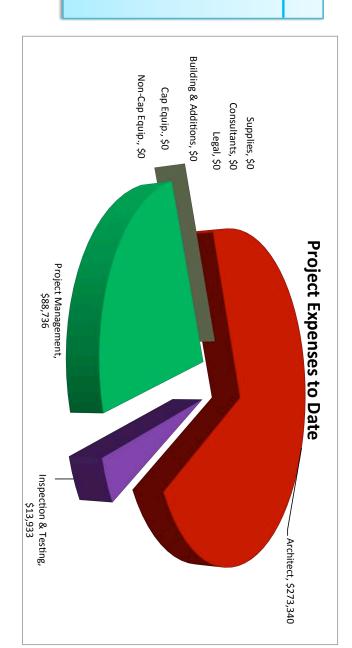

7-2005	J.: 1224	00/40 E:50I	10111	Cambinad Totale
riojecis	buuget	OS/ TO FILIAL		Combined lotals
AA 7100061				
Media and Technology Complex - Academy Site (103)				
Consultants		\$0	\$0	\$0
Supplies		\$0	\$0	\$0
Legal		\$16,903	\$0	\$16,903
Other Contract Services		\$3,993	\$2,836	\$6,830
Advertising		\$0	\$0	\$0
Building & Additions		\$0	\$538	\$538
Architect		\$2,097,553	\$2,344,913	\$4,442,466
Engineering		\$16,459	\$20,275	\$36,734
Inspection & Testing		\$64,905	\$19,051	\$83,956
Project Management		\$121,786	\$172,405	\$294,190
Cap Equipment		\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0
Total		\$2,321,599	\$2,560,018	\$4,881,617
Project Budget	\$61,480,824	Received		
Less Other Funding*	\$3,780,000	\$803,412		
Net	\$57,700,824	\$57,700,824 * Other Funding Source:	ırce:	
Actual Measure AA Expenditures	\$4,881,617	\$4,881,617 KCRW Foundation \$3,780	\$3,780,000 commited,	ted,
Running Balance	\$52,819,207	\$52,819,207 \$803,412 received		

Media and Technology Complex -Academy Site


Project Description:Renovation and new extension to the existing building, new building for KCRW, and a new parking structure

Facility Size:
Building - 47,172 sq/ft
Parking Structure - 450 spaces

Status:

Building in design development Parking structure in DSA

Architect:Clive Wilkinson Architects

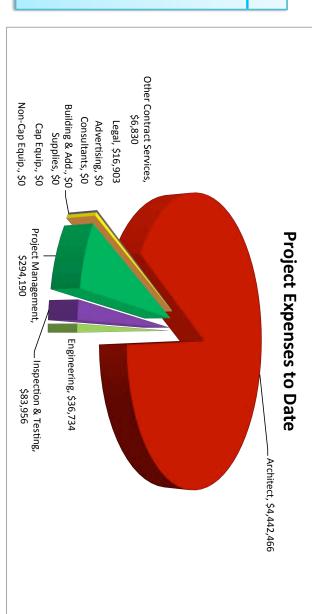

Projects	Budget	09/10 Final	10/11	Combined Totals
AA 7100060				
Repl. Health/PE/Fitness/Dance Building with Central Plant (104)				
Consultants		\$0	\$0	\$0
Supplies		\$0	\$0	\$0
Other Contract Services		\$120	\$38	\$158
Building & Additions		\$0	\$0	\$0
Architect		\$256,076	\$814,843	\$1,070,918
Engineering		\$0	\$4,747	\$4,747
Inspection & Testing		\$36,892	\$490	\$37,382
Project Management		\$34,968	\$86,436	\$121,404
Total		\$328,056	\$906,553	\$1,234,609
Project Budget	\$40,200,333			
Less Other Funding*	\$4,816,093	\$4,816,093 * Other Funding Source:	œ.	
Net	\$35,384,240	\$35,384,240 Measure S \$4,816,093 allo	3 allocated	
Actual Measure AA Expenditures	\$1,234,609			
Running Balance	\$34,149,631			

Repl. Health/PE/Fitness/Dance **Building with Central Plant**


Project Description:

plant Replacement of locker rooms, fitness center, dance studios, and new central


Facility Size: 62,000 sq/ft

Status: In design development

Architect:Gensler Architects

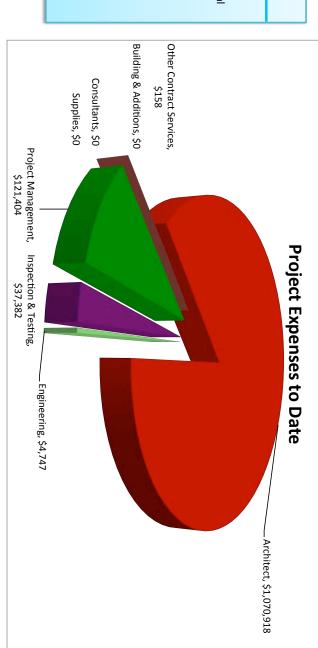

Projects	Budget	09/10 Final	10/11	Combined Totals
AA 7100047				
Madison East Wing Seismic Upgrade (107)				
Consultants		\$0	\$0	\$0
Supplies		\$0	\$0	\$0
Legal		\$0	\$0	\$0
Other Contract Services		\$0	\$305	\$305
Building & Additions		\$0	\$656	\$656
Architect		\$76,073	\$289,912	\$365,985
Inspection & Testing		\$0	\$15,730	\$15,730
Project Management		\$5,557	\$78,801	\$84,358
Total		\$81,630	\$385,405	\$467,035
Project Budget	\$12,292,000			
Less Other Funding	\$0			
Net	\$12,292,000			
Actual Measure AA Expenditures	\$467,035			
Running Balance	\$11,824,965			
3	* 3			

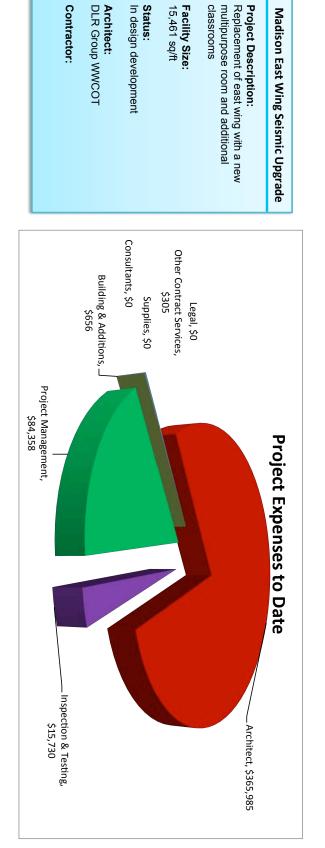

Facility Size: 15,461 sq/ft

Status:

In design development

Architect:
DLR Group WWCOT

Droingt	Budget	09/40 Einal	40/44	Combined Totals
	3			
AA 7100068				
Renovation to Corsair Stadium (108)				
Other Contract Services		\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0
Architect		\$0	\$9,174	\$9,174
Engineering		\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0
Project Management		\$0	\$4,540	\$4,540
Total		\$0	\$13,714	\$13,714
Project Budget	\$11,203,000			
Less Other Funding	\$0			
Net	\$11,203,000			
Actual Measure AA Expenditures	\$13,714			
Running Balance	\$11,189,286			
AA 7100067				
Business & Facilities Infrastructure (111)				
Other Contract Services		\$0	\$0,289	\$6,289
Building & Additions Architect		\$0	\$34,672	\$34,6/2 \$0
Enaineerina		\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0
Project Management		\$0	\$2,926	\$2,926
Non-Cap Equipment		\$0	\$86,285	\$86,285
Total		\$0	\$130,172	\$130,172
Project Budget	\$6,140,952			
Less Other Funding	\$0			
Net A Compatitude	\$6,140,952			
Principa Balanco Actual Measure AA Experioliules	\$130,172			
	#0,0 0,1 00			
AA 7100064				
Community Classroom & Facility Projects (114)				
Other Contract Services		\$0	\$1,656	\$1,656
Building & Additions		\$0	\$1,091	\$1,091
Architect		\$0	\$214,196	\$214,196
Engineering		\$0	\$1,668	\$1,668
Inspection & Testing		\$0	\$2,210	\$2,210
Project Management		\$135	\$68,015	\$68,150
Total		\$135	\$288,835	\$288,970
Project Budget	\$3,221,000			
Net	\$3 221 000			
Actual Measure AA Expenditures	\$288,970			
Running Balance	\$2,932,030			

Projects	Budget	09/10 Final	10/11	Combined Totals
AA 7100057				
Real Property Acquisition (115)				
Legal		\$0	\$0	\$0
Site Acquisition		\$1,739,979	\$4,025,000	\$5,764,979
Inspection & Testing		\$8,689	\$7,986	\$16,674
Project Management		\$0	\$0	\$0
Total		\$1,748,667	\$4,032,986	\$5,781,653
Project Budget	\$6,000,000			
Less Other Funding	\$0			
Net	\$6,000,000			
Actual Measure AA Expenditures	\$5,781,653			
Running Balance	\$218,347			
AA 7100058 Positions Well-ways Grounds Barking Left and Carriers (446)				
Legal		\$0	\$0	\$0
Other Contract Services		\$218	\$750	\$968
Building & Additions		\$185,345	\$6,731	\$192,076
Inspection & Testing		\$13,380	\$3,120	\$16,500
Project Management		\$24,404	\$6,839	\$31,243
Total		\$223,347	\$17,440	\$240,787
Project Budget	\$350,000			
Less Other Funding	\$0			
Net	\$350,000			
Actual Measure AA Expenditures	\$240,787			
Running Balance	\$109,213			
AA 7100069				
Infrastructure & Technology - Technology (117)				
Maintenance Contract		\$0	\$9,472	\$9,472
Building & Additions		\$0	\$0	\$0
Architect		\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0
Project Management		\$0	\$0	\$0
Cap Equipment		\$0	\$207,423	\$207,423
Non-Cap Equipment		\$0	\$0	\$0
Total		\$0	\$216,896	\$216,896
Project Budget	\$500,000			
Less Other Funding	\$0			
Net	\$500,000			
Actual Measure AA Expenditures	\$216,896			
Running Balance	\$283,104			

Innology - Utility (118) Budget Us/10 Final 10/11 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$2,760 \$2,760 \$2,760 \$2,760 \$2,760 \$2,760 \$497,240 \$497,240 \$0 \$2,760 <td< th=""><th>\$13,685,354</th><th>\$8,784,620</th><th>\$4,900,734</th><th></th><th>Grand Total</th></td<>	\$13,685,354	\$8,784,620	\$4,900,734		Grand Total
Innology - Utility (118) Budget U9/10 Final 10/11 Combined of State of Sta					
Innology - Utility (118) Budget 09/10 Final 10/11 Combined in the property of the p				\$497,240	Running Balance
Hnology - Utility (118) Sudget W/10 Final 10/11 Combined				\$2,760	Actual Measure AA Expenditures
Hnology - Utility (118) Sudget W/10 Final 10/11 Combined				\$500,000	Net
Hinology - Utility (118) Hinget W/10 Final 10/11 Combined				\$0	Less Other Funding
Hology - Utility (118) Sudget W/10 Final 10/11 Combined				\$500,000	Project Budget
Hrojects Budget 09/10 Final 10/11 Combined Iotali 10/11	\$2,760	\$2,760	\$0		Total
Hrojects Budget 09/10 Final 10/11 Combined Iotali 10/11	\$0	\$0	\$0		Non-Cap Equipment
Hrojects Budget 09/10 Final 10/11 Combined Iotali 10/11	\$2,760	\$2,760	\$0		Cap Equipment
Projects Budget 09/10 Final 10/11 Combined lotality chnology - Utility (118) \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0	\$0	\$0		Project Management
Projects Budget 09/10 Final 10/11 Combined lotality chnology - Utility (118) \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0	\$0	\$0		Inspection & Testing
Projects Budget 09/10 Final 10/11 Combined lotals chnology - Utility (118) \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0	\$0	\$0		Architect
Budget 09/10 Final 10/11 Combined lotals	\$0	\$0	\$0		Building & Additions
Budger Us/10 Final 10/11	\$0	\$0	\$0		Legal
Budget 09/10 Final 10/11					nfrastructure & Technology - Utility (118)
Budget 09/10 Final 10/11					AA 7100069
Budget 09/10 Final 10/11					
D. J	Combined Totals	10/11	09/10 Final	Budget	Projects

SANTA MONICA COMMUNITY COLLEGE DISTRICT Bond Sales / Expenses Report As of March 31, 2011

\$17,556,122	Total Available as of 4-1-11
\$1,127	Unsold Bond Amount
\$17,554,995	Total Available Remaining
\$142,443,878	Expenses as of 3-31-11
\$159,998,873	Total Available
\$10,998,992	2010
\$11,999,987	2007
\$89,999,923	2005
\$21,999,971	2004
\$25,000,000	2002
Amount	Bond Issue Date
	Measure U Bond \$160,000,000


\$17,556,122	Total Available as of 4-1-11
\$1,127	Unsold Bond Amount
\$17,554,995	Total Available Remaining
\$142,443,878	Expenses as of 3-31-11
\$159,998,873	Total Available
\$10,998,992	2010
\$11,999,987	2007
\$89,999,923	2005
\$21,999,971	2004
\$25,000,000	2002
Amount	Bond Issue Date
	.00000000000000000000000000000000000000

\$/1,/23,000	IOtal Available as 01 4-1-11
903 OCT 173	Total Aviable as of 1 1 11
\$20,002,143	Unsold Bond Amount
\$51,727,465	Total Available Remaining
\$71,770,392	Expenses as of 3-31-11
\$123,497,857	Total Available
\$56,997,857	2009
\$8,500,000	2007
\$58,000,000	2005
Amount	Bond Issue Date
	Measure S Bond \$143,500,000 (1)

\$71,729,608	Total Available as of 4-1-11
\$20,002,143	Unsold Bond Amount
\$51,727,465	Total Available Remaining
\$71,770,392	Expenses as of 3-31-11
\$123,497,857	Total Available
\$56,997,857	2009
\$8,500,000	2007
\$58,000,000	2005
Amount	Bond Issue Date

	\$100,000,000	2010
\$0 +	Amount	Bond Issue Date
		Measure AA Bond \$295,000,000
\$100,000,000		
7200,000,000	\$71,729,608	Total Available as of 4-1-11
\$200 000 000	\$20,002,143	Unsold Bond Amount
\$300,000,000		
200	\$51,727,465	Total Available Remaining
\$400,000,000	\$71,770,392	Expenses as of 3-31-11
	\$123,497,857	Total Available
\$500,000,000	\$56,997,857	2009
	\$8,500,000	2007
\$600.000.000	\$58,000,000	2005
4,00,000,000	Amount	Bond Issue Date
\$700 000 000		

Total Bond \$	\$598,500,000
Total Available \$	\$383,496,730
Total Expenses as of 3-31-11 \$	\$227,899,624
Total Available Remaining \$	\$155,597,106
Total Unsold Bond \$	\$215,003,270



\$512,487	\$6,936,898	\$5,694,648	Available Interest as of 6-30-10
\$0	\$393,004	\$0	Arbitrage Payment as of 6-30-10
\$512,487	\$7,329,902	\$5,694,648	As of 6-30-10
Measure AA	Measure S	Measure U	Interest

Unsold Bond Amount
Total Available as of 4-1-11

\$195,000,000 **\$281,314,646**

\$100,000,000 \$13,685,354 \$86,314,646

Expenses as of 3-31-11
Total Available Remaining

Total Available

\$35,575	\$20,688	As of 6-30-10
Measure S	Measure U	Cost of Issuance Refund
