
# SANTA MONICA Community college District



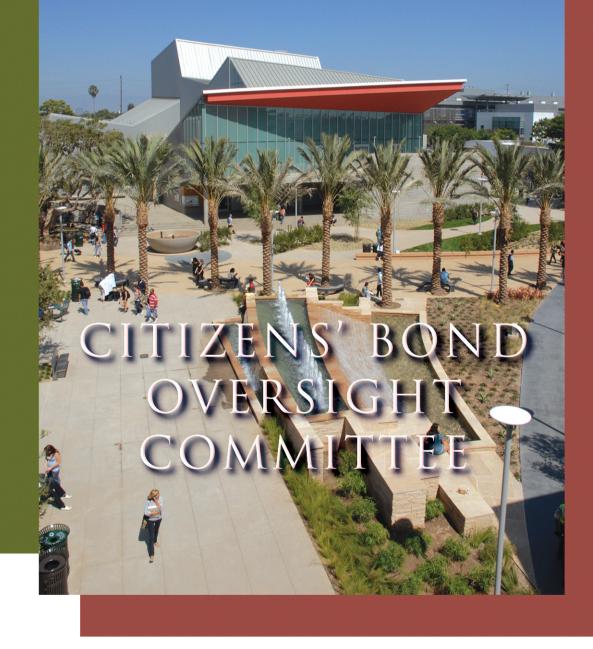

A meeting of the Santa Monica Community College District Citizens' Bond Oversight Committee will be held on Wednesday, **April 20, 2016 at 8 a.m.** The meeting will be held in Drescher 300-E (the Loft) at Santa Monica College, 1900 Pico Boulevard, Santa Monica, California.

## Public Comments

Individuals may address the Citizens' Bond Oversight Committee concerning any subject that lies within the jurisdiction of the Citizens' Bond Oversight Committee by submitting an information card with name and topic on which comment is to be made. The Chair reserves the right to limit the time for each speaker.

## 1. CALL TO ORDER

## 2. <u>ROLL CALL</u>

Jeffrey Graham, Chair Sion Roy, Vice-Chair Sharon Barovsky Michael Dubin Katherine Reuter Aurelia Rhymer Sonya Sultan Sam Zivi

## 3. <u>APPROVAL OF MINUTES</u>

Citizens' Bond Oversight Committee meeting of January 20, 2016 (enclosed)

## 4. <u>REPORTS and DISCUSSION</u> (reports enclosed)

- SMC Bond Capital Construction Budget Summary as of March 31,2016
- Bond Budgets Measure U Measure S Measure AA
- Measure U Reports
   Project Schedule
   Expenditures
- Measure S Reports Project Schedule Expenditures
- Measure AA Reports Project Schedule Expenditures
- Bond Sales/Expenses Report
- SMC Bond Program Contractor List

## 5. INFORMATION – EXPIRING TERMS OF MEMBERS OF THE CITIZENS' BOND OVERSIGHT COMMITTEE

The term of the following member(s) of the Citizens' Bond Oversight Committee is expiring effective **June 30, 2016** and is eligible for reappointment:

- Jeffery Graham, Local Business
- Katherine Reuter, Senior Citizens' Organization
- Samuel Zivi, Local Community/Business/Senior Citizens' Organization
- Aurelia Rhymer, Associated Student representative, will be selected in September.

The term of the following member(s) of the Citizens' Bond Oversight Committee is expiring effective **June 30, 2017** and is eligible for reappointment:

- Sharon Barovsky, Local Community-Malibu
- Michael Dubin, Business Community/Taxpayers Organization
- Sonya Sultan, Local/Business Community
- Sion Roy, Business Community/Taxpayers Association

The Board of Trustees will follow a recruitment and application process to appoint/reappoint members to fill the vacancies.

## 6. PUBLIC COMMENTS

## 7. <u>SCHEDULE OF MEETINGS, 2016-2017</u>

Wednesdays at 8 a.m. July 20, 2016

## 8. ADJOURNMENT

 a. The next meeting of the Citizens' Bond Oversight Committee will be held on Wednesday, July 20, 2016 at 8 a.m. in Drescher Hall Room 300-E (the Loft) at Santa Monica College, 1900 Pico Boulevard, Santa Monica, California.



A meeting of the Santa Monica Community College District Citizens' Bond Oversight Committee was held on Wednesday, January 20, 2016 in Drescher Hall Room 300-E (the Loft) at Santa Monica College, 1900 Pico Boulevard, Santa Monica, California.

## 1. <u>CALL TO ORDER</u> - 8:02 a.m.

2. <u>ROLL CALL</u>

Jeffrey Graham, Chair – Not Present Sion Roy – Present Sharon Barovsky - Present Michael Dubin – Not Present Katherine Reuter – Present Aurelia Rhymer – Present Sonya Sultan – Present Sam Zivi – Present

## Others Present:

Chris Bonvenuto, Chief Director, Business Services Greg Brown, Director of Facilities and Planning Don Girard, Senior Director, Government Relations/Institutional Communications Ramin Nematollahi, Citizens' Bond Oversight Committee Coordinator Charlie Yen, Director, Contracts Emil Zordilla, Assistant Director, Facilities Planning Lisalee Wells, representing Santa Monica College District Bond Counsel, Nixon Peabody Renee S. Graves, representing Vicenti, Llloyd, Stutzman LLP

## 3. <u>APPROVAL OF MINUTES – October 21, 2015</u>

Motion was made by Katherine Reuter and seconded by Sonya Sultan to approve the minutes of Citizen's Bond Oversight Committee meeting on October 21, 2015. *Unanimously approved.* 

## 4. CONFLICT OF INTEREST FORMS

Members were reminded to sign and submit their Conflict of Interest forms for 2016.

5. <u>ROLES/RESPONSIBILITY OF CITIZENS' BOND OVERSIGHT COMMITTEE</u>: Lisalee Wells, representing the Santa Monica College District's bond counsel Nixon Peabody, provided an orientation and update for Citizens' Bond Oversight Committee role and responsibility. Discussion involved about revising the Citizens' Bond Oversight Committee By-Laws term limits from serving two, two-year-terms to three, two-year-terms in accordance with new changes, Lisalee Wells will present the revised ByLaws. Additionally the committee expressed interest in school site visits, including KCRW, and arrangements will be made to accommodate. The presentation covered the following topics:

## General Obligation Bonds

Historical Framework (Proposition 39) Cost of Borrowing Procedural Steps Campaign Promises (Project Lists) Bond Proceeds Citizens' Bond Oversight Committee Organizational representation Brown Act/Basic Requirements Annual Report

## Oversight Purpose of Committee Arbitrage Private Use projects

6. <u>2014-2015 PROP 39 FINANCIAL AUDIT AND PERFORMANCE AUDIT REPORTS</u>: Renée S. Graves, representing the District's auditing firm of Vicenti Lloyd & Stutzman, LLP, and Chris Bonvenuto, Chief Director of Fiscal Services, provided an overview of the 2014-2015 Prop 39 Financial Audit and Performance Audit Reports. The Auditor indicated that there were no instances of noncompliance in both audits and did not identify any exceptions or deficiencies. Both audits will be presented to the Board of Trustees along with the District's Audit Report at the Board meeting on February 2, 2016.

Motion was made by Sonya Sultan seconded by Katherine Reuter to accept the **2014-2015 Prop 39 Financial Audit and Performance Audit Report**. *Unanimously approved by the committee.* 

## 7. <u>REPORTS and DISCUSSION</u>

## Measure U, S and AA and Bond Sales Expenses Reports (reports included with agenda)

The SMC Bond Capital Construction Budget Summary as of December 31, 2015 reports the following:

Measure U Budget:	\$160,000,000
Measure S Budget:	\$143,500,000
Measure AA Budget	\$295,000,000
Other Funding Received:	\$ 43,968,930
Other Funding Pending:	\$ 53,980,950
Total Budget:	\$696,449,880
Estimate at Completion:	\$696,449,880
Bond Funds Remaining:	\$240,612,175

**Measure U:** Total Measure U expenditures last period were **\$216,758**; total remaining funds are **\$14,275,854**. Remaining Measure U funds will be used for the Student Services Project.

**Measure S**: Total expenditures last period were **\$2,958,027** total remaining funds are **\$57,535,638**. Remaining Measure S funds will be used for the Early Childhood Education Center, Health/P.E./Fitness/Central Plant project, Malibu, and the Student Services Project.

**Measure AA**: Total expenditures last period were **\$8,153,016**; total remaining funds are **\$168,800,683**. Remaining Measure AA funds will be used for the Academy of Entertainment and Technology, Information Technology, Health/P.E./Fitness/Central Plant Project, Madison East Wing, the Student Services Project, and security projects.

The Bond Sales/Expenses Report indicates total bond amounts, bond issue dates/amounts, unsold bond amount and total available as of December 31, 2015:

Total Bond	\$598,500,000
Total Available	\$528,492,559
Total Expenses	\$357,887,825
Total Available Remaining	\$170,604,734
Total Unsold Bond	\$ 70,007,441

The SMC Bond Construction Program Contractor List as of December 31, 2015 was presented for information.

Current information on all bond construction projects are available at: <a href="http://smcbondprogram.com/">http://smcbondprogram.com/</a>

Agendas, minutes and other related material regarding the Citizens' Bond Oversight Committee are available at: <u>http://www.smc.edu/CBOC</u>

8. <u>PUBLIC COMMENTS</u>:

None

9. <u>SCHEDULE OF MEETINGS, 2015-2016</u> Wednesday at 8 a.m., April 20, 2016

## **10.** <u>ADJOURNMENT</u> – 9:33 a.m.


The next meeting of the Citizens' Bond Oversight Committee will be held on Wednesday, April 20, 2016 at 8 a.m. in Drescher Hall 300-E (the Loft) at Santa Monica College, 1900 Pico Boulevard, Santa Monica, California.

	Santa Monica Col	lege Bond Ca	pital Constru		Summary as	of 3-31-2016					
Project Number	Project Name	Measure U Budget	Measure S Budget	Measure AA Budget	Interest	Other Funding Received *	Other Funding Pending **	Total Budget	Estimate at Completion	Status	Bond Funds Remaining
U-A	Purchase of BAE Airport Site	\$30,280,878		Duugot			i onang	\$30,280,878	\$30,280,878	Completed	\$
	Emeritus College Facility	\$8,909,940				\$693,842		\$9,603,782	\$9,603,782		\$
	Purchase of 1738 Pearl Street	\$749,208				. ,		\$749,208	\$749,208		\$
	PE Temp. Bldg. Replacement	\$2,797,033						\$2,797,033	\$2,797,033		\$
	Remodel Library Village for Math	\$1,458,690						\$1,458,690	\$1,458,690		\$
	SM Airport Campus Site Improvements	\$4,170,264						\$4,170,264	\$4,170,264		\$
	SM Airport Campus West Building	\$19,709,741						\$19,709,741	\$19,709,741		 \$1
U-H	Theater Arts Renovation	\$19,544,314						\$19,544,314	\$19,544,314	· · ·	;
U-I	Earthquake Rpl. Liberal Arts North	\$6,505,400				\$6,002,325		\$12,507,725	\$12,507,725		;
U-K	Earthquake Rpl. Liberal Arts South	\$6,108,150				\$10,625,070		\$16,733,220	\$16,733,220		 \$
U-L	Shuttle Replacement Parking	\$18,969,509				+		\$18,969,509	\$18,969,509		\$
U-M	North Quad Plaza	\$11,388,463						\$11,388,463	\$11,388,463		\$
U-Q	Infrastructure & Safety	\$4,003,084						\$4,003,084	\$4,003,084		\$(
	Restroom Improvements	\$17,501						\$17,501	\$17,501		\$(
	Athletic Fields Phase I, Corsair Field	<i></i>	\$4,372,535			\$67,530		\$4,440,065	\$4,440,065		\$
	Athletic Fields Phase I, John Adams		\$2,969,807			<i></i> ,550		\$2,969,807	\$2,969,807		\$(
	Pico Promenade Improvements, Phase I		\$1,018,009					\$1,018,009	\$1,018,009	-	\$(
S-13	Adv. Architecture Related Exp for AA		\$1,010,005					\$1,010,005	\$1,010,005 \$0		\$(
AA-114	Community Classroom & Facility Projects		Ç0	\$3,162,183				\$3,162,183	\$3,162,183		\$(
U-T	14th and Pico Project	\$319,242		<i>\$</i> 3,102,103				\$319,242	\$319,242		\$(
U-N	Letters & Sci Demo/Restore	\$313,242						\$0	\$0		\$(
	Real Property Acquisition		\$45,597	\$14,802,902				\$0 \$14,848,499	\$14,848,499		\$(
	Renovation of Corsair Stadium		Ş45,597	\$14,802,902 \$35,299				\$35,299	\$35,299 \$35,299		\$(
	Performing Arts Complex		\$37,697,625	\$55,299		\$2,992,576		\$40,690,201	\$40,690,201		\$(
	Music Complex	\$2,011,371	357,097,025			\$2,618,113		\$4,629,484	\$4,629,484	-	\$(
	Career Opportunity Center	\$2,011,571		\$0		\$2,010,115		\$4,629,484	\$4,629,484 \$0	-	\$(
AA-118	Infrastructure & Technology - Utility			ېر \$27,753				\$0 \$27,753	\$0 \$27,753		\$(
	Business & Facilities Infrastructure			\$1,968,124				\$1,968,124	\$1,968,124		\$(
AA-111 AA-117	Infrastructure & Technology - Technology			\$1,908,124 \$2,434,417				\$1,908,124 \$2,434,417	\$2,434,417	-	\$(
	Energy Efficiency Projects		\$293,361	\$2,434,417 \$3,016,773		\$708,637		\$2,434,417 \$4,018,771	\$2,434,417 \$4,018,771		\$(
AA-102	Infrastructure & Technology - Information Technology Relocation		\$295,501	\$24,392,627		\$708,057		\$4,018,771	\$4,018,771		\$1,877,085
AA-102 AA-103						¢000.444	ćE 044.0E0			-	
	Media and Technology Complex - Academy Site			\$87,816,489		\$990,441	\$5,844,950			In Construction	\$25,480,934
	Madison East Wing Seismic Upgrade		¢11 CO2 202	\$23,550,625				\$23,550,625		In Construction	\$8,980,556
	Replacement Health/PE/Fitness Central Plant Building		\$11,603,383					\$51,989,845		In Construction	\$28,429,691
AA-119	Emergency Lighting, Fire Alarm, and Security System		6706 222	\$9,570,794				\$9,570,794		In Construction	\$4,287,069
S-15	Signage Safety/Information		\$706,223	640 460 474				\$706,223		In Construction	\$14,183
AA-101	Environmental Performance - Central Plant Connections		¢4.675.000	\$10,460,471				\$10,460,471		In Construction	\$9,509,854
	Satellite Campus Parking Facilities and Roadway		\$4,675,000	\$2,535,375			ć1 240 000	\$7,210,375	\$7,210,375		\$1,187,958
	Early Childhood Development/Childcare		\$7,000,000	64 775 000	\$1,858,578		\$4,318,000				\$6,009,568
	Malibu Site Acquisition and Facility	620 622 575	\$25,000,000	\$1,775,991		<u></u>		\$26,775,991	\$26,775,991		\$19,486,437
	Student Services Building	\$20,638,446	\$46,692,750		\$16,032,783	\$1,321,000		\$109,862,122		-	\$69,561,562
U-S, S-11, AA-112		\$2,110,430	\$716,428	\$750,000				\$3,576,858		-	\$672,044
	Other Bond Related Expenses	40	\$609,282	4.0.000				\$609,282	\$609,282	-	\$255,153
	Replacement Math and Science Extension Building	\$308,336		\$40,088,000			\$40,088,000		\$80,484,336		\$40,083,050
AA-105	Drescher - Academic Modernization, Bookstore, Pico Promenade II		4.0	\$2,258,878				\$2,258,878	\$2,258,878	-	\$2,253,796
S-16, AA-212	Cost of Issuance		\$100,000	\$500,000				\$600,000	\$600,000	-	\$315,000
	Management Reserve			\$289,694	\$2,105,934			\$2,395,628	\$2,395,628		\$289,694
	Project Totals	\$160,000,000	\$143,500,000	\$295,000,000	\$19,997,295	\$26,019,534	\$50,250,950	\$694,767,779	\$694,767,779		\$218,693,634
	* City of SM: \$10,206,823; FEMA: \$1,962,572; State: \$5,779,000; Pr Emeritus College Foundation: \$693,842; Bond Interest and Cost of I	•		; SCE: \$633,639	9; Gas Co.: \$88,2	262; Madison Fc	oundation: \$2,9	92,576; KCRW: \$	958,462;		
	** City of SM: 4,318,000; KCRW: \$5,844,950; State: \$40,088,000										4/1

### SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure U Bond Budget

As of March 31, 2016

	Project Name	Completion	Project Budget	Measure U Allocation	Other Funding	Measure U Expenditures as of 3/31/16	Measure U Expenditures as of 12/31/15	Measure U Expenditures Last Period	Total Measure U Remaining
А	Purchase of BAE Airport Site	Completed	\$30,280,878	\$30,280,878	\$0	\$30,280,878	\$30,280,878	\$0	\$0
В	Emeritus College Facility	Completed	\$9,603,782	\$8,909,940	\$693,842	\$8,909,940	\$8,909,940	\$0	\$0
С	Purchase of 1738 Pearl Street	Completed	\$749,208	\$749,208	\$0	\$749,208	\$749,208	\$0	\$0
D	PE Temp. Bldg. Replacement	Completed	\$2,797,033	\$2,797,033	\$0	\$2,797,033	\$2,797,033	\$0	\$0
Е	Remodel Library Village for Math	Completed	\$1,458,690	\$1,458,690	\$0	\$1,458,690	\$1,458,690	\$0	\$0
F	SM Airport Campus Site Improvements	Completed	\$4,170,264	\$4,170,264	\$0	\$4,170,264	\$4,170,264	\$0	\$0
G	SM Airport Campus West Building	Completed	\$19,709,741	\$19,709,741	\$0	\$19,709,741	\$19,709,741	\$0	\$0
Н	Theater Arts Renovation	Completed	\$19,544,314	\$19,544,314	\$0	\$19,544,314	\$19,544,314	\$0	\$0
I	Earthquake Rpl. Liberal Arts North	Completed	\$12,507,725	\$6,505,400	\$6,002,325	\$6,505,400	\$6,505,400	\$0	\$0
J	Music Complex	Completed	\$4,629,484	\$2,011,371	\$2,618,113	\$2,011,371	\$2,011,371	\$0	\$0
К	Earthquake Rpl. Liberal Arts South	Completed	\$16,733,220	\$6,108,150	\$10,625,070	\$6,108,150	\$6,108,150	\$0	\$0
L	Shuttle Replacement Parking	Completed	\$18,969,509	\$18,969,509	\$0	\$18,969,509	\$18,969,509	\$0	\$0
М	North Quad Plaza	Completed	\$11,388,463	\$11,388,463	\$0	\$11,388,463	\$11,388,463	\$0	\$0
Ν	Letters & Sci Demo/Restore	Completed	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0	Student Services Building	November 2018	\$109,862,122	\$20,638,446	\$89,223,676	\$7,385,483	\$6,362,592	\$1,022,891	\$13,252,963
Р	Science Complex Addition	Completed	\$87,944,336	\$308,336	\$87,636,000	\$308,336	\$308,336	\$0	\$0
Q	Infrastructure & Safety	Completed	\$4,003,084	\$4,003,084	\$0	\$4,003,084	\$4,003,084	\$0	\$0
R	Restroom Improvements	Completed	\$17,501	\$17,501	\$0	\$17,501	\$17,501	\$0	\$0
S	Master Planning	Completed	\$2,110,430	\$2,110,430	\$0	\$2,110,430	\$2,110,430	\$0	\$0
Т	14th and Pico Project	Completed	\$319,242	\$319,242	\$0		\$319,242	\$0	\$0
	Project Totals		\$356,799,026	\$160,000,000	\$196,799,026	\$146,747,037	\$145,724,146	\$1,022,891	\$13,252,963

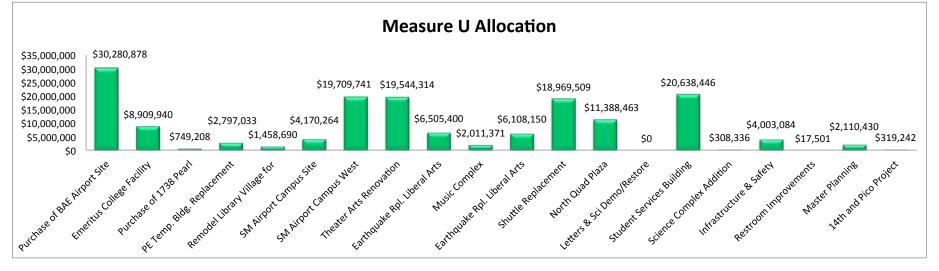


## SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure U Bond Budget History as of March 31, 2016

	Project Name	Completion	Preliminary Measure U Budget	Measure U Budget as of 12/31/15	Measure U Budget as of 3/31/16	Variance	Measure U Remaining as of 3/31/16
Α	Purchase of BAE Airport Site	Completed	\$30,000,000		\$30,280,878	\$0	\$0
В	Emeritus College Facility	Completed	\$8,883,381	\$8,909,940	\$8,909,940		\$0
С	Purchase of 1738 Pearl Street	Completed	\$749,208	\$749,208	\$749,208	\$0	\$0
D	PE Temp. Bldg. Replacement	Completed	\$2,673,247	\$2,797,033	\$2,797,033	\$0	\$0
E	Remodel Library Village for Math	Completed	\$1,425,565	\$1,458,690	\$1,458,690	\$0	\$0
F	SM Airport Campus Site Improvements	Completed	\$6,200,000	\$4,170,264	\$4,170,264	\$0	\$0
G	SM Airport Campus West Building	Completed	\$20,071,124	\$19,709,741	\$19,709,741	\$0	\$0
Н	Theater Arts Renovation	Completed	\$16,992,296	\$19,544,314	\$19,544,314	\$0	\$0
I.	Earthquake Rpl. Liberal Arts North	Completed	\$5,352,752	\$6,505,400	\$6,505,400	\$0	\$0
J	Music Complex	Completed	\$4,802,537	\$2,011,371	\$2,011,371	\$0	\$0
K	Earthquake Rpl. Liberal Arts South	Completed	\$2,863,566	\$6,108,150	\$6,108,150	\$0	\$0
L	Shuttle Replacement Parking	Completed	\$17,256,000	\$18,969,509	\$18,969,509	\$0	\$0
М	North Quad Plaza	Completed	\$3,939,759	\$11,388,463	\$11,388,463	\$0	\$0
Ν	Letters & Sci Demo/Restore	Completed	\$1,192,250	\$0	\$0	\$0	\$0
0	Student Services Building	November 2018	\$23,952,004	\$20,638,446	\$20,638,446	\$0	\$13,252,963
Р	Science Complex Addition	Completed	\$10,613,910	\$308,336	\$308,336	\$0	\$0
Q	Infrastructure & Safety	Completed	\$5,000,000	\$4,003,084	\$4,003,084	\$0	\$0
R	Restroom Improvements	Completed	\$400,000	\$17,501	\$17,501	\$0	\$0
S	Master Planning	Completed	\$500,000	\$2,110,430	\$2,110,430	\$0	\$0
Т	14th and Pico Project	Completed	\$14,662,000	\$319,242	\$319,242	\$0	\$0
	Project Totals		\$177,529,599	\$160,000,000	\$160,000,000	\$0	\$13,252,963

#### SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure S Bond Budget

As of March 31, 2016

	Project Name	Completion	Project Budget	Measure S Allocation	Other Funding	Measure S Expenditures as of 3/31/16	Measure S Expenditures as of 12/31/15	Measure S Expenditures Last Period	Total Measure S Remaining
1	Athletic Fields Phase I, Corsair Field	Completed	\$4,440,065	\$4,372,535	\$67,530	\$4,372,535	\$4,372,535	\$0	\$0
1A	Athletic Fields Phase I, John Adams	Completed	\$2,969,807	\$2,969,807	\$0	\$2,969,807	\$2,969,807	\$0	\$0
2	Performing Arts Complex	Completed	\$40,690,201	\$37,697,625	\$2,992,576	\$37,697,625	\$37,697,625	\$0	\$0
3	Career Opportunity Center	Completed	\$0	\$0	\$0	\$0	\$0	\$0	\$0
4	Replacement Health/PE/Fitness Building	February 2017	\$51,643,399	\$11,603,383	\$40,040,016	\$11,603,383	\$10,872,855	\$730,528	\$0
5	Early Childhood Development/Childcare	December 2018	\$13,176,578	\$7,000,000	\$6,176,578	\$990,432	\$671,512	\$318,920	\$6,009,568
6	Malibu Site Acquisition and Facility	November 2018	\$26,775,991	\$25,000,000	\$1,775,991	\$7,289,554	\$7,235,833	\$53,721	\$17,710,446
7	Energy Efficiency Projects	Completed	\$510,683	\$293,361	\$217,322	\$293,361	\$293,361	\$0	\$0
8	Satellite Campus Parking Facilities and Roadway Improvements	On-Going	\$7,210,375	\$4,675,000	\$2,535,375	\$3,891,747	\$3,891,535	\$212	\$783,253
9	Parking Garage, Grounds and Equipment - Student Services	November 2018	\$109,862,122	\$46,692,750	\$63,169,372	\$15,561,294	\$15,546,814	\$14,480	\$31,131,456
10	Pico Promenade Improvements	Completed	\$1,018,009	\$1,018,009	\$0	\$1,018,009	\$1,018,009	\$0	\$0
11	Master Planning	Completed	\$716,428	\$716,428	\$0	\$716,428	\$716,428	\$0	\$0
12	Other Bond Related Expenses	On-Going	\$609,282	\$609,282	\$0	\$354,129	\$343,405	\$10,724	\$255,153
13	Adv. Architecture Related Exp for AA	Completed	\$0	\$0	\$0	\$0	\$0	\$0	\$0
14	Real Property Acquisition	Completed	\$45,597	\$45,597	\$0	\$45,597	\$45,597	\$0	\$0
15	Signage Safety/Information	On-Going	\$706,223	\$706,223	\$0	\$692,040	\$289,046	\$402,994	\$14,183
16	Cost of Issuance	On-Going	\$100,000	\$100,000	\$0	\$0	\$0	\$0	\$100,000
	Project Totals		\$260,474,760	\$143,500,000	\$116,974,760	\$87,495,941	\$85,964,362	\$1,531,579	\$56,004,059

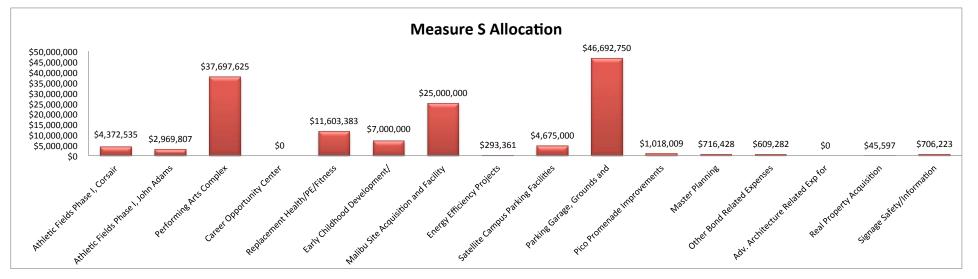


## SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure S Bond Budget History as of March 31, 2016

	Project Name	Completion	Preliminary Measure S Budget	Measure S Budget as of 12/31/15	Measure S Budget as of 3/31/16	Variance	Measure S Remaining as of 3/31/16
1	Athletic Fields Phase I, Corsair Field	Completed	\$1,800,000	\$4,372,535	\$4,372,535	\$0	\$0
1A	Athletic Fields Phase I, John Adams	Completed	\$35,200,000	\$2,969,807	\$2,969,807	\$0	\$0
2	Performing Arts Complex	Completed	\$24,000,000	\$37,697,625	\$37,697,625	\$0	\$0
3	Career Opportunity Center	Completed	\$20,000,000	\$0	\$0	\$0	\$0
4	Replacement Health/PE/Fitness Building	February 2017	\$20,000,000	\$11,603,383	\$11,603,383	\$0	\$0
5	Early Childhood Development/Childcare	December 2018	\$7,000,000	\$7,000,000	\$7,000,000	\$0	\$6,009,568
6	Malibu Site Acquisition and Facility	Novemver 2018	\$25,000,000	\$25,000,000	\$25,000,000	\$0	\$17,710,446
7	Energy Efficiency Projects	Completed	\$2,000,000	\$293,361	\$293,361	\$0	\$0
8	Satellite Campus Parking Facilities and Roadway Improvements	On-Going	\$0	\$4,775,000	\$4,675,000	-\$100,000	\$783,253
9	Parking Garage, Grounds and Equipment - Student Services	November 2018	\$0	\$46,692,750	\$46,692,750	\$0	\$31,131,456
10	Pico Promenade Improvements, Phase I	Completed	\$0	\$1,018,009	\$1,018,009	\$0	\$0
11	Master Planning	Completed	\$0	\$716,428	\$716,428	\$0	\$0
12	Other Bond Related Expenses	On-Going	\$0	\$609,282	\$609,282	\$0	\$255,153
13	Adv. Architecture Related Exp for AA	Completed	\$0	\$0	\$0	\$0	\$0
14	Real Property Acquisition	Completed	\$0	\$45,597	\$45,597	\$0	\$0
15	Signage Safety/Information	On-Going	\$0	\$606,223	\$706,223	\$100,000	\$14,183
16	Cost of Issuance	On-Going	\$0	\$100,000	\$100,000	\$0	\$100,000
	Project Totals		\$135,000,000	\$143,500,000	\$143,500,000	\$0	\$56,004,059

#### SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure AA Bond Budget As of March 31, 2016

	Project Name	Completion	Project Budget	Measure AA Allocation	Other Funding	Measure AA Expenditures as of 3/31/16	Measure AA Expenditures as of 12/31/15	Measure AA Expenditures Last Period	Total Measure AA Remaining
101	Environmental Performance - Central Plant Connections	August 2017	\$10,460,471	\$10,460,471	\$0	\$950,617	\$932,421	\$18,196	\$9,509,854
102	Infrastructure & Technology - Information Technology Relocation	Completed	\$24,392,627	\$24,392,627	\$0	\$22,515,542	\$21,031,632	\$1,483,910	\$1,877,085
103	Media and Technology Complex - Academy Site	November 2016	\$94,651,880	\$87,816,489	\$6,835,391	\$62,335,555	\$52,113,615	\$10,221,940	\$25,480,934
104	Replacement Health/PE/Fitness/ Dance Building with Central Plant	February 2017	\$51,989,845	\$40,386,462	\$11,603,383	\$11,956,771	\$6,875,686	\$5,081,085	\$28,429,691
105	Drescher - Academic Modernization, Bookstore, Pico Promenade	June 2019	\$2,258,878	\$2,258,878	\$0	\$5,082	\$5,082	\$0	\$2,253,796
106	Replacement Math and Science Extension Building	June 2021	\$80,484,336	\$40,088,000	\$40,396,336	\$4,950	\$4,950	\$0	\$40,083,050
107	Madison East Wing Seismic Upgrade	September 2016	\$23,550,625	\$23,550,625	\$0	\$14,570,069	\$12,322,126	\$2,247,943	\$8,980,556
108	Renovation of Corsair Stadium	Completed	\$35,299	\$35,299	\$0	\$35,299	\$35,299	\$0	\$0
109	Career Opportunity and Advancement Center (Bundy)	Completed	\$0	\$0	\$0	\$0	\$0	\$0	\$0
110	Malibu Center	November 2018	\$26,775,991	\$1,775,991	\$25,000,000	\$0	\$0	\$0	\$1,775,991
111	Business & Facilities Infrastructure	On-Going	\$1,968,124	\$1,968,124	\$0	\$1,968,124	\$1,968,124	\$0	\$0
112	Master Planning, Program Management, Overhead	On-Going	\$750,000	\$750,000	\$0	\$77,956	\$77,956	\$0	\$672,044
113	Energy Efficiency Projects	On-Going	\$3,508,088	\$3,016,773	\$491,315	\$3,016,773	\$3,016,773	\$0	\$0
114	Community Classroom & Facility Projects	Completed	\$3,162,183	\$3,162,183	\$0	\$3,162,183	\$3,162,183	\$0	\$0
115	Real Property Acquisition	Completed	\$14,802,902	\$14,802,902	\$0	\$14,802,902	\$14,802,902	\$0	\$0
116	Roadways, Walkways, Grounds, Parking Lots, and Garages	On-Going	\$7,210,375	\$2,535,375	\$4,675,000	\$2,130,670	\$2,130,670	\$0	\$404,705
117	Infrastructure & Technology - Technology	On-Going	\$2,434,417	\$2,434,417	\$0	\$2,434,417	\$2,434,417	\$0	\$0
118	Infrastructure & Technology - Utility	Completed	\$27,753	\$27,753	\$0	\$27,753	\$27,753	\$0	\$0
119	Emergency Lighting, Fire Alarm, and Security System	On-Going	\$9,570,794	\$9,570,794	\$0	\$5,283,725	\$4,972,728	\$310,997	\$4,287,069
120	Student Services	November 2018	\$109,862,122	\$25,177,143	\$84,684,979	\$0	\$0	\$0	\$25,177,143
121	Cost of Issuance	On-Going	\$500,000	\$500,000	\$0	\$285,000	\$285,000	\$0	\$215,000
	Management Reserve	On-Going	\$289,694	\$289,694	\$0	\$0	\$0	\$0	\$289,694
	Project Totals		\$468,686,404	\$295,000,000	\$173,686,404	\$145,563,388	\$126,199,317	\$19,364,071	\$149,436,612



## SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure AA Bond Budget History as of March 31, 2016

	Project Name	Completion	Preliminary Measure AA Budget	Measure AA Budget as of 12/31/15	Measure AA Budget as of 3/31/16	Variance	Measure AA Remaining as of 3/31/16
101	Environmental Performance - Central Plant Connections	August 2017	\$12,034,042	\$9,486,271	\$10,460,471	974,200	\$9,509,854
102	Infrastructure & Technology - Information Technology Relocation	Completed	\$13,287,218	\$23,978,879	\$24,392,627	413,748	\$1,877,085
103	Media and Technology Complex - Academy Site	November 2016	\$57,480,824	\$85,709,065	\$87,816,489	2,107,424	\$25,480,934
104	Replacement Health/PE/Fitness/ Dance Building with Central Plant	February 2017	\$29,232,317	\$40,040,016	\$40,386,462	346,446	\$28,429,691
105	Drescher - Academic Modernization, Bookstore, Pico Promenade II	June 2019	\$34,026,480	\$2,258,878	\$2,258,878	0	\$2,253,796
106	Replacement Math and Science Extension Building	June 2021	\$68,259,000	\$43,818,000	\$40,088,000	(3,730,000)	\$40,083,050
107	Madison East Wing Seismic Upgrade	September 2016	\$6,146,000	\$23,107,323	\$23,550,625	443,302	\$8,980,556
108	Renovation of Corsair Stadium	Completed	\$11,203,000	\$35,299	\$35,299	0	\$0
109	Career Opportunity and Advancement Center (Bundy)	Completed	\$32,384,000	\$0	\$0	0	\$0
110	Malibu Center	November 2018	\$6,069,031	\$1,775,991	\$1,775,991	0	\$1,775,991
111	Business & Facilities Infrastructure	On-Going	\$17,506,952	\$2,000,000	\$1,968,124	(31,876)	\$0
112	Master Planning, Program Management, Overhead	On-Going	\$2,000,000	\$750,000	\$750,000	0	\$672,044
113	Energy Efficiency Projects	On-Going	\$5,371,136	\$3,751,947	\$3,016,773	(735,174)	\$0
114	Community Classroom & Facility Projects	Completed	\$0	\$3,162,183	\$3,162,183	0	\$0
115	Real Property Acquisition	Completed	\$0	\$14,802,902	\$14,802,902	0	\$0
116	Roadways, Walkways, Grounds, Parking Lots, and Garages	On-Going	\$0	\$2,535,375	\$2,535,375	0	\$404,705
117	Infrastructure & Technology - Technology	On-Going	\$0	\$2,512,181	\$2,434,417	(77,764)	\$0
118	Infrastructure & Technology - Utility	Completed	\$0	\$27,753	\$27,753	0	\$0
119	Emergency Lighting, Fire Alarm, and Security System	On-Going	\$0	\$9,570,794	\$9,570,794	0	\$4,287,069
120	Student Services	November 2018	\$0	\$25,177,143	\$25,177,143	0	\$25,177,143
121	Cost of Issuance	On-Going	\$0	\$500,000	\$500,000	0	\$215,000
	Management Reserve	On-Going	\$0	\$0	\$289,694	289,694	\$289,694
	Project Totals		\$295,000,000	\$295,000,000	\$295,000,000	\$0	\$149,436,612


#### SANTA MONICA COMMUNITY COLLEGE DISTRICT Bond Sales / Expenses Report As of March 31, 2016

Measure U Bond \$160,000,000		
Bond Issue Date		Amount
	2002	\$25,000,000
	2004	\$21,999,971
	2005	\$89,999,923
	2007	\$11,999,987
	2010	\$10,998,992
Total Available		\$159,998,873
Expenses as of 3-31-16		\$146,747,037
Total Available Remaining		\$13,251,836
Unsold Bond Amount		\$1,127
Total Available as of 4-1-16		\$13,252,963

Measure S Bond \$143,500,000 (1)		
Bond Issue Date		Amount
	2005	\$58,000,000
	2007	\$8,500,000
	2009	\$56,997,857
Total Available		\$123,497,857
Expenses as of 3-31-16		\$87,495,941
Total Available Remaining		\$36,001,916
Unsold Bond Amount		\$20,002,143
Total Available as of 4-1-16		\$56,004,059

Measure AA Bond \$295,000,000		
Bond Issue Date		Amount
	2010	\$100,000,000
	2014	\$144,995,829
Total Available		\$244,995,829
Expenses as of 3-31-16		\$145,563,388
Total Available Remaining		\$99,432,441
Unsold Bond Amount		\$50,004,171
Total Available as of 4-1-16		\$149,436,612

Total Bond	\$598,500,000
Total Available	\$528,492,559
Total Expenses as of 3-31-16	\$379,806,366
Total Available Remaining	\$148,686,193
Total Unsold Bond	\$70,007,441

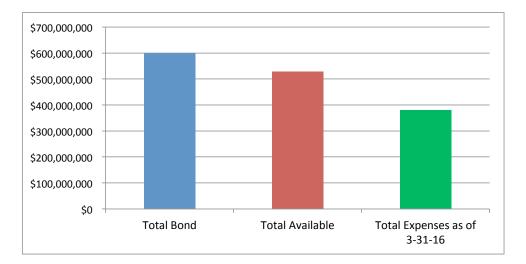

Interest	Measure U	Measure S	Measure AA
As of 6-30-15	\$6,681,152	\$9,795,885	\$3,884,032
Arbitrage Payment as of 6-30-15	\$0	\$420,037	\$0
Available Interest as of 6-30-15	\$6,681,152	\$9,375,848	\$3,884,032

Cost of Issuance Refund	Measure U	Measure S
As of 6-30-15	\$20,688	\$35,575

(1) Original Bond \$135,000,000.00, refunding on 2-15-07 received additional \$8,500,000.00

## SANTA MONICA COMMUNITY COLLEGE DISTRICT

## Measure U Project Schedule As of March 31, 2016

	Project Name	Completion	20	14		20	15	201	6		2017	7	2	2018	}
А	Purchase of BAE Airport Site	Completed													
В	Emeritus College Facility	Completed													
С	Purchase of 1738 Pearl Street	Completed													
D	PE Temp. Bldg. Replacement	Completed													
Е	Remodel Library Village for Math	Completed													
F	SM Airport Campus Site Improvements	Completed													
G	SM Airport Campus West Building	Completed													
Н	Theater Arts Renovation	Completed													
I	Earthquake Rpl. Liberal Arts North	Completed													
J	Music Complex	Completed													
К	Earthquake Rpl. Liberal Arts South	Completed													
L	Shuttle Replacement Parking	Completed													
М	North Quad Plaza	Completed													
Ν	Letters & Sci Demo/Restore	Completed													
0	Student Services Building	November 2018													
Р	Science Complex Addition	Completed			Τ										
Q	Infrastructure & Safety	Completed													
R	Restroom Improvements	Completed													
S	Master Planning	Completed													
Т	14th and Pico Project	Completed													
	* 014 Aliment October 10 - 10	0.11				4			_	_					
	* SM Airport Campus also known as Bundy	Site		In C	ons	truct	ion								

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16	Combined Totals
110,000	Buuget	02/00111101	00/04111101	04/001/11/01	00/00111101	oolor i mai	enree i mai	00/00 1 11101	00/10111101	10/11/1mai	11/12 1 110	12/10/1110	10/1411101	14/10 mar	10/10	oombilied lotais
U7100010														1		
Purchase of BAE Airport Site (A)																
Site Acquisition		\$0	\$0	\$0	\$30,280,878	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$30,280,878
Total		\$0			\$30,280,878				\$0			\$0			\$0	
Project Budget	\$30,280,878															
Less Other Funding	\$0															
Net	\$30,280,878															
Actual Measure U Expenditures	\$30,280,878															
Running Balance	\$0															
U7100028																
Emeritus College Facility (B)																
Site Acquisition		\$8,658,675	\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$8,658,675
Legal		\$14,649	\$3,009	\$20,421	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$38,078
Architect		\$93,735	\$27,831	\$161	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$121,727
Engineering		\$18,400	\$0	\$0	\$0		\$0			\$0	\$0				\$0	\$18,400
Supply		\$0	\$4,461	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,461
Building & Additions		\$0	\$17,496	\$0	\$4,000	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$21,496
Cap Equipment		\$0	\$49,406	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$49,406
Non-Cap Equipment		\$0	-\$2,197	\$0			\$0			\$0					\$0	
Total		\$8,785,459	\$100,007	\$20,582	\$3,892	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$8,909,940
Project Budget	\$9,603,782	Received				· · · · ·								• • • •		
Less Other Funding*	\$693,842	\$693,842		* Other Fundin	g Source:											
Net	\$8,909,940					\$693,842 receiv	ed									
Actual Measure U Expenditures	\$8,909,940				0											
Running Balance	\$0															
°																
U7100006																
1738 Pearl Street (C)																
Site Acquisition		\$0	\$704,534	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$704,534
Site Improvement		\$0	\$3,250	\$0			\$0			\$0	\$0				\$0	\$3,250
Building & Additions		\$0	\$41,424	\$0	\$0		\$0			\$0					\$0	\$41,424
Total		\$0		\$0			\$0			\$0					\$0	
Project Budget	\$749,208															
Less Other Funding	\$0															
Net	\$749,208															
Actual Measure U Expenditures	\$749,208															
Running Balance	\$0															

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16	Combined Totals
U7100026																
PE Temporary Building Replacement (D)																
Architect		\$148,055	\$42,372		\$485	\$0	\$0		\$0	\$0	\$0	\$0		\$0	\$0	\$197,133
Building & Additions		\$43,866	\$1,922,493		\$0		\$0	\$0	\$0						\$0	\$2,382,291
Inspection & Testing		\$6,455	\$136,510	\$716	\$0		\$0					\$0			\$0	\$143,681
Project Management		\$4,800	\$56,247		\$0		\$0								\$0	\$66,272
Advertising and Moving Expenses		\$763	\$0	\$6,893	\$0		\$0								\$0	\$7,656
Total		\$203,939	\$2,157,622	\$434,987	\$485	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,797,033
Project Budget	\$2,797,033															
Less Other Funding	\$0															
Net	\$2,797,033															
Actual Measure U Expenditures	\$2,797,033															
Running Balance	\$0															
U7100310																
Remodel Library Village for Math (E)																
Moving Exp.		\$0	\$38,625		\$0		\$0								\$0	\$38,625
Building & Additions		\$0	\$1,036,490	\$115,653	\$0		\$0								\$0	\$1,152,143
Architect		\$104,992	\$27,141	\$1,340	\$486		\$0								\$0	\$133,959
Engineering		\$0	\$2,658		\$0		\$0		\$0						\$0	\$2,658
Inspection & Testing		\$0	\$27,083		\$0		\$0								\$0	\$52,258
Project Management		\$0	\$51,679		\$0		\$0								\$0	\$56,079
Advertising and Moving Expenses		\$207	\$10,137		\$0		\$0		\$0		\$0	\$0			\$0	\$22,967
Total		\$105,199	\$1,193,813	\$159,191	\$486	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,458,690
Project Budget	\$1,458,690															
Less Other Funding	\$0															
Net	\$1,458,690															
Actual Measure U Expenditures	\$1,458,690															
Running Balance	\$0															


Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16	Combined Totals
U7100027																
SM Airport Campus Site Improvements (F)																
Supplies		\$0	\$26,234	\$975	\$5,873	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$33,082
Misc Fees		\$0		\$0	\$0	\$34,274	\$0						\$0		\$0	\$34,299
Other Contract Services		\$3,860	\$11,508	\$8,434	\$1,501	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$25,302
Site Improvement		\$0	\$0	\$15,182	\$5,790	\$7,237	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$28,209
Building & Additions		\$0	\$1,495,697	\$1,670,788	\$4,824	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,171,309
Architect		\$104,934	\$500	\$0	\$43,570	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$149,004
Engineering		\$35,000	\$148,304	\$950	\$10,040	\$0	\$0	\$0	\$0				\$0		\$0	\$194,294
Inspection & Testing		\$5,032	\$118,662	\$191,271	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$314,965
Project Management		\$750	\$155,798	\$38,425	\$1,365	\$220	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$196,558
City Fees, Advertising and Security System		\$16,587	\$1,802	\$327	\$150	\$4,375	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$23,241
Total		\$166,163	\$1,958,530	\$1,926,352	\$73,113	\$46,106	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,170,264
Project Budget	\$4,170,264															
Less Other Funding	\$0															
Net	\$4,170,264															
Actual Measure U Expenditures	\$4,170,264															
Running Balance	\$0															
U7110027																
SM Airport Campus West Building (G)																
Supply		\$0	\$0	\$17,650	\$28,017	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$45,667
Other Contract Services		\$0	\$0	\$0	\$3,576	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,576
Moving Expenses		\$0		\$180	\$15,824	\$0	\$0				\$0	\$0			\$0	
Building & Additions		\$0	\$0	\$15,037,532	\$1,256,065	\$46,946	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$16,340,543
Architect		\$0	\$971,954	\$1,043,950	\$49,779	\$1,147	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,066,830
Engineering		\$0	\$2,920	\$9,800	\$5,010	\$963	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$18,693
Inspection & Testing		\$0	\$21,173	\$126,510	\$9,856	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$157,539
Project Management		\$0	\$14,450	\$313,715	\$13,956	\$0	\$0			\$0	\$0	\$0	\$0	\$0	\$0	\$342,121
Cap Equipment		\$0	\$49,795	\$326,382	\$4,792	\$0	\$0						\$0		\$0	
Non-Cap Equipment		\$0			\$57,240	\$0	\$0						\$0		\$0	
Total		\$0	\$1,060,292	\$17,156,277	\$1,444,115	\$49,056	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$19,709,741
Project Budget	\$19,709,741															
Less Other Funding	\$0															
Net	\$19,709,741															
Actual Measure U Expenditures	\$19,709,741															
Running Balance	\$0															

Ducie ata	Dudaat	00/00 Einel				00/07 Einel	07/00 5:	00/00 Ein al	00/40 5:		44/40 Einel	40/40 Einel		A AIAE Elizat	45/40	O a subject of Tabala
Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16	Combined Totals
U7100025	1															
Theatre Arts Renovation (H)																
Supplies		\$0	\$8,904	-\$14	\$12,858	\$16.619	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$38,367
Legal		\$0	\$0	\$0	\$0		\$0	\$0		\$0		\$0	\$0		\$0	\$00,001
Moving Services		\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$0		\$0	\$0		\$0	\$14.061
Other Contract Services		\$0	\$0	\$0	\$0		\$0	\$5,245	\$0	\$0			\$0		\$0	\$5,245
Rental / Lease		\$0	\$1,446	\$2,200	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0		\$0	\$3,646
Building & Additions		\$528	\$1.326.630	\$4,540,487	\$10.897.603	\$56,122	\$25.220	\$0		\$0		\$0	\$0		\$0	\$16.846.590
Architect		\$289,913	\$369,213	\$423,416	\$82.639	\$0	\$0	\$0		\$0			\$47,365		\$0	\$1,212,545
Engineering		\$6,174	\$2,981	\$16,606	\$2,375	\$1,250	\$0	\$0		\$0		\$0	\$0		\$0	\$29,386
Inspection & Testing		\$150	\$14,785	\$353,890	\$297,675	\$1,116	\$0	\$0		\$0		\$0	\$0		\$0	\$667,616
Project Management		\$150	\$45,698	\$184,219	\$193,898	\$14.818	\$230	\$0		\$0		\$0	\$0		\$0	\$439.013
Cleaning, Storage and Installation		\$0	\$812	\$0	\$2.548		\$0	\$0		\$0			\$0		\$0	\$5,627
Cap Equipment		\$0	\$31,638	\$0	\$6,458	\$59,689	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$97,785
Non-Cap Equipment		\$0	\$2,388	\$0	\$36,749	\$145,294	\$0	\$0	\$0	\$0		\$0	\$0		\$0	\$184,432
Total		\$296.915			\$11,532,803	\$311,236	\$25,450	\$5,245		\$0					\$0	
Project Budget	\$19,544,314	1	1 7 7	1 - 7 7 1	1 / 1 / 1		,	/		1.1			1 7:			1 - 1 - 1 -
Less Other Funding	\$0															
Net	\$19.544.314															
Actual Measure U Expenditures	\$19,544,314															
Running Balance	\$0															
	ţ.															
U7100110																
Earthquake Rpl. Liberal Arts North (I)														1 1		
Supplies		\$0														
Legal	1		\$0	\$0	\$0	\$1.408	\$0	\$75	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1.483
	1 1								\$0 \$0						\$0 \$0	\$1,483 \$887
Uner Connact Services		\$0	\$0	\$0	\$0 \$0 \$0	\$887	\$0 \$0 \$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$887
Other Contract Services Building & Additions					\$0 \$0	\$887	\$0 \$0		\$0 \$0		\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$887 \$75
Building & Additions		\$0 \$0 \$265	\$0 \$0 \$0	\$0 \$0 \$1,043,660	\$0 \$0 \$5,916,281	\$887 \$75 -\$973,001	\$0 \$0 \$321,345	\$0 \$0 \$14,898	\$0 \$0 \$0	\$0 \$0 -\$834,764	\$0 \$0 \$0	\$0 \$0 -\$1,127,809	\$0 \$0 \$0	\$0 \$0 \$0	\$0 \$0 \$0	\$887 \$75 \$4,360,876
Building & Additions Architect		\$0 \$0 \$265 \$0	\$0 \$0 \$0 \$611,732	\$0 \$0 \$1,043,660 \$102,824	\$0 \$0 \$5,916,281 \$209,490	\$887 \$75 -\$973,001 \$216,563	\$0 \$0 \$321,345 \$21,215	\$0 \$0 \$14,898 \$3,465	\$0 \$0 \$0 \$0	\$0 \$0 -\$834,764 \$0	\$0 \$0 \$0 \$0 \$0	\$0 \$0 -\$1,127,809 \$0	\$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0	\$887 \$75 \$4,360,876 \$1,165,289
Building & Additions		\$0 \$0 \$265	\$0 \$0 \$0	\$0 \$0 \$1,043,660	\$0 \$0 \$5,916,281	\$887 \$75 -\$973,001	\$0 \$0 \$321,345	\$0 \$0 \$14,898	\$0 \$0 \$0	\$0 \$0 -\$834,764	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 -\$1,127,809 \$0	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0	\$887 \$75 \$4,360,876
Building & Additions Architect Engineering		\$0 \$0 \$265 \$0 \$3,248	\$0 \$0 \$0 \$611,732 \$4,295	\$0 \$0 \$1,043,660 \$102,824 \$0	\$0 \$0 \$5,916,281 \$209,490 \$250	\$887 \$75 -\$973,001 \$216,563 \$0	\$0 \$0 \$321,345 \$21,215 \$250	\$0 \$0 \$14,898 \$3,465 \$0	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 -\$834,764 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 -\$1,127,809 \$0 \$0	\$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$887 \$75 \$4,360,876 \$1,165,289 \$8,043
Building & Additions Architect Engineering Inspection & Testing Project Management		\$0 \$0 \$265 \$0 \$3,248 \$0 \$0 \$0	\$0 \$0 \$611,732 \$4,295 \$0 \$26,072	\$0 \$1,043,660 \$102,824 \$0 \$28,312 \$33,549	\$0 \$0 \$5,916,281 \$209,490 \$250 \$326,203	\$887 \$75 -\$973,001 \$216,563 \$0 \$77,942 \$124,222	\$0 \$0 \$321,345 \$21,215 \$250 \$0 \$0	\$0 \$0 \$14,898 \$3,465 \$0 \$0 \$1,155	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$286	\$0 \$0 -\$834,764 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 -\$1,127,809 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$887 \$75 \$4,360,876 \$1,165,289 \$8,043 \$432,458 \$314,475
Building & Additions Architect Engineering Inspection & Testing Project Management Advertising and Fees		\$0 \$265 \$0 \$3,248 \$0	\$0 \$0 \$611,732 \$4,295 \$0	\$0 \$0 \$1,043,660 \$102,824 \$0 \$28,312 \$33,549 \$7,334	\$0 \$5,916,281 \$209,490 \$250 \$326,203 \$128,937	\$887 \$75 -\$973,001 \$216,563 \$0 \$77,942 \$124,222 \$0	\$0 \$0 \$321,345 \$21,215 \$250 \$0 \$255	\$0 \$0 \$14,898 \$3,465 \$0 \$0 \$1,155 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$286 \$0	\$0 \$0 -\$834,764 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 -\$1,127,809 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$887 \$75 \$4,360,876 \$1,165,289 \$8,043 \$432,458
Building & Additions Architect Engineering Inspection & Testing Project Management Advertising and Fees Cap-Equipment		\$0 \$265 \$3,248 \$3,248 \$0 \$0 \$0	\$0 \$0 \$611,732 \$4,295 \$0 \$26,072 -\$4	\$0 \$1,043,660 \$102,824 \$0 \$28,312 \$33,549	\$0 \$0 \$5,916,281 \$209,490 \$250 \$326,203 \$128,937 \$0	\$887 \$75 -\$973,001 \$216,563 \$0 \$77,942 \$124,222	\$0 \$0 \$321,345 \$21,215 \$250 \$0 \$255 \$0	\$0 \$0 \$14,898 \$3,465 \$0 \$0 \$1,155	\$0 \$0 \$0 \$0 \$0 \$0 \$286 \$0	\$0 \$0 -\$834,764 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 -\$1,127,809 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$887 \$75 \$4,360,876 \$1,165,289 \$8,043 \$432,458 \$314,475 \$7,330 \$37,935
Building & Additions Architect Engineering Inspection & Testing Project Management Advertising and Fees Cap-Equipment Non-Cap Equipment		\$0 \$265 \$3,248 \$0 \$3,248 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$611,732 \$4,295 \$0 \$26,072 -\$4 \$0 \$0 \$0 \$0	\$0 \$0 \$1,043,660 \$102,824 \$0 \$28,312 \$33,549 \$7,334 \$0 \$0 \$0 \$0	\$0 \$0 \$5,916,281 \$209,490 \$250 \$326,203 \$128,937 \$0 \$0 \$0 \$2,033	\$887 -\$973,001 \$216,563 \$0 \$77,942 \$124,222 \$25,356 \$170,425	\$0 \$321,345 \$21,215 \$250 \$0 \$12,579 \$4,093	\$0 \$0 \$14,898 \$3,465 \$0 \$0 \$1,155 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$286 \$0 \$286 \$0 \$0 \$0 \$0 \$0	\$0 \$0 -\$834,764 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 -\$1,127,809 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$887 \$75 \$4,360,876 \$1,165,289 \$8,043 \$43,2458 \$314,475 \$7,330 \$37,935 \$176,550
Building & Additions Architect Engineering Inspection & Testing Project Management Advertising and Fees Cap-Equipment	\$12.507.725	\$0 \$265 \$265 \$3,248 \$0 \$3,248 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$611,732 \$4,295 \$0 \$26,072 -\$4 \$0	\$0 \$0 \$1,043,660 \$102,824 \$28,312 \$33,549 \$7,334 \$0	\$0 \$0 \$5,916,281 \$209,490 \$250 \$326,203 \$128,937 \$0 \$0 \$0 \$2,033	\$887 \$75 -\$973,001 \$216,563 \$0 \$77,942 \$124,222 \$0 \$25,356	\$0 \$321,345 \$21,215 \$250 \$0 \$255 \$0 \$12,579	\$0 \$0 \$14,898 \$3,465 \$0 \$0 \$1,155 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$286 \$0 \$286 \$0 \$0 \$0 \$0 \$0	\$0 \$0 -\$834,764 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 -\$1,127,809 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$887 \$75 \$4,360,876 \$1,165,289 \$8,043 \$432,458 \$314,475 \$7,330 \$37,935
Building & Additions Architect Engineering Inspection & Testing Project Management Advertising and Fees Cap-Equipment Non-Cap Equipment Total	\$12,507,725 \$6.002,325	\$0 \$265 \$0 \$3,248 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$3,513 Received	\$0 \$0 \$611,732 \$4,295 \$0 \$26,072 -\$4 \$0 \$0 \$0 <b>\$642,095</b>	\$0 \$1,043,660 \$102,824 \$0 \$28,312 \$33,549 \$7,334 \$0 \$0 <b>\$1,215,679</b>	\$0 \$0 \$5,916,281 \$209,490 \$250 \$326,203 \$128,937 \$0 \$0 \$2,033 <b>\$6,583,194</b>	\$887 -\$973,001 \$216,563 \$0 \$77,942 \$124,222 \$25,356 \$170,425	\$0 \$321,345 \$21,215 \$250 \$0 \$12,579 \$4,093	\$0 \$0 \$14,898 \$3,465 \$0 \$0 \$1,155 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$286 \$0 \$286 \$0 \$0 \$0 \$0 \$0	\$0 \$0 -\$834,764 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 -\$1,127,809 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$887 \$75 \$4,360,876 \$1,165,289 \$8,043 \$43,2458 \$314,475 \$7,330 \$37,935 \$176,550
Building & Additions Architect Engineering Inspection & Testing Project Management Advertising and Fees Cap-Equipment Non-Cap Equipment <b>Total</b> Project Budget		\$0 \$265 \$0 \$3,248 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$611.732 \$4.295 \$0 \$26.072 -\$4 \$0 \$0 \$0 \$0 \$0 \$642,095	\$0 \$0 \$1,043,660 \$102,824 \$0 \$28,312 \$33,549 \$7,334 \$0 \$0 <b>\$1,215,679</b> Other Funding	\$0 \$0 \$5,916,281 \$229,490 \$250 \$326,203 \$128,937 \$0 \$0 \$2,033 <b>\$6,583,194</b> g Source:	\$887 \$75 \$973,001 \$216,563 \$0 \$77,942 \$124,222 \$124,222 \$00 \$25,356 \$170,425 <b>\$356,123</b>	\$0 \$321,345 \$21,215 \$250 \$0 \$12,579 \$4,093	\$0 \$0 \$14,898 \$3,465 \$0 \$0 \$1,155 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$286 \$0 \$286 \$0 \$0 \$0 \$0 \$0	\$0 \$0 -\$834,764 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 -\$1,127,809 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$887 \$75 \$4,360,876 \$1,165,289 \$8,043 \$43,2458 \$314,475 \$7,330 \$37,935 \$176,550
Building & Additions Architect Engineering Inspection & Testing Project Management Advertising and Fees Cap-Equipment Non-Cap Equipment Total Project Budget Less Other Funding*	\$6,002,325	\$0 \$265 \$0 \$3,248 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$3,513 Received	\$0 \$0 \$0 \$611,732 \$4,295 \$26,072 -\$4 \$0 \$26,072 -\$4 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$1,043,660 \$102,824 \$0 \$28,312 \$33,549 \$7,334 \$0 \$0 <b>\$1,215,679</b> Other Funding City of Santa M	\$0 \$5,916,281 \$209,490 \$250 \$326,203 \$128,937 \$0 \$0 \$2,033 <b>\$6,583,194</b> g Source: tonica \$4,039,7	\$887 \$75 \$973,001 \$216,563 \$0 \$77,942 \$124,222 \$124,222 \$00 \$25,356 \$170,425 <b>\$356,123</b>	\$0 \$0 \$321,345 \$21,215 \$250 \$0 \$255 \$0 \$12,579 \$4,093 \$359,737	\$0 \$0 \$14,898 \$3,465 \$0 \$0 \$1,155 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$286 \$0 \$286 \$0 \$0 \$0 \$0 \$0	\$0 \$0 -\$834,764 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 -\$1,127,809 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$887 \$75 \$4,360,876 \$1,165,289 \$8,043 \$43,2458 \$314,475 \$7,330 \$37,935 \$176,550

Projects	Budget	02/02 Einel	02/04 Final	04/05 Einel	05/06 Final	06/07 Final	07/08 Einel	08/00 Einel	00/40 Einel	40/44 Einel	44/42 Einel	42/42 Einal	13/14 Final	14/15 Final	15/16	Combined Totals
Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Fillal	00/07 Final	07/06 Final	00/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 FINAI	14/15 Final	15/16	Complined Totals
U7100013. U7100047																
Music Complex (J)																
Advertising		\$0	\$0	\$436	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$436
Supplies		\$0	\$0				\$19.094	\$0		\$0			\$0	\$0	\$0	\$19,288
Consultants		\$0	\$0		\$0	\$0	\$36,000	\$0		\$0			\$0	\$0	\$0	\$36,000
Other Contract Services		\$0	\$0		\$0		\$180	\$0		\$0			\$0	\$0	\$0	\$180
Moving Services		\$0	\$0	\$0	\$0	\$0	\$6,330	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$6.330
Building & Additions		\$0	\$0	\$356,464	\$1,293,726	-\$737,213	\$273,531	\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$1,186,509
Architect		\$0	\$187,922		\$37,227	\$38,448	\$4,052	\$14,356		\$681	\$225		\$2,038	\$0	\$0	\$311,441
Engineering		\$0	\$0		\$0	\$0	\$0	\$21,370		\$0			\$0	\$0	\$0	\$21,370
Inspection & Testing		\$0	\$0	\$29,740	\$19.265	\$26,238	\$35,880	\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$111,122
Project Management		\$0	\$170		\$36,351	\$56,914	\$16,200	\$1.288		\$0			\$0	\$0	\$0	
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$62,600	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$62,600
Non-Cap Equipment		\$0	\$0		\$0	\$29.852	\$78,582	\$0		\$0			\$0	\$0	\$0	\$108,434
Total		\$0	\$188.092	\$445.879	\$1.386.568	-\$585.566	\$532.447	\$37.014		\$681	\$225	\$3.992	\$2.038	\$0	\$0	
Project Budget	\$4.629.484	Received														
Less Other Funding*	\$2,618,113	\$2,618,113		* Other Fundin	g Source:											
Net	\$2,011,371	1 12 27 2		Prop T Refinar		received										
Actual Measure U Expenditures	\$2,011,371															
Running Balance	\$0															
U7100111																
Earthquake Rpl. Liberal Arts South (K)																
Supply		\$0	\$0	\$855	\$2,497	\$379	\$23,811	\$75		\$0	\$0	\$0	\$0	\$0	\$0	\$27,618
Legal		\$0	\$0	\$0	\$0	\$0	\$2,203	\$50	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,253
Moving Services		\$0	\$0	\$0	\$0	\$0	\$4,063	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,063
Consultants		\$0	\$0	\$0	\$17,265	\$41,435	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$58,700
Other Contract Services		\$0	\$0	\$6,154	\$202	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$6,356
Building & Additions		\$0	\$0	\$26,302	\$3,091,306	\$5,706,802	-\$4,642,459	\$0	\$91,516	\$0	\$0	\$0	\$0	\$0	\$0	\$4,273,467
Architect		\$0	\$0	\$836,555	-\$503,297	\$163,506	\$183,877	\$39,984	\$2,549	\$0	\$0	\$0	\$0	\$0	\$0	\$723,174
Engineering		\$0	\$0	\$3,125	\$150	\$5,344	\$500	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$9,119
Inspection & Testing		\$0	\$0	\$0	\$179,798	\$296,015	\$68,273	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$544,086
Project Management		\$0	\$0	\$0	\$43,989	\$262,598	\$52,690	\$1,722	\$1,278	\$0	\$0	\$0	\$0	\$0	\$0	\$362,276
Cap-Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$58,726	\$45,388	-\$7,074	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$97,040
							-\$4,261,655	\$34,757	\$95,342	\$0						
Total		\$0	\$0	\$872,991	\$2,831,909	\$6,534,806	-94,201,0001	a) a	990,04ZI	201	30	301	20	501	\$0	\$6,108,150
	\$16,733,220	\$0 Received	\$0	\$872,991	\$2,831,909	\$6,534,806	-\$4,201,055	\$34,/5/	\$55,542	<b>φ</b> υ	<b>\$</b> 0	<b>\$</b> 0	<b>\$</b> 0	\$0	\$0	\$6,108,150
Total	\$16,733,220 \$10,625,070			* Other Fundin		\$6,534,806	-\$4,201,035	<b>\$34,757</b>	\$50,042	<del>پ</del> ۵	<b>\$</b> 0	<b>\$</b> 0		\$0	\$0	\$6,108,150
Total Project Budget		Received			g Source:		-\$4,261,655	\$34,757	\$ <b>3</b> 3,342	\$U	<b>پ</b> ول	φu		J \$0	\$0	\$6,108,150
Total Project Budget Less Other Funding*	\$10,625,070	Received		* Other Fundin	g Source: Ionica \$6,167,0	70 received	-\$4,261,655	\$34,757	\$50,042	<b>پ</b> ور ۵۵	3U	ţ, ţ	<u>\$0</u>	J \$U	<u>\$0</u>	\$6,108,150

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16	Combined Totals
U7100221																
Shuttle Replacement Parking (L)																
Supplies		\$0	\$0	\$0	\$0	\$0	\$1,347	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,347
Legal		\$0	\$0	\$0	\$8,462	\$35,103	\$0	\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$43,565
Site Acquisition		\$0	\$0	\$0	\$0	\$16,903,087	\$0	\$0		\$0	\$0	\$0			\$0	\$16,903,087
Site Improvement		\$0	\$0	\$0	\$0	\$3,027	\$0	\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$3,027
Building & Additions		\$0	\$0	\$0	\$0		\$1,252,224	\$2,353	\$0	\$0	\$0	\$0			\$0	\$1,738,577
Architect		\$0	\$0	\$0	\$0		\$7,208	\$0		\$0	\$0	\$0			\$0	\$58,777
Inspection & Testing		\$0	\$0	\$0	\$0		\$41,250	\$0		\$0	\$0	\$0			\$0	\$181,072
Project Management		\$0	\$0	\$0	\$0		\$32,425	\$0		\$0	\$0	\$0			\$0	\$40,056
Total		\$0	\$0	\$0	\$8,462	\$17,624,240	\$1,334,455	\$2,353	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$18,969,509
Project Budget	\$18,969,509															
Less Other Funding	\$0															
Net	\$18,969,509															
Actual Measure U Expenditures	\$18,969,509															
Running Balance	\$0															
U7100321																
North Quad Plaza (M)																
Legal		\$0	\$0	\$0	\$0		\$3,825	\$5,604		\$0	\$0	\$0			\$0	\$9,429
Building & Additions		\$0	\$0	\$0	\$0	-\$443	\$6,130,081	\$3,634,487	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$9,764,125
Architect		\$0	\$231,055	\$8,444	\$140,048	\$435,618	\$171,225	\$68,633		\$10,483	\$0	\$0			\$0	\$1,068,407
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0			\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$186,220	\$107,477		\$0	\$0	\$0			\$0	\$294,025
Project Management		\$0	\$0	\$760	\$210	\$2,200	\$135,601	\$55,782		\$0	\$0	\$0			\$0	\$195,158
Printing		\$0	\$1,900	\$0	\$0		\$0	\$0		\$0	\$0	\$0			\$0	\$1,900
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$55,420		\$0	\$0	\$0			\$0	\$55,420
Total		\$0	\$232,955	\$9,204	\$140,258	\$437,375	\$6,626,952	\$3,927,402	\$3,834	\$10,483	\$0	\$0	\$0	\$0	\$0	\$11,388,463
Project Budget	\$11,388,463															
Less Other Funding	\$0															
Net	\$11,388,463															
Actual Measure U Expenditures	\$11,388,463															
Running Balance	\$0															

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16	Combined Totals
U7100500, U7126450, U7100334, U7100142																
Student Services Building (O)																
Supplies		\$2,014		\$0	\$0	\$0	\$0			\$0	\$0	\$0	\$0	\$0	\$0	\$2,732
PC Upgrades		\$0	\$765	\$0	\$0	\$0	\$0			\$0	\$0	\$0	\$0	\$0	\$0	\$765
Consultants		\$0		\$0	\$0	\$9,334	\$55,693	\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$65,027
Legal		\$0	\$0	\$0	\$0	\$38	\$2,775	\$31,776		\$0	\$0	\$0	\$0	\$0	\$0	\$34,588
Other Contract Services		\$210	\$0	\$0	\$0	\$0	\$17,561	\$17,495	\$18,817	-\$70	\$0	\$0	\$0	\$0	\$0	\$54,014
Moving		\$7,571		\$0	\$0	\$0	\$0	\$616	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$8,187
Building & Additions		\$359,141	\$2,441	\$0	\$0	\$0	\$0			\$0	\$0	\$0	\$776	\$560	\$857,369	\$1,220,287
Architect		\$31,782	\$0	\$235,230	\$0	\$43,992	\$0	\$690,099	\$208,521	\$38,643	\$48,442	\$388,611	\$973,427	\$2,502,652	\$254,235	\$5,415,634
Engineering		\$1,838		\$0	\$0	\$0	\$0		\$27,363	\$3,171	\$0	\$0	\$0	\$55,680	\$43,375	\$137,631
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$25,670		\$0	\$0	\$0	\$0	\$2,478	\$0	\$51,629	\$114,465
Project Management		\$4,650	\$0	\$2,470	\$0	\$1,100	\$0	\$124,148	\$0	\$0	\$0	\$6,675	\$15,650	\$11,616	\$89,978	\$256,287
Cap Equipment		\$59,063	\$0	\$0	\$0	\$0	\$8,745	\$8,056	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$75,864
Total		\$466,268	\$3,207	\$237,700	\$0	\$54,464	\$110,445	\$913,802	\$254,701	\$41,744	\$48,442	\$395,286	\$992,330	\$2,570,508	\$1,296,586	\$7,385,483
Project Budget	\$109,862,122	Received		* Other Funding	g Source:											
Less Other Funding*	\$89,223,676	\$1,321,000		State of Califor	nia \$1,321,000	received										
Net	\$20,638,446		-	Measure S \$46	,692,750, Meas	sure AA \$25,177	,143 allocated									
Actual Measure U Expenditures	\$7,385,483			Measure U, S &	& AA Interests \$	16,032,783 allo	cated									
Running Balance	\$13,252,963															



Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16	Combined Totals
U7100090																1
Science Complex Additional (P)																
Architect		\$0	\$0	\$0	\$0	\$246.425	\$61,911	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$308.336
Total		\$0	\$0		\$0 \$0	\$246,425	\$61,911	\$0 \$0		\$0					\$0 \$0	\$308,336
Project Budget	\$87.944.336	ψυ		* Other Fundin		ΨZ40,423	401,911	ψŪ	ΨΟ	ψŪ	ψŪ	ψŪ	ψŪ	<b>Ψ</b> 0	ΨU	4500,550
Less Other Funding	\$87.636.000			State of Califor		) nending										
Net	\$308,336			Measure AA \$4												
Actual Measure U Expenditures	\$308,336			incusure / v ( $\phi$ -	0,010,000 0100	alcu										
Running Balance	\$000,000															
Raming Balarioo	, ¢0															
U6780000, U7100022, U7100331, U7100550,																
U7100005, U7100030, U7100031, U7100029,																
U7100003, U7100008, U7100332, U7100072,																
U7100042, U7100056, U7100039																
Infrastructure & Safety (Q)																
Supplies		\$0	\$0	\$254	\$0	\$0	\$0	\$1,700	\$1,393	\$0	\$0	\$0	\$0	\$0	\$0	\$3,347
Consultants		\$0	\$0	\$0	\$0	\$0	\$0	\$16,734	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$16,734
Maintenance Agreement		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$14,673	\$12,979	\$12,979	\$0	\$0	\$0	\$40,632
Legal		\$0	\$0	\$0	\$0	\$0	\$3,527	\$3,294		\$0		\$0		\$0	\$0	\$6,821
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$7,825	\$81,445	\$203,383	\$3,320				\$0	\$0	\$295,973
Building & Additions		\$681,900	\$195,175	\$20,600	\$0	\$200,620	\$733	\$0		\$0				\$0	\$0	\$1,099,028
Architect		\$69,081	\$42,108	\$0	\$155,321	\$448,507	\$91,127	\$4,227		\$0			\$0	\$0	\$0	\$809,005
Engineering		\$8,050	\$0	\$0	\$6,750	\$12,000	\$18,429	\$2,360		\$0			\$0	\$0	\$0	\$47,589
Inspection & Testing		\$2,241	\$4,250	\$0	\$0	\$0	\$5,807	\$0		\$0				\$0	\$0	\$12,298
Project Management		\$0	\$2,805	\$0	\$0	\$3,520	\$1,840	\$38	\$196	\$0	\$0	\$0	\$0	\$0	\$0	\$8,399
Cap Equipment		\$0	\$0	\$343,861	\$0	\$0	\$0	\$895,171	\$349,531	\$40,002				\$0	\$0	\$1,628,565
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,216	\$0	\$29,694	\$0	\$0	\$0	\$0	\$33,910
Advertising		\$0	\$785	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$785
Total		\$761,272	\$245,122	\$364,715	\$162,071	\$664,647	\$129,287	\$1,004,968	\$558,718	\$57,995	\$42,673	\$11,614	\$0	\$0	\$0	\$4,003,084
Project Budget	\$4,003,084															
Less Other Funding	\$0															
Net	\$4,003,084															
Actual Measure U Expenditures	\$4,003,084															
Running Balance	\$0															

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16	Combined Totals
110,000	Budget	02/00111101	00/04 1 11/01	04/00111101	00,00111101	ouror i mai	on oo maa	00/00 1 11141	00/101111	10/1111111	11/12 1 110	12/10111101	10/14111101	14/10111101	10/10	Combined Totals
U7100007																
Restroom Improvement (R)																
Supplies		\$0	\$564	\$0	\$1,075	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,639
Other Contract Services		\$0	\$0	\$0	\$3,803	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,803
Building & Additions		\$0	\$1,305	\$0	\$7,891	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$9,196
Inspection & Testing		\$0	\$2,043	\$0	\$820	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,863
Total		\$0	\$3,912	\$0	\$13,589	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$17,501
Project Budget	\$17,501															
Less Other Funding	\$0															
Net	\$17,501															
Actual Measure U Expenditures	\$17,501															
Running Balance	\$0															
°																
U7100004. U7110020																
Master Planning (S)																
Consultants		\$9,000	\$26,516	\$158,449	\$374,329	\$125.404	\$17.998	\$363,342	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,075,038
Architect		\$0	\$17,617	\$126,433	\$104,083	\$126,701	\$346,827	\$276,985			\$0		\$0		\$0	\$998,647
Rental / Lease		\$0		\$6,453	\$0	\$0	\$0				\$0		\$0		\$0	\$6,453
Postage		\$0		\$30,000	\$0	\$0	\$0				\$0		\$0		\$0	\$30,000
Reimbursement to SMC		\$0		\$00,000	\$180	\$0	\$0				\$0		\$0		\$0	\$180
Project Management		\$0		\$0	\$0	\$0	\$0				\$0		\$0		\$0	\$113
Total		\$9.000	\$44.133	\$321,335	\$478.593	\$252.105	\$364,825						\$0		\$0	
Project Budget	\$2,110,430	\$5,000	ψ <del>11</del> ,100	<b>402</b> 1,000	<i>\\\\\\\\\\\\\</i>	<i>\</i> 202,100	<b>\$004,020</b>	\$040,400	ψŪ	ψŪ	ψŪ	ţ,	ψŪ	\$0	ψŪ	ψ <u>2</u> ,110,400
Less Other Funding	\$0															
Net	\$2,110,430															
Actual Measure U Expenditures	\$2,110,430															
Running Balance	\$0															
	ψŪ															
U7100024	1															
14th and Pico Project (T)																
Consultants		\$0	\$888	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$888
Architect		\$258.601	\$47,343	\$0	\$0 \$0	\$0	\$0				\$0		\$0 \$0		\$0	\$305.944
Inspection & Testing		\$12,070	\$0	\$0	\$0 \$0	\$0	\$0				\$0		\$0		\$0	\$12,070
Project Management		\$12,070		\$0	\$0 \$0	\$0 \$0	\$0				\$0		\$0 \$0		\$0	\$340
Total		\$270.671		\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0						\$0 \$0		\$0 \$0	\$319.242
Project Budget	\$319.242	\$270,671	\$40,571	φU	φU	φU	φU	<b>\$</b> U	<b>\$</b> 0	φU	<b>۵</b> ۵	<b>\$</b> 0	φU	<b>\$</b> 0	φU	\$319,242
Less Other Funding	\$319,242															
Net Actual Measure U Expenditures	\$319,242 \$319,242															
Running Balance	\$0															
	· · · ·															
Grand Total		\$11,068,400	\$10,432,055	\$28,685,697	\$54,940,416	\$25,278,771	\$5,283,853	\$6,585,573	\$912,880	-\$723,860	\$91,341	-\$716,916	\$1,041,732	\$2,570,508	\$1,296,586	\$146,747,037


Note: Project N had no expenses

## SANTA MONICA COMMUNITY COLLEGE DISTRICT


## Measure S Project Schedule As of March 31, 2016

	Project Name	Completion	20	14			20 <sup>-</sup>	15	20	16			201	7		20 <sup>,</sup>	18
1	Athletic Fields Phase I, Corsair Field	Completed															
1A	Athletic Fields Phase I, John Adams	Completed															
2	Performing Arts Center	Completed															
3	Career Opportunity Center	Completed															
4	Replacement Health/PE/Fitness Building	February 2017						·									
5	Early Childhood Development/Childcare	December 2018														I	
6	Malibu Site Acquisition and Facility	November 2018															
7	Energy Efficiency Projects	Completed															
8	Satellite Campus Parking Facilities and Roadway Improvements	On-Going															
9	Parking Garage, Grounds and Equipment - Student Services	November 2018		·		ľ		, i									
10	Pico Promenade Improvements	Completed															
11	Master Planning	Completed															
12	Other Bond Related Expenses	On-Going															
13	Adv. Architecture Related Exp for AA	Completed															
14	Real Property Acquisition	Completed															
15	Signage Safety/Information	On-Going															
16	Cost of Issuance	On-Going															
			In	Plai	nnir	na			In	Cor	nstr	uct	ion		-		+

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16	Combined Totals
S7100019														
Athletic Field Phase I, Corsair Field (1)														
Legal		\$0	\$0	\$0	\$301	\$175	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$476
Building & Additions		\$0		\$0	\$300,380		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,879,475
Architect		\$27,332	\$43,815	\$197,557	\$252,736	\$279,173	\$26,563	\$0	\$0	\$0	\$0	\$0	\$0	\$827,176
Inspection & Testing		\$0	\$0	\$0	\$23,411	\$57,585	\$640	\$296	\$0	\$0	\$0	\$0	\$0	\$81,932
Project Management		\$0	\$0	\$0	\$9,871	\$42,374	\$565	\$0	\$0	\$0	\$0	\$0	\$0	\$52,810
Cap Equipment		\$0	\$0	\$0	\$0	\$483,017	\$35,271	\$0	\$0	\$0	\$0	\$0	\$0	\$518,288
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$2,066	\$10,312	\$0	\$0	\$0	\$0	\$0	\$0	\$12,378
Total		\$27,332	\$43,815	\$197,557	\$586,699	\$3,443,485	\$73,350	\$296	\$0	\$0	\$0	\$0	\$0	\$4,372,535
Project Budget	\$4,440,065	Received												
Less Other Funding*	\$67,530	\$67,530		* Other Fundin										
Net	\$4,372,535			Metropolitan W	ater District \$6	7,530 received								
Actual Measure S Expenditures	\$4,372,535													
Running Balance	\$0													



Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16	Combined Totals
S7100038														
Athletic Field Phase I, John Adams (1A)														
Legal		\$0	\$0	\$0	\$75	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$75
Building & Additions		\$0	\$0	\$0	\$16,556	\$1,395,261	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,411,817
Architect		\$0	\$5,807	\$93,941	\$12,150	\$31,818	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$143,715
Inspection & Testing		\$0	\$2,874	\$3,207	\$0	\$49,984	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$56,066
Project Management		\$0	\$0	\$0	\$10,921	\$45,170	\$38	\$0	\$0	\$0	\$0	\$0	\$0	\$56,128
Cap Equipment		\$0	\$0	\$0	\$0	\$1,290,672	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,290,672
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$11,334	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$11,334
Total		\$0	\$8,681	\$97,148	\$39,701	\$2,824,239	\$38	\$0	\$0	\$0	\$0	\$0	\$0	\$2,969,807
Project Budget	\$2,969,807													
Less Other Funding	\$0													
Net	\$2,969,807													
Actual Measure S Expenditures	\$2,969,807													
Running Balance	\$0													



Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16	Combined Totals
S7100012														
Performing Arts Center (2)														
Consultants		\$0	\$0	\$0	\$121,790	\$76,639	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$198,429
Other Contract Services		\$0	\$0	\$4,269	\$0	\$22,729	\$22	\$68	\$0	\$0	\$0	\$0	\$0	\$27,088
Supplies		\$0	\$0	\$0	\$14,565	\$5,810	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$20,375
Legal		\$0	\$0	\$34,329	\$275,667	\$492,731	\$15,629	\$0	\$0	\$0	\$0	\$0	\$0	\$818,356
Advertising		\$0	\$0	\$0	\$320	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$320
Building & Additions		\$7,784,151	\$10,292,986	\$8,930,813	\$2,991,903	\$1,629,990	\$50,000	\$0	\$0	\$0	\$0	\$0	\$0	\$31,679,843
Architect		\$0	\$811,312	\$182,457	\$412,309	\$121,588	\$108	\$1,962	\$0	\$0	\$87,054	\$0	\$0	\$1,616,790
Engineering		\$0	\$3,600	\$5,250	\$1,500	\$9,650	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$20,000
Inspection & Testing		\$104,308	\$722,685	\$411,193	\$210,381	\$22,256	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,470,823
Project Management		\$31,984	\$155,732	\$248,876	\$263,690	\$47,915	\$3,244	\$0	\$0	\$0	\$0	\$0	\$0	\$751,44
Cap Equipment		\$0	\$0	\$130,218	\$292,565	\$342,693	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$765,476
Non-Cap Equipment		\$0	\$0	\$15,124	\$93,106	\$220,455	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$328,685
Total		\$7,920,443	\$11,986,315	\$9,962,528	\$4,677,797	\$2,992,455	\$69,003	\$2,030	\$0	\$0	\$87,054	\$0	\$0	\$37,697,625
Project Budget	\$40,690,201	Received								•		•		
Less Other Funding*	\$2,992,576	\$2,992,576		* Other Funding	g Source:									
Net	\$37,697,625			Madison Project	t Foundation \$	2,992,576 rece	ived							
Actual Measure S Expenditures	\$37,697,625			-										
Running Balance	\$0													
Performing Arts Center Project Description:						Project E	xpenses	to Date						
Construction of a state-of-the-art 499 seat performing arts theater Status:											Building & Add	litions, \$31,679,84	13	
Completed, 2008 Architect:														
Renzo Zecchetto												Architect, \$1,527,	774	
			Advertising,	\$320								Architect fee paid		
Contractor:			0.								-	Foundation	,	
FTR International			Legal, \$818	8,356										
			Supplies, \$20,3	75							_ Engineering, \$	520,000		
			5upplies, 520,5					Cap Equip.,						
		Other Cont	ract Services, \$2	7,088				\$765,476	Proier	t Management, S		Inspection & Test	ang, \$1,470,823	
					Consultants, \$1	198,429 📈	Non-Cap Equi	n \$328.685		, management, ç	,,,,,,,,,,			

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16	Combined Totals
110jecta	Buuget	04/00111181	00/001111	00/07 1 11141	07/001 11121	00/05 1 11/41	05/101 111	10/11 mai	11/12 1 11/41	12/10111101	15/14/11/14	14/10/1110	10/10	Combined Totals
S7100033, S7100144, S7100060														
Replacement Health/PE/Fitness Building (4)														
Supplies		\$4,809	\$288	\$0	\$0	\$0	\$163	\$0	\$0	\$0	\$0	\$0	\$0	\$5,260
Legal		\$0	\$0	\$0		\$1.413	\$75	\$0		\$0	\$0		\$0	\$1,488
Other Contract Services		\$1,634	\$25.934	\$0		\$253	\$165	\$0		\$0	\$0		\$0	\$27,985
Repair Facility		\$0	\$4,861	\$0		\$0	\$0	\$0		\$0	\$0		\$0	\$4,861
Building & Additions		\$0	\$0	\$0		\$112,410	\$526.552	\$0		\$0	\$0		\$4,775,714	\$11,451,757
Architect		\$0	\$0	\$0		\$0	\$41,044	\$0		\$0	\$0		\$0	\$41,044
Inspection & Testing		\$0	\$0	\$0		\$6,518	\$14,363	\$0		\$0	\$0		\$0	\$20,881
Project Management		\$0	\$0	\$0		\$9.070	\$23,425	\$0		\$0	\$0		\$0	\$32,495
Cap Equipment		\$0	\$0	\$0		\$0	\$0	\$17,613		\$0	\$0		\$0	\$17,613
Total		\$6,443	\$31,083	\$0		\$129,663	\$605,787	\$17,613		\$0	\$0			\$11,603,383
Project Budget	\$51.643.399	<i>t</i> ,,	<i><b>+</b>,</i>		+-	<i>+</i> ·,···	<i>,</i>	<i><b>‡</b>,<b>e</b>e</i>	÷-	<b>†</b> •		+-,,	<i>,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,</i>	+,,
Less Other Funding*	\$40,040,016			* Other Fundin	a Source:									
Net	\$11,603,383				40,040,016 allo	cated								
Actual Measure S Expenditures	\$11,603,383				,, anot									
Running Balance	\$0													
	ψŬ													
S7100045		-												
Early Childhood Development/Childcare (5)														
Consultants		\$0	\$0	\$0	\$9,200	\$0	\$0	\$0	\$0	\$4,800	\$12.930	\$14.078	\$1,388	\$42,395
Legal		\$0	\$0 \$0	\$0		\$0	\$0 \$0	\$0		\$0 \$0	<u> </u>		\$1,690	\$1,690
Architect		\$0	\$0 \$0	\$0		\$0		\$0		\$51,792	\$142,428		\$432,949	\$771.103
Inspection & Testing		\$0	\$0 \$0	\$0		\$0	\$0 \$0	\$0		\$37.796	\$7.475		\$2.323	\$48.416
Project Management		\$0	\$0	\$0		\$0		\$1,246		\$58,247	\$33,435		\$3,118	\$126,828
Total		\$0 \$0	\$0 \$0	\$0 \$0		\$0 \$0				\$152,635	\$196,268		\$441,467	\$990.432
Project Budget	\$13,176,578	÷ -	ψU	ψυ	<b>\$3,200</b>	ψU	ψυ	ψ1,240	Ψ <b>22,</b> 3 <del>4</del> 0	ψ102,000	ψ130,200	φ100,070	φ <del>1</del> ,1, <del>1</del> 07	ψ <b>330,</b> 432
Less Other Funding*	\$6,176,578	\$0		* Other Fundin	a Source:									
Net	\$7.000.000	φU			g 3001ce. Ionica \$4,318,0	00 committed								
Actual Measure S Expenditures	\$990,432				erest \$1,858,578									
Running Balance	\$6,009,568			measure 5 mile	iest φ1,000,070									
	\$0,009,000													
S7100077, S7100015	1	1										1		
Malibu Site Acquisition and Facilities (6)		\$0	\$0	\$0	\$0	\$30,000	\$0	\$0	\$72,157	\$68,109	\$30,342	\$66,277	\$47,440	\$314,326
Consultants		\$0 \$0	\$0 \$27.722	\$0 \$16,787	\$0 \$6,159	\$30,000 \$504	\$0 \$0	\$0 \$0		\$68,109	\$30,342 \$1,360		\$47,440 \$14,229	\$314,326 \$145.612
Legal Other Contract Services		\$0 \$0	\$27,722 \$0	\$16,787		\$504 \$0	\$0 \$0	\$0 \$0		\$0 \$0	\$1,360		\$14,229	\$145,612 \$3,912
		\$0 \$0	\$0 \$0	\$0 \$0		\$0 \$0	\$0 \$0	\$0 \$0		\$0 \$0	\$536		\$0 \$0	\$536
Building & Additions Architect		\$0 \$0	\$0 \$0	<u>\$0</u> \$0		\$0 \$0		\$0		\$0 \$257,584	\$536 \$732,891		\$0 \$34,124	\$536 \$1,199,175
		\$0 \$0	\$0 \$0	\$0 \$0		\$0 \$0		\$0 \$0		\$257,584 \$785	\$732,891 \$562		\$34,124	
Engineering Inspection & Testing		\$U \$4,388	\$0 \$3,750	\$0 \$141,462	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0		\$785 \$15,575	\$562 \$22.939		\$0 \$0	\$1,346 \$297,096
Project Management		\$4,388 \$0	\$3,750 \$0	\$141,462	\$0 \$0	\$0 \$0	\$0 \$0	\$0	\$98,022 \$55,064	\$15,575 \$53,185	\$22,939		\$0 \$50,276	\$297,096 \$327,552
Storm/Waste Water Treatment Center		\$0 \$0	\$0 \$2,500,000	\$220 \$0		\$0	\$0 \$0	\$2,886		\$53,185	<u>\$47,778</u> \$0		\$50,276 \$0	\$327,552 \$5,000,000
		\$U \$4,388	\$2,500,000 \$2,531,472	\$U \$158,468		\$2,500,000 \$2,530,504	\$0 \$0			\$0 \$395,237	\$0 \$836,407		\$0 \$146,069	\$5,000,000 \$7,289,554
Total Broject Budget	\$26 775 001	<b></b>	əz,əə1,472	<b>\$150,468</b>	\$0,159	<b></b> \$∠,530,504	\$0	<b>⊅</b> ∠,886	<b>⊅∠∠0,30</b> 1	<b>\$395,23</b> 7	<b>३०</b> ७७,407	ə449,662	<b>\$140,069</b>	¢1,209,554
Project Budget Less Other Funding*	\$26,775,991 \$1,775,991			* Other Fundin	a Sourco:									
	\$1,775,991 \$25,000,000					tod								
Net				weasure AA \$	1,775,991 alloca	ileu								
Actual Measure S Expenditures	\$7,289,554													
Running Balance	\$17,710,446													

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16	Combined Totals
S7100043, S7100066														
Energy Efficiency Projects (7)														
Legal		\$0		\$0	\$0	\$988	\$0	÷ •		\$0	\$0		\$0	\$988
Building & Additions		\$0		\$0	\$0	\$106,921	\$355,294	-\$180,342		\$0	\$0		\$0	\$281,873
Engineering		\$0		\$0	\$10,500	\$0	\$0	\$0		\$0	\$0		\$0	\$10,500
Inspection & Testing		\$0		\$0	\$0	\$0	\$0	\$0		\$0	\$0		\$0	\$0
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$0	\$0	\$0	\$10,500	\$107,910	\$355,294	-\$180,342	\$0	\$0	\$0	\$0	\$0	\$293,361
Project Budget	\$510,683	Received												
Less Other Funding*	\$217,322	\$217,322	1	* Other Funding	g Source:									
Net	\$293,361		•	SCE & The Ga	s Co. \$217,322	received								
Actual Measure S Expenditures	\$293,361													
Running Balance	\$0													
S7100091, S7100092, S7100147														
Satellite Campus Parking Facilities and Roadway I	mprovements (	8)												
Legal		\$0	\$0	\$0	\$300	\$175	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$475
Other Contract Services		\$0	\$0	\$0	\$300	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$300
Advertising		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Consultants		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$278,178	\$1,860,152	\$449,543	\$37,777	\$0	\$0	\$0	\$64	\$0	\$2,625,714
Architect		\$0	\$0	\$324,919	\$324,864	\$136,911	\$34,490	\$1,397	\$2.289	\$0	\$0	\$0	\$0	\$824.871
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$30,896	\$5,470	\$12,165	\$48,531
Inspection & Testing		\$0		\$0	\$31,100	\$185,947	\$28,218	\$360	\$0	\$0	\$0		\$0	\$245,626
Project Management		\$0		\$0	\$18,288	\$64,880	\$31,137	\$8,659		\$2,569	\$10,730	\$6,046	\$535	\$142,844
Non-Cap Equipment		\$0		\$0	\$0	\$0	\$3,387	\$0	\$0	\$0	\$0	\$0	\$0	\$3,387
Total		\$0		\$324,919	\$653,031	\$2,248,065	\$546.775	\$48,194	\$2,289	\$2.569	\$41,626	\$11.580	\$12,700	\$3,891,747
Project Budget	\$7,210,375		عال عاد 11,000 عاد 12,100 عاد 12,000 عاد 14,000 عاد 12,000 عاد 10,000 عاد 10,000 عاد 10,000 عاد 10,000 عاد 10,00											, ,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,
Less Other Funding	\$2,535,375		* Other Funding Source:											
Net	\$4,675,000				,535,375 alloca	ated								
Actual Measure S Expenditures	\$3,891,747				,,									
Running Balance	\$783,253													

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16	Combined Totals	
<b>i</b>															
S7100142															
Parking Garage and Grounds - Student Services (9)															
Supplies		\$0	\$0	\$0		\$1,745	\$0	\$0		\$0			\$0		
Consultants		\$0	\$0	\$0		\$20,700	\$0	\$0		\$0	\$0		\$0		
Legal		\$0	\$0	\$0		\$2,154	\$17,486	\$4,800	\$2,257	\$17,221	\$0		\$0	\$47,488	
Other Contract Services		\$0	\$0	\$0		\$1,508	\$10,952	\$1,986	\$46	\$0	\$12,083		\$0	\$31,608	
Site Improvement		\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$1,086	\$0		\$0	\$2,394	
Building & Additions		\$0	\$0	\$0		\$2,555,940	\$5,925,152	\$78,717	\$77,320	\$5,509	\$715		\$0	\$8,643,353	
Architect		\$0 \$0	\$0 \$0	\$0			\$0	\$37,111	\$75,163	\$0 \$9,735	\$0		\$0 \$0	\$5,053,094	
Engineering Inspection & Testing		\$0 \$0	\$0 \$0	\$0 \$0		\$4,813 \$131,009	\$38,330 \$161.847	\$42,968 \$54,069	\$50,952 \$32,306	\$9,735	\$0 \$4,123		\$0 \$13,794	\$146,797 \$450,352	
Project Management		\$0 \$0	\$0 \$0	<u>\$0</u> \$0		\$158,766	\$373,559	\$184,069	\$92,118	\$224,994	\$59,525		\$13,794	\$450,352	
Cap Equipment		\$0	\$0	\$0 \$0		\$158,760	\$14,393	\$104,088	\$92,118	<del>\$224,994</del> \$0	<del>\$39,323</del> \$0		\$13,703	\$1,130,520	
Non-Cap Equipment		\$0	\$0			\$0 \$0	\$14,393	\$0 \$0	\$0 \$11,381	\$0 \$0	\$0 \$0		\$0	\$14,393	
Total		\$0 \$0		\$0 \$0				\$403,737	\$342,192	\$289,454	\$76,445		\$27,556	\$15,561,294	
	\$109 862 122	φU				\$3,330,003	\$0,541,715	\$403,737	<i>4</i> 542,152	\$205,454	\$70,443	\$02,755	\$27,550	\$13,301,234	
Less Other Funding*	\$109,862,122         * Other Funding Source:           \$63,169,372         State of California \$1,321,000 received           \$46,692,750         Mease U \$20,638,446, Measure AA \$25,177,143 allocated														
Net	\$63,169,372 State of California \$1,321,000 received														
Actual Measure S Expenditures	\$63,169,372         State of California \$1,321,000 received           \$46,692,750         Mease U \$20,638,446, Measure AA \$25,177,143 allocated           \$15,561,294         Measure U, S & AA interests \$16,032,783 allocated														
Running Balance	\$63,169,372         State of California \$1,321,000 received           \$46,692,750         Mease U \$20,638,446, Measure AA \$25,177,143 allocated           \$15,561,294         Measure U, S & AA interests \$16,032,783 allocated														
Parking Garage and Grounds - Student Services	\$15,561,294 Measure U, S & AA interests \$16,032,783 allocated														
Project Description: Consolidates various student services departments and college administration in a single complex at the front of the campus	\$46,692,750         Mease U \$20,638,446, Measure AA \$25,177,143 allocated           \$15,561,294         Measure U, S & AA interests \$16,032,783 allocated           \$31,131,456         Measure S Share of Project Expenses to Date														
Facility Size: 110,000 sq/ft & 500 cars underground parking structure															
Status:			Site Improveme	ent. \$2.394											
Phase 1 completed															
Phase 2 In DSA		Oth	er Contract Servi	ces, \$31,608	$\sim$ $\square$										
			1.00	gal, \$47,488											
Architect:			Leg	5aı, 247,400											
Steinberg Architects, Morris Architects			Consultar	nts, \$20,700											
			consultar	, 920,700						Engine	ering, \$146,797				
Contractor:			Sunn	lies, \$3,206		```									
Minaco			Jupp				$\backslash$					6450 252			
					Cap Equip	oment, \$14,393	└ Project M	anagement, \$1,1	136,526	Ins	spection & Testi	ng, \$450,352			

Projects	Budget	04/05 Einal	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16	Combined Totals
10,603	Buuget	u-#/uuriniai	55/00 i mai	55/07 T mai	silvo i illai	55/05 i iiidi	55/101 mai	ai		12/10 1 mai	10/17 1 mai	#/151111a1	10/10	
S7100044														
Pico Promenade Improvements (10)														
Building & Additions		\$0	\$0	\$0	\$690	\$883.401	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$884.091
Architect		\$0	\$0 \$0	\$0		\$28,540	\$864	\$0	\$0 \$0	\$0	\$0		\$0	
Inspection & Testing		\$0	\$0 \$0	\$0 \$0		\$7,591	\$004	\$0	\$0 \$0	\$0	\$0		\$0 \$0	
Project Management		\$0	\$0 \$0	\$0 \$0		\$25,548	\$0 \$0	\$0		\$0	\$0		\$0 \$0	
Total		\$0 \$0	\$0 \$0			\$945,080	\$864	\$0 \$0		\$0 \$0	\$0 \$0		\$0 \$0	
Project Budget	\$1.018.009		φU	<b>4</b> 0	\$72,000	\$945,060	\$0 <b>0</b> 4	<b>4</b> 0	φU	φU	<b>\$</b> 0	<b>3</b> 0	φU	\$1,010,009
Less Other Funding	\$1,018,009													
Net	\$0													
	\$1,018,009													
Actual Measure S Expenditures														
Running Balance	\$0													
07400004														
S7100004														
Master Planning (11)			<b>*</b> 0	**			¢444.540	£10.000		<b>*</b> 0	**		**	C4E4 000
Consultants		\$0	\$0	\$0				\$13,320	\$0	\$0	\$0		\$0	
Printing		\$0	\$0	\$0		\$0		\$0	\$0	\$0	\$0		\$0	
Advertising		\$0	\$0	\$0		\$0		\$0	\$0	\$0	\$0		\$0	
Other Contract Services		\$0	\$0	\$0		\$0		\$200	\$0	\$0	\$0		\$0	
Architect		\$0	\$0	\$0		\$0	\$192,358	\$24,736	\$0	\$0	\$0		\$0	
Project Management		\$0	\$0	\$0		\$0	\$16,638	\$9,341	\$0	\$0	\$7,845		\$0	
Filling Fees		\$0	\$0	\$0				\$2,842	\$0	\$0	\$0		\$0	
Total		\$0	\$0	\$0	\$0	\$0	\$658,143	\$50,439	\$0	\$0	\$7,845	\$0	\$0	\$716,428
Project Budget	\$716,428													
Less Other Funding	\$0													
Net	\$716,428													
Actual Measure S Expenditures	\$716,428													
Running Balance	\$0													
S7100048														
Other Bond Related Expenses (12)														
Consultants		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,971	\$2,524	\$6,239	\$669	\$12,404
Lease/Rental		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$11,142	\$15,099	\$15,285	\$14,809	\$9,335	\$65,671
Supplies		\$0	\$0	\$0				\$0	\$0	\$0	\$0		\$0	
Legal		\$0	\$0	\$0		\$0		\$15,649	\$13,401	\$450	\$503		\$9,186	
Software License		\$0	\$0	\$0		\$0		\$1,997	\$0	\$3,565	\$0		\$0	
Advertising		\$0	\$0	\$0		\$0		\$0	\$0	\$0	\$0		\$0	
Other Contract Services		\$0	\$0	\$0			\$17,206	\$23,558	\$19.208	\$15.816	\$13.627	\$13.952	\$12,741	\$117,907
Moving Services		\$0	\$0	\$0		\$0	\$400	\$0	\$0	\$0	\$0		\$0	\$400
Project Management		\$0	\$0	\$0		\$0		\$13,179	\$11,963	\$0 \$0	\$0		\$0	
Cap Equipment		\$0	\$0	\$0		\$0	\$0	\$10,086	\$0	\$0 \$0	\$0		\$0	
Non-Cap Equipment		\$0	\$0 \$0	\$0 \$0				\$2,860	\$0 \$0	\$0	\$0		\$0	
Total		\$0	\$0 \$0	\$0			\$50,185		\$55,713	\$37,901	\$31,939		\$31,932	
Project Budget	\$609,282		\$U	<b>\$</b> 0	<b>پ</b> ۵	φ1,000	<i>4</i> 00,100	φ0 <i>1</i> ,320	<i>\$33,1</i> 13	φ31,301	<b>431,335</b>	\$11,330	φ <b>31,93</b> 2	<i>\$</i> 554,125
Less Other Funding	\$009,282													
Net	\$609,282													
	\$609,282													
Actual Measure S Expenditures	\$354,129													
Running Balance	j \$∠55,153													

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16	Combined Totals
110/0013	Buuget	04/00111101	00,001 11101	00/07 1 11/01	entree i mai	00/00111101	00/10111101	io, iii iiidi	11/12 1 11.0	12/10111101	10/14/11/10	1-#10111101	10/10	Combined Totals
S7100049														
Adv Architecture Related Exp for AA (13)														
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$0		\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0		\$45,734	-\$45,734	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0		\$0		\$0	\$0	\$0		\$0	\$0		\$0	\$0
Total		\$0				\$45,734	-\$45,734	\$0	\$0		\$0		\$0	\$0
Project Budget	\$0					¥ 10,1 0 1	<i></i>	֥	֥	÷-		÷-		+-
Less Other Funding	\$0													
Net	\$0													
Actual Measure S Expenditures	\$0													
Running Balance	\$0													
	ψυ	1												
S7100057														
Real Property Acquisition (14)														
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$18.721	\$0	\$0	\$0	\$0	\$0	\$0	\$18,721
Architect		\$0		\$0 \$0			\$0	\$0 \$0		\$0	\$0 \$0		\$0	\$0
Engineering		\$0		\$0			\$0 \$0	\$0 \$0		\$0 \$0	\$0		\$0	\$0 \$0
Inspection & Testing		\$0		\$0 \$0			\$6.336	\$0		\$0	\$0		\$0	\$6,336
Project Management		\$0					\$20,540	\$0 \$0		\$0 \$0	\$0		\$0	\$20,540
Total		\$0					\$45,597	\$0 \$0		\$0	\$0 \$0		\$0	\$45,597
Project Budget	\$45,597		φU	φU	φU	ψŪ	\$40,001	φU	φU	φU	φU	φ <b>υ</b>	φU	\$40,001
Less Other Funding	\$0													
Net	\$45,597													
Actual Measure S Expenditures	\$45,597													
Running Balance	\$0													
Running Balance	\$U													
S7100072		1										· · ·		
Campus Signage (15)														
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$303	\$0	\$0	\$0	\$0	\$0	\$303
Consultants		\$0					\$32,225	\$23,725		\$0 \$0	\$0		\$0 \$0	\$55,950
Other Contract Services		\$0		\$0 \$0			<del>\$32,223</del> \$0	\$23,725 \$187	<u>\$0</u> \$0	\$836	\$0 \$0		\$0 \$0	\$1,022
Architect		\$0		<u>\$0</u> \$0			\$0 \$0			\$030 \$0	<u> </u>		\$0 \$0	\$1,022 \$0
Building & Additions		\$0		<u>\$0</u> \$0		\$0	\$0 \$0	\$638	\$0 \$0	\$0 \$0	<del>پر</del> \$1,440		\$407,999	\$0 \$411,401
Inspection & Testing		\$0		<u>\$0</u> \$0			\$0 \$0			\$0 \$0	<u>\$1,440</u> \$0		\$407,999 \$0	\$411,401 \$0
Project Management		\$0		\$0 \$0			\$0 \$0	<del>پ</del> و \$22,953	\$0 \$0	\$0 \$0	\$0		\$0 \$27,505	\$0 \$67,106
Cap Equipment		\$0		<u>\$0</u> \$0			\$0 \$0	\$22,953 \$156,258	\$0 \$0	\$0	<u>\$8,260</u> \$0			\$67,106 \$156,258
Total		\$0 \$0					\$0 \$32,225	\$156,258 \$204,064	\$0 <b>\$0</b>		\$0 \$9,700		\$0 \$435,504	\$156,258 \$692,040
Project Budget	\$706,223		\$0	\$0	\$0	\$0	<b>⊅</b> 3∠,225	<b>⊅</b> ∠04,064	\$0	<b>\$636</b>	ə9,700	ə9,/12	ə4 <b>3</b> 5,504	<b>\$092,040</b>
Less Other Funding														
	\$0													
Net	\$706,223													
Actual Measure S Expenditures Running Balance	\$692,040 \$14,183													


Grand Total	\$7.958.606	\$14.601.366 \$10.740.621	\$8.321.918	\$20.819.624	\$8.933.245	\$617.492	\$651.441	\$878.632	\$1.287.285	\$6.814.769	\$5,870,942	\$87.495.942

## SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure AA Project Schedule As of March 31, 2016


	Project Name	Completion	20	)15	20	016	2017		2018	20	19	20	20
101	Environmental Performance - Central Plant Connections	August 2017											
102	Infrastructure & Technology - Information Technology Relocation	Completed											
103	Media and Technology Complex - Academy Site	November 2016											
104	Replacement Health/PE/Fitness/Dance Building with Central Plant	February 2017											
105	Drescher - Academic Modernization, Bookstore, Pico Promenade	June 2019											
106	Replacement Math and Science Extension Building	June 2021											
107	Madison East Wing Seismic Upgrade	September 2016	·										
108	Renovation of Corsair Stadium	Completed											
109	Career Opportunity and Advancement Center (Bundy)	Completed											
110	Malibu Center	November 2018											
111	Business & Facilities Infrastructure	On-Going											
112	Master Planning, Program Management, Overhead	On-Going											
113	Energy Efficiency Projects	On-Going											
114	Community Classroom & Facility Projects	Completed											
115	Real Property Acquisition	Completed											
116	Roadways, Walkways, Grounds, Parking Lots, and Garages	On-Going											
117	Infrastructure & Technology - Technology	On-Going											
118	Infrastructure & Technology - Utility	Completed											
119	Emergency Lighting, Fire Alarm, and Security System	On-Going											
120	Student Services	November 2018											
121	Cost of Issuance	On-Going											
				In	Plann	ing	In Con	istruc	tion				

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16	Combined Totals
AA 7100062									
Environmental Performance - Central Plant Connections (101)									
Legal		\$0	\$0	\$0		\$0	\$0	\$0	
Other Contract Services		\$0	\$0	\$49,837	\$16,239	\$0	\$0	\$0	\$66,076
Consultants		\$0	\$0	\$0	\$0	\$28	\$0	\$0	\$28
Building & Additions		\$0	\$0	\$0	\$361	\$729	\$640	\$913	\$2,644
Architect		\$0	\$385	\$148,311	\$176,897	\$36,256	\$0	\$0	\$361,849
Engineering		\$48,500	\$0	\$4,000	\$0	\$152,010	\$39,638	\$40,067	\$284,215
Inspection & Testing		\$0	\$0	\$7,688	\$0	\$0	\$0	\$0	\$7,688
Project Management		\$0	\$17,263	\$55,116	\$48,685	\$61,908	\$19,313	\$25,710	\$227,994
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$48,500	\$17,648	\$264,951	\$242,307	\$250,931	\$59,591	\$66,689	\$950,617
Project Budget	\$10,460,471								
Less Other Funding	\$0								
Net	\$10,460,471								
Actual Measure AA Expenditures	\$950,617								
Running Balance	\$9,509,854								


Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16	Combined Totals
AA 7100063									
Infrastructure & Technology - IT Relocation (102)									
Supplies		\$0	\$0	\$965	\$8,442	\$3,137	\$2,600	\$0	\$15,144
Consultants		\$0	\$0	\$0	\$0	\$408	\$0	\$3,675	\$4,083
Maintenance Contract		\$0	\$0	\$0	\$0	\$107,390	\$0	\$77,074	\$184,464
Legal		\$0	\$0		\$1,363	\$50	\$0	\$0	\$1,413
Printing		\$0	\$0	\$0	\$0	\$1,624	\$0	\$0	\$1,624
Postage		\$0	\$0	\$0	\$0	\$1,567	\$0	\$0	\$1,567
Other Contract Services		\$0	\$0	\$2,163	\$15,259	\$23,356	\$0	\$19,050	\$59,828
Moving		\$0	\$0	\$0	\$577	\$266	\$27,655	\$22,618	\$51,116
Site Improvement		\$0	\$0	\$0	\$24	\$0	\$0	\$0	\$24
Building & Additions		\$0	\$0	\$0	\$1,767,083	\$9,667,362	\$4,288,987	\$786,777	\$16,510,210
Architect		\$105,049	\$482,261	\$505,580	\$183,181	\$287,201	\$236,860	\$116,848	\$1,916,980
Engineering		\$0	\$0	\$10,037	\$11,065	\$17,147	\$19,512	\$12,222	\$69,983
Inspection & Testing		\$10,291	\$8,793	\$21,449	\$137,523	\$499,982	\$200,262	\$708	\$879,008
Project Management		\$33,460	\$76,290	\$84,991	\$331,754	\$431,730	\$297,951	\$22,978	\$1,279,153
Cap Equipment		\$0	\$0	\$0	\$29,422	\$645,830	-\$29,090	\$589,604	\$1,235,765
Non-Cap Equipment		\$0	\$0	\$0	\$18,344	\$10,852	\$277,219	-\$1,232	\$305,182
Total		\$148,800	\$567,344	\$625,185	\$2,504,035	\$11,697,901	\$5,321,956	\$1,650,321	\$22,515,542
Project Budget	\$24,392,627								
Less Other Funding	\$0								
Net	\$24,392,627								
Actual Measure AA Expenditures	\$22,515,542								
Running Balance	\$1,877,085								

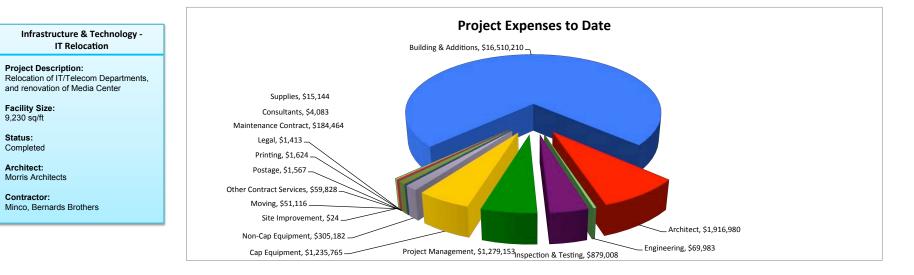

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16	Combined Totals
AA 7100061									
Media and Technology Complex - Academy Site (103)									
Consultants		\$0	\$0	\$20,675	\$12,576	\$9,488	\$7,789	\$515	\$51,042
Supplies		\$0	\$0	\$0	\$19,481	\$1,048	\$289	\$0	\$20,818
Legal		\$16,903	\$0	\$7,958	\$43,363	\$5,066	\$26,186	\$31,665	\$131,140
Other Contract Services		\$3,993	\$5,763	\$13,456	\$39,188	\$0	\$0	\$0	\$62,400
Moving Expenses		\$0	\$0	\$0	\$38,756	\$0	\$0	\$0	\$38,756
Software Support		\$0	\$0	\$0	\$1,982	\$0	\$0	\$0	\$1,982
Site Improvement		\$0	\$0	\$0	\$100,505	\$664	\$606	\$476	\$102,251
Building & Additions		\$0	\$538	\$1,498,660	\$3,543,657	\$11,820,615	\$17,734,534	\$13,493,011	\$48,091,014
Architect		\$2,097,553	\$2,508,588	\$295,753	\$265,481	\$778,015	\$517,794	\$421,117	\$6,884,300
Engineering		\$16,459	\$29,293	\$9,102	\$29,223	\$8,203	\$72,993	\$21,958	\$187,231
Inspection & Testing		\$64,905	\$27,527	\$123,842	\$235,287	\$563,746	\$1,381,801	\$447,321	\$2,844,427
Project Management		\$121,786	\$233,826	\$269,249	\$506,917	\$800,315	\$930,115	\$860,903	\$3,723,110
Cap Equipment		\$0	\$0	\$0	\$186,301	\$0	\$0	\$0	\$186,301
Non-Cap Equipment		\$0	\$0	\$0	\$10,782	\$0	\$0	\$0	\$10,782
Total		\$2,321,599	\$2,805,534	\$2,238,694	\$5,033,499	\$13,987,159	\$20,672,105	\$15,276,965	\$62,335,555
Project Budget	\$94,651,880	Received							
Less Other Funding*	\$6,835,391	\$990,441	* Other Funding So	ource:					
Net	\$87,816,489		KCRW Foundation	\$6,803,412 comm	nited, \$958,462 re	ceived			
Actual Measure AA Expenditures	\$62,335,555		Edison \$31,979.48	received					
Running Balance	\$25,480,934								




Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16	Combined Totals
AA 7100060									
Repl. Health/PE/Fitness/Dance Building with Central Plant (104)									
Consultants		\$0	\$0	\$0	\$14	\$62	\$2,304	\$51	\$2,431
Supplies		\$0	\$0	\$0	\$0	\$7,089	\$195	\$484	\$7,768
Site Improvement		\$0	\$0	\$0	\$0	\$0	\$559	\$0	\$559
Off Campus Printing		\$0	\$0	\$0	\$0	\$0	\$2,165	\$0	\$2,165
Postage		\$0	\$0	\$0	\$0	\$0	\$1,505	\$0	\$1,505
Other Contract Services		\$120	\$38	\$112	\$32,634	\$0	\$1,019	\$581	\$34,504
Building & Additions		\$0	\$0	\$0	\$817	\$4,188	\$1,623	\$4,720,127	\$4,726,754
Architect		\$256,076	\$1,568,564	\$1,790,207	\$518,973	\$177,583	\$364,853	\$261,464	\$4,937,721
Engineering		\$0	\$8,507	\$31,650	\$7,871	\$6,529	\$9,276	\$55,045	
Inspection & Testing		\$36,892	\$490	\$21,150	\$1,285	\$360	\$133,756	\$584,110	\$778,043
Project Management		\$34,968	\$113,379	\$118,783	\$94,768	\$108,528	\$463,418	\$403,585	
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$9,015	\$0	\$9,015
Total		\$328,056	\$1,690,978	\$1,961,901	\$656,362	\$304,338	\$989,689	\$6,025,446	\$11,956,771
Project Budget	\$51,989,845								
Less Other Funding*	\$11,603,383		Other Funding So	ource:					
Net	\$40,386,462	I	Measure S \$11,603	3,383 allocated					
Actual Measure AA Expenditures	\$11,956,771								
Running Balance	\$28,429,691								

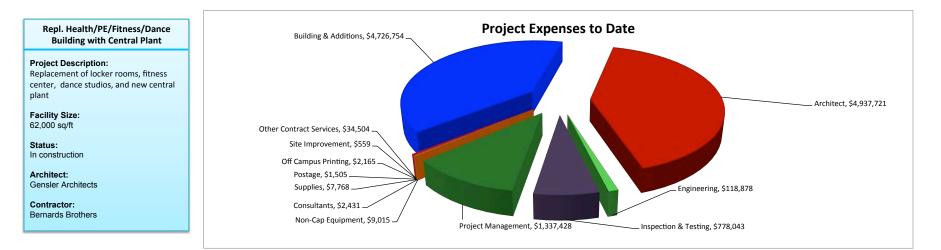

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16	Combined Totals
AA 7100065									
Drescher - Academic Modernization, Bookstore, Pico Promenade (105)									
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Site Acquisition		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$0	\$5,082	\$0	\$0	\$0	\$0	\$5,082
Total		\$0	\$0	\$5,082	\$0	\$0	\$0	\$0	\$5,082
Project Budget	\$2,258,878								
Less Other Funding	\$0								
Net	\$2,258,878								
Actual Measure AA Expenditures	\$5,082								
Running Balance	\$2,253,796								
AA 7100090									
Replacement Math and Science Extension Building (106)									
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Site Acquisition		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$0	\$0	\$0	\$4,950	\$0	\$0	\$4,950
Total		\$0	\$0	\$0	\$0	\$4,950	\$0	\$0	\$4,950
Project Budget	\$80,484,336								
Less Other Funding	\$40,396,336		* Other Funding Se						
Net	\$40,088,000		Measure U \$308,3	36 allocated					
Actual Measure AA Expenditures	\$4,950		State of California	\$40,088,000 pend	ling				
Running Balance	\$40,083,050								

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16	Combined Totals
AA 7100047									
Madison East Wing Seismic Upgrade (107)									
Consultants		\$0	\$0			\$135	\$28	\$0	\$163
Off Campus Printing		\$0	\$0		\$0	\$0	\$285	\$0	\$285
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$364	\$997	\$0	\$0	\$1,328	\$474	\$3,163
Building & Additions		\$0	\$656			\$4,248	\$6,030,371	\$4,343,534	\$10,691,452
Architect		\$76,073	\$398,050			\$57,480	\$199,100	\$113,328	\$1,460,065
Engineering		\$0	\$0	\$10,707		\$0	\$13,792	\$19,177	\$44,454
Inspection & Testing		\$0	\$19,848	\$16,752	\$3,036	\$5,851	\$676,323	\$255,507	\$977,318
Project Management		\$5,557	\$128,878			\$118,242	\$494,874	\$353,383	\$1,280,952
Cap Equipment		\$0	\$0	\$30,603	\$0	\$0	\$0	\$0	\$30,603
Non-Cap Equipment		\$0	\$0	\$71,827		\$0	\$0	\$0	\$81,614
Total		\$81,630	\$547,796	\$1,106,691	\$146,492	\$185,956	\$7,416,101	\$5,085,403	\$14,570,069
Project Budget	\$23,550,625	5							
Less Other Funding	\$0								
Net	\$23,550,625	5							
Actual Measure AA Expenditures	\$14,570,069	9							
Running Balance	\$8,980,556	3							



Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16	Combined Totals
AA 7100068		[]						,,	
Renovation to Corsair Stadium (108)		i							(
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0		\$0	\$0	\$0		\$0	
Architect		\$0		\$0	\$0	\$0			
Engineering		\$0		\$0	\$0	\$0		\$0	
Inspection & Testing		\$0		\$0 \$0	\$0	\$0		\$0	
Project Management		\$0		\$0	\$0	\$0	\$0		
Total		\$0		\$0	\$0	\$0	\$0		
Project Budget	\$35,299	<u> </u>	400,200		ψU	ψŪ			
Less Other Funding	\$0								
Net	\$35,299								
Actual Measure AA Expenditures	\$35,299								
Running Balance	\$0	1							
Ranning Balance	ψυ								
AA 7100067, 7100152, 7100155, 7100157		· · · · · · · · · · · · · · · · · · ·	r	r					
Business & Facilities Infrastructure (111)									·
		\$0		0.0	£1.402	\$4,840	\$0	0.2	\$6,333
Supplies Service Fee		\$0	\$0 \$0	\$0 \$0	\$1,493 \$12,885	\$4,840 \$0	\$0 \$0		
Consultants						\$0 \$14		\$0	
		\$0 \$0	\$0	\$0	\$0	\$14		\$0 \$0	\$22 \$1,366
Maintenance Contract		\$0	\$0 \$0	\$0 \$75	\$0 \$0	\$1,366	\$0 \$0	\$0 \$1,105	\$1,300
Legal			\$0			\$375			
Software License		\$0 \$0		\$0 \$6,988	\$0 \$750	\$375		\$0 \$0	\$375 \$16,236
Other Contract Services									
Moving Services		\$0		\$0	\$395	\$0	\$0	\$0	
Building & Additions		\$0		\$198,667	\$200,585	\$284,668	\$0	\$0	
Architect		\$0 \$0	\$0	\$80,626	\$170,132	\$37,906 \$9,735		\$0	
Engineering				\$0	\$3,705		\$6,840	\$0 \$0	
Inspection & Testing		\$0		\$8,142	\$10,938	\$10,500	\$0		\$29,580
Project Management		\$0 \$0	\$3,073	\$154,904	\$87,291	\$139,821	\$3,571	\$0	
Cap Equipment				\$0	\$35,892	\$80,090	\$0	\$0	
Non-Cap Equipment		\$0	\$89,204	\$0	\$84,590	\$193,782		\$0	
Total		\$0	\$133,238	\$449,401	\$608,656	\$763,095	\$12,628	\$1,105	\$1,968,124
Project Budget	\$1,968,124								
Less Other Funding	\$0								
Net	\$1,968,124								
Actual Measure AA Expenditures	\$1,968,124								
Running Balance	\$0								
AA 7100004									L
Master Planning, Program Management, Overhead (112)									L
Supplies		\$0		\$0	\$0	\$0		\$0	\$0
Architect		\$0		\$0	\$0	\$0		\$1,791	\$1,791
Project Management		\$0	\$0	\$0	\$0	\$76,015		\$0	\$76,165
Cap Equipment		\$0		\$0	\$0	\$0		\$0	
Non-Cap Equipment		\$0		\$0	\$0	\$0		\$0	
Total		\$0	\$0	\$0	\$0	\$76,015	\$150	\$1,791	\$77,956
Project Budget	\$750,000								
Less Other Funding	\$0	l							
Net	\$750,000	i -							
		(							
Actual Measure AA Expenditures	\$77,956	1							

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16	Combined Totals
· · · · · · · · · · · · · · · · · · ·									
AA 7100154									
Energy Efficiency Projects (113)									
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	
Building & Additions		\$0	\$0	\$189	\$2,108,853	\$990,389	-\$97,621	\$0	
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	
Inspection & Testing		\$0	\$0	\$0	\$4,020	\$0	\$10,118	\$0	
Project Management		\$0	\$0	\$0	\$0	\$0	\$825	\$0	
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	
Total		\$0	\$0	\$189	\$2,112,873	\$990,389	-\$86,678	\$0	\$3,016,773
Project Budget	\$3,508,088								
Less Other Funding	\$491,315		* Other Funding S	ource:					
Net	\$3,016,773		DWP \$18,715.00 i	received					
Actual Measure AA Expenditures	\$3,016,773		SCE \$446,519.77	received					
Running Balance	\$0		Gas Co. \$26,080 I	received					
	· · · ·								
AA 7100064									
Community Classroom & Facility Projects (114)									
Supplies		\$0	\$0	\$0	\$124	\$0	\$0	\$0	\$124
Legal		\$0	\$0	\$1,867	\$1,418	\$0	\$0	\$0	
Other Contract Services		\$0	\$3,720	\$1,869	\$0	\$0	\$0	\$0	
Building & Additions		\$0	\$434,578	\$1,369,441	\$408,696	-\$1,003	\$0	\$0	
Architect		\$0	\$263,833	\$48,120	\$1,318	\$0	\$0	\$0	
Engineering		\$0	\$3.220	\$3,143	\$0	\$0	\$0	\$0	\$6,363
Inspection & Testing		\$0	\$41,002	\$80,885	\$1,495	\$0	\$0	\$0	
Project Management		\$135	\$117,247	\$143,780	\$27,570	\$0	\$0	\$0	
Non-Cap Equipment		\$0	\$0	\$209,726	\$0	\$0	\$0	\$0	
Total		\$135	\$863,599	\$1,858,831	\$440,621	-\$1,003	\$0	\$0	
Project Budget	\$3,162,183			, , ,	1 .7.5	,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,			1.1, 2.7, 2.2
Less Other Funding	\$0								
Net	\$3.162.183								
Actual Measure AA Expenditures	\$3,162,183								
Running Balance	\$0								
- J	1								
AA 7100057									
Real Property Acquisition (115)									
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$39	\$7.000	\$0	\$15,800	\$0	\$0	
Site Acquisition		\$1,739,979	\$4,001,204	\$9,022,207	\$0	\$0	\$0	\$0	
Inspection & Testing		\$8.689	\$7.986	\$0	\$0	\$0	\$0	\$0	
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$0	
Total		\$1.748.667	\$4,009,228	\$9,029,207	\$0	\$15,800	\$0	\$0	
Project Budget	\$14.802.902	ψ1,1 <del>4</del> 0,007	ψ-1,000,220	<i>\\</i> ,\\ <b>22</b>	ψυ	ų 10,000	ψυ	ψυ	¥14,002,002
Less Other Funding	\$0								
Net	\$14,802,902								
Actual Measure AA Expenditures	\$14,802,902								
Running Balance	\$0								
	ψ0								

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16	Combined Totals
AA 7100058, 7100151, 7100156, 7100059									
Roadways, Walkways, Grounds, Parking Lots, and Garages (116)									
Supplies		\$0	\$0	\$0	\$0	\$4,616	\$0	\$0	
Legal		\$0	\$0	\$0	\$125	\$0	\$0	\$0	
Consultants		\$0	\$0	\$0	\$48,090	\$5,018	\$0	\$0	
Other Contract Services		\$218	\$770	\$122	\$25,249	\$0	\$0	\$0	\$26,358
Building & Additions		\$185,345	\$6,731	\$113,784	\$321,603	\$975,401	\$0	\$0	
Architect		\$0	\$0	\$0	\$103,569	\$19,225	\$1,240	\$0	
Engineering		\$0	\$0	\$0	\$1,095	\$1,445	\$0	\$0	
Inspection & Testing		\$13,380	\$7,865	\$13,553	\$20,126	\$42,865	\$0	\$0	
Project Management		\$24,404	\$12,439	\$21,945	\$54,095	\$104,943	\$1,411	\$0	
Total		\$223,347	\$27,804	\$149,403	\$573,951	\$1,153,512	\$2,652	\$0	\$2,130,670
Project Budget	\$7,210,375								
Less Other Funding	\$4,675,000		* Other Funding Se	ource:					
Net	\$2,535,375		Measure S \$4,675	,000 allocated					
Actual Measure AA Expenditures	\$2,130,670								
Running Balance	\$404,705								
AA 7100069									
Infrastructure & Technology - Technology (117)									
Software		\$0	\$0	\$0	\$0	\$0	\$218	\$0	\$218
Supplies		\$0	\$0	\$13,646	\$7,587	\$0	\$16,966	\$0	
Maintenance Contract		\$0	\$9,472	\$46,300	\$210,581	\$18,944	\$42,415	\$9,472	\$337,186
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$49,589	\$0	\$49,589
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Cap Equipment		\$0	\$207.423	\$33,063	\$576,294	\$0	\$1,145,668	\$0	\$1,962,449
Non-Cap Equipment		\$0	\$0	\$42,827	\$500	\$0	\$3,447	\$0	\$46,775
Total		\$0	\$216,896	\$135,838	\$794,963	\$18,944	\$1,258,304	\$9,472	\$2,434,417
Project Budget	\$2,434,417			· / I	. , .				. , ,
Less Other Funding	\$0								
Net	\$2,434,417								
Actual Measure AA Expenditures	\$2,434,417								
Running Balance	\$0								
5									
AA 7100150									
Infrastructure & Technology - Utility (118)									
Sofeware License		\$0	\$12,000	\$0	\$0	\$0	\$0	\$0	\$12,000
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0 \$0
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	
Inspection & Testing		\$0		\$0	\$0	\$0	\$0	\$0	
Project Management		\$0	\$3,240	\$0 \$0	\$0	\$0 \$0	\$0	\$0	
Cap Equipment		\$0	\$0	\$7,534	\$0	\$0 \$0	\$0	\$0	
Non-Cap Equipment		\$0	\$0	\$0 \$0	\$0	\$0 \$0	\$0	\$0	
Total		\$0 \$0		\$7,534	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	
Project Budget	\$27,753		\$20,219	φ1,034	\$U	\$U	φU	<b>Φ</b> 0	φ21,753
Less Other Funding	\$27,753								
Net	\$0								
Actual Measure AA Expenditures	\$27,753								
	\$27,753								
Running Balance	\$0								

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16	Combined Totals
AA 7100153									
Emergency Lighting, Fire Alarm, and Security System (119)									1
Supplies		\$0	\$0	\$0	\$0	\$2,348	\$0	\$0	
Consultants		\$0	\$0	\$0	\$0	\$0	\$16	\$0	
Telecom Fee		\$0	\$0	\$0	\$0	\$0	\$800	\$0	
Maintenance Contract		\$0	\$0	\$648	\$0	\$39,700	\$0	\$2,700	\$43,048
Software Suppoert		\$0	\$0	\$24,765	\$0	\$106,367	\$0	\$2,232	
Other Contract Services		\$0	\$0	\$0	\$0	\$47,695	\$0	\$4,643	\$52,337
Building & Additions		\$0	\$0	\$0	\$0	\$110	\$2,648,866	\$961,982	\$3,610,958
Architect		\$0	\$0	\$0	\$0	\$0	\$18,925	\$0	\$18,925
Enginnering		\$0	\$0	\$0	\$0	\$211,030	\$389,013	\$111,980	\$712,023
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$41,100	\$41,100
Project Management		\$0	\$0	\$0	\$0	\$51,008	\$52,044	\$63,445	\$166,496
Cap Equipment		\$0	\$0	\$0	\$0	\$89,415	\$0	\$5,871	\$95,286
Non-Cap Equipment		\$0	\$0	\$6,087	\$0	\$392,586	\$8,348	\$0	\$407,022
Total		\$0	\$0	\$31,500	\$0	\$940,259	\$3,118,012	\$1,193,953	\$5,283,725
Project Budget	\$9,570,794								
Less Other Funding	\$0								
Net	\$9,570,794								
Actual Measure AA Expenditures	\$5,283,725								
Running Balance	\$4,287,069								
AA									
Cost of Issuance (121)									
Cost of Issuance		\$0	\$0	\$0	\$0	\$0	\$285,000	\$0	
Total		\$0	\$0	\$0	\$0	\$0	\$285,000	\$0	\$285,000
Project Budget	\$500,000								
Less Other Funding	\$0								
Net	\$500,000								
Actual Measure AA Expenditures	\$285,000								
Running Balance	\$215,000								
			<u> </u>	<u> </u>	<u> </u>				
Grand Total		\$4,900,734	\$10,935,584	\$17,864,407	\$13,113,759	\$30,388,248	\$39,049,510	\$29,311,146	\$145,563,387

## SMC Bond Program Contractor List as of 3-31-2016

Student Services (Measure U #0, Measure S #9, Measure AA #120): Architect – Steinberg Architects, Morris Architects Contractor – Minco Engineering – IVA, Cogent Energy Engineering, XL Fire Inspection & Testing – Geo Labs, BTC Labs - Vertical V, Peak Survey, LPI Project Management – LPI
Replacement Health/PE/Fitness/Dance Building (Measure S #4, Measure AA #104): Architect – Gensler Architects Contractor – Bernards Brothers Engineering – IVA, Glumac

Inspection & Testing – Geo Labs, Ellis Environmental, Twining, Rango Inc. Project Management – LPI

Early Childhood Development (Measure S #5): Architect – Carde Ten Architects Consultant – Child Educational Center Contractor – N/A Engineering – N/A Inspection & Testing – Geo Labs Project Management – LPI

Malibu Site (Measure S #6, Measure AA #110): Architect – Quatro Design Group Contractor – N/A Consultant – m2 Strategic, Parker Environmental Engineering – Ensitu Services Inspection & Testing – Peak Surveys, Ellis Environmental, JL Inspection Project Management – LPI

Energy Efficiency Projects (Measure S #7, Measure AA #113): Architect – N/A Contractor – Compass Energy Solutions, Johnson Controls Engineering – Compass Energy Solutions, Johnson Controls Inspection & Testing – Ellis Environmental

Environmental Performance (Measure AA #101): Architect – Kishimoto Architects Contractor – SJ Amoroso Construction Engineering – P2S Engineering Inspection & Testing – Cannon, Peak Surveys Project Management – LPI Information Technology Relocation (Measure AA #102): Architect – Morris Architects Contractor – Minco, Bernards Brothers Engineering – IVA, P2S Engineering Inspection & Testing – Cannon, Peak Surveys, Geo Labs, Ellis Environmental, Twining, JL Inspection, Rango Inc. Project Management – LPI Media and Technology Complex (Measure AA #103): Architect - Clive Wilkinson Architects, Morris Architects Contractor – H.B. Parkco Construction, Fast Track Construction, **CW** Driver Consultant – EEG Services Engineering – IVA, P2S Engineering Inspection & Testing – Twining, Geo Labs, BTC Labs – Vertical V. **JL** Inspection, EEG Services, Ellis Environmental, Rango Inc. Project Management – LPI Madison East Wing Seismic Upgrade (Measure AA #107): Architect - DLR Group - WWCOT, LPI Contractor – Trimax, Bernards Brothers Engineering – IVA, Glumac Inspection & Testing – Twining, Peak Surveys, LPI, All Group Engineering, EEG Services, Ellis Environmental Project Management – LPI Business & Facilities Infrastructure (Measure AA #111): Architect – LPI, Gwynne Pugh Urban Studio Contractor – REC+S, Inc., Omega Construction. Concept Consultant, Inc. Engineering – N/A Inspection & Testing – Ellis Environmental, JL Inspection Project Management – LPI Community Classroom & Facility Project (Measure AA #114) Architect – Morris Architects Contractor – Waisman Construction, Spinitar, Trimax Engineering – IVA Inspection & Testing – LPI, Twining Project Management – LPI

Satellite Campus Parking Facilities and Roadway Improvements (Measure S #8) Architect – N/A Contractor – N/A Engineering – MK Engineering Group Inspection & Testing – N/A Project Management – LPI

Roadways, walkways, Grounds, Parking Lots, and Garages (Measure AA #116) Architect – LPI, DLR Group - WWCOT Contractor – Trimax, Pub Construction Consultant – Walker Parking Engineering – MK Engineering Inspection & Testing – Ellis Environmental, Peak Surveys, LPI Project Management – LPI

Emergency Lighting, Fire Alarm, and Security System (Measure AA #119) Architect – N/A Contractor – Red Hawk Fire and Security, Nexus Consultant – IVA Engineering – MDC Engineers Inspection & Testing – Rango Inc. Project Management – LPI

Signage Safety/Information (Measure S #15) Architect – N/A Contractor – Sign Excellence Consultant – APCO Engineering – N/A Inspection & Testing – N/A Project Management – LPI
